

micro.P3.express

minimalist project management system for micro-projects

Draft




This slide deck is in the public domain and everyone can adapt and use it for commercial or non-commercial purposes without asking for permission.

(CC0 1.0 Universal Public Domain Dedication)

micro.P3.express can be adapted and used by everyone for commercial and non-commercial purposes without asking for permission, as long as appropriate attribution is given.

(CC-BY International License)

- 
- ① High-level overview
 - ② Full review
 - ③ NUPP
 - ④ Tailoring

Mega-Projects

Small, Medium, and Large Projects

Micro-Projects

Approximately 1 to 7 people
Done in organizations of any size

P3.express

micro.P3.express

Mega-Projects

Small, Medium, and Large Projects


Micro-Projects

Approximately 1 to 7 people
Done in organizations of any size

P3.express

micro.P3.express

Open, minimalist
project management systems

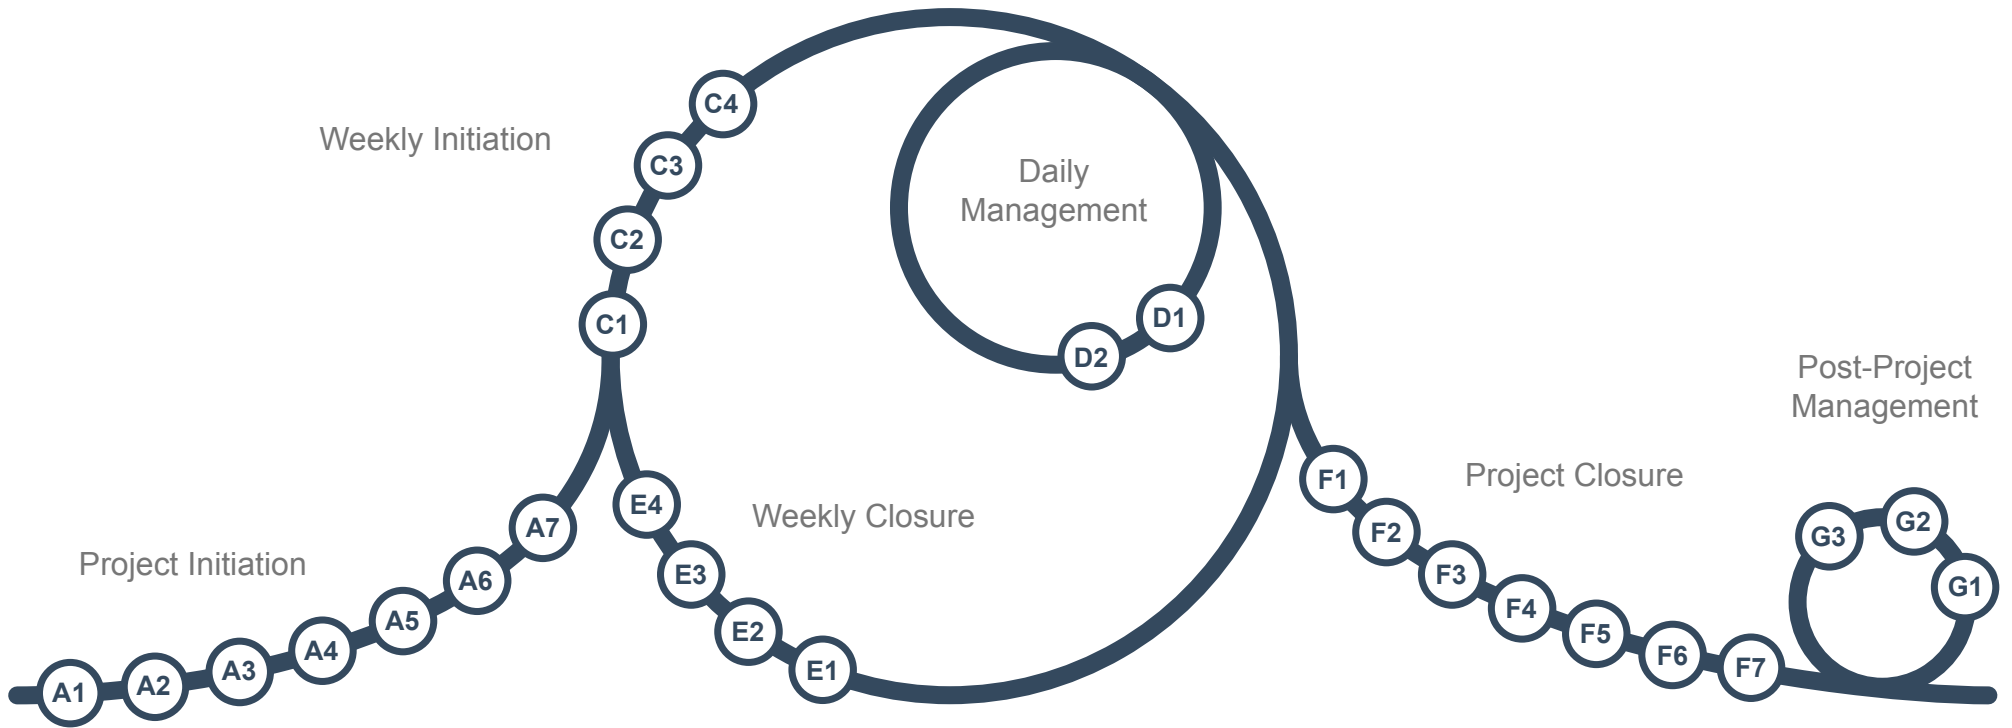

Weekly Initiation

Daily Management


Post-Project Management

Project Initiation

Weekly Closure

Project Closure


The Process

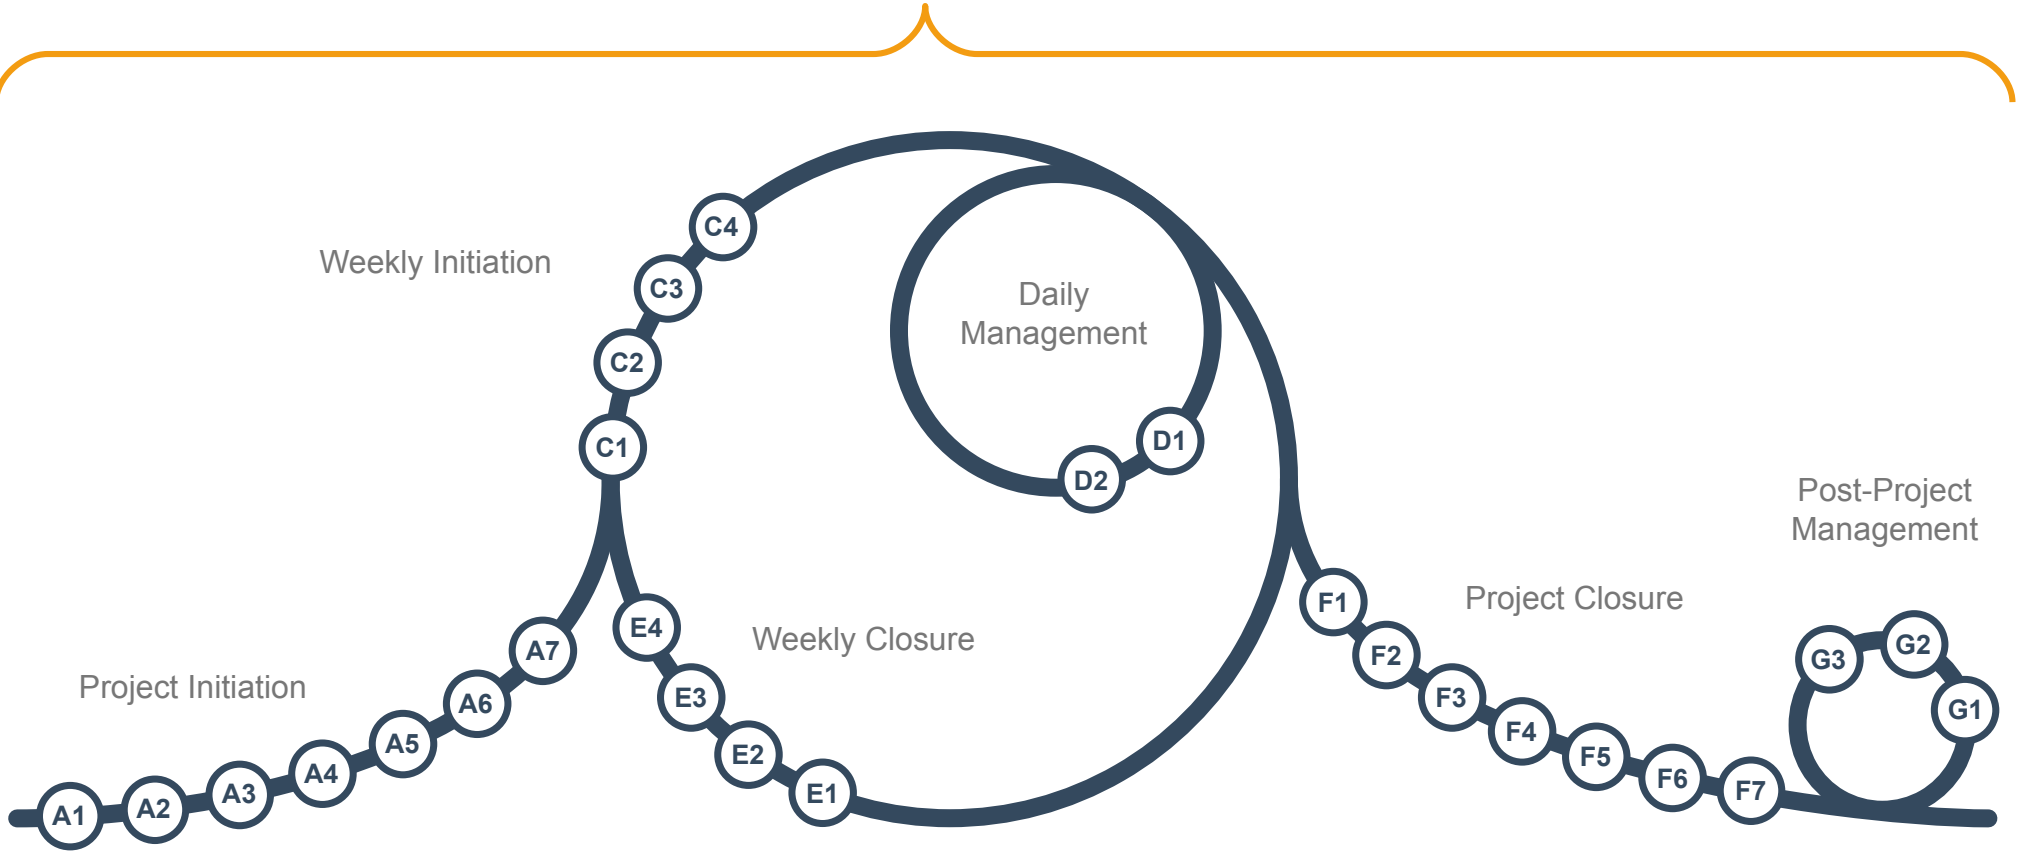




27 Management Activities


6 Activity Groups

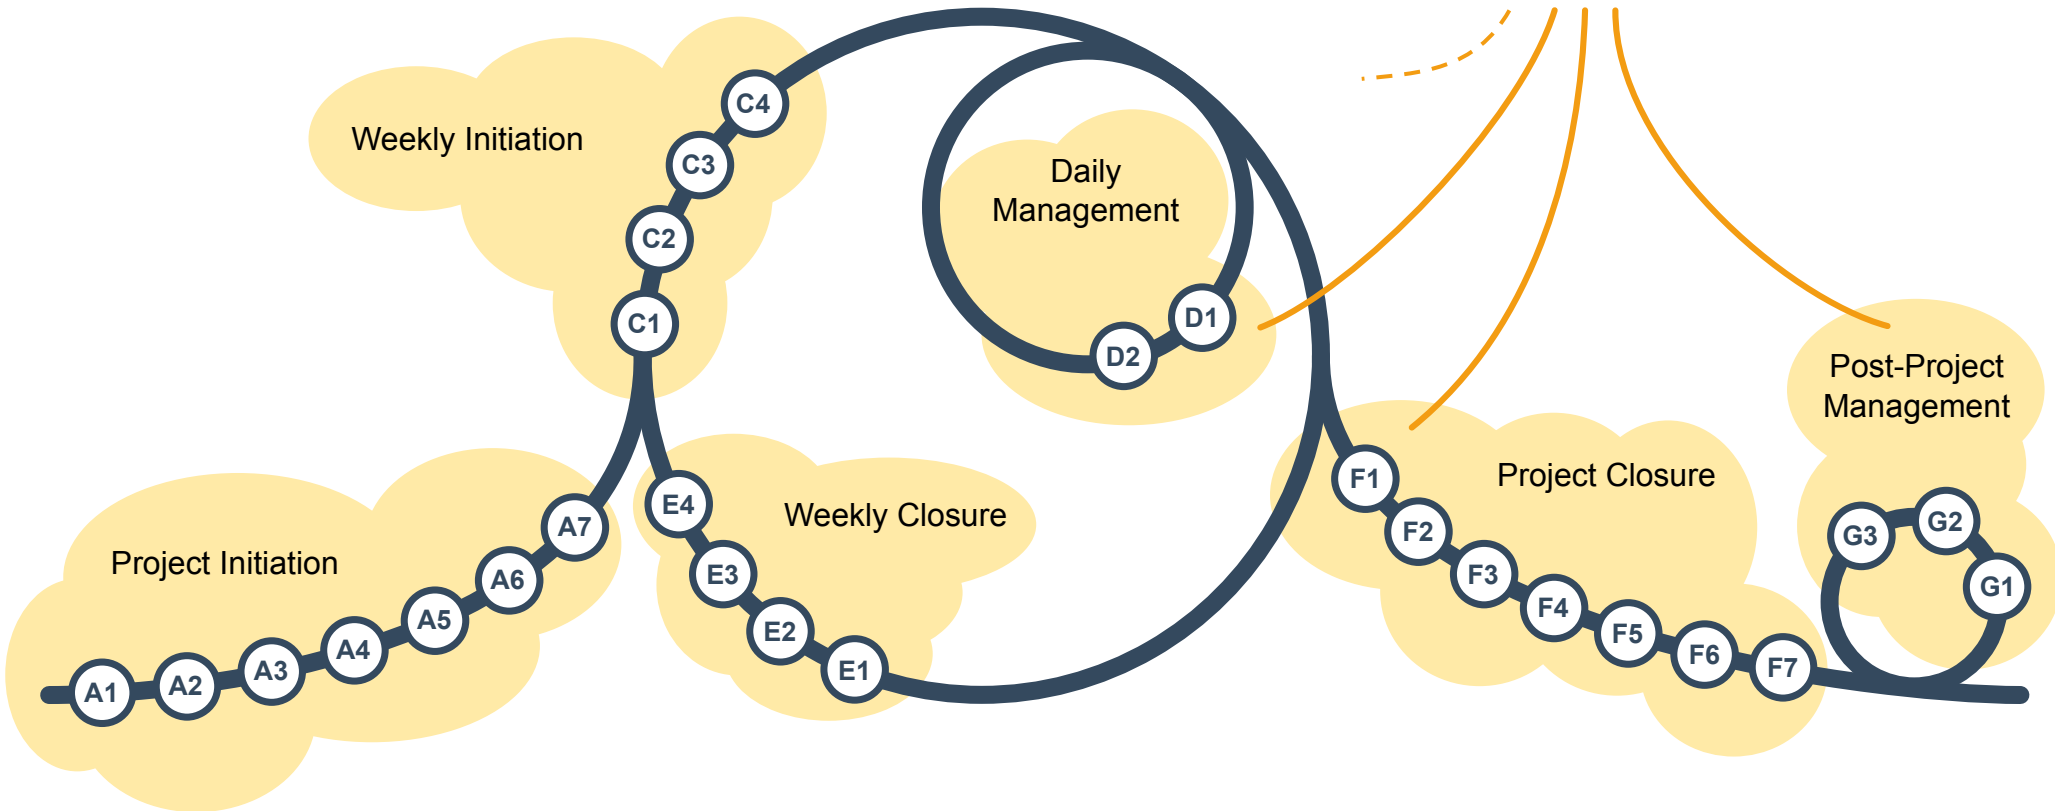


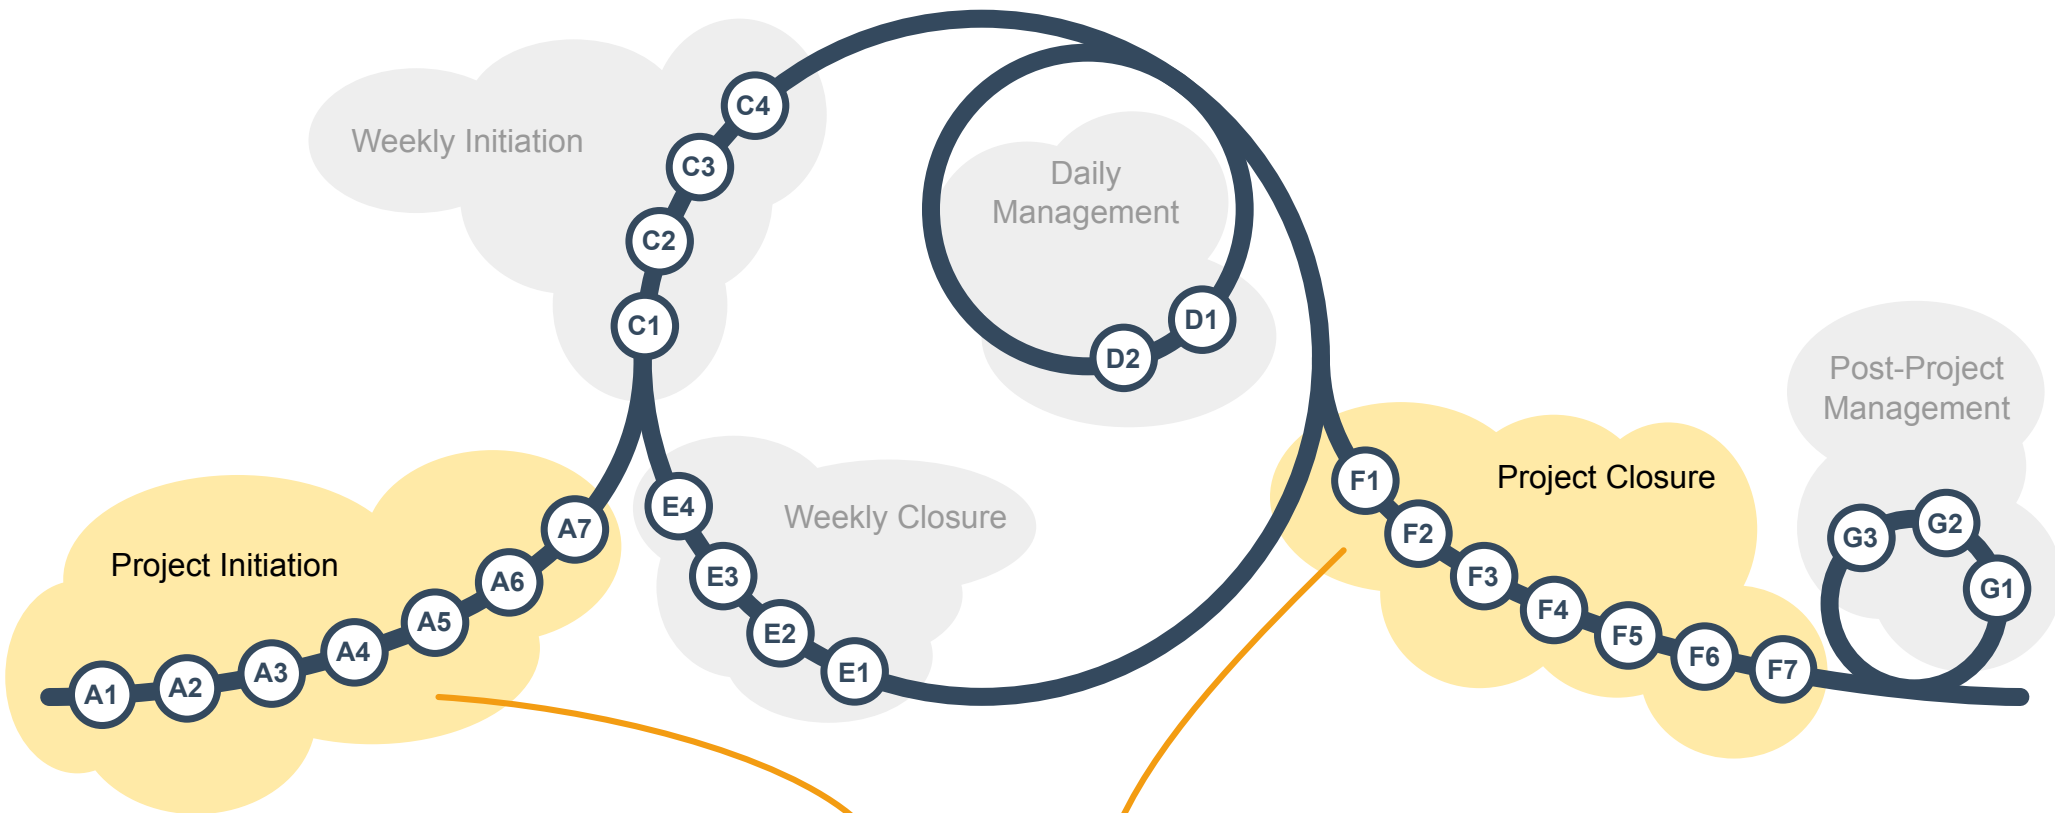

2 Linear Activity Groups

4 Cyclic Activity Groups

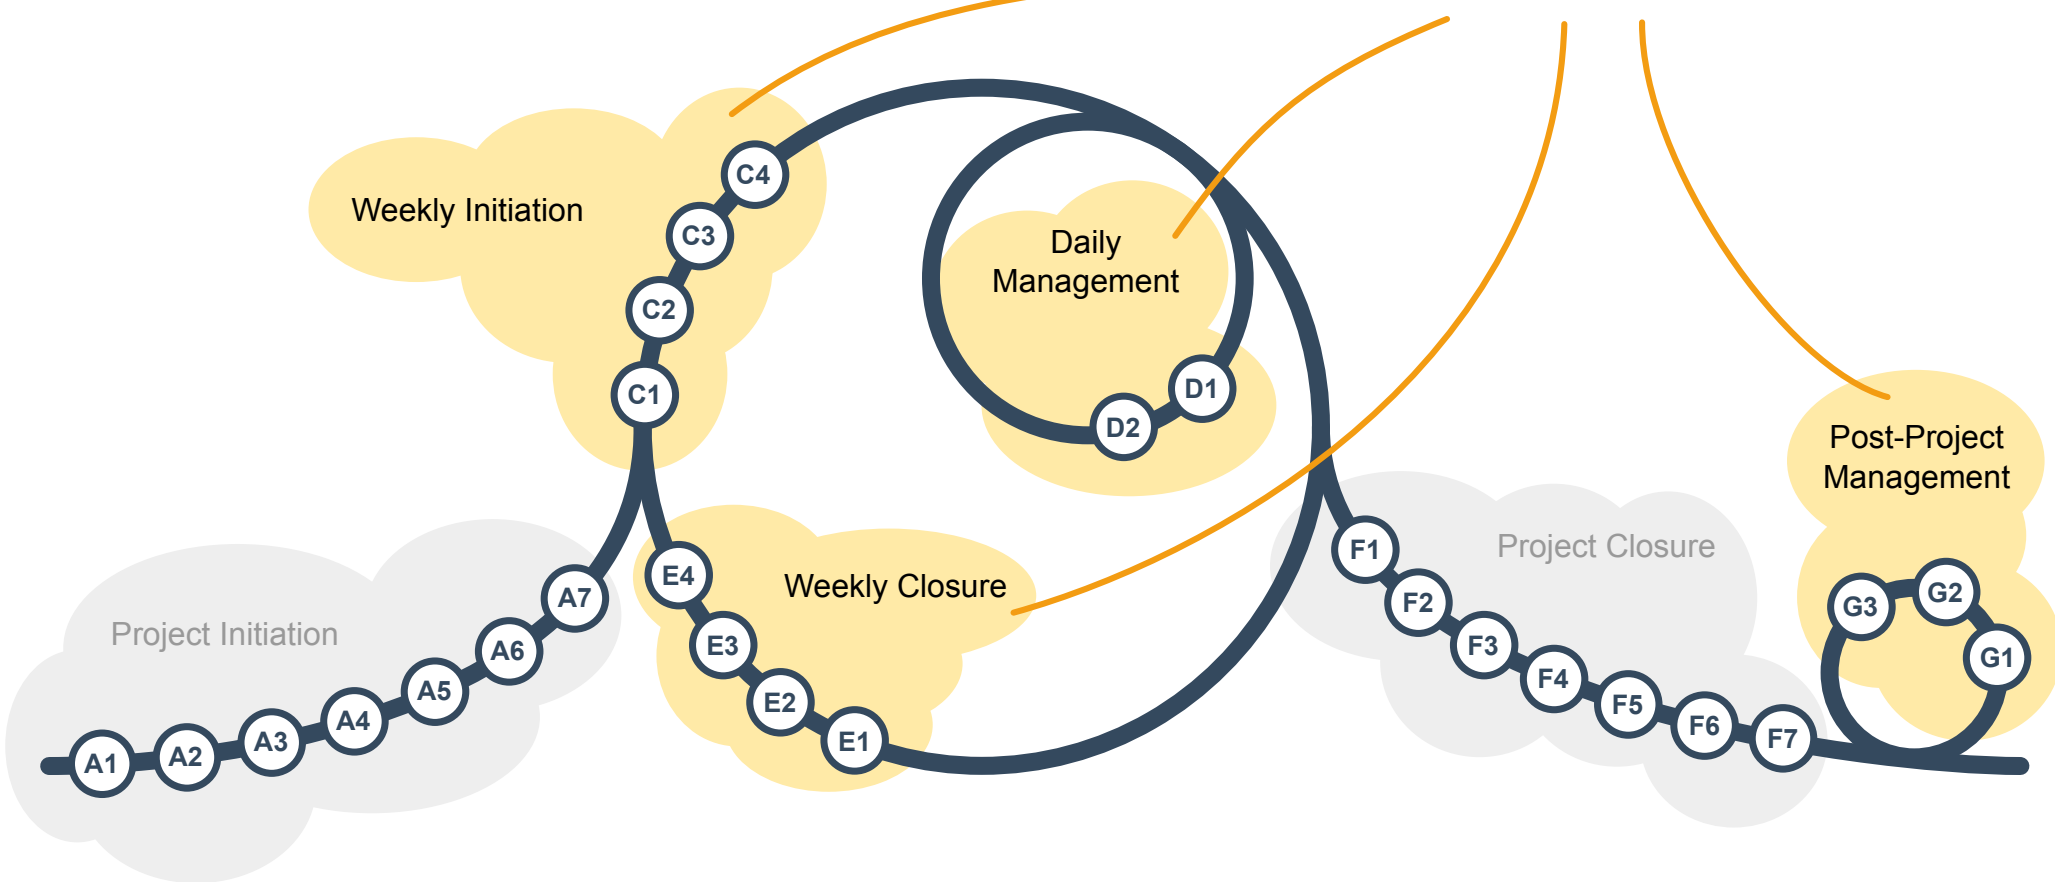

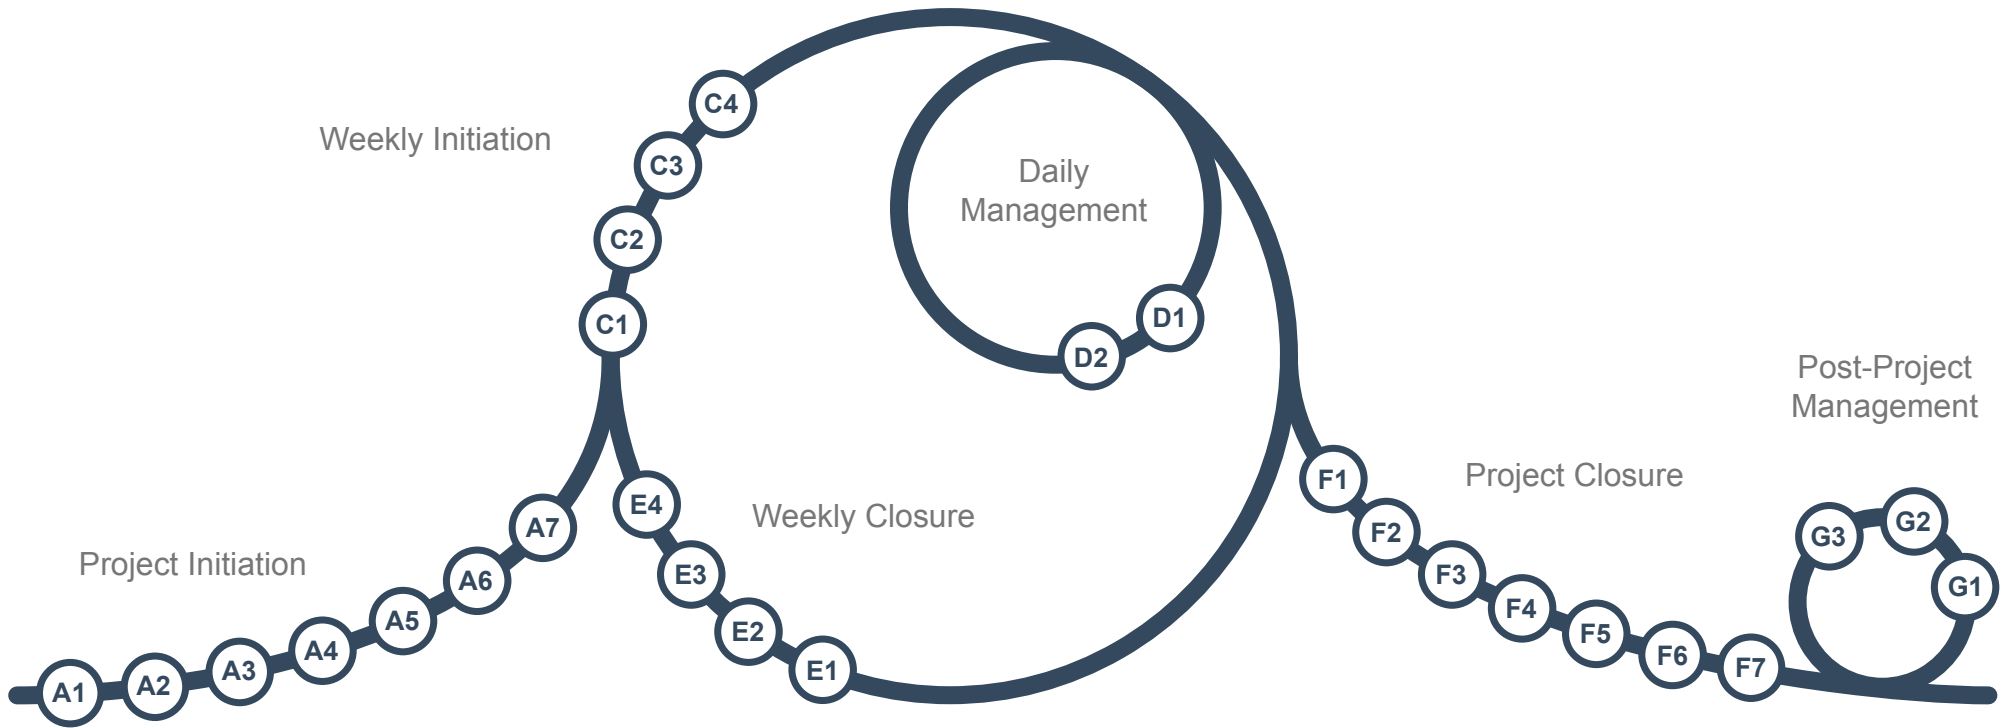

Weekly Initiation

Daily Management

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E3

E2

E1

E4

F1

F2

F3

F4

F5


F6


F7


G3


G2


G1

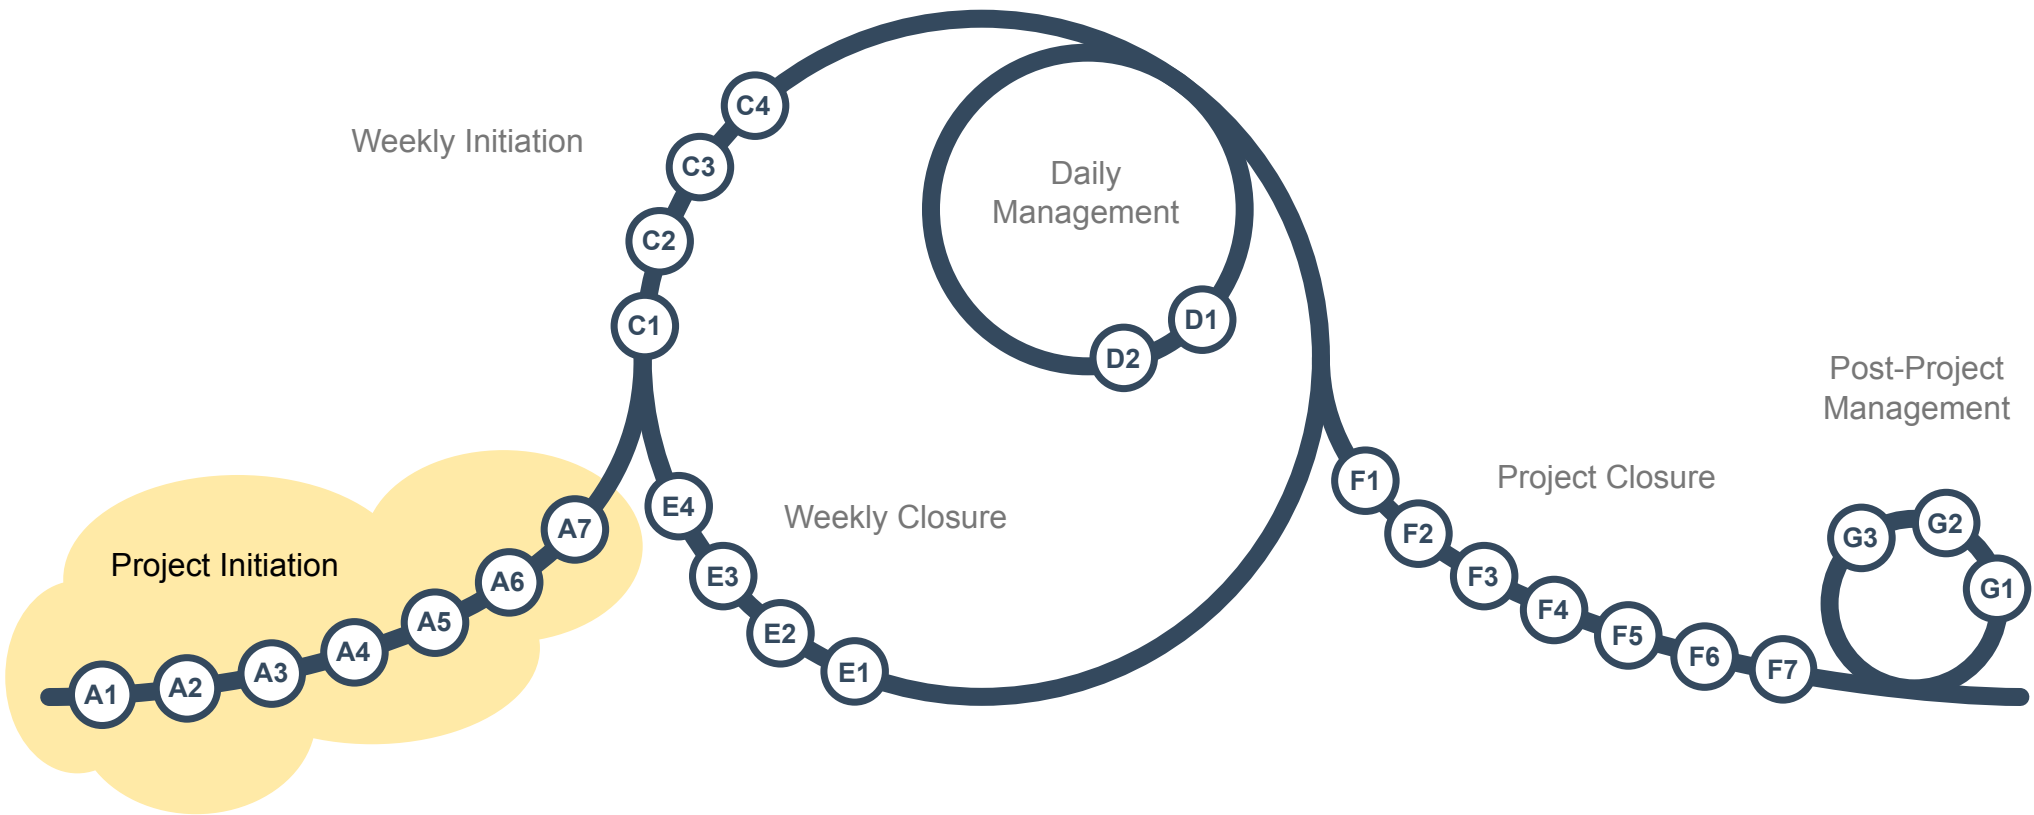


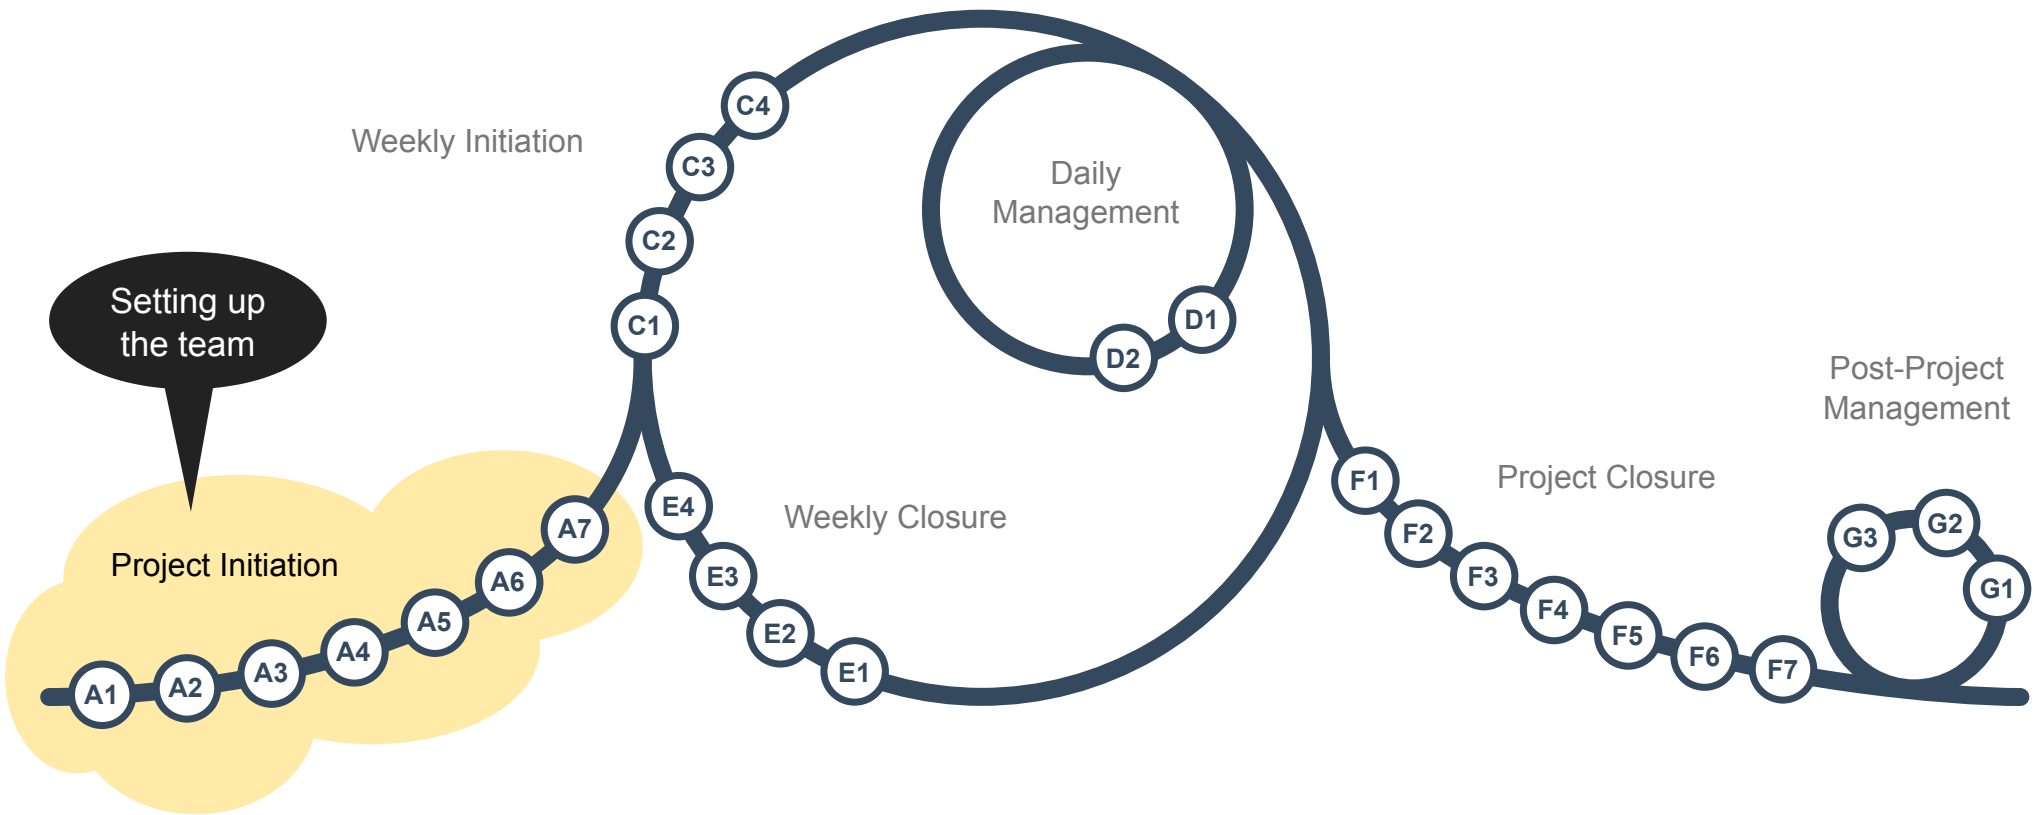

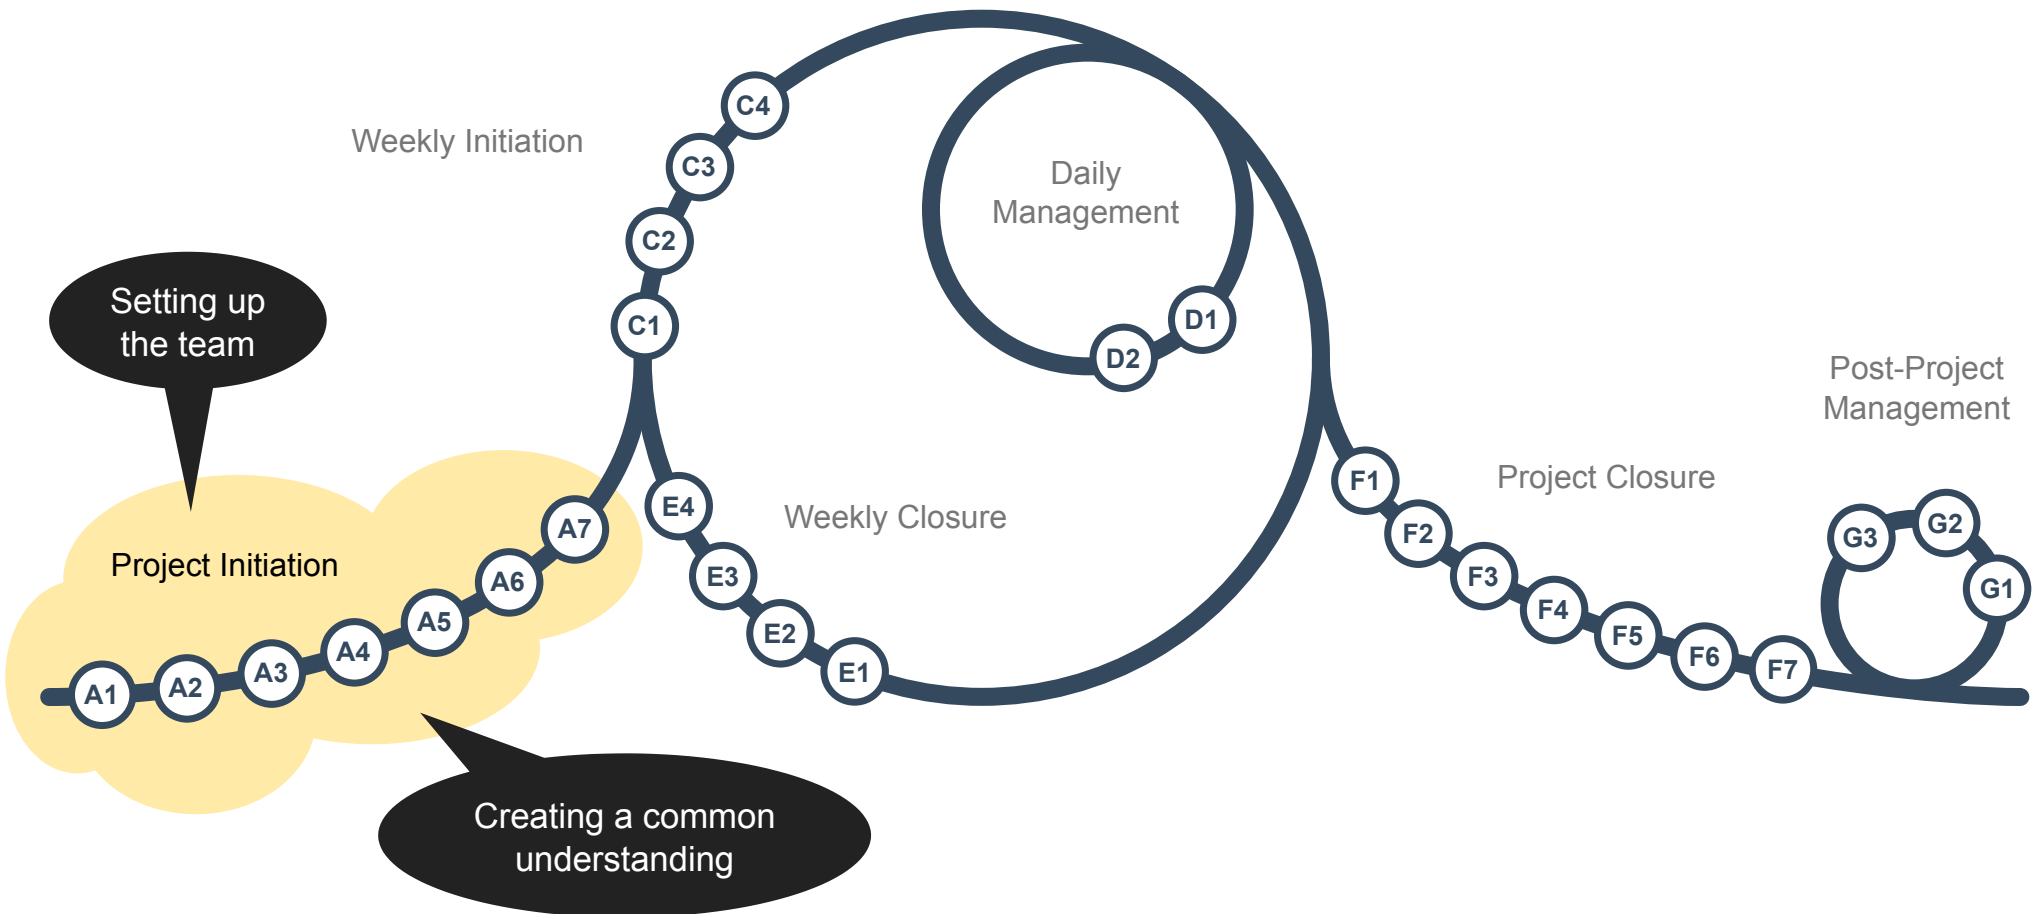

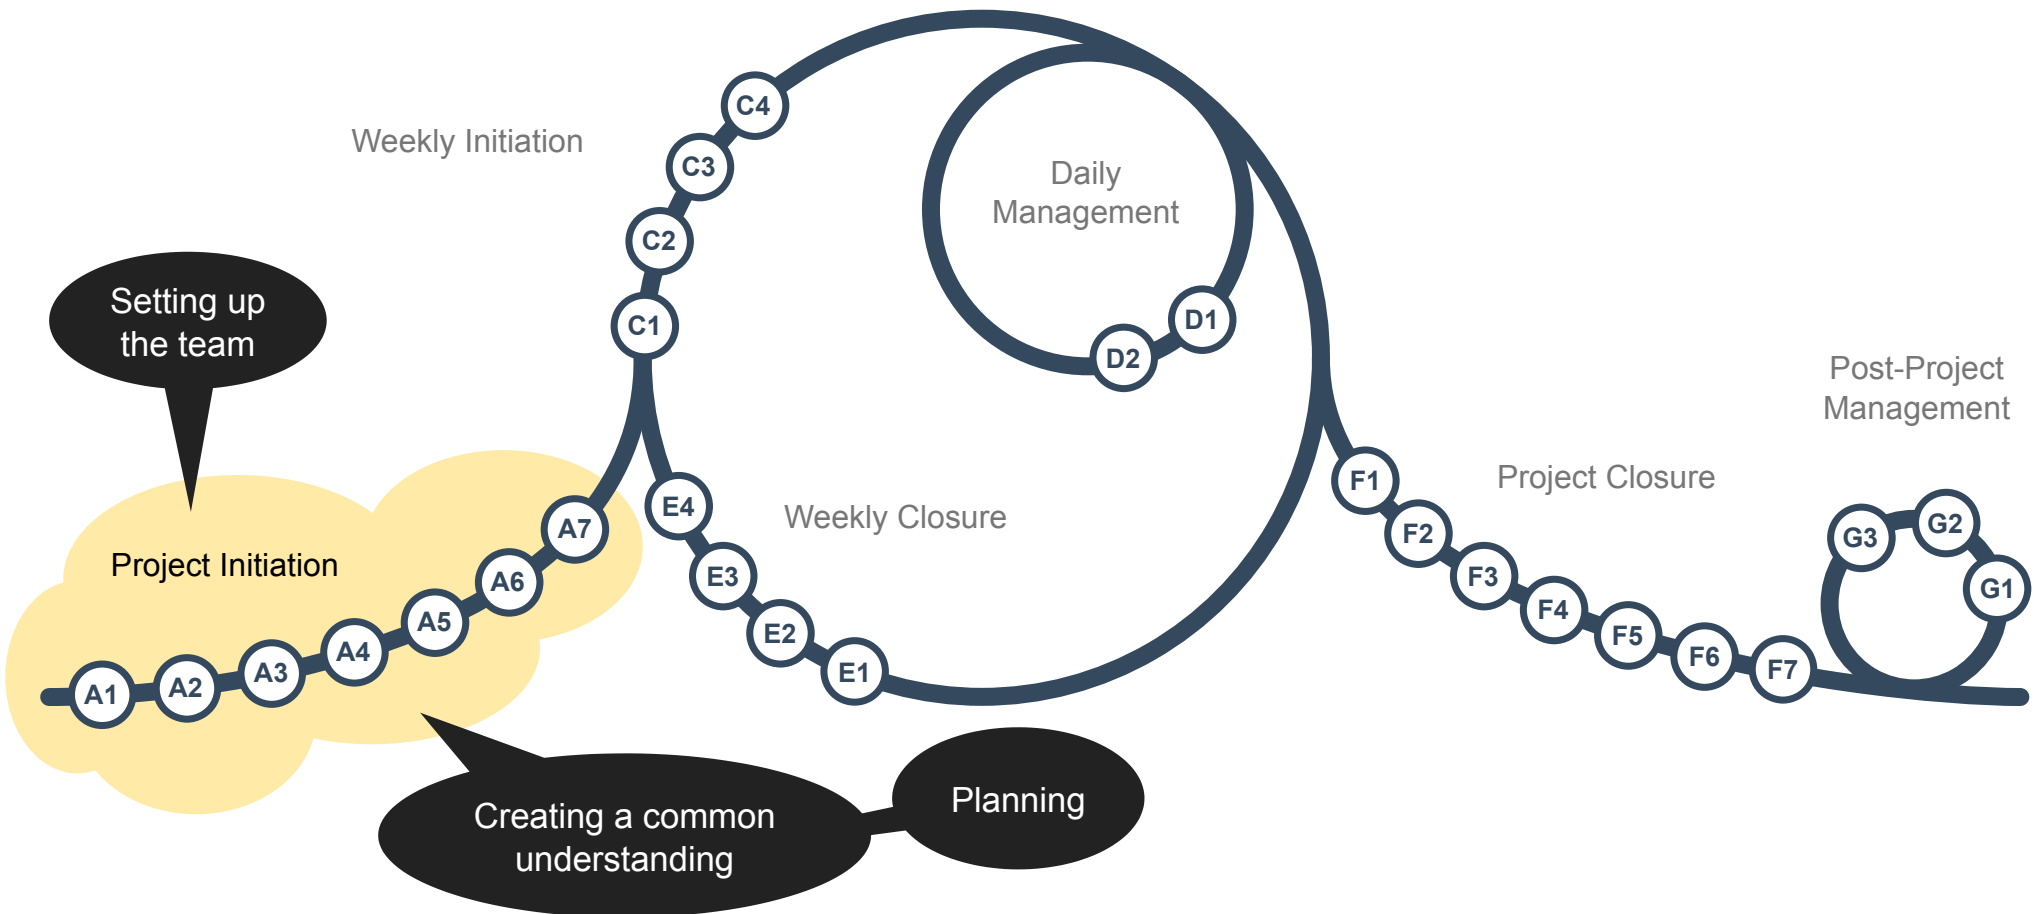

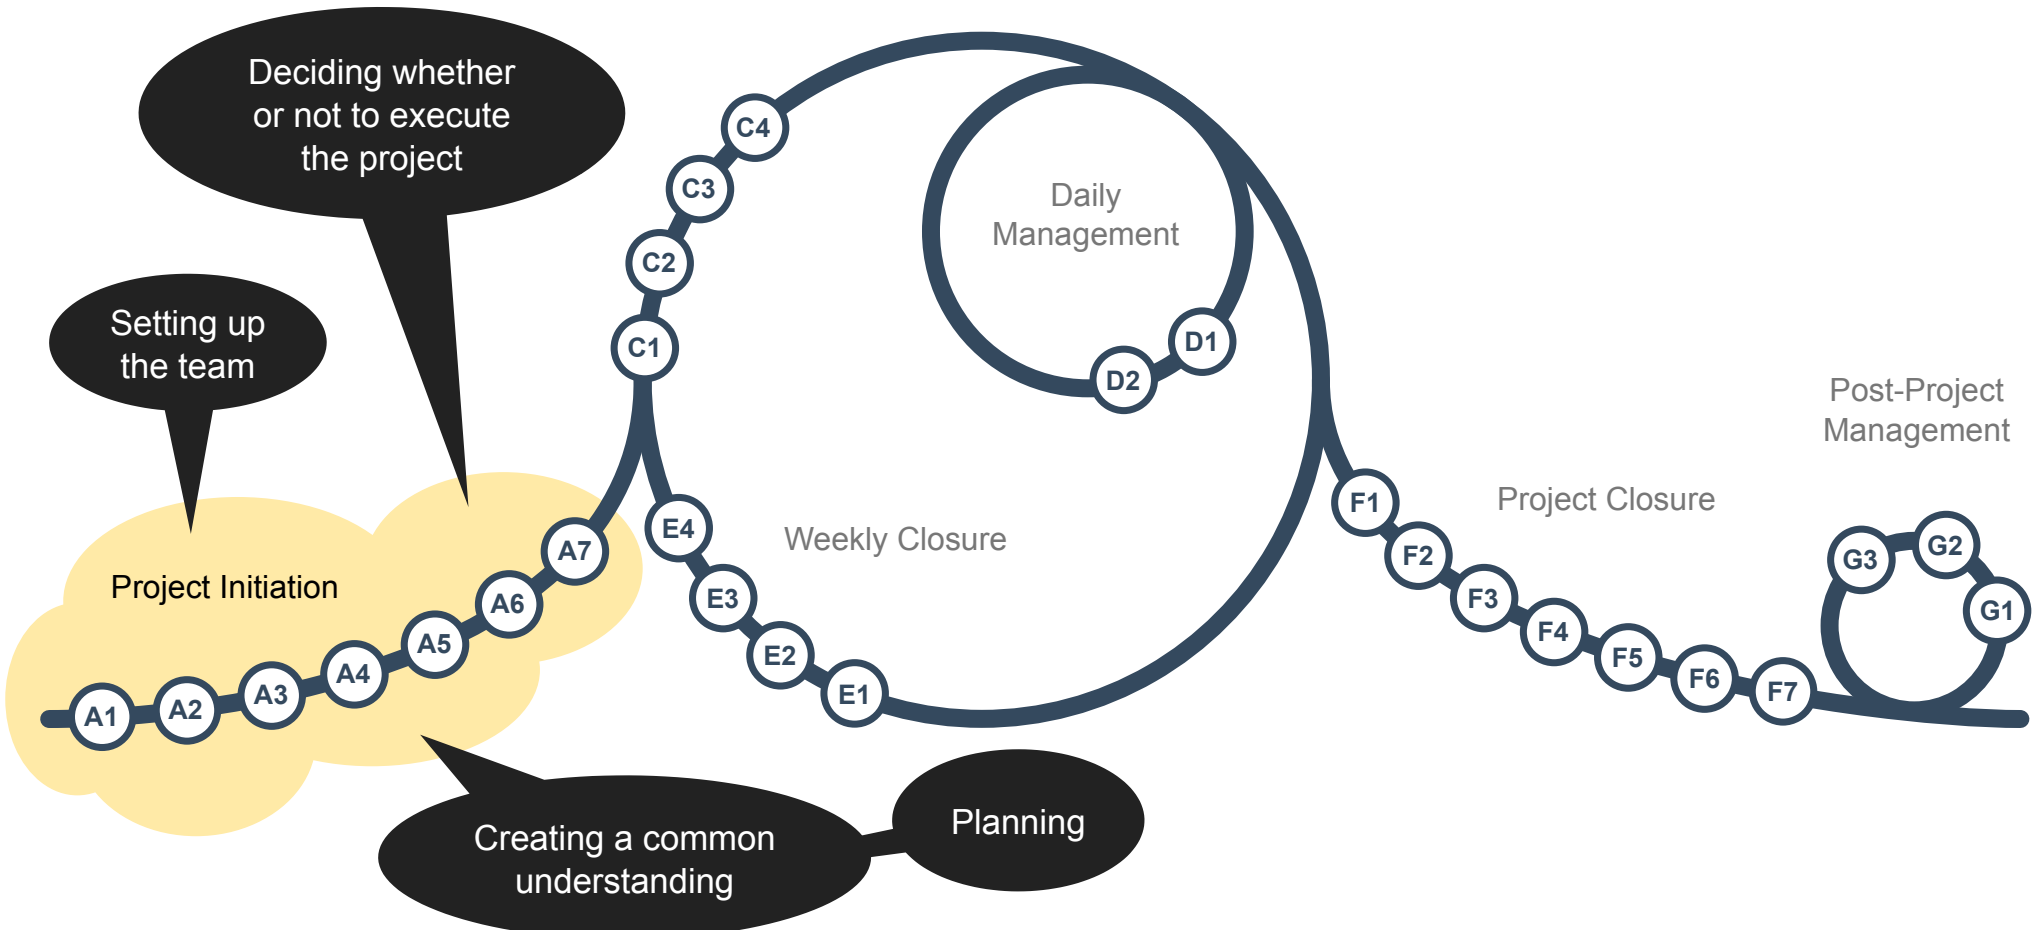

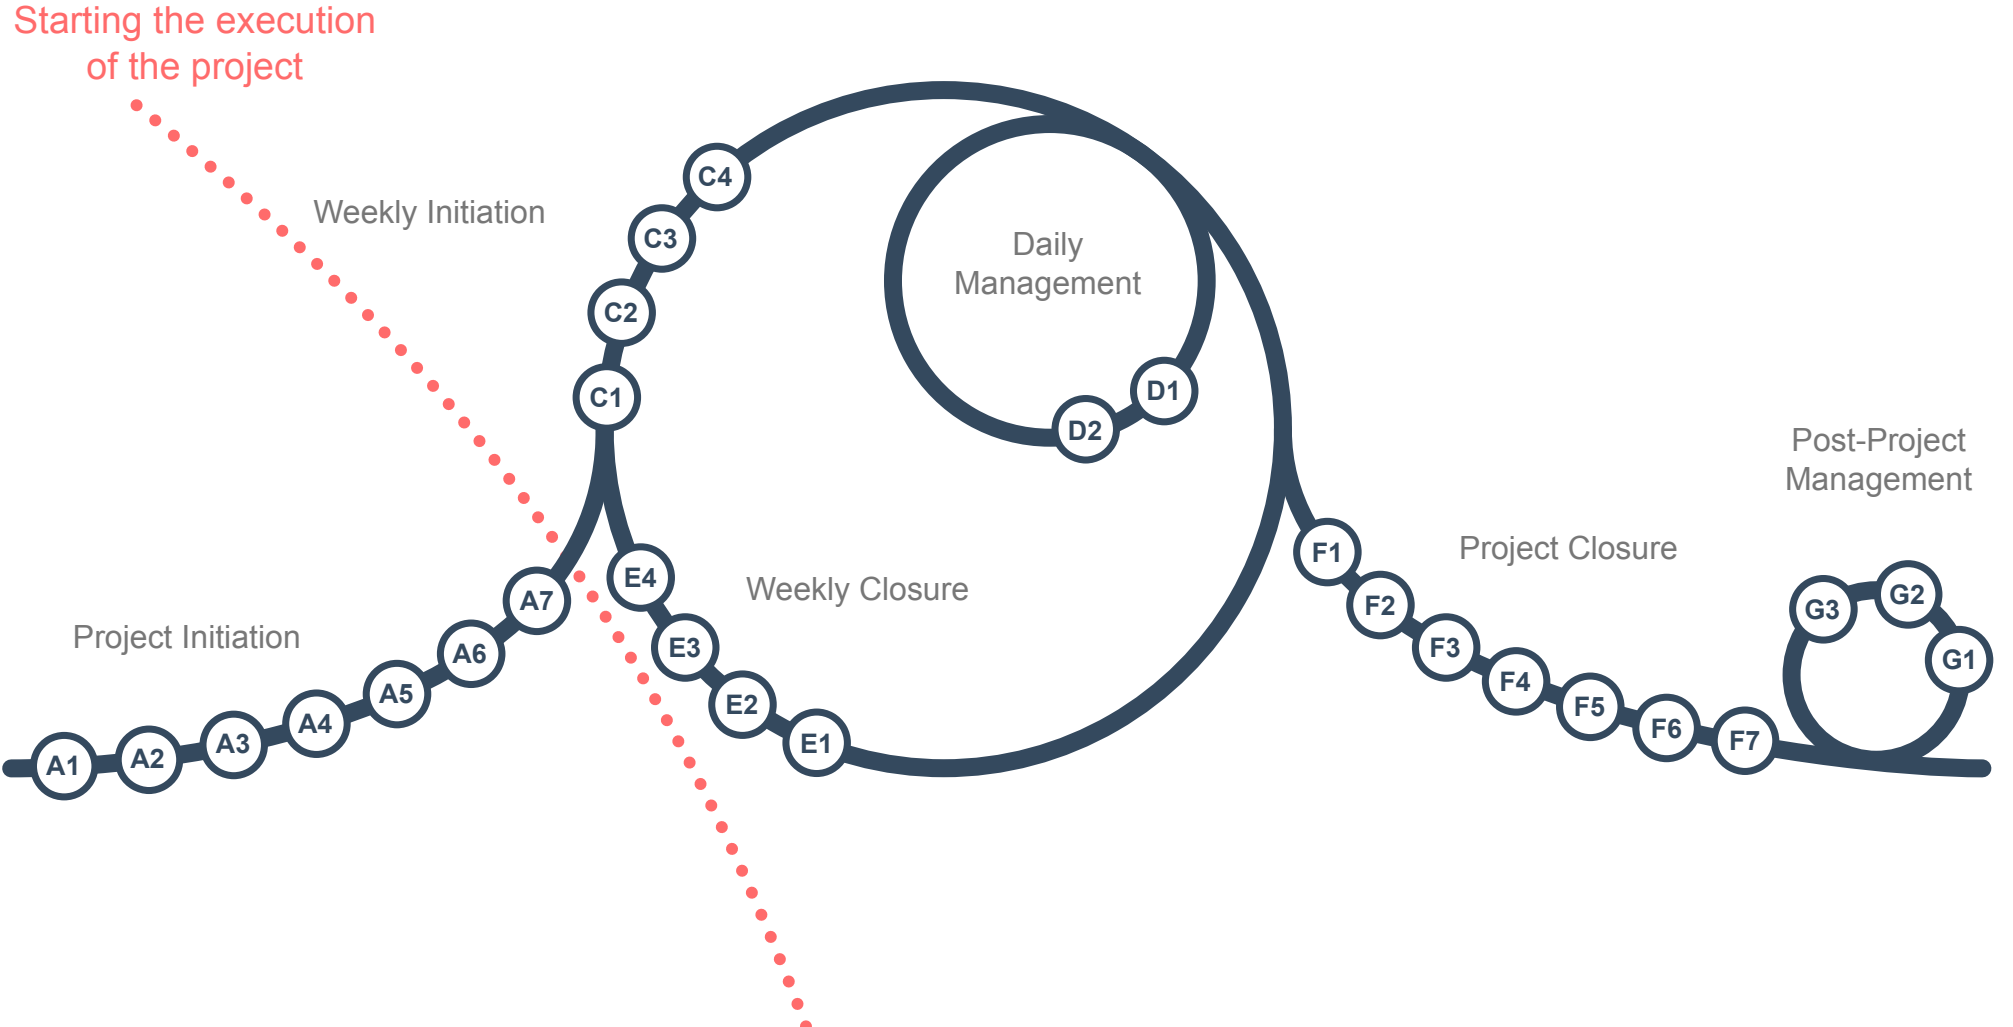

Starting the execution
of the project

Weekly Initiation


Daily
Management

Post-Project
Management

Project Initiation

Weekly Closure

Project Closure

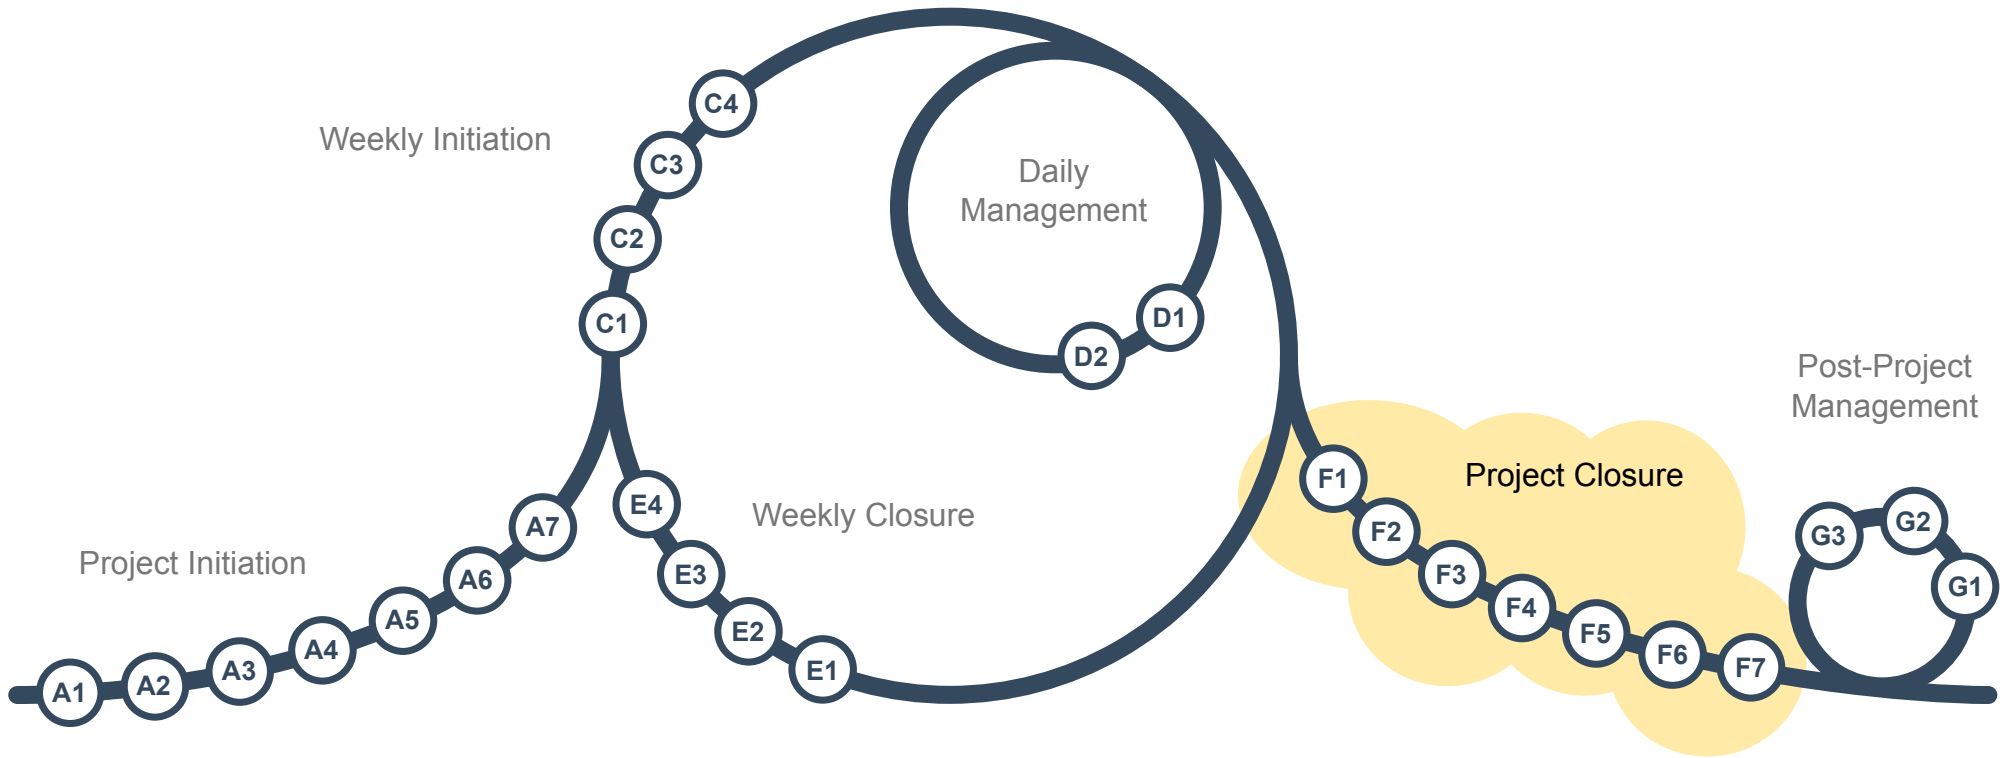

Project Initiation


Weekly Initiation

Daily Management

Weekly Closure

Project Closure

Post-Project Management

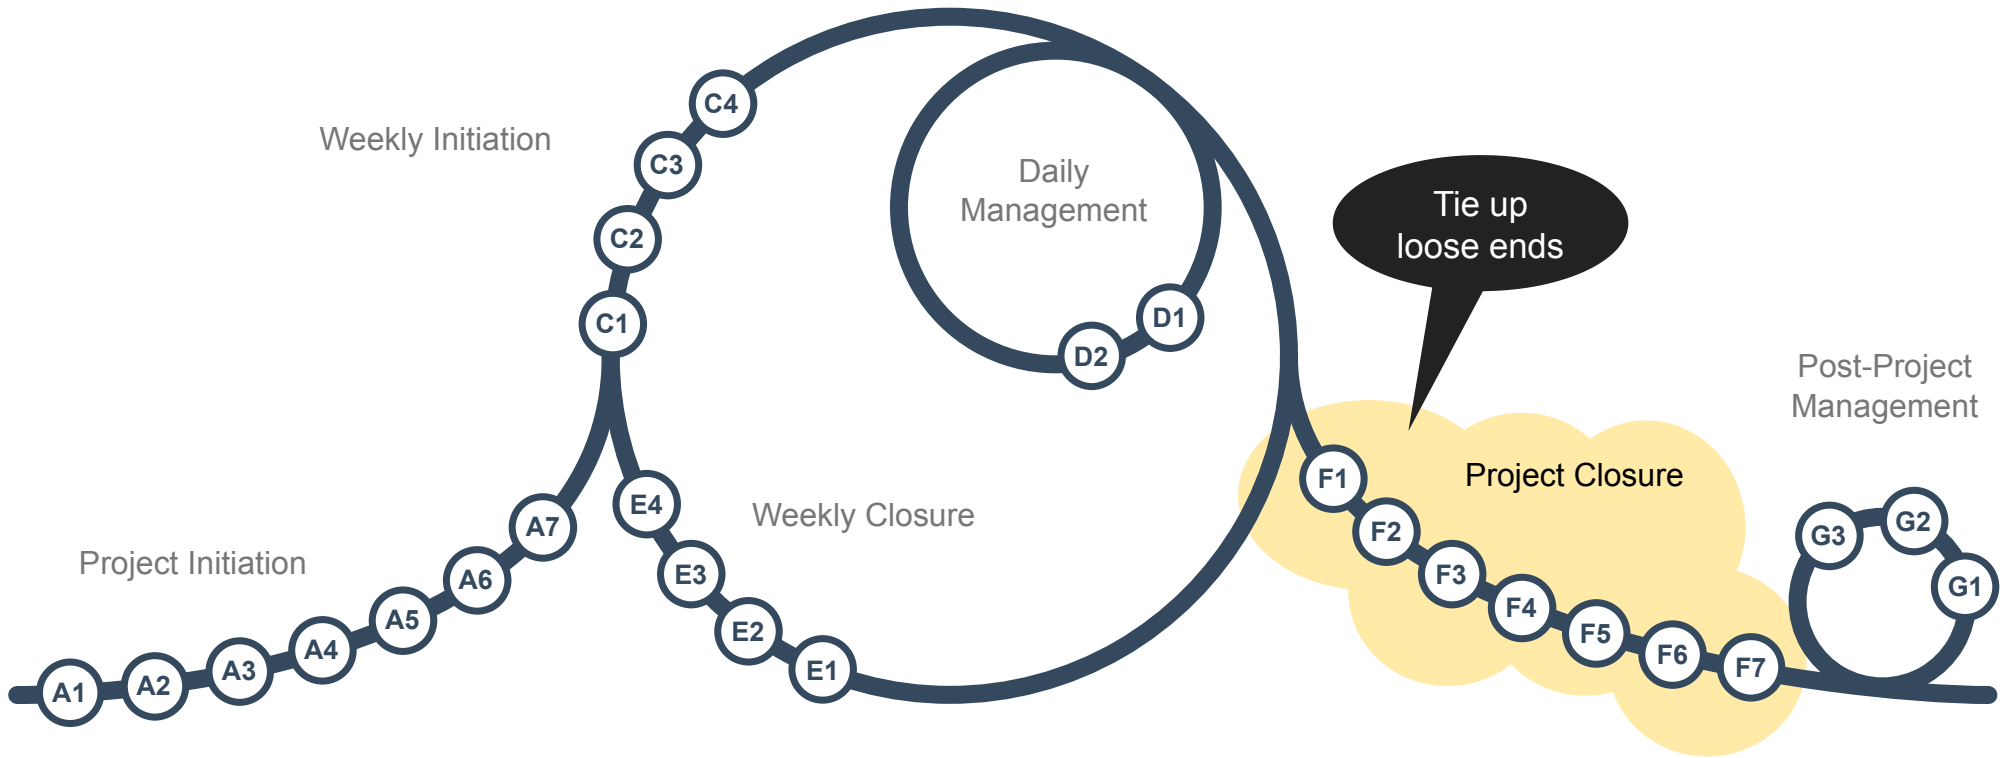

Weekly Initiation

Daily Management


Tie up loose ends

Post-Project Management

Project Closure

Weekly Closure

Project Initiation

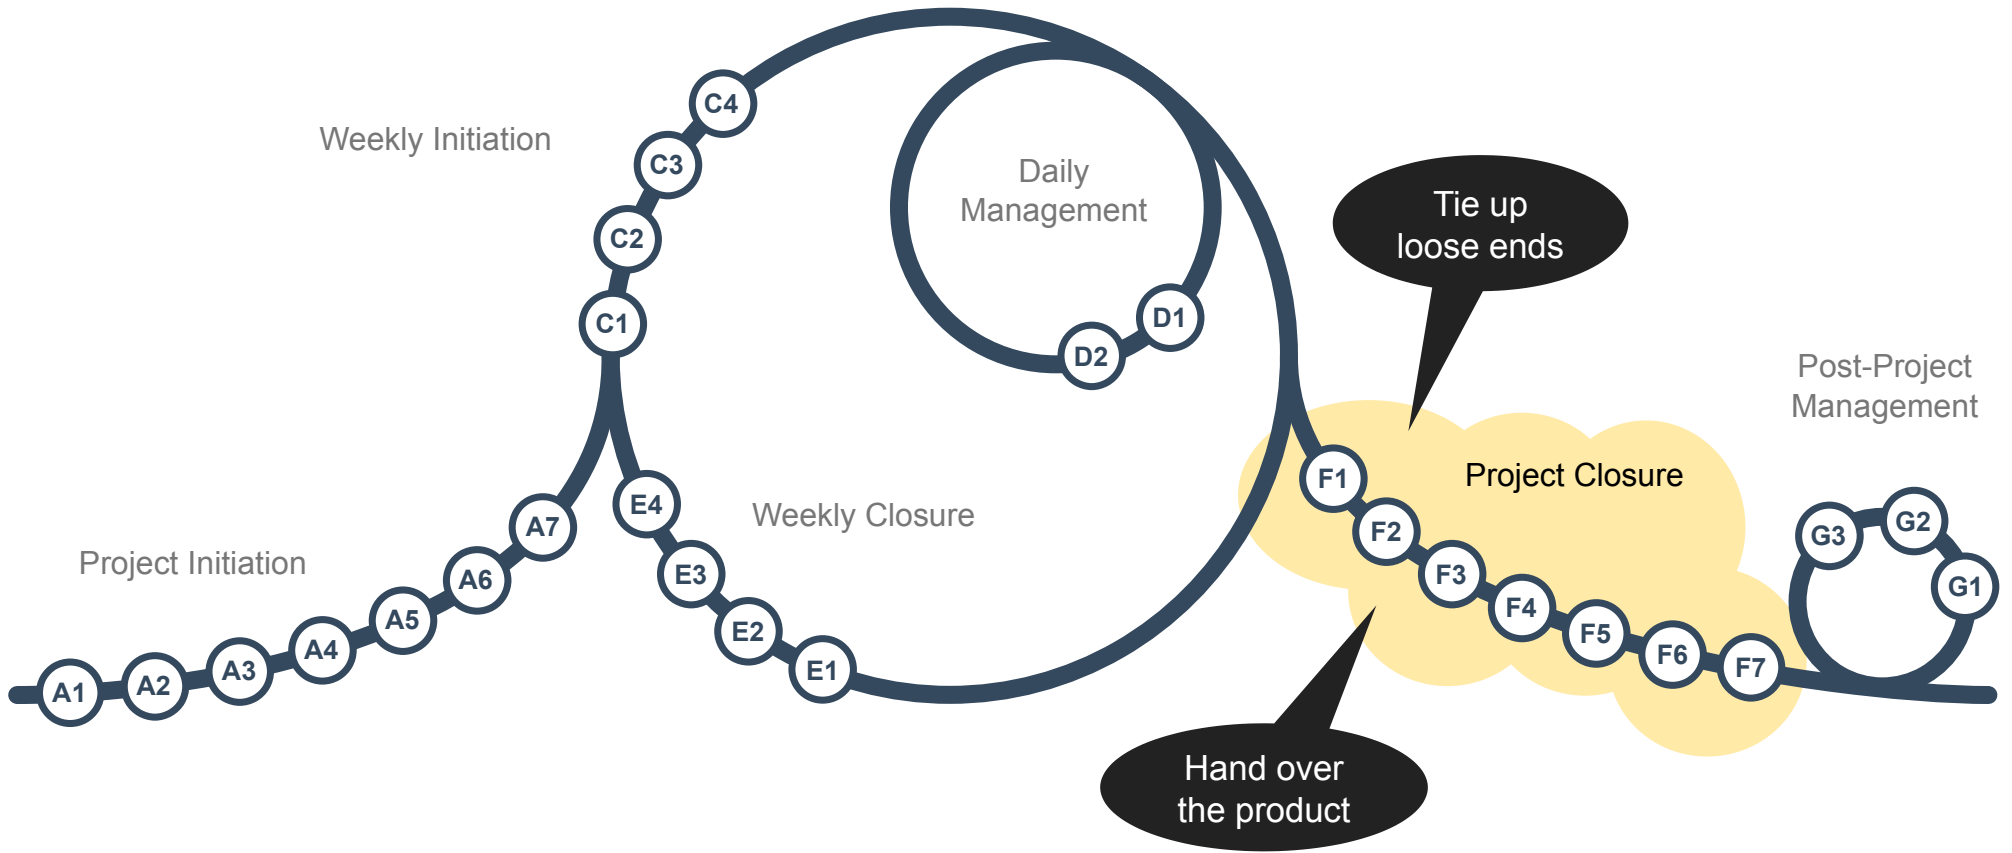

Weekly Initiation

Daily Management

Tie up loose ends

Post-Project Management

Project Closure

Weekly Closure

Project Initiation

Hand over the product

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E1

E2

E3

E4

F1

F2

F3

F4

F5


F6

F7

G3

G2

G1

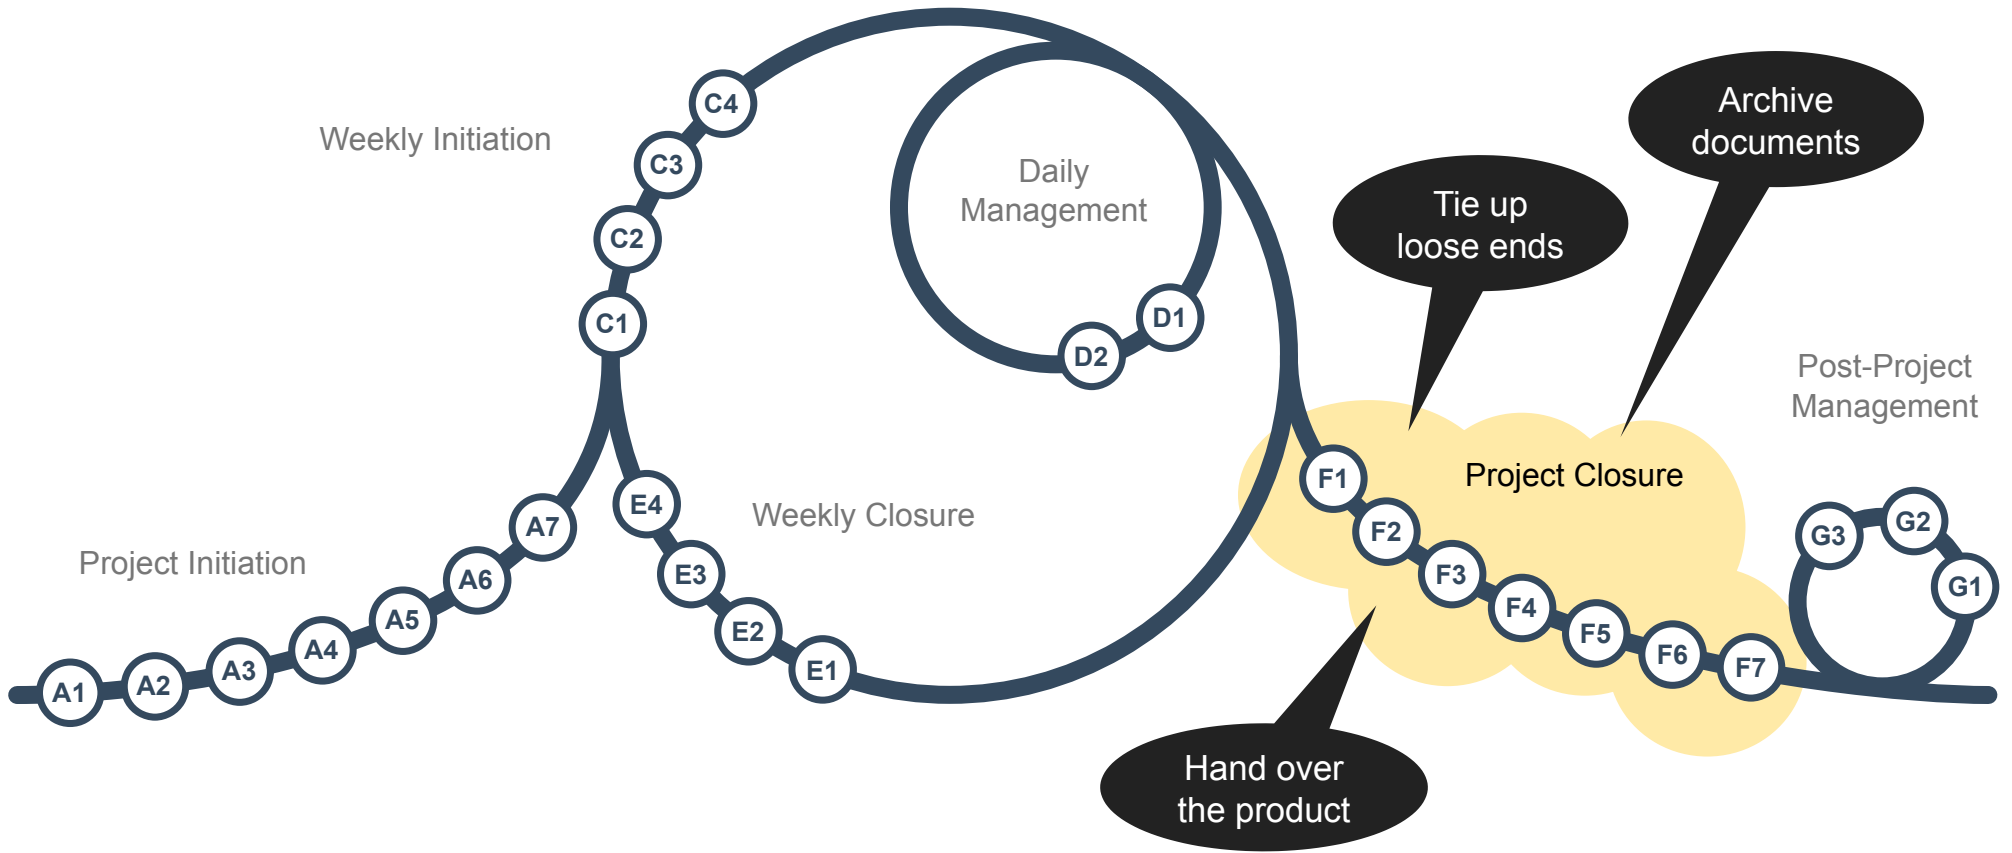

Weekly Initiation

Daily Management

Archive documents

Tie up loose ends

Post-Project Management

Project Closure

Project Initiation

Weekly Closure

Hand over the product

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E1

E2

E3

E4

F1

F2

F3

F4

F5


F6


F7

G3

G2

G1

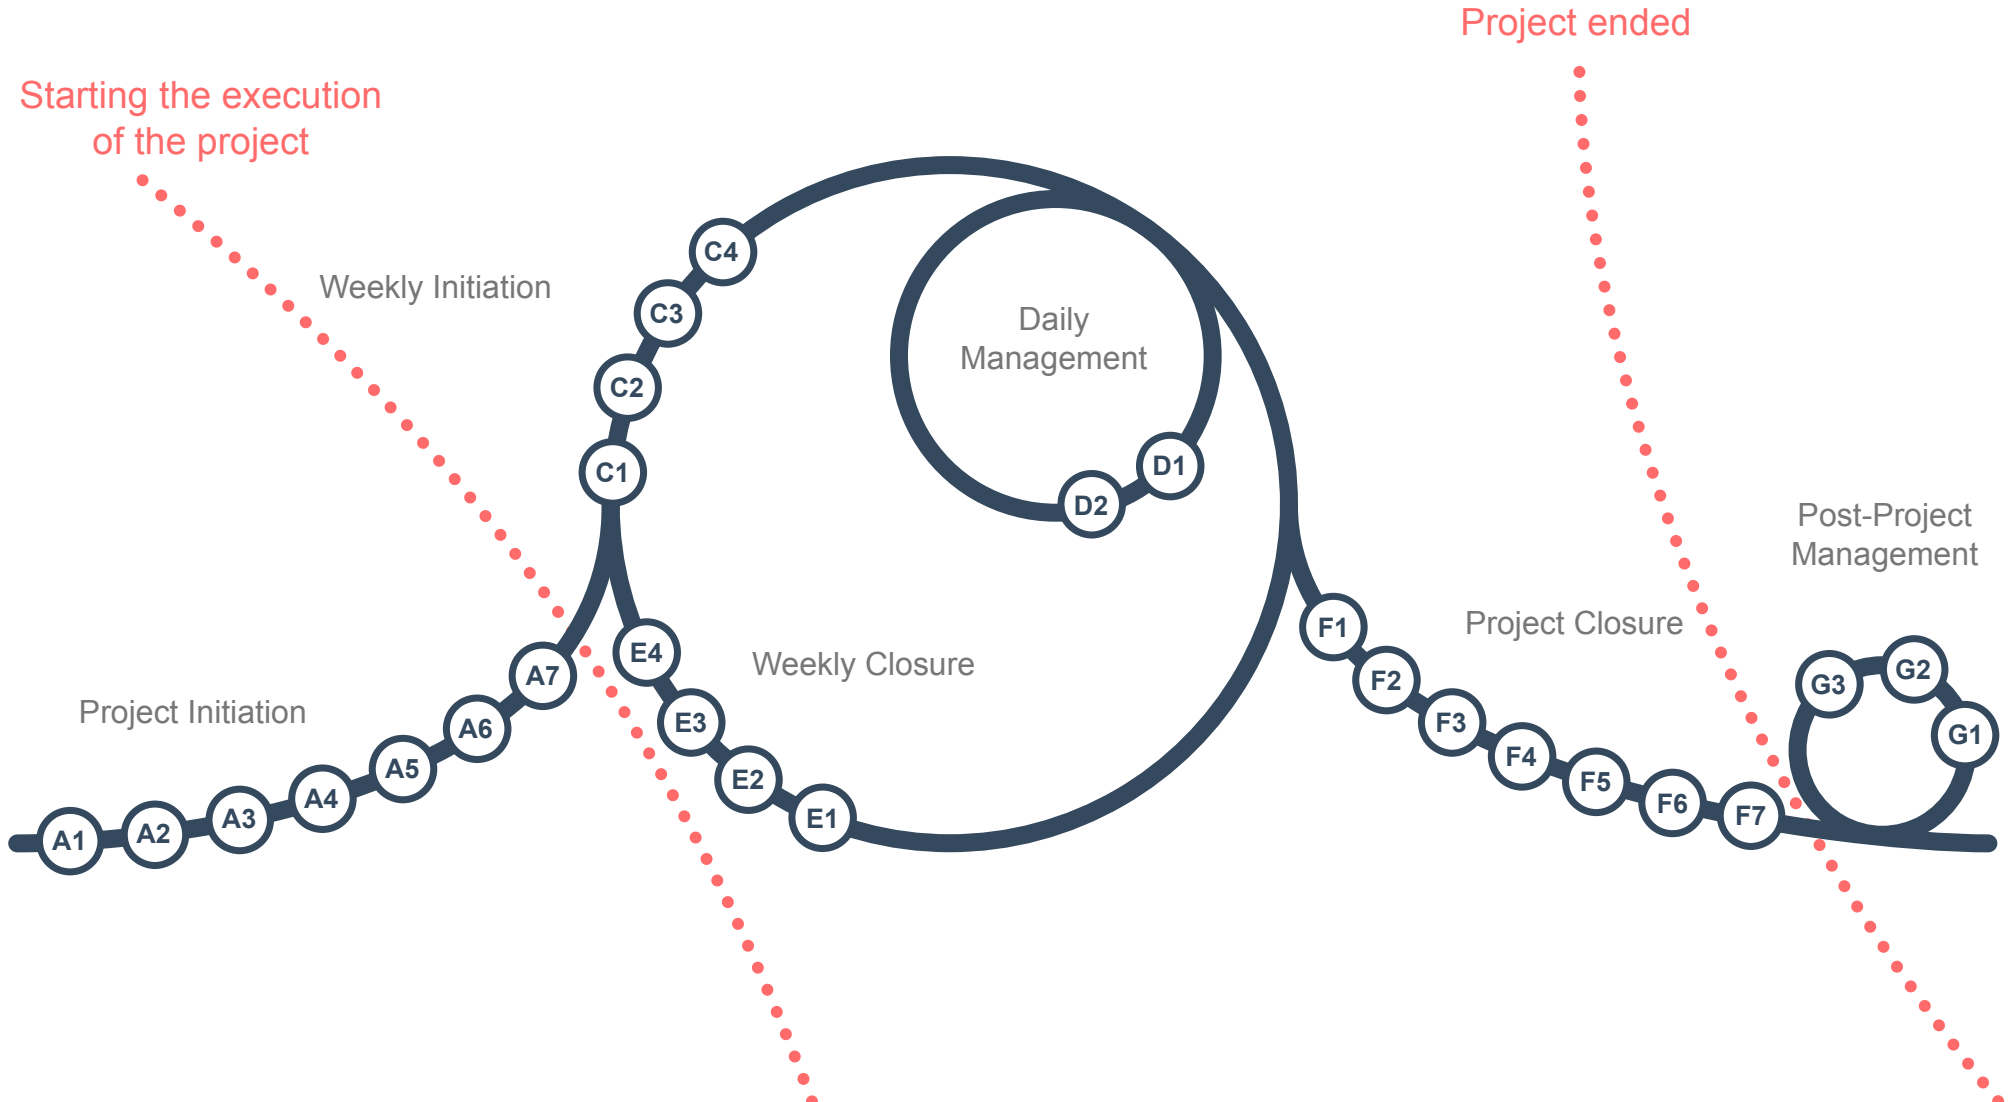

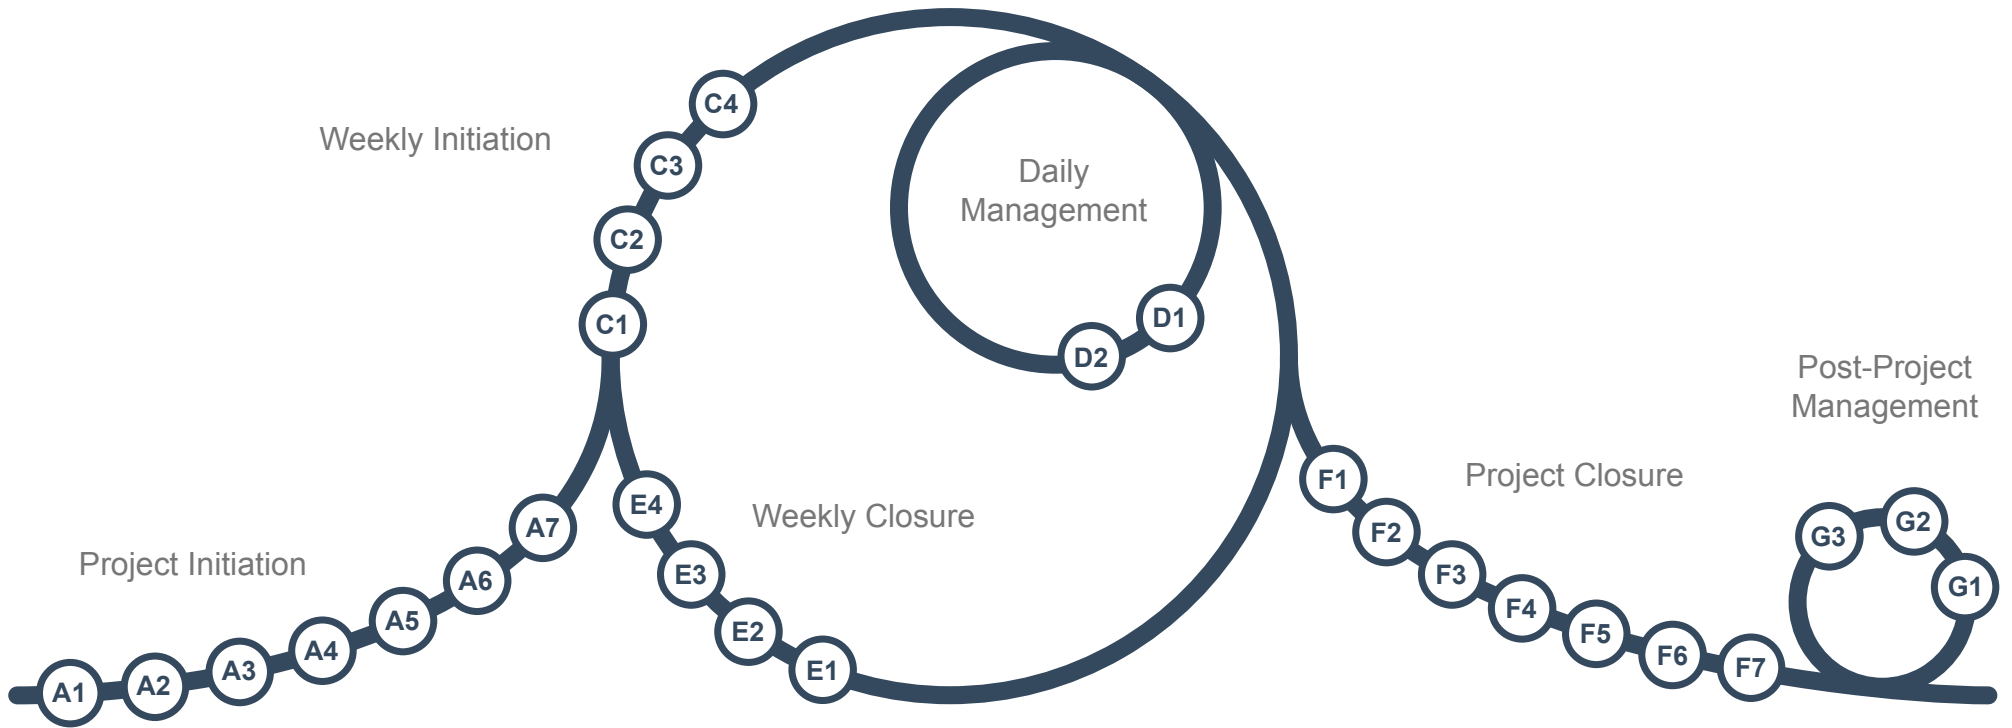

Weekly Initiation


Daily Management

Post-Project Management


Project Initiation


Weekly Closure

Project Closure

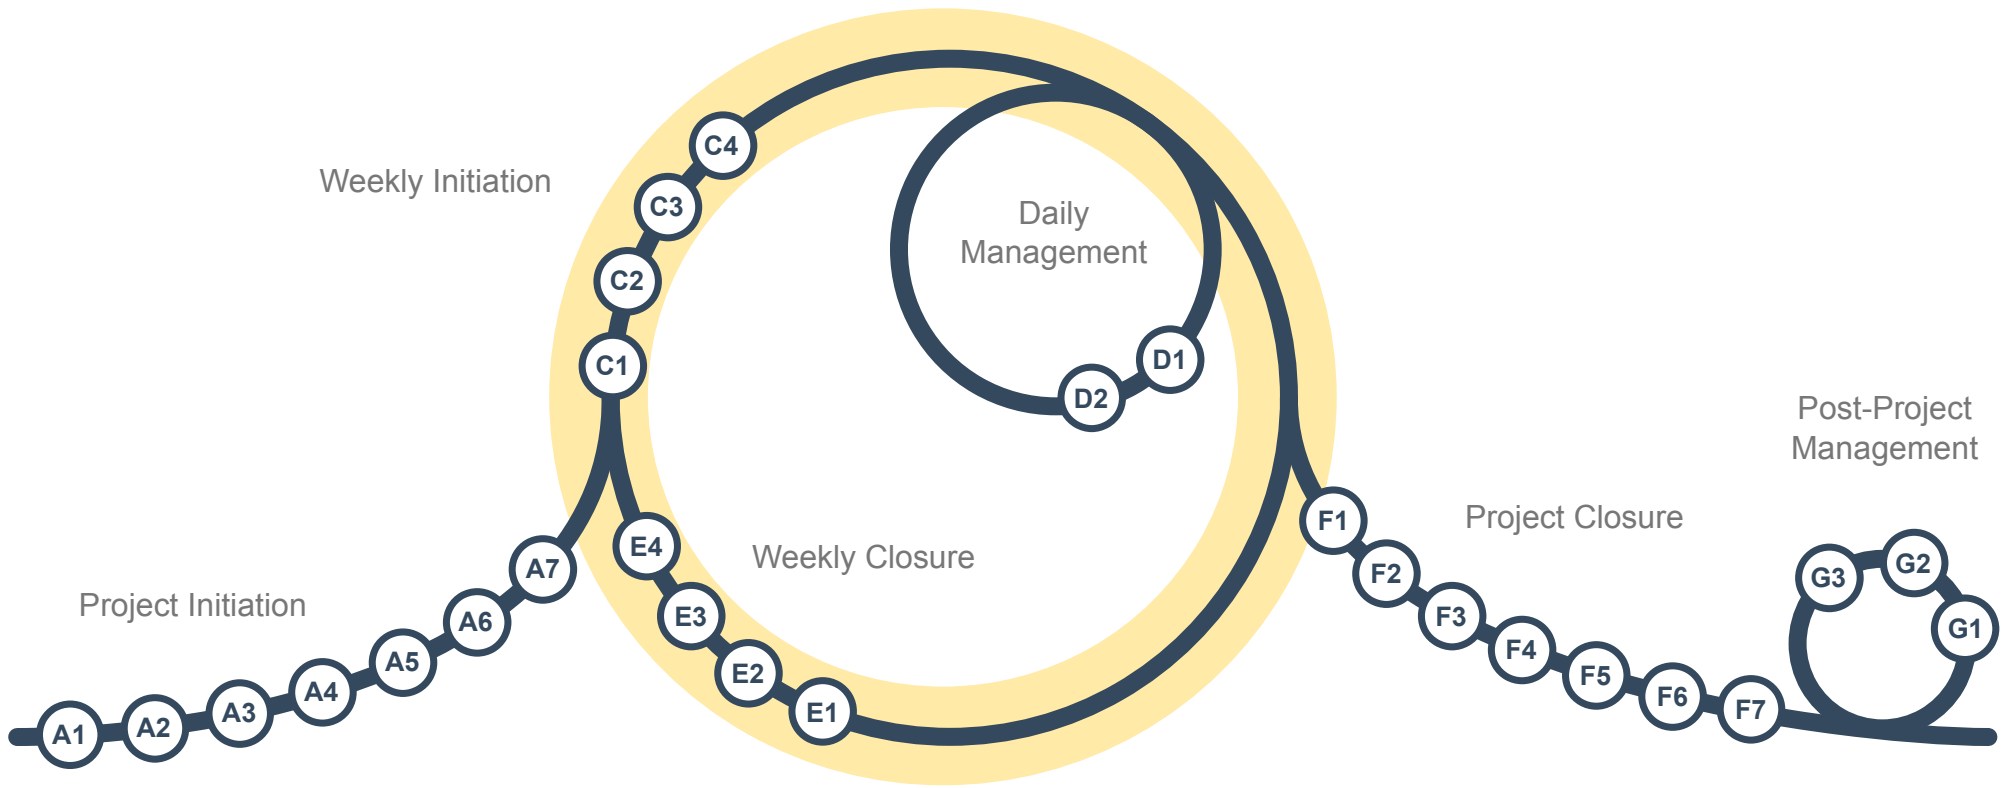

Monthly for stretched micro-projects

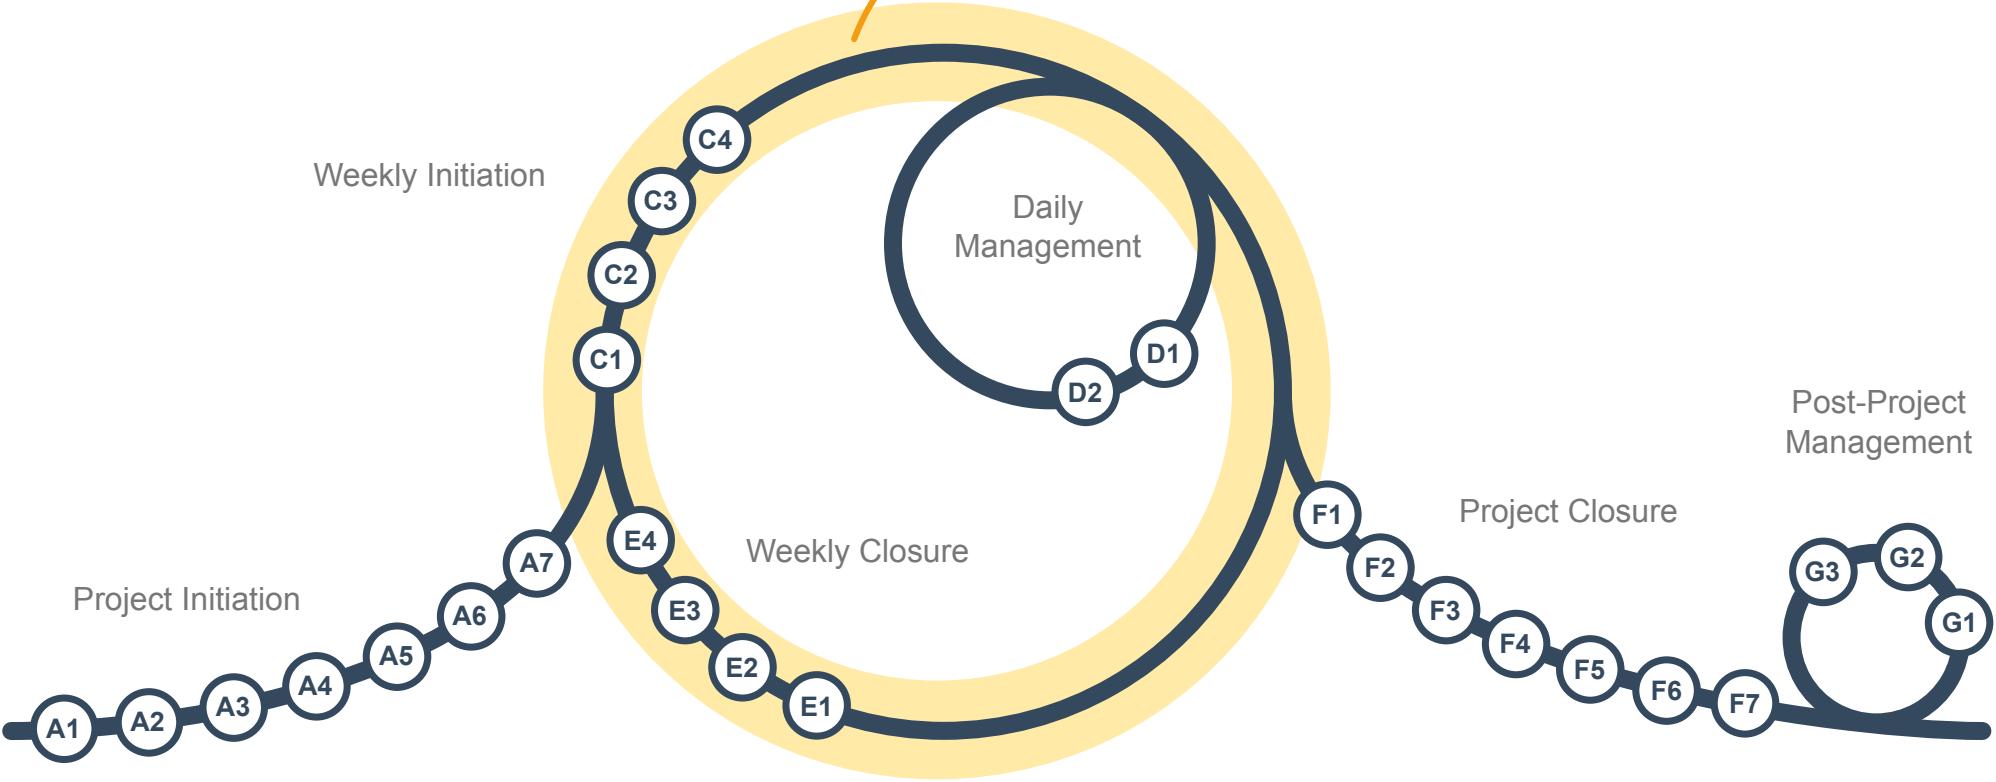

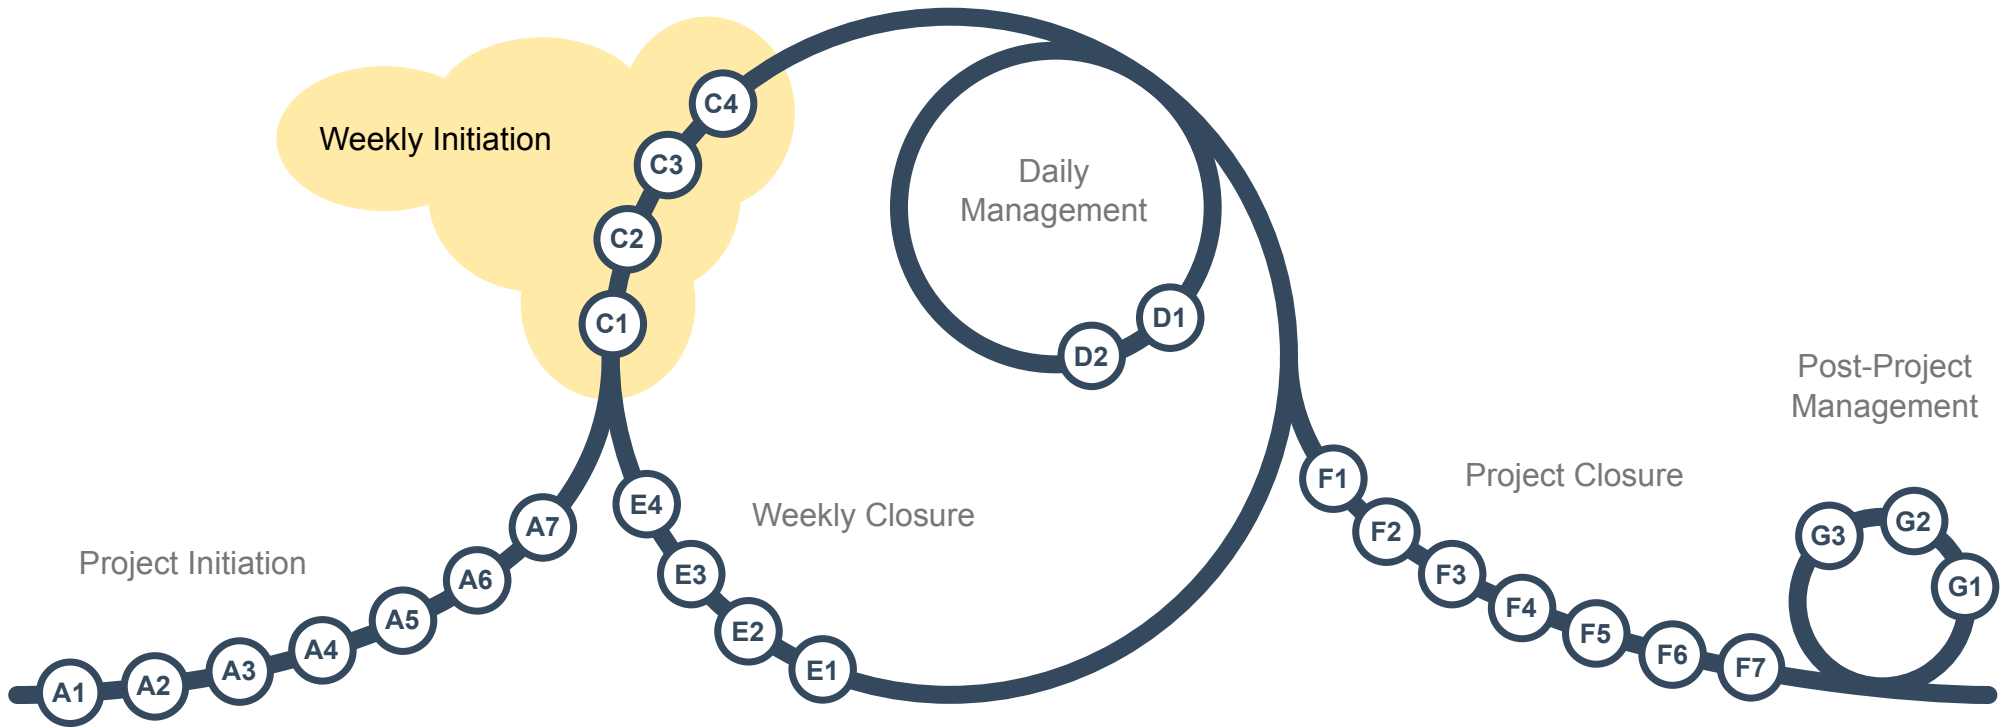

Project Initiation


Weekly Initiation

Weekly Closure

Daily Management

Project Closure

Post-Project Management

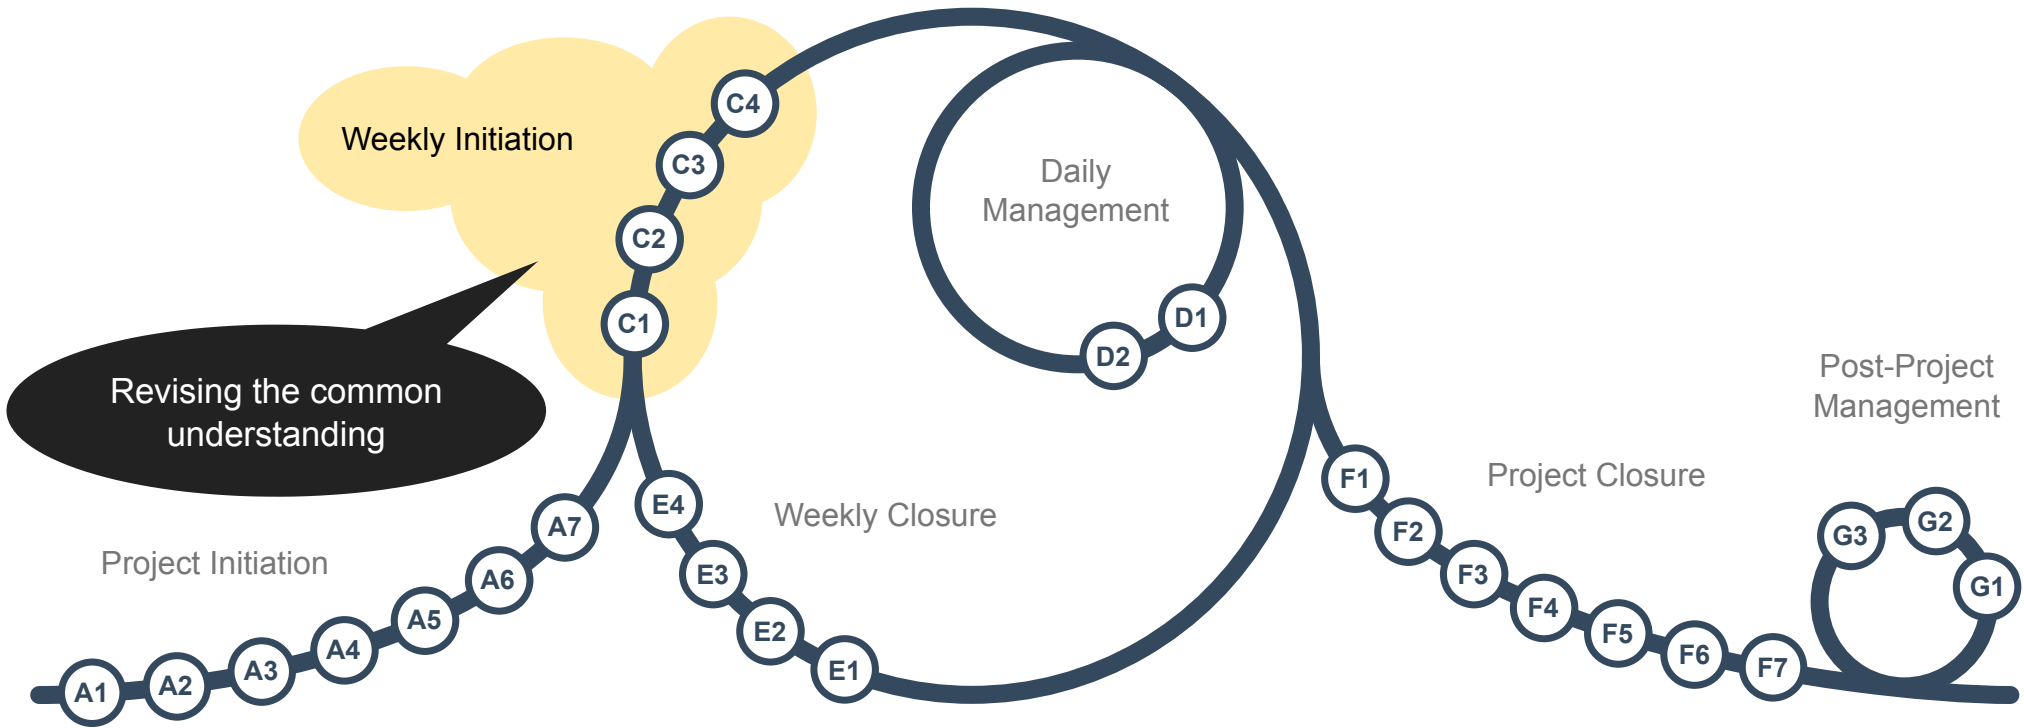

Weekly Initiation

Revising the common understanding

Daily Management

Weekly Closure

Project Initiation

Project Closure

Post-Project Management

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C1

C2

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6


F7


G3


G2

G1

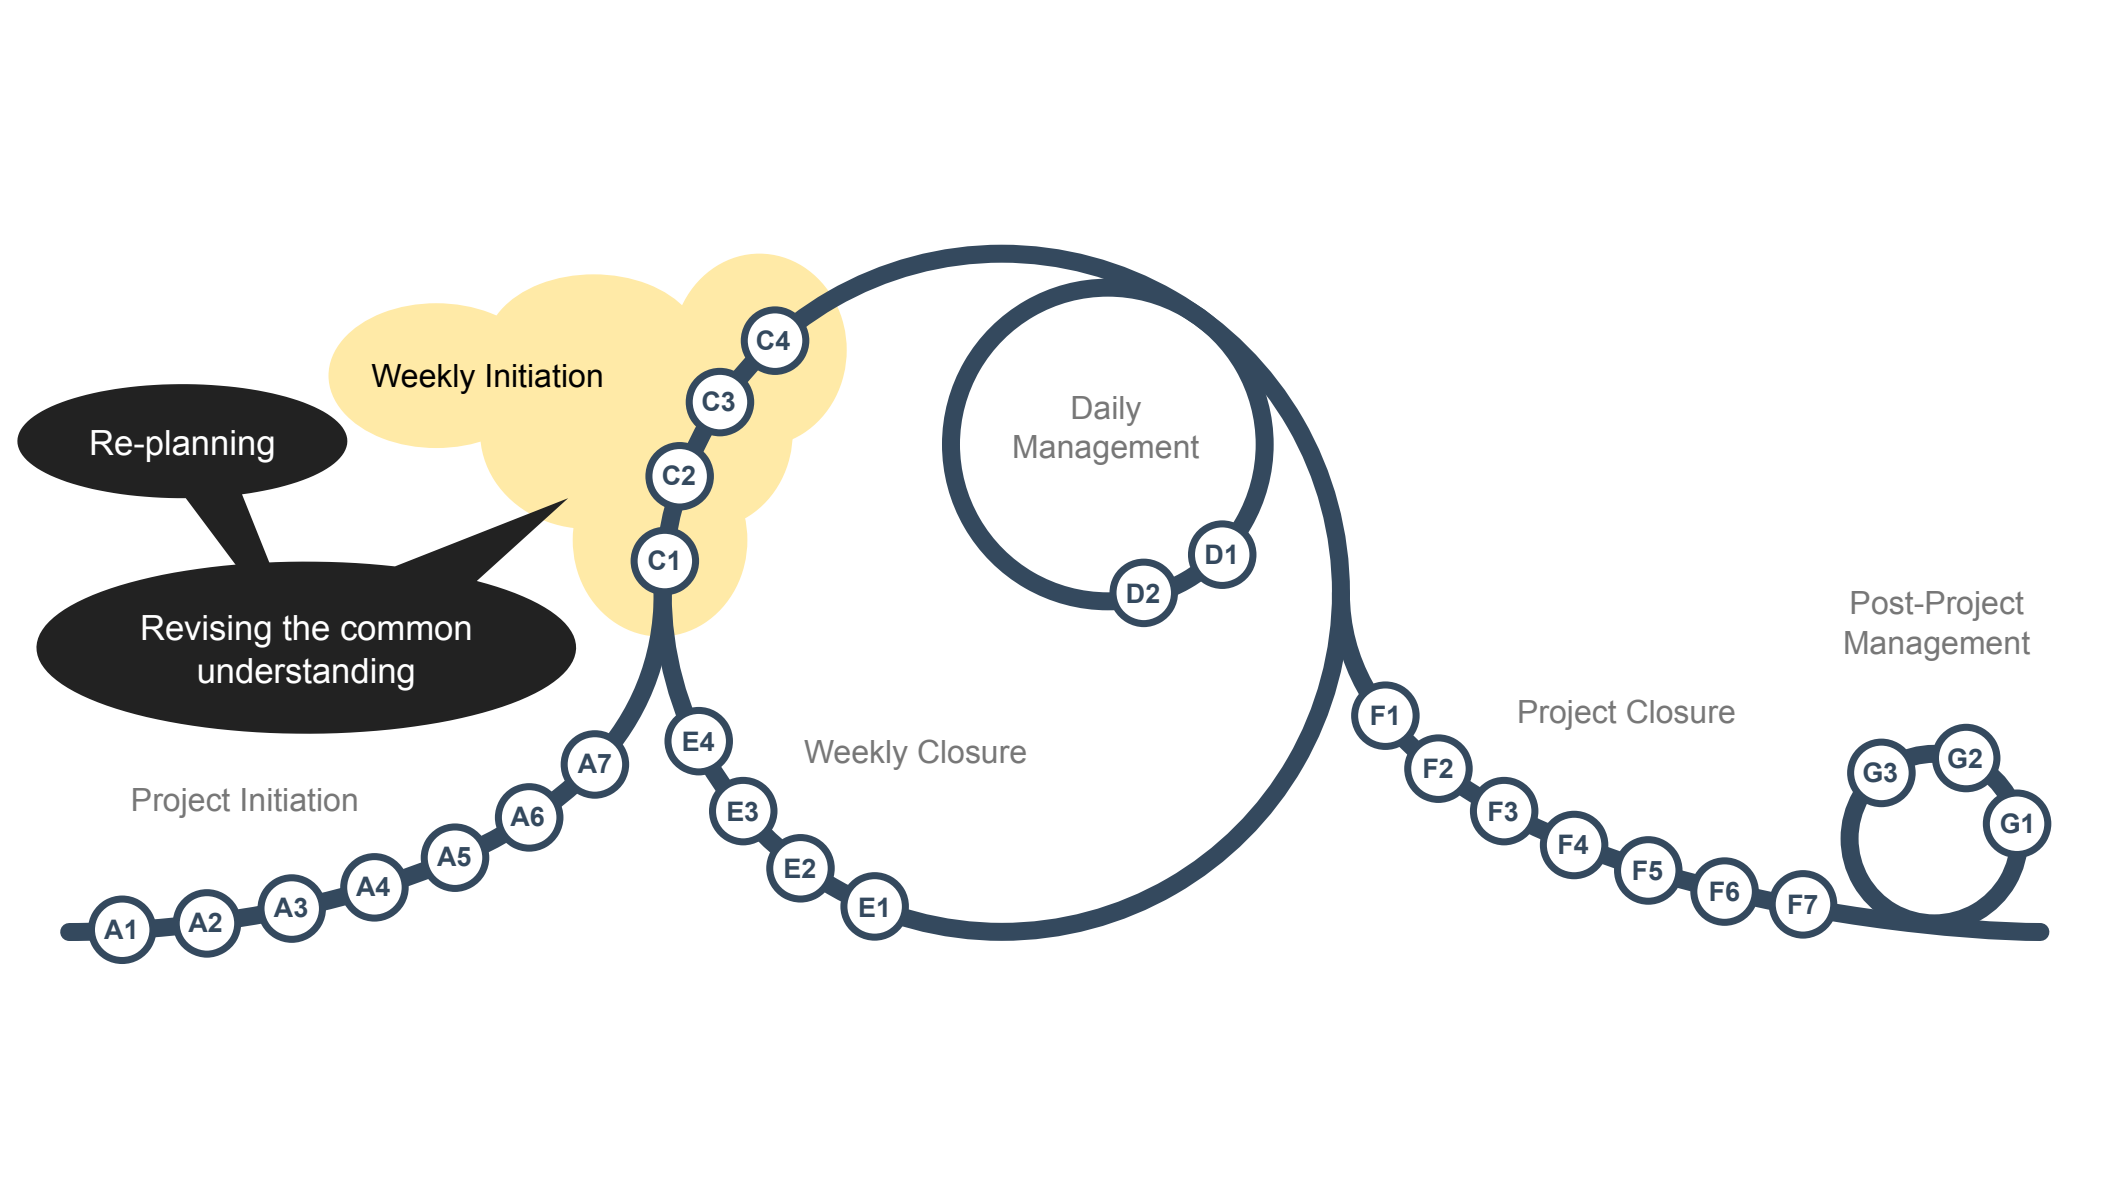

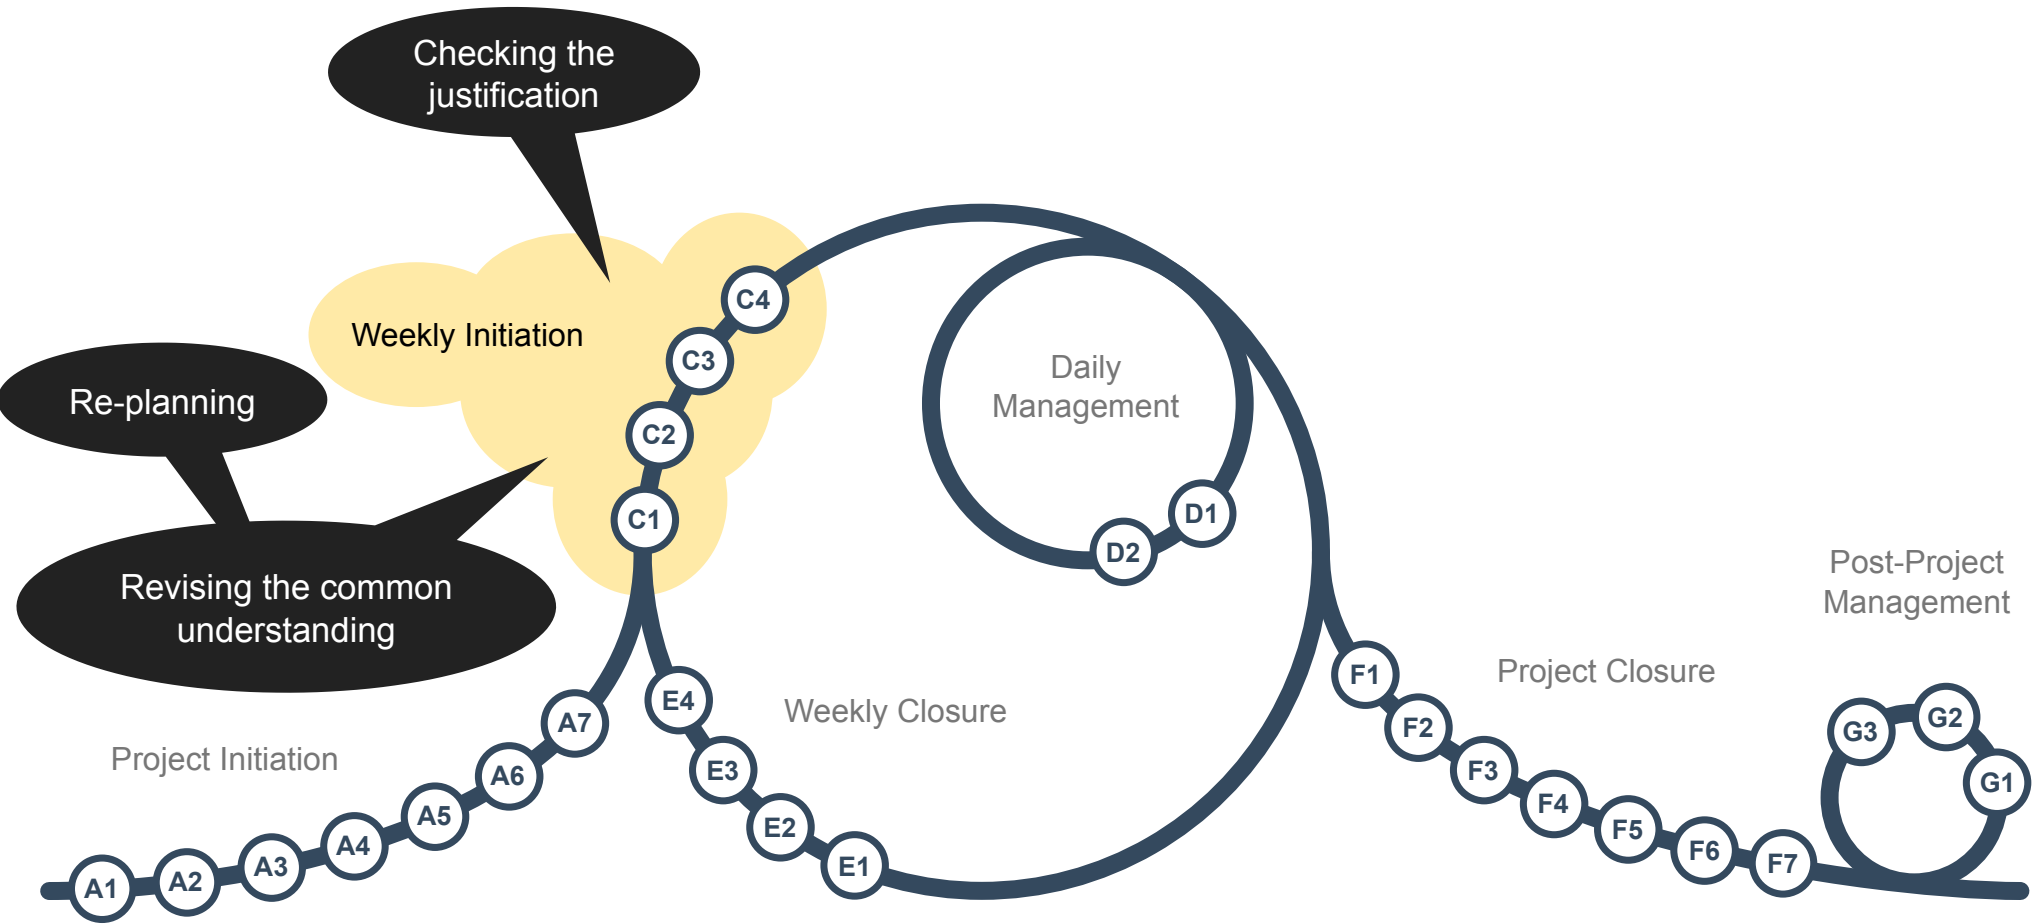

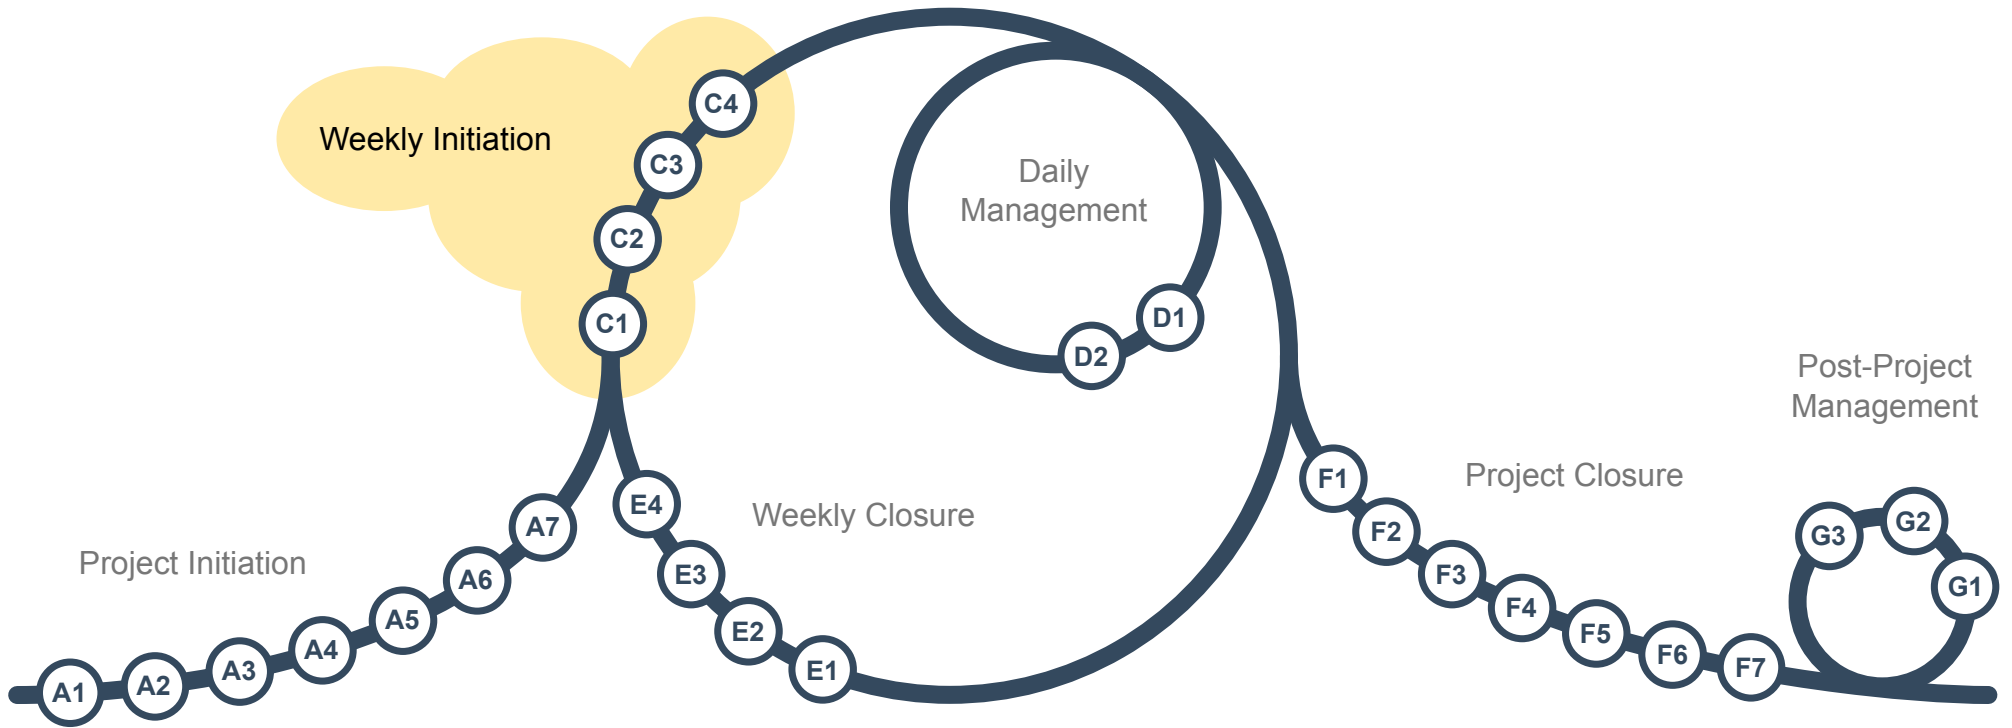

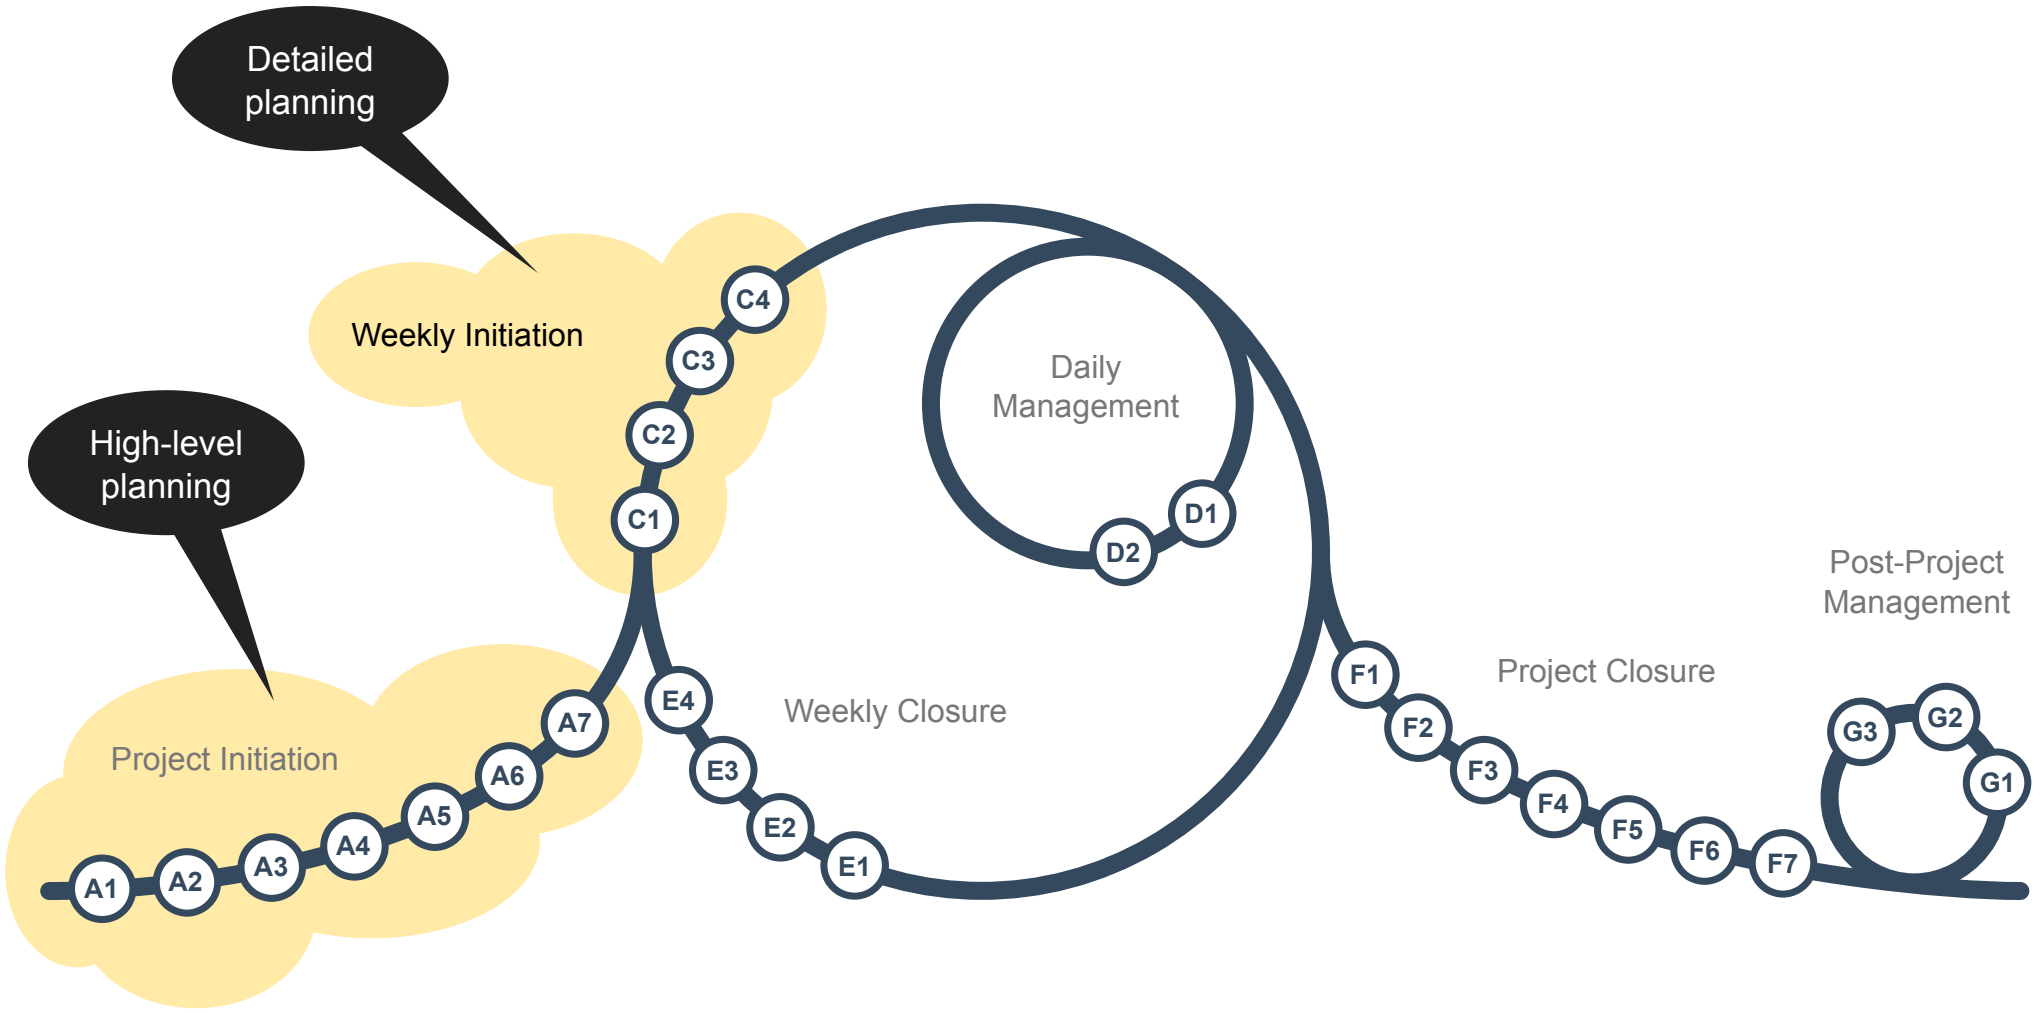

Detailed planning

High-level planning

Weekly Initiation


Daily Management

Project Initiation

Weekly Closure

Project Closure

Post-Project Management

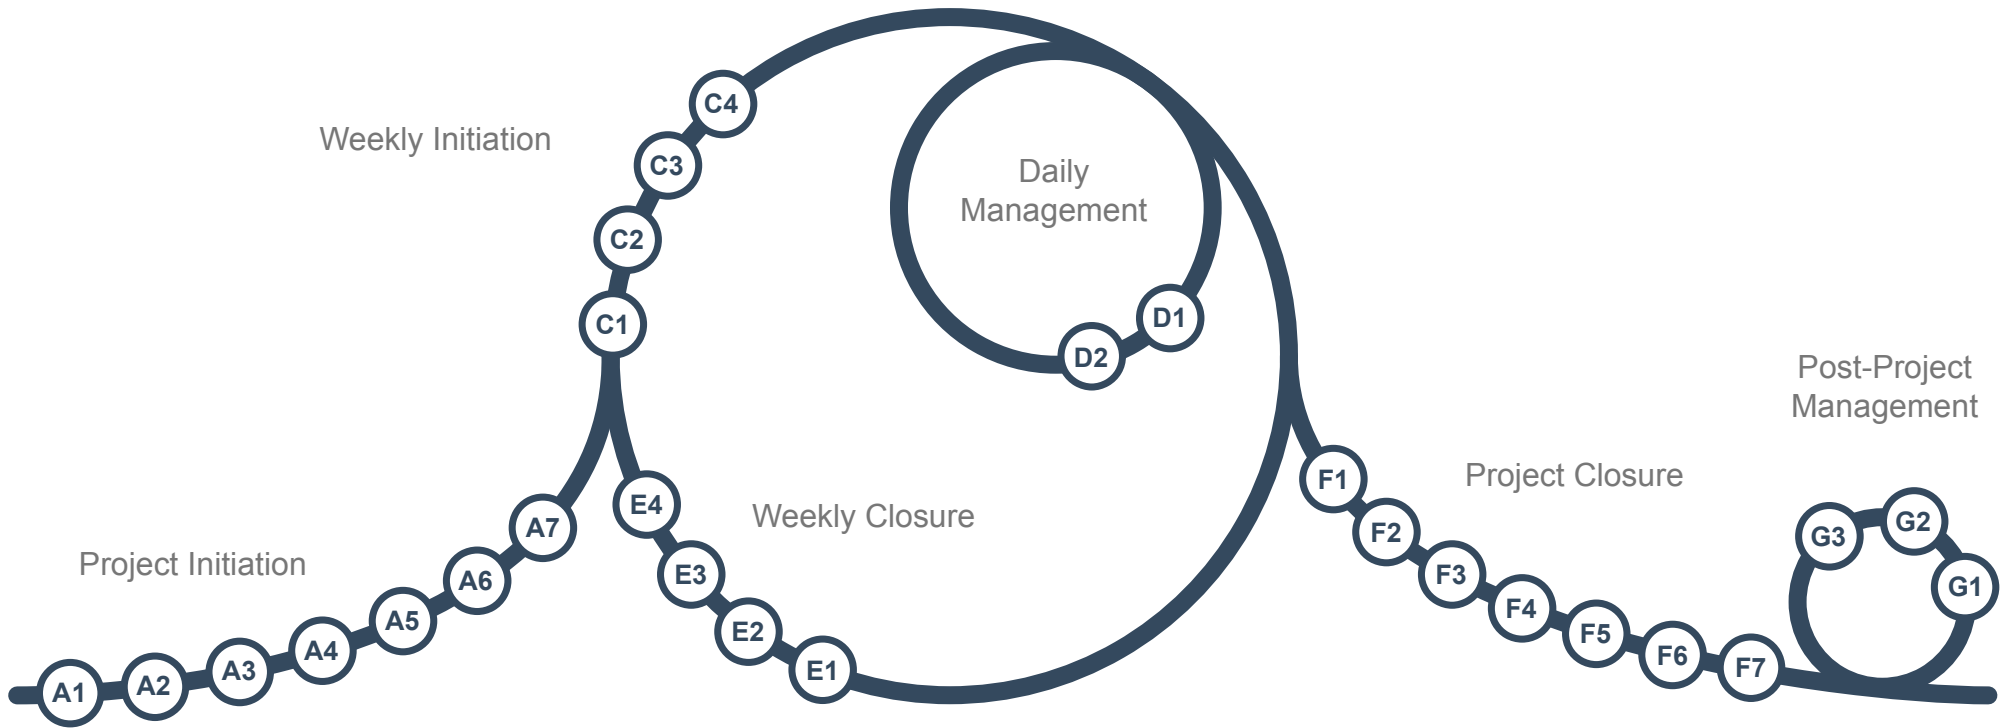

Project Initiation

Weekly Initiation

Daily Management

Weekly Closure

Project Closure

Post-Project Management

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E2

E3

E4

E1

F1

F2

F3

F4

F5


F6

F7

G3

G2

G1

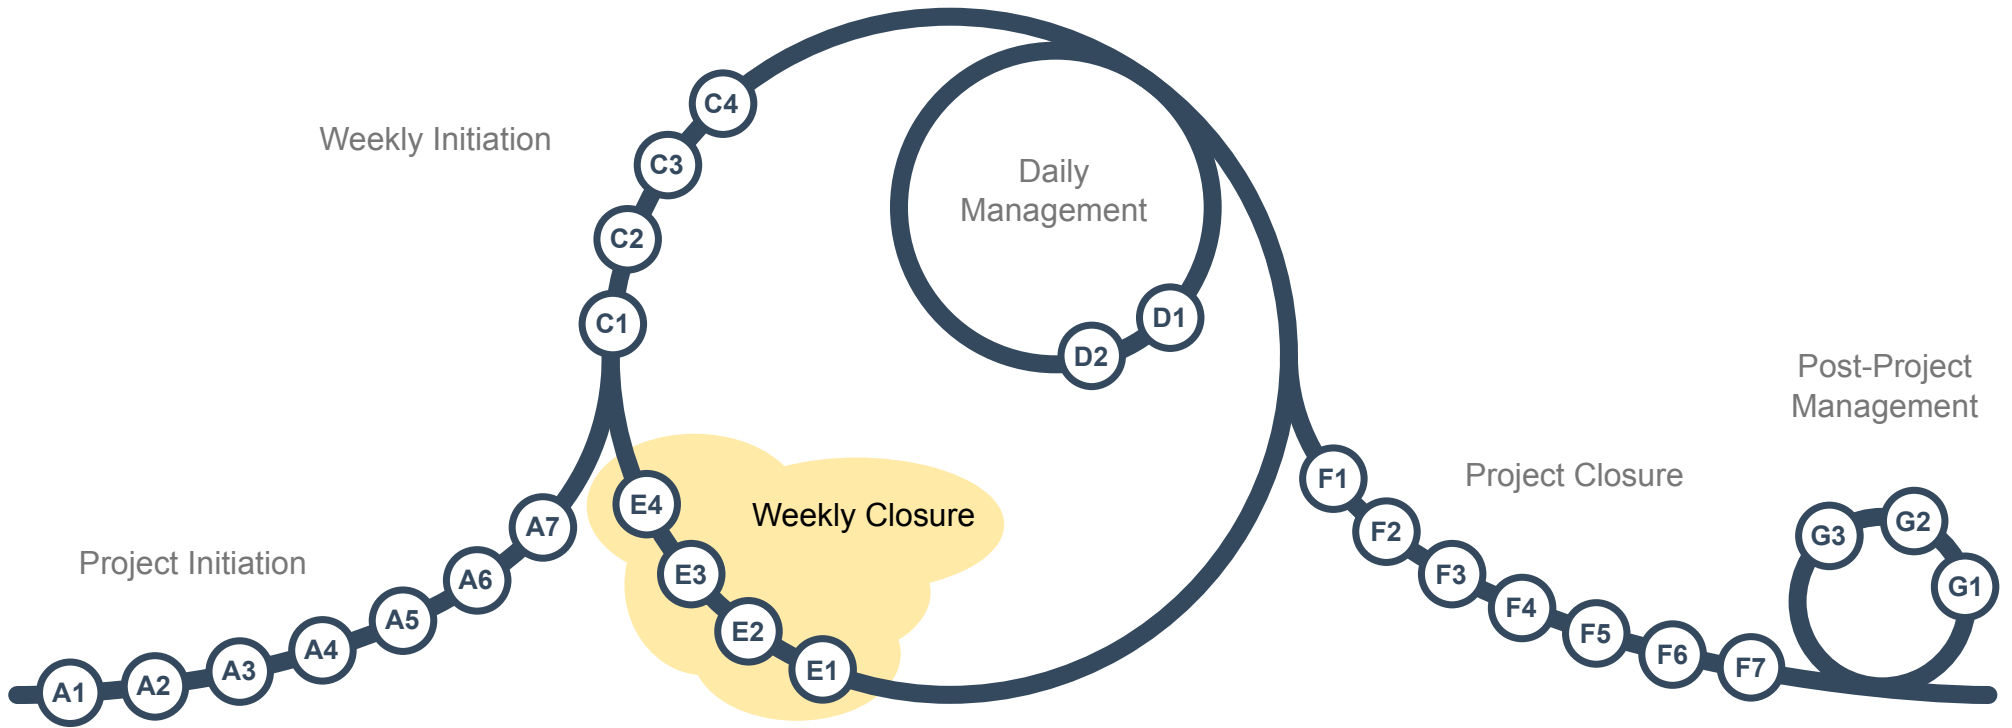

Weekly Initiation

Daily Management

Post-Project Management

Project Closure

Weekly Closure

Project Initiation

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C1

C2

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6


F7


G3


G2

G1

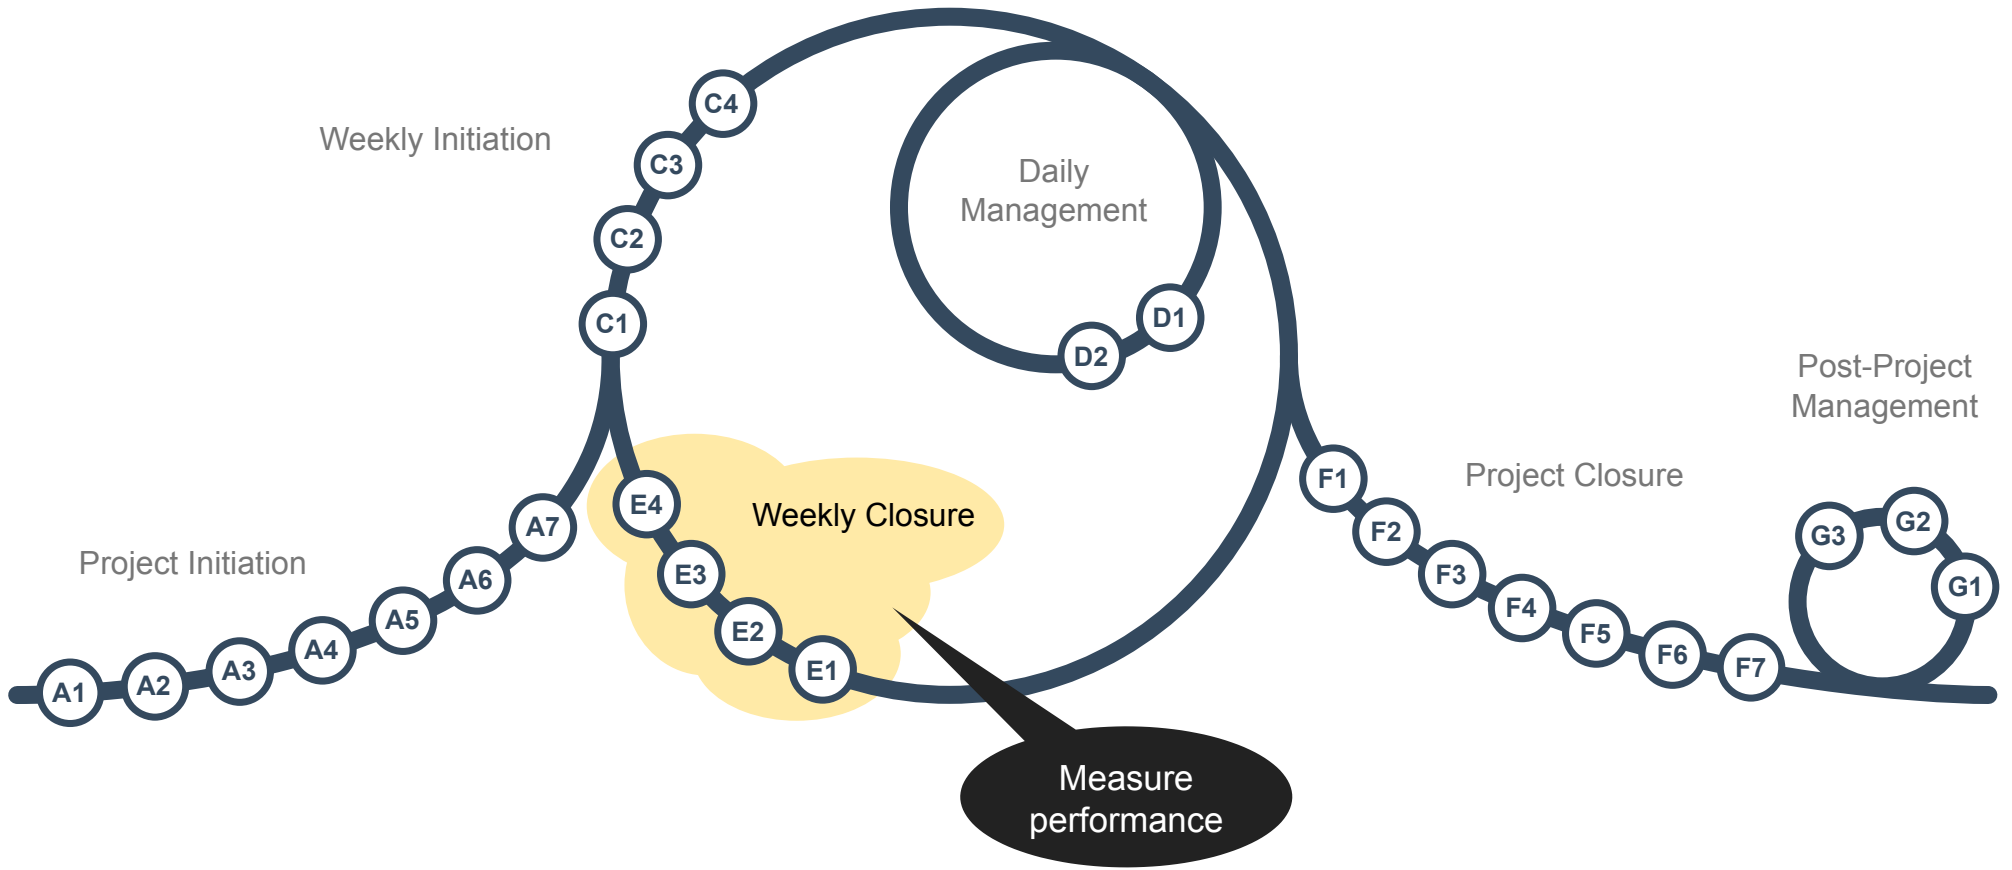

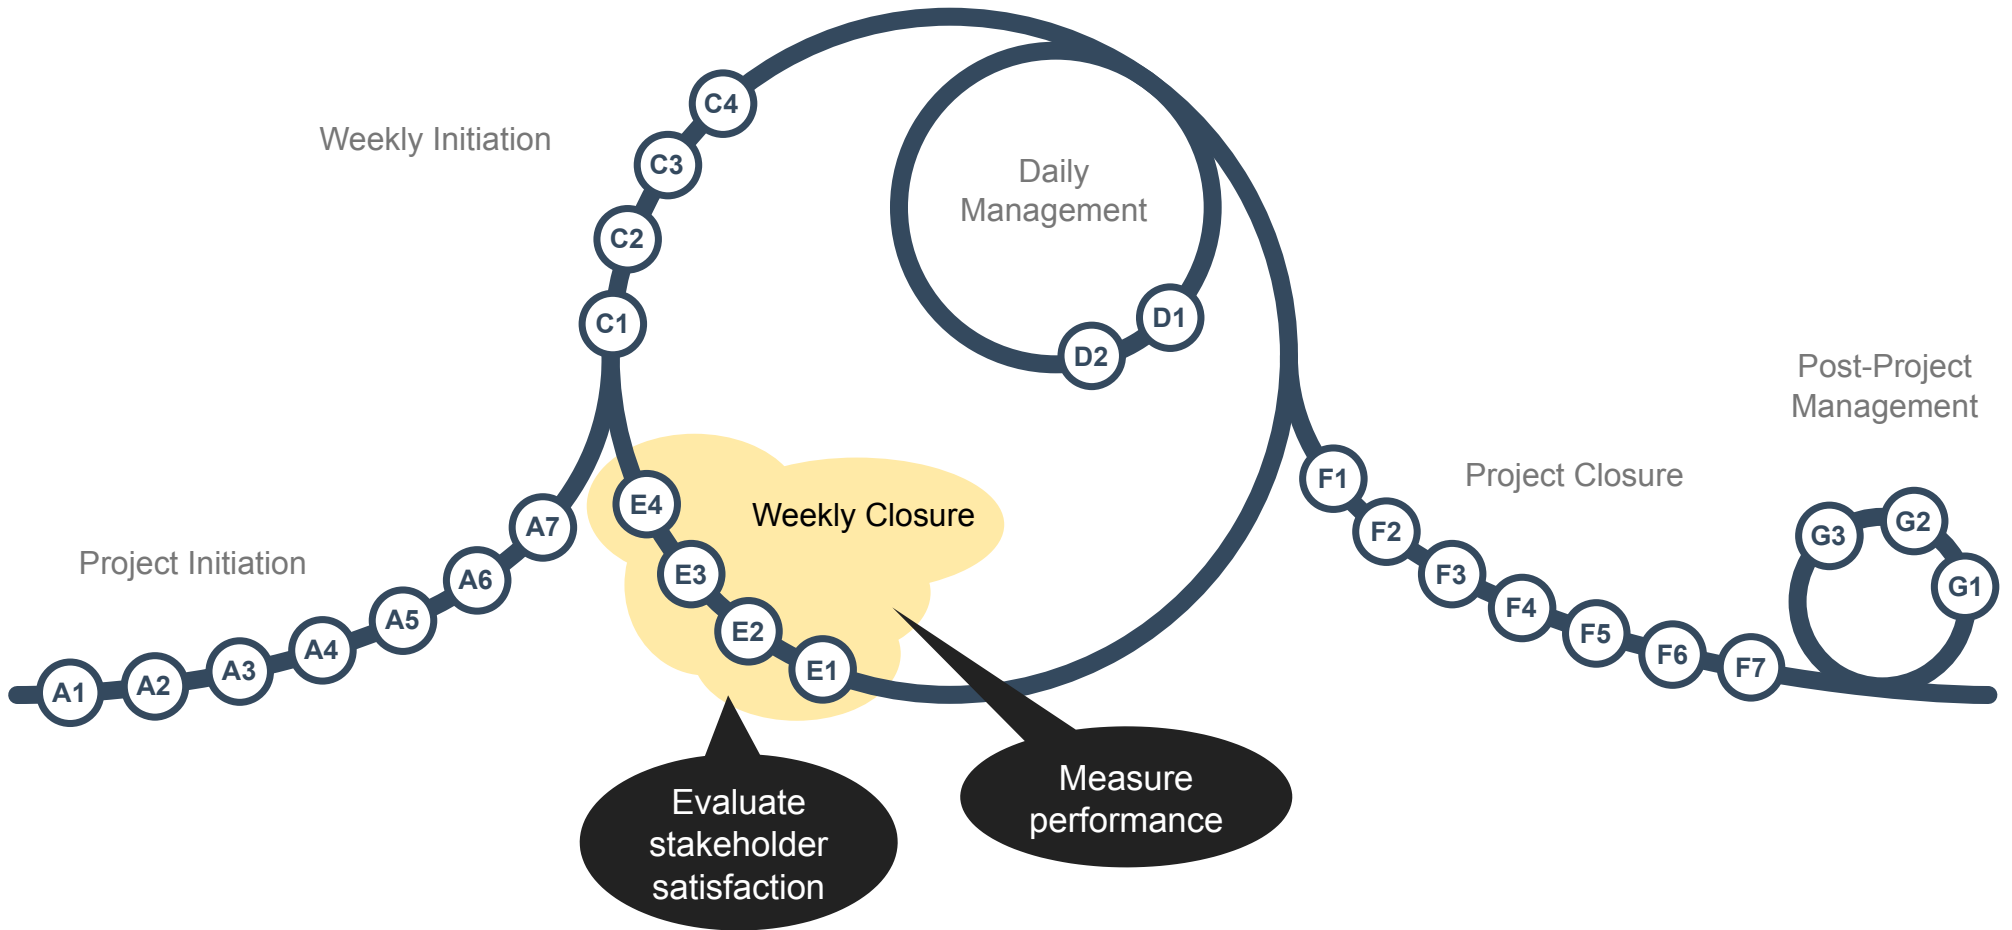

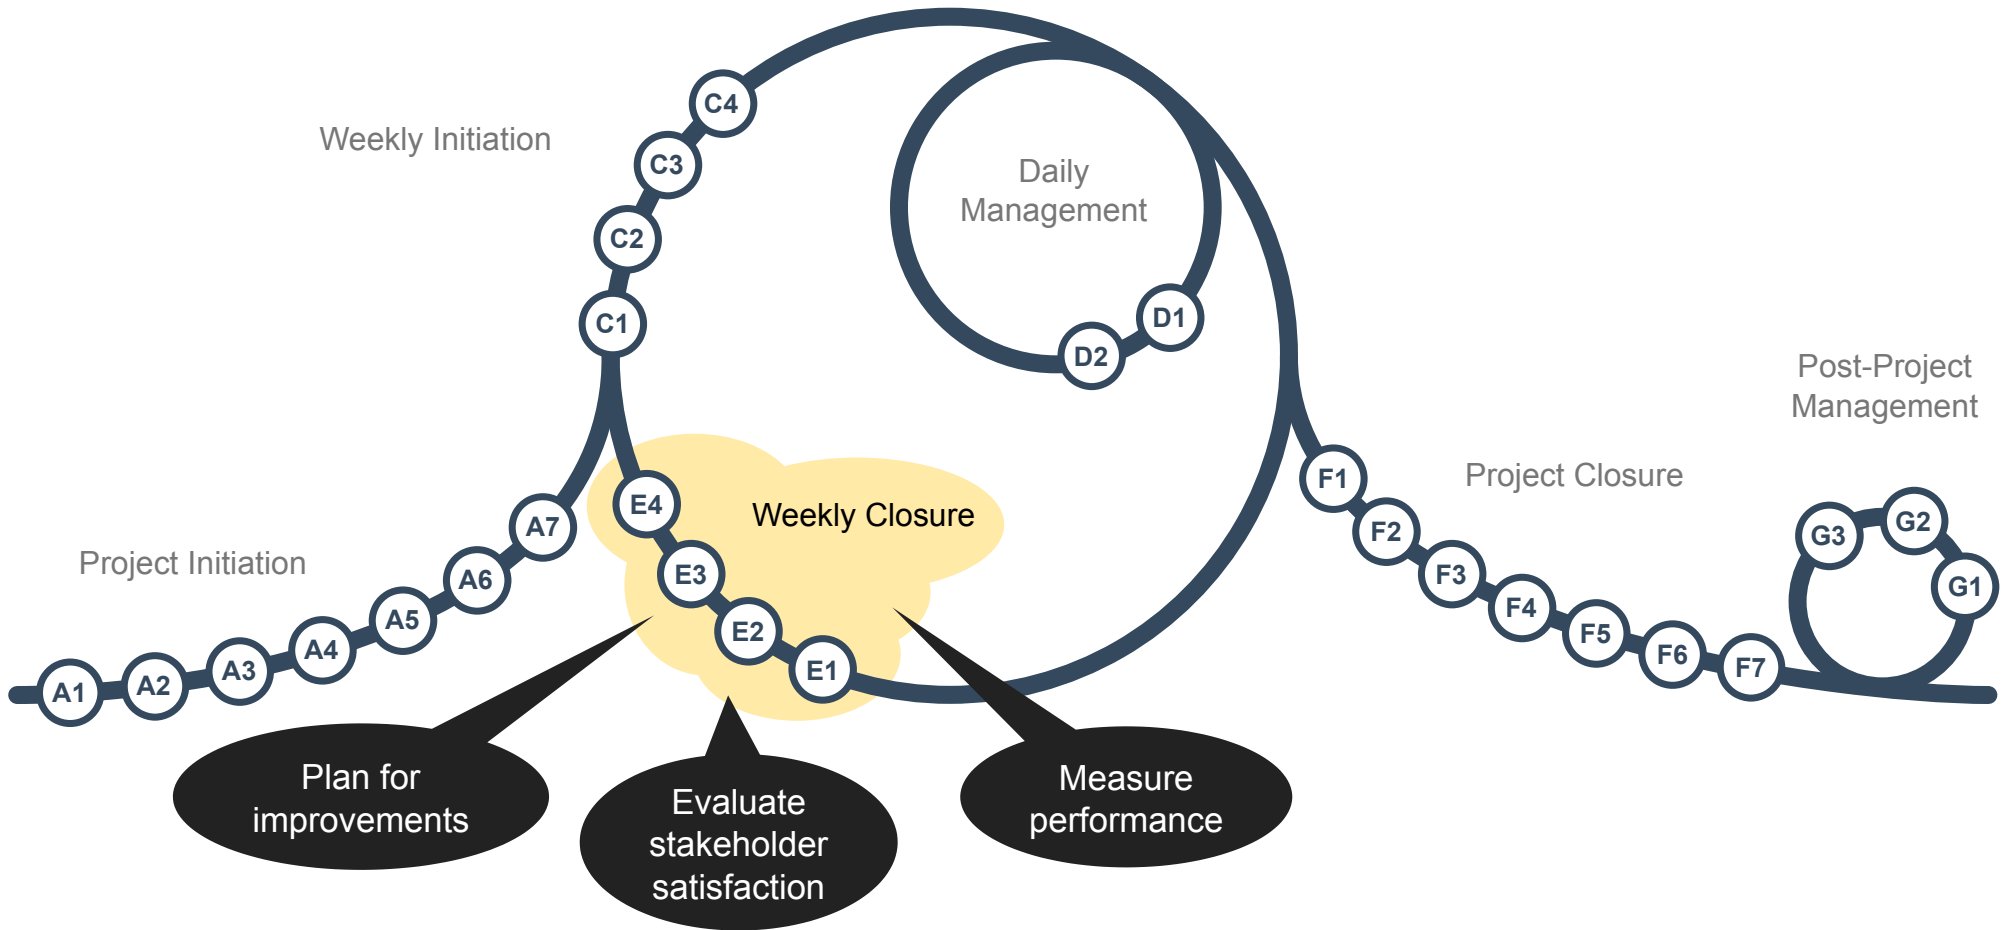

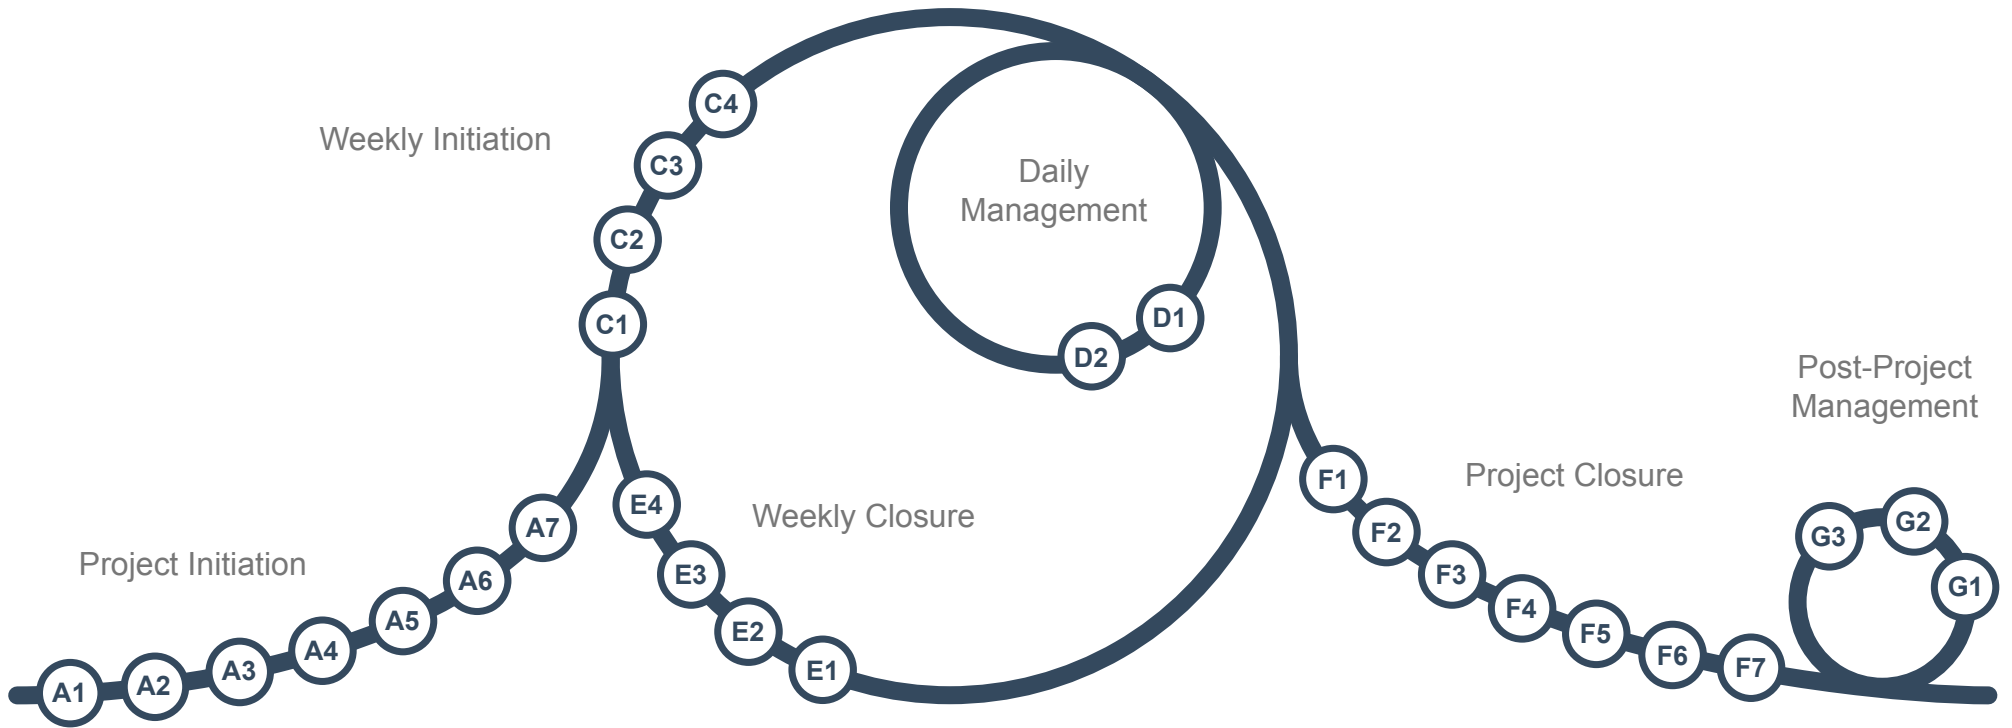

Weekly Initiation

Daily Management

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E1

E2

E3

E4

F1

F2

F3

F4

F5


F6


F7


G3


G2


G1

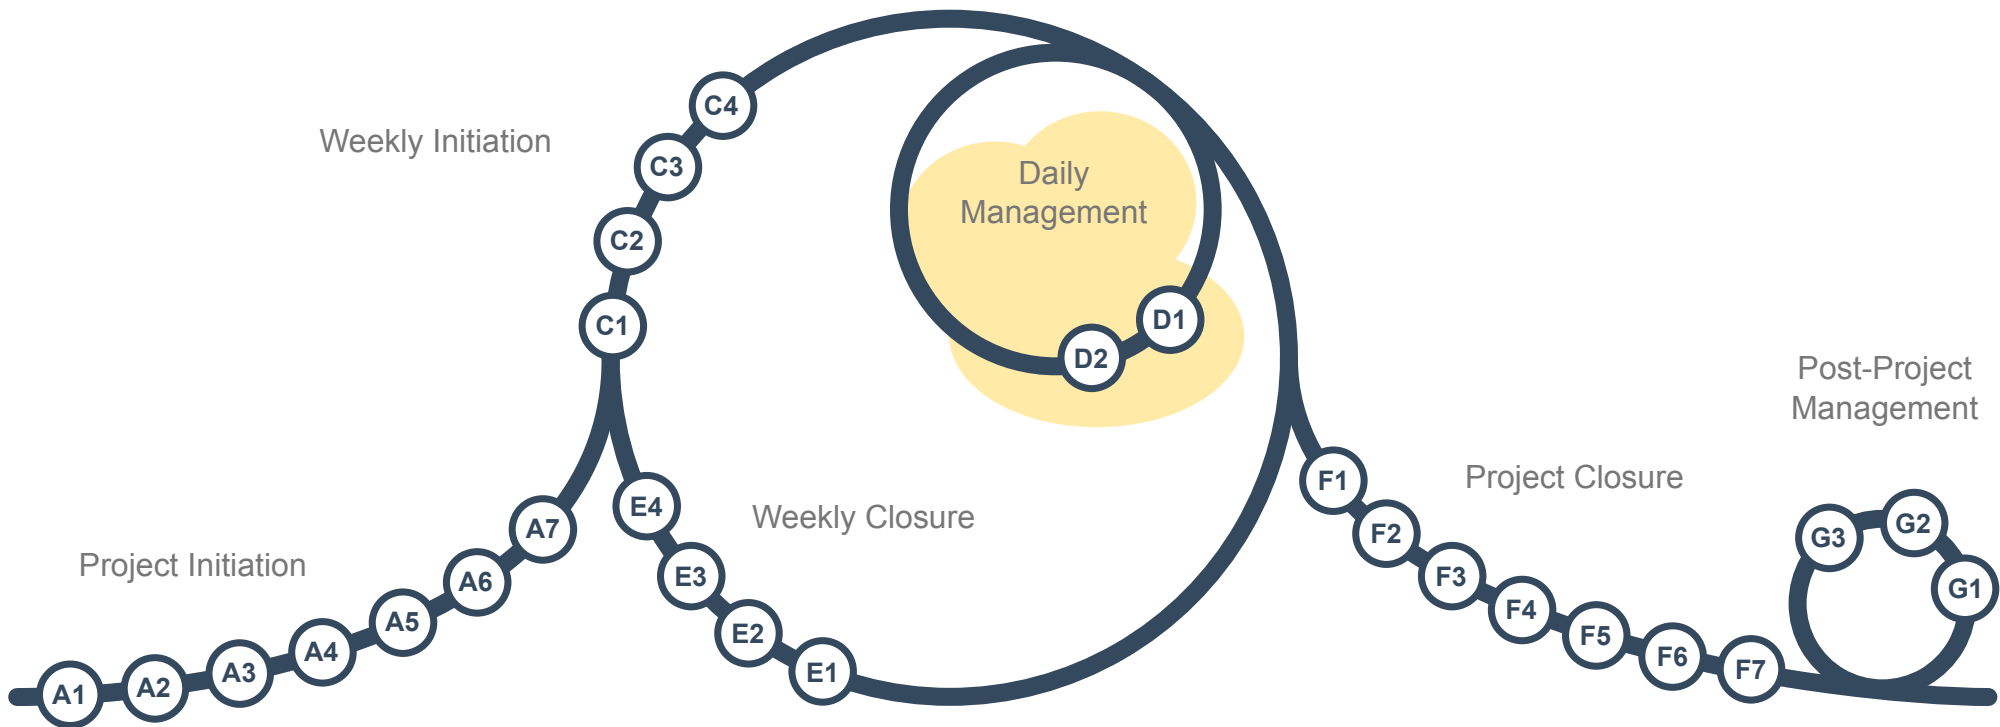


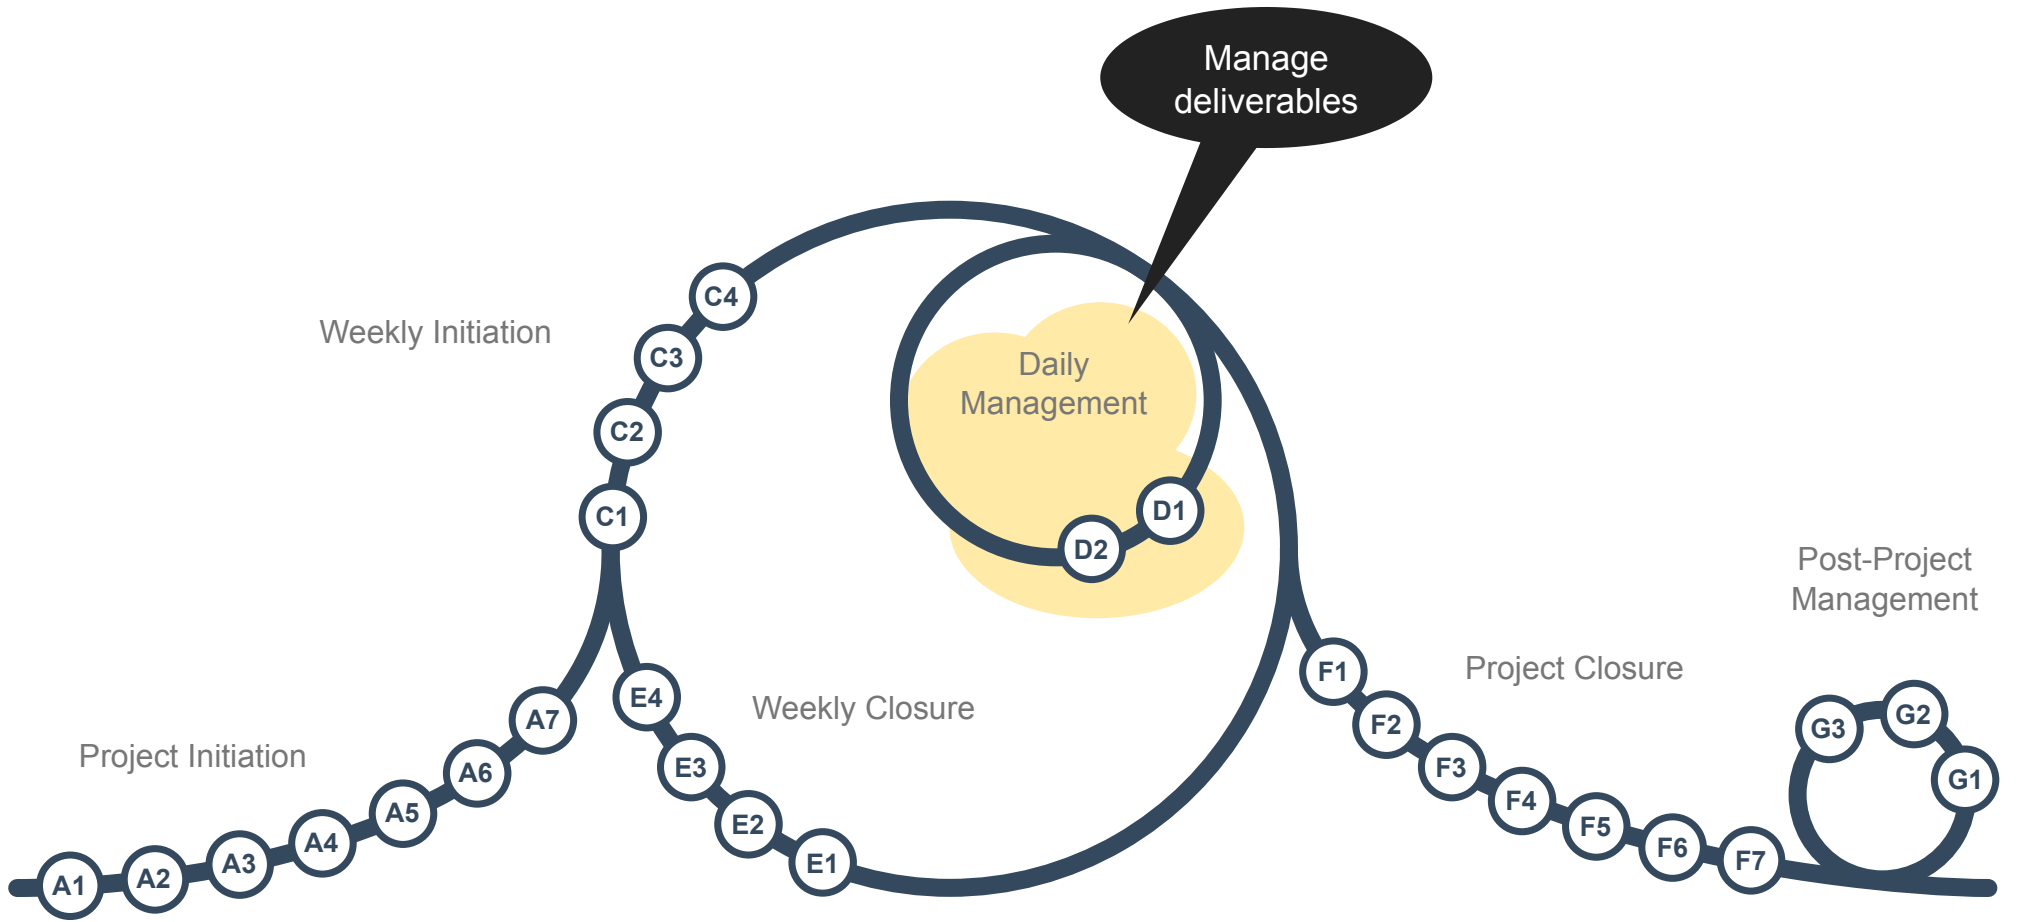


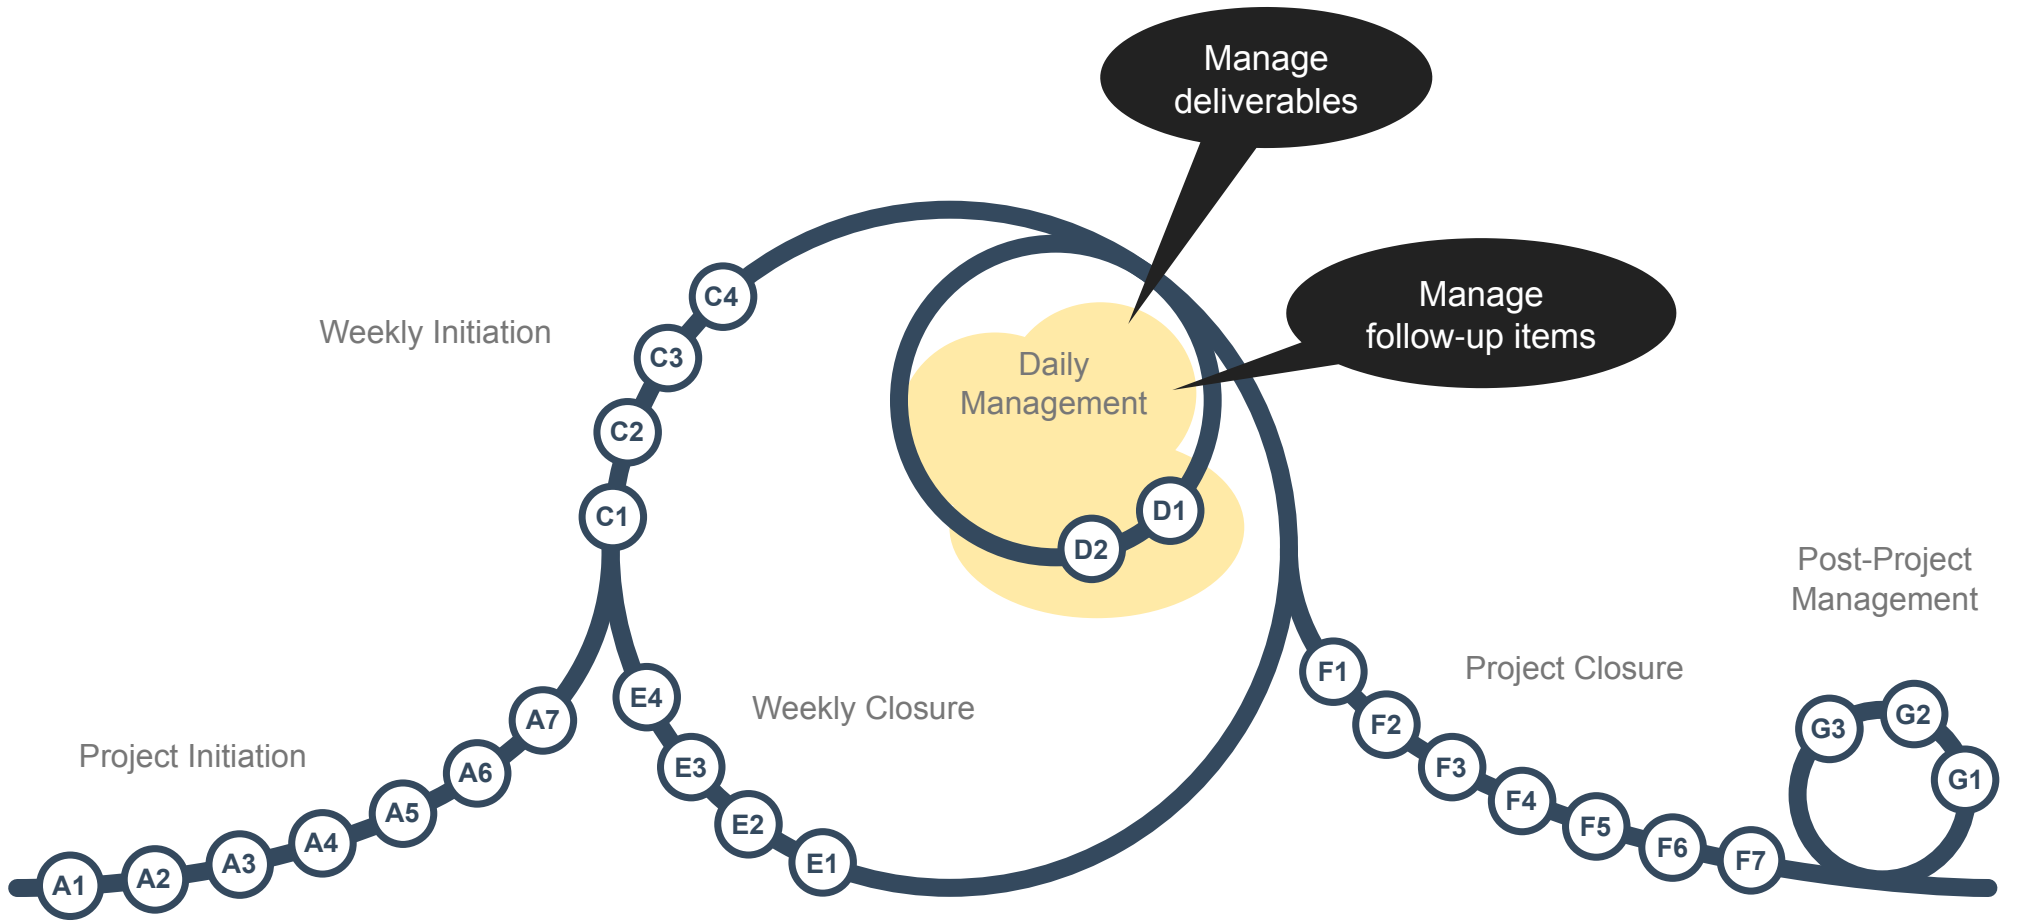


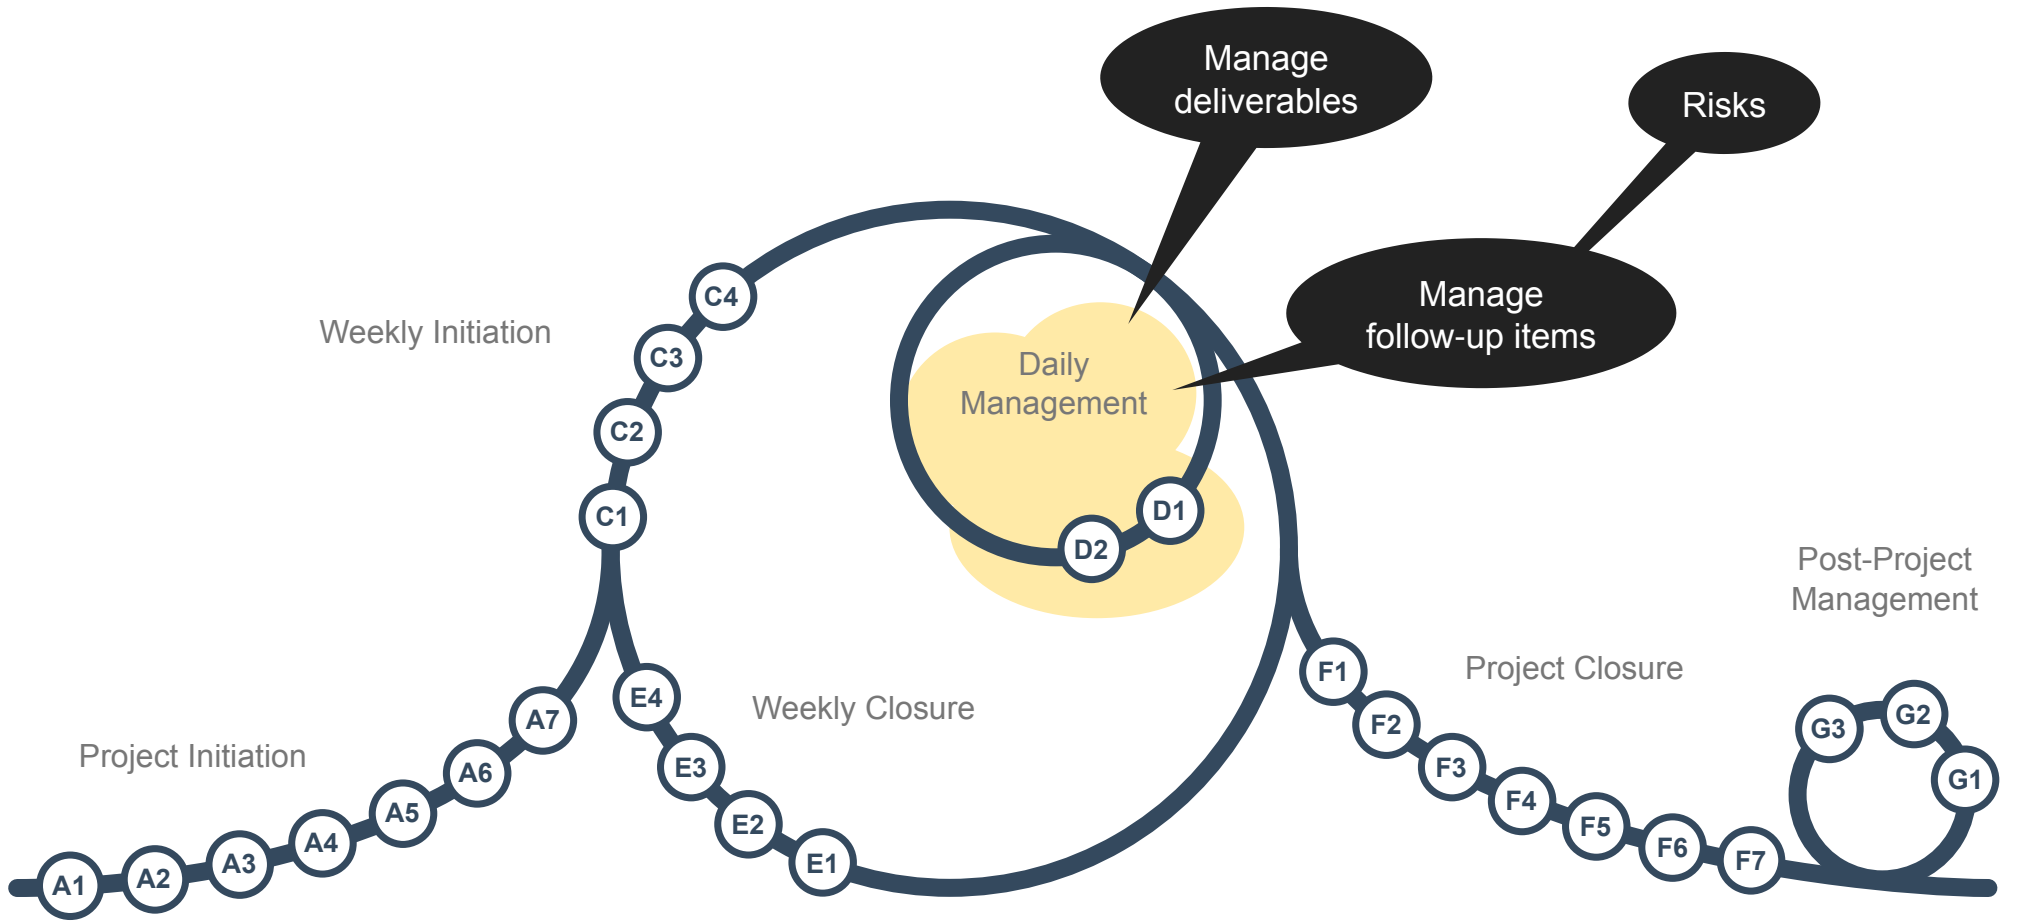


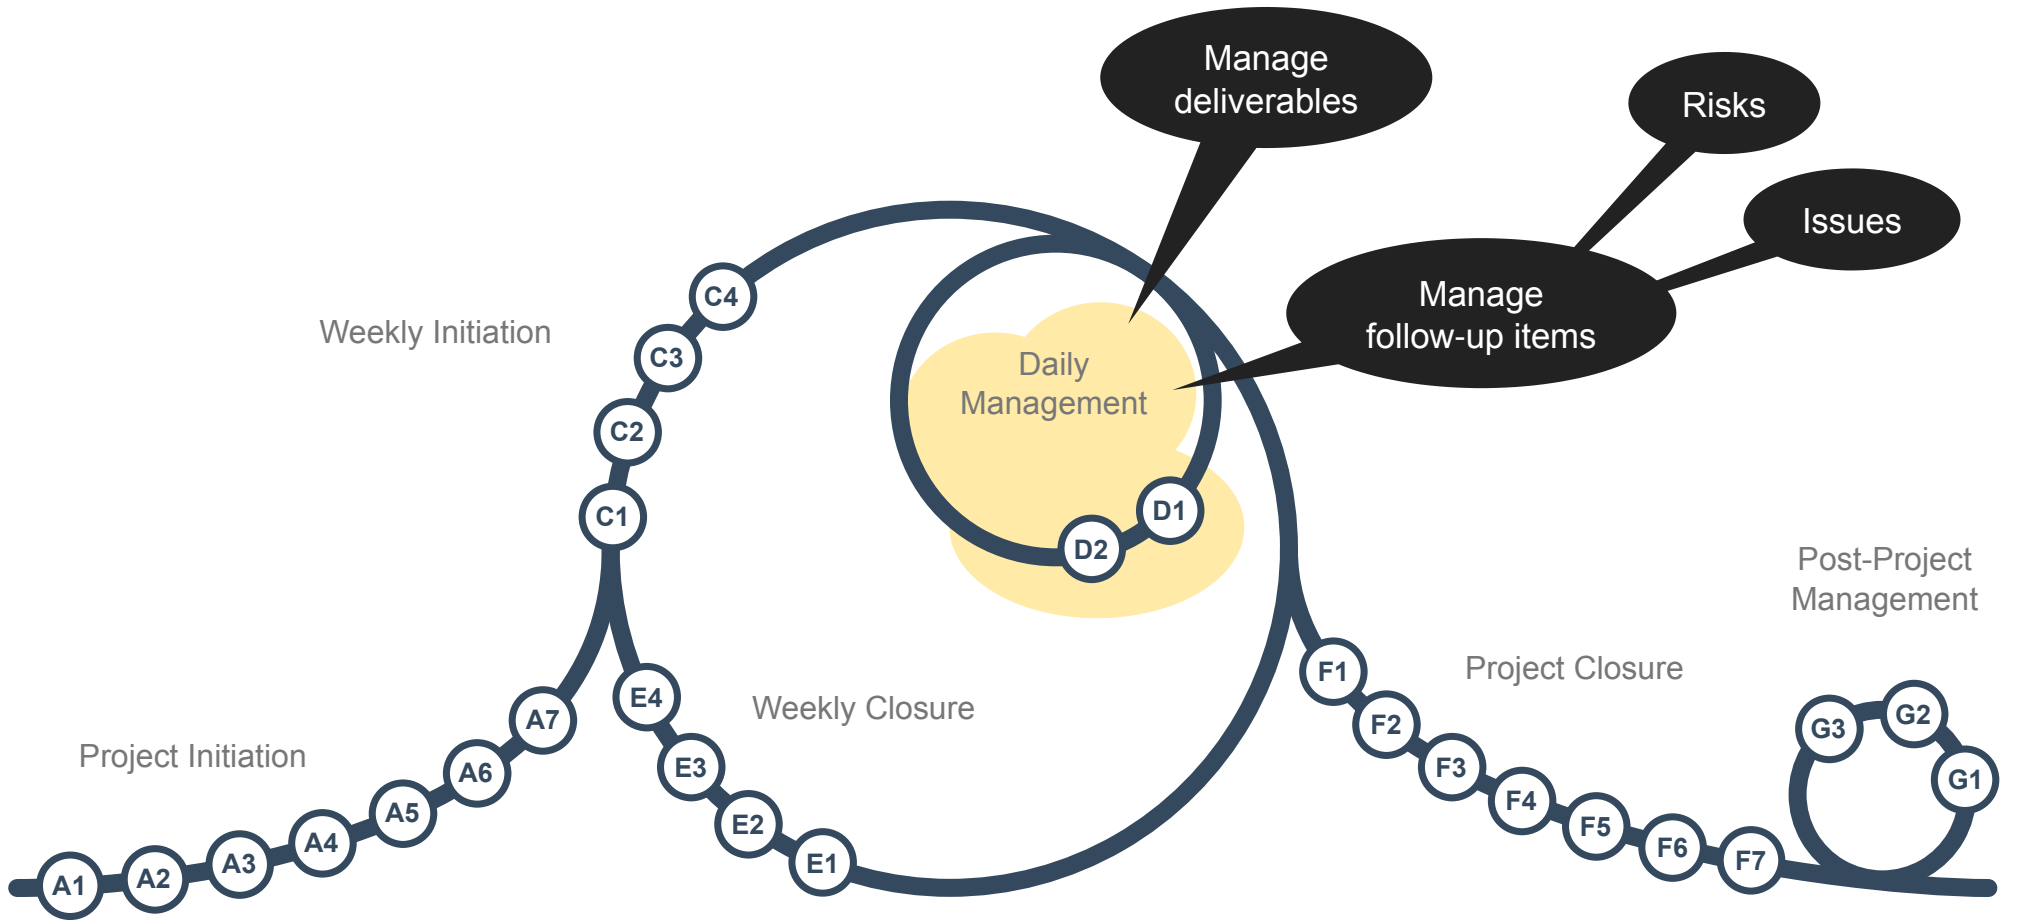

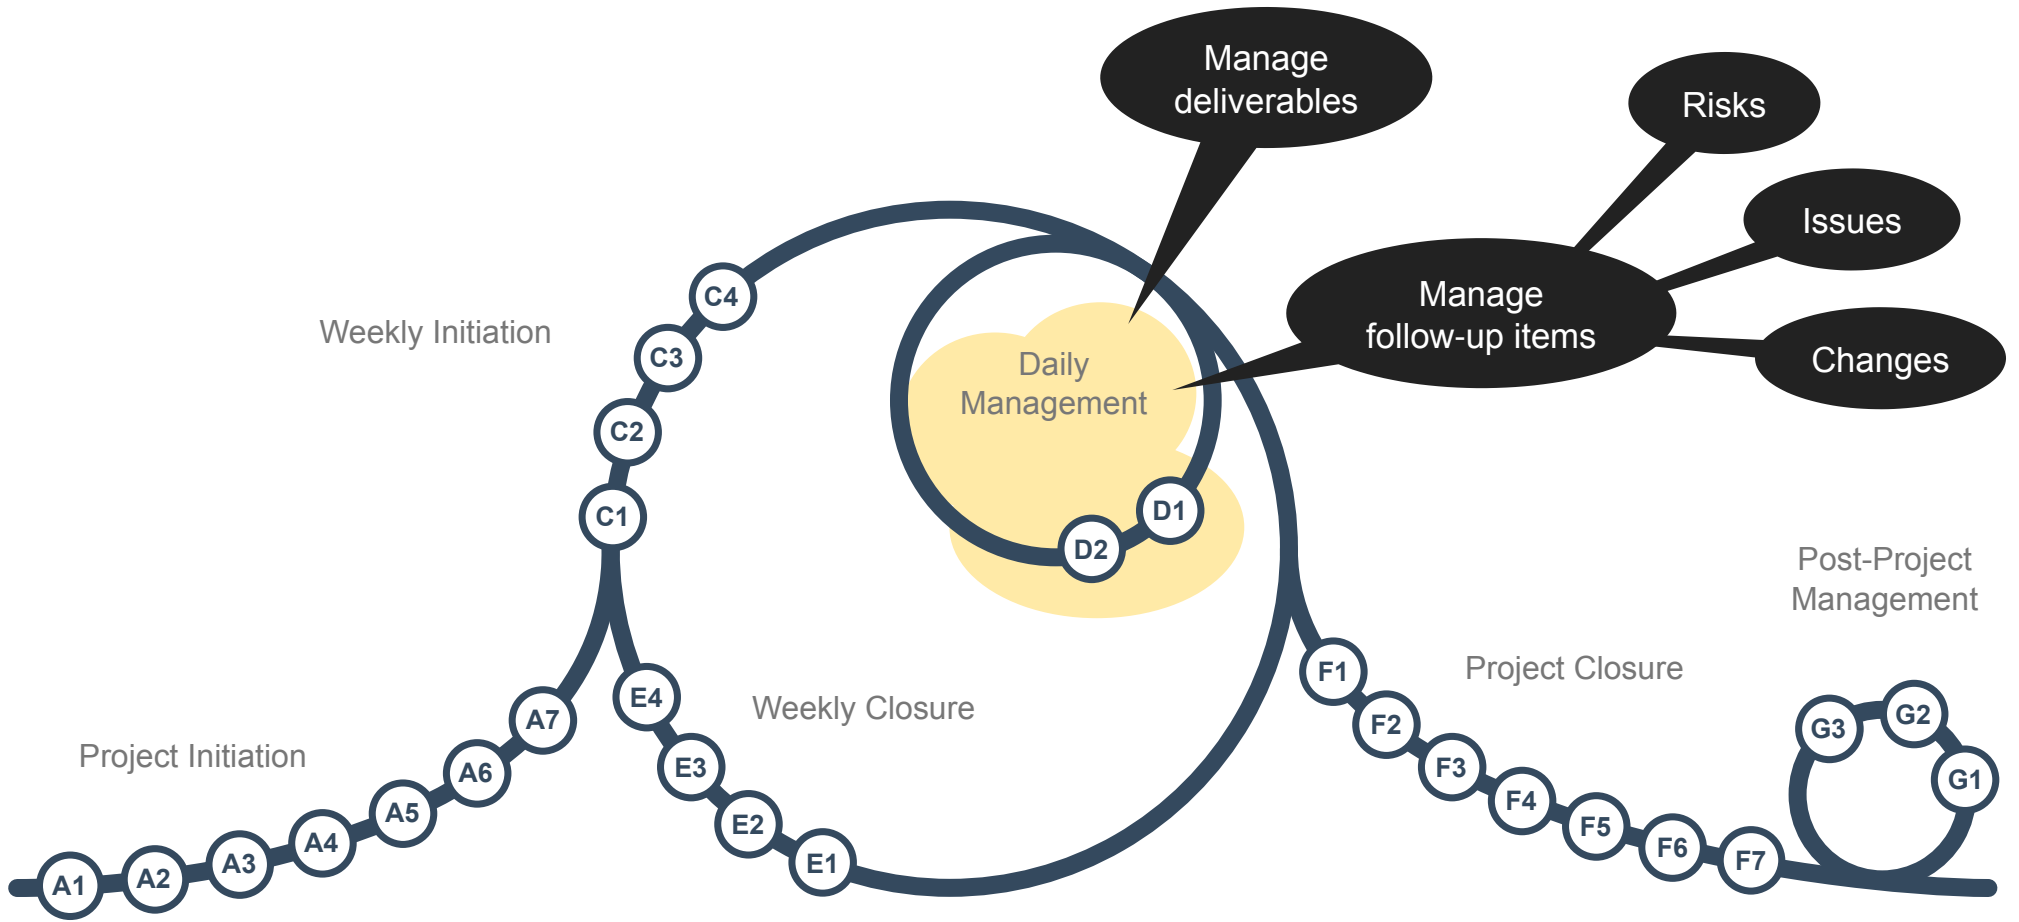

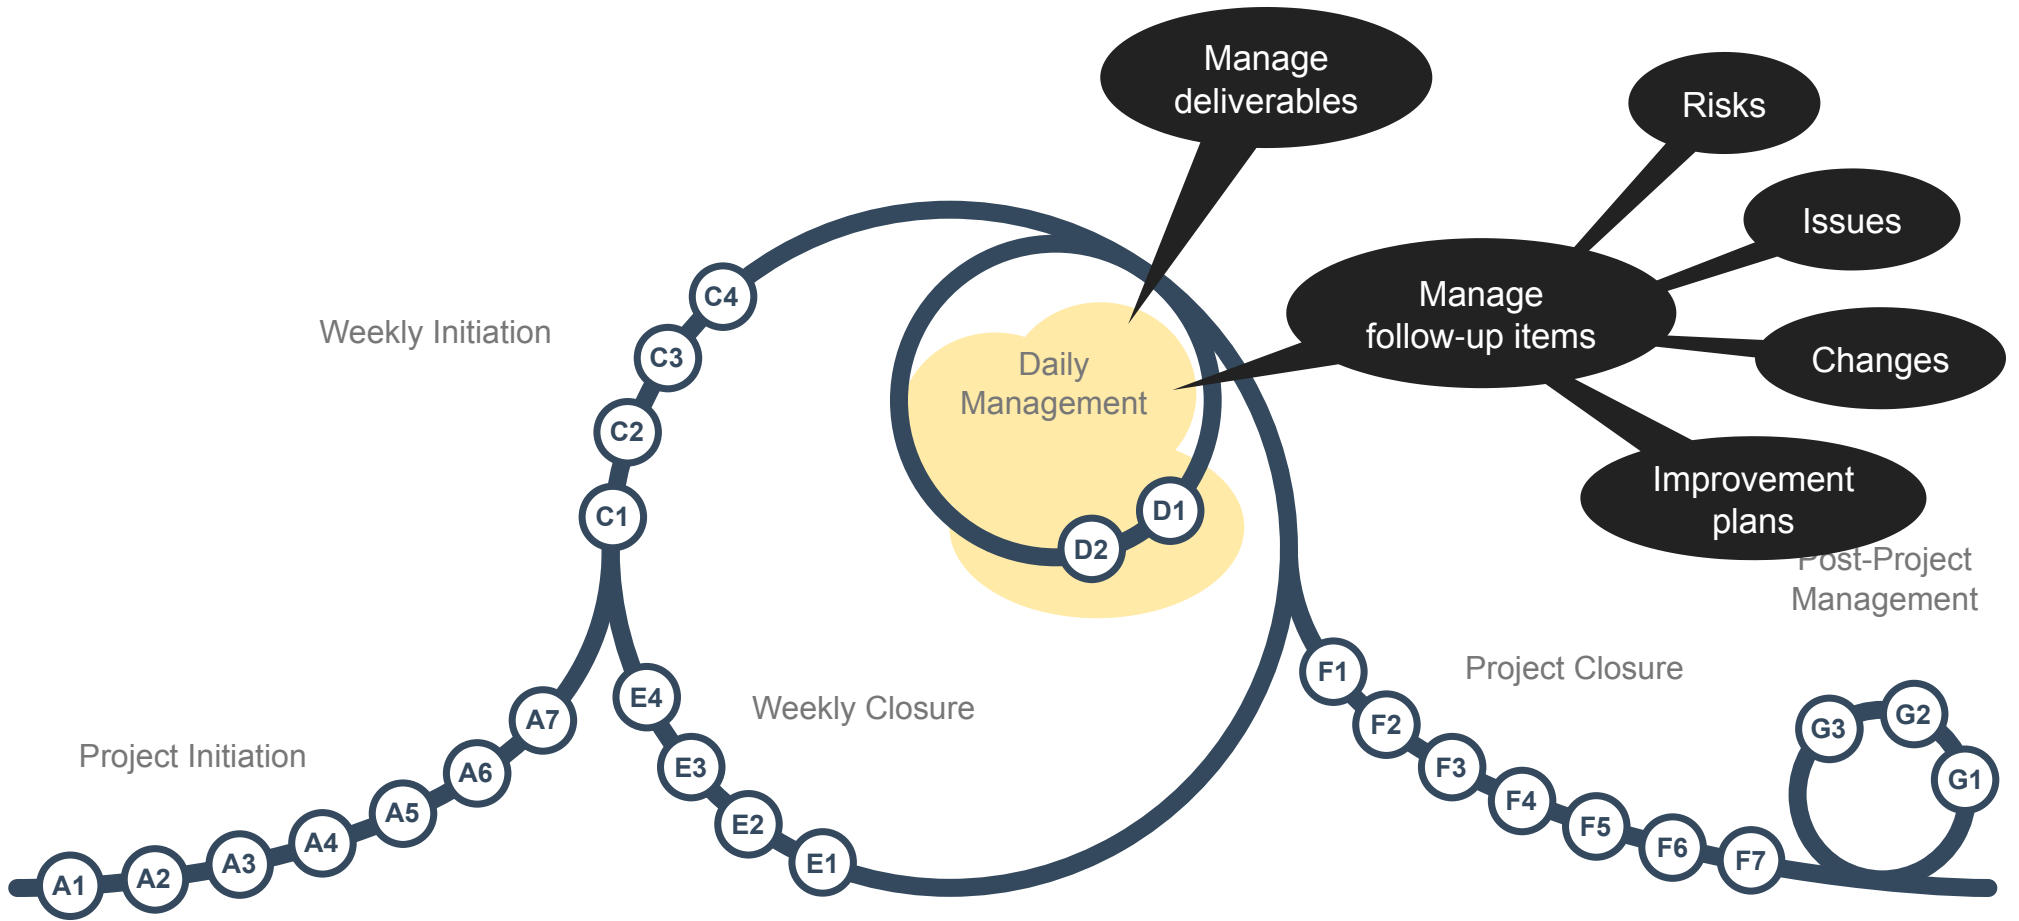

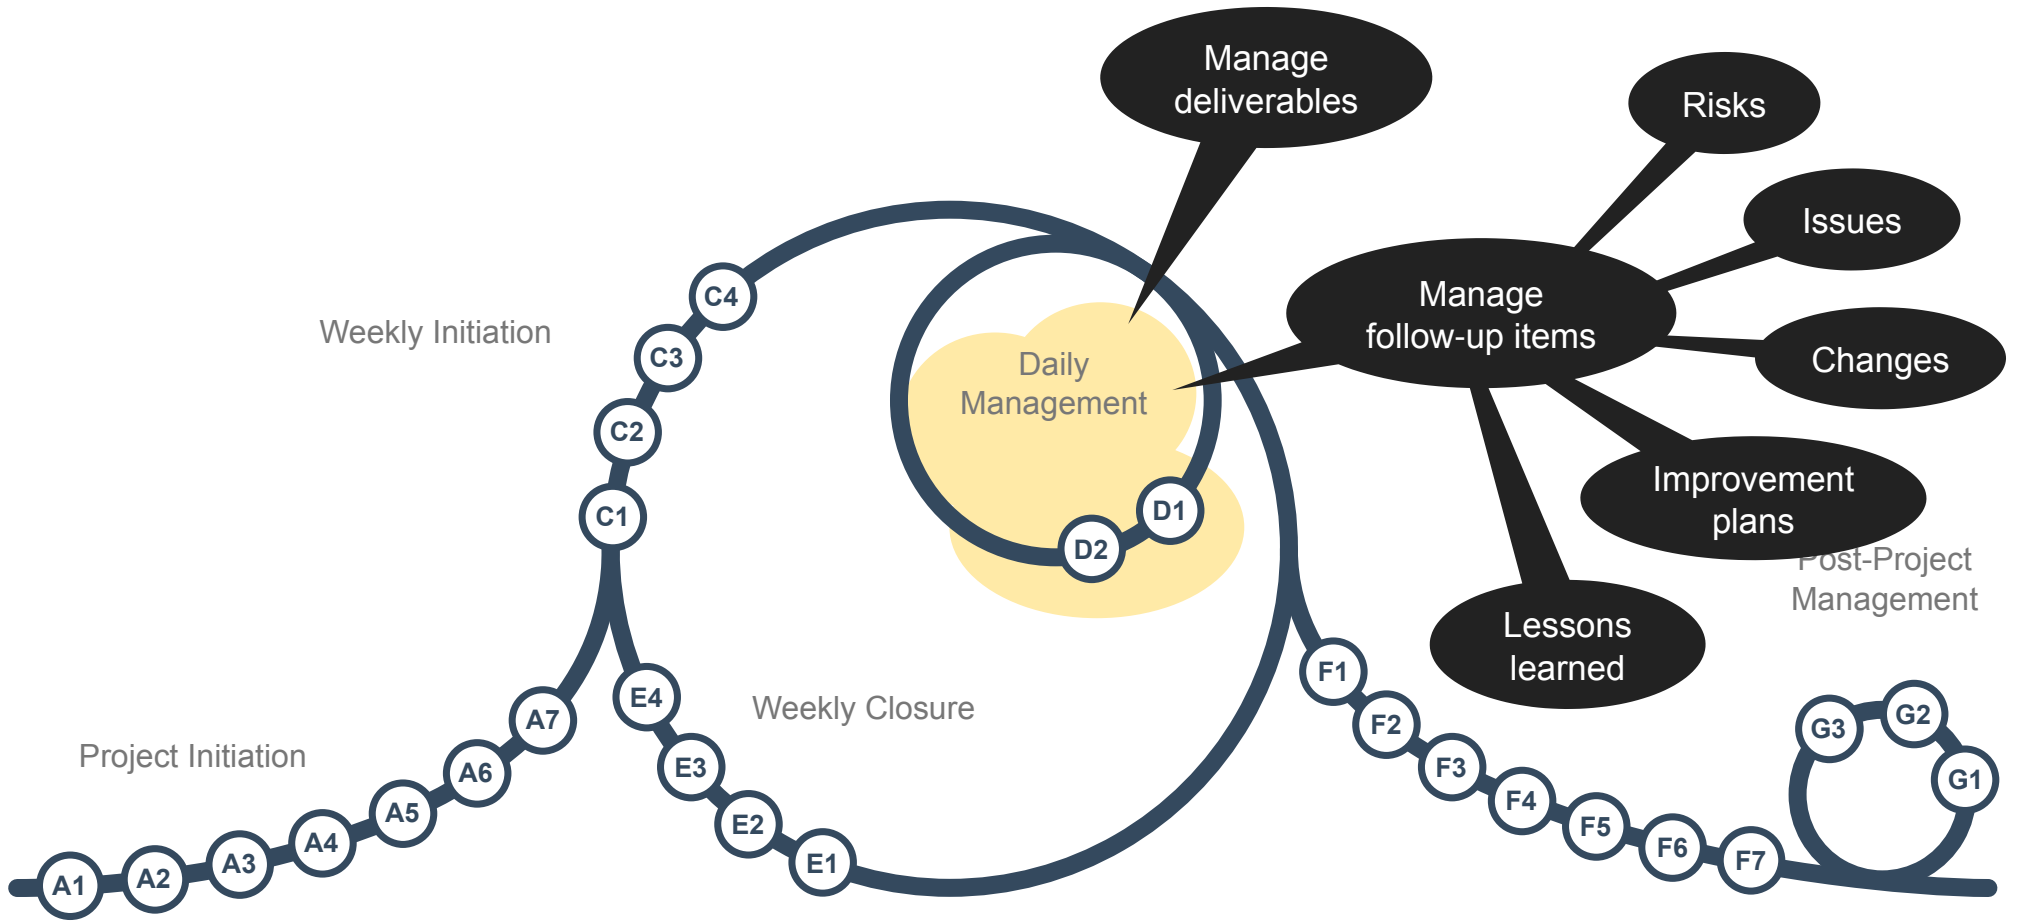

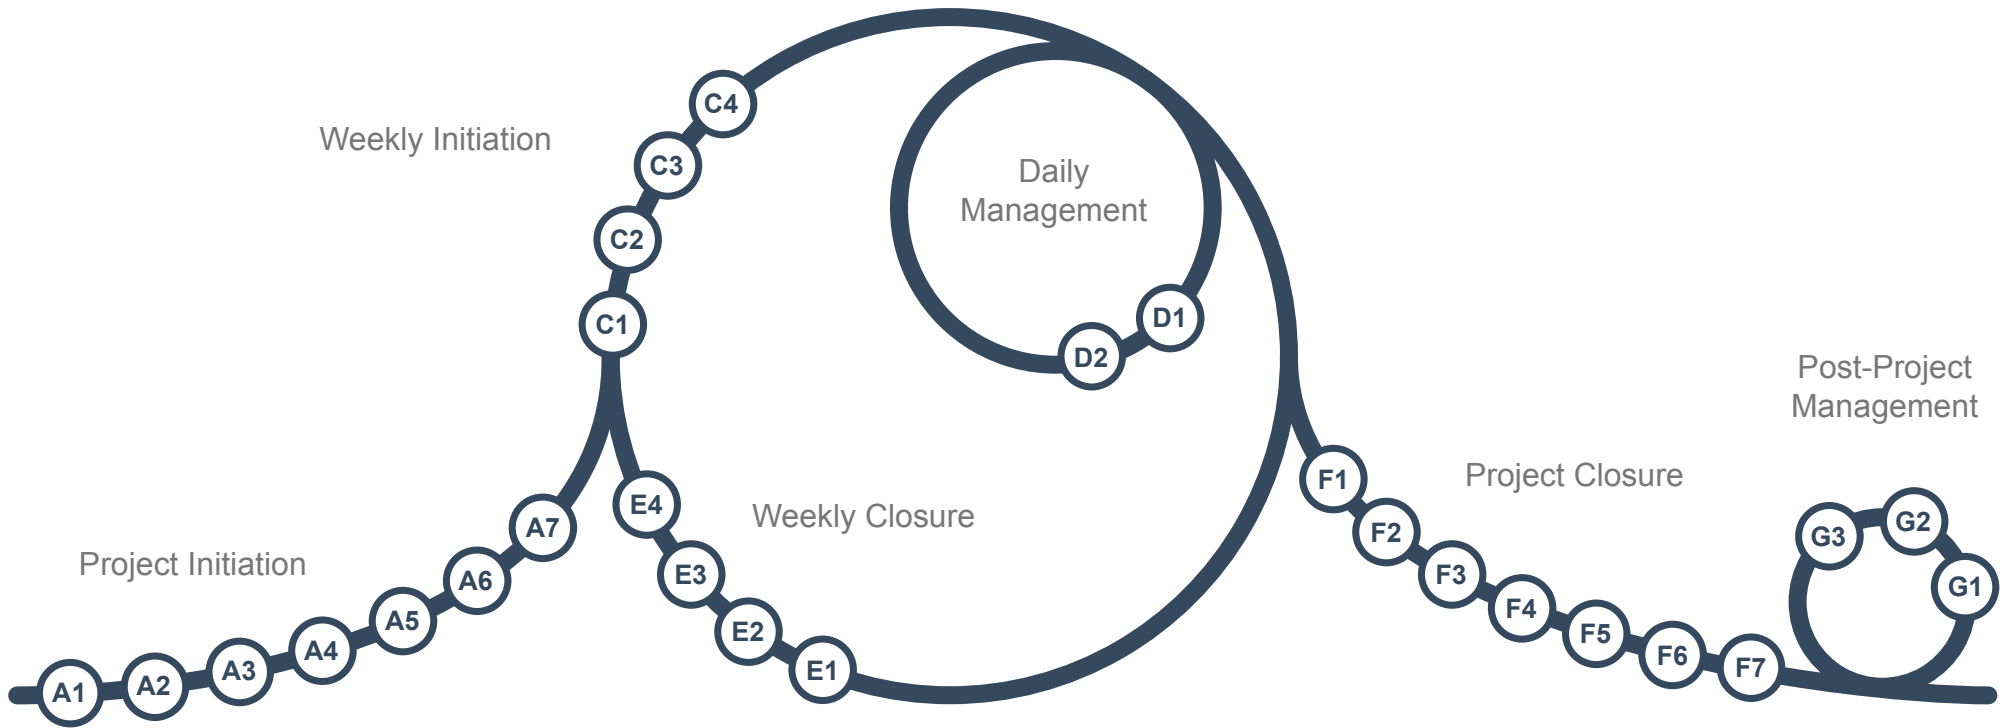

Weekly Initiation


Daily Management


Post-Project Management

Project Initiation

Weekly Closure

Project Closure

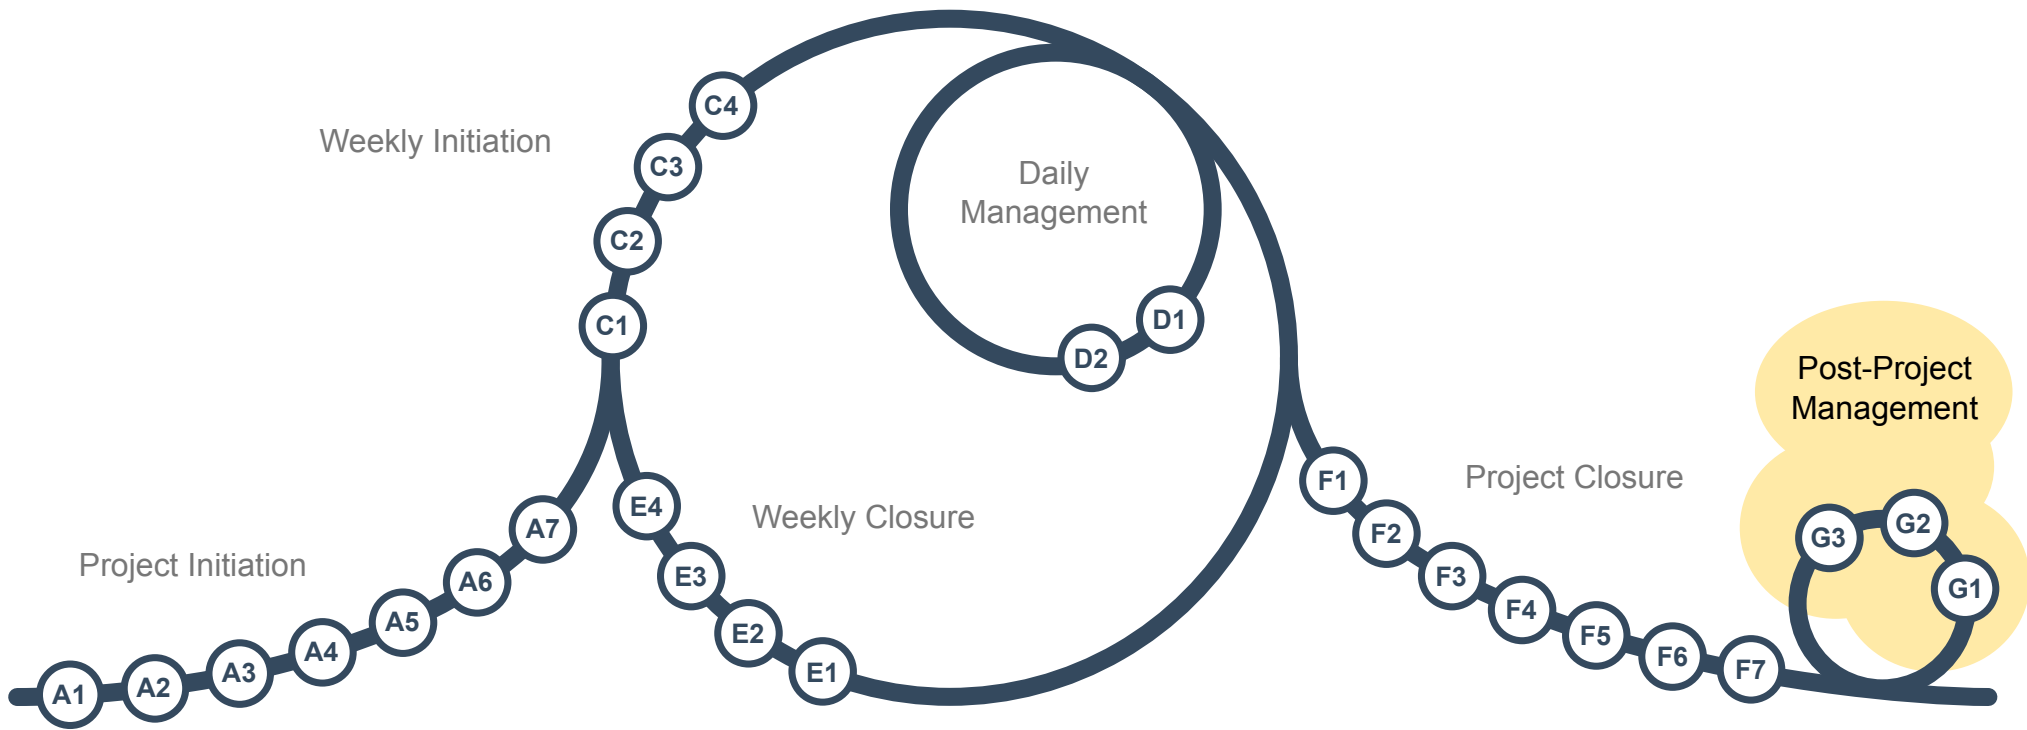

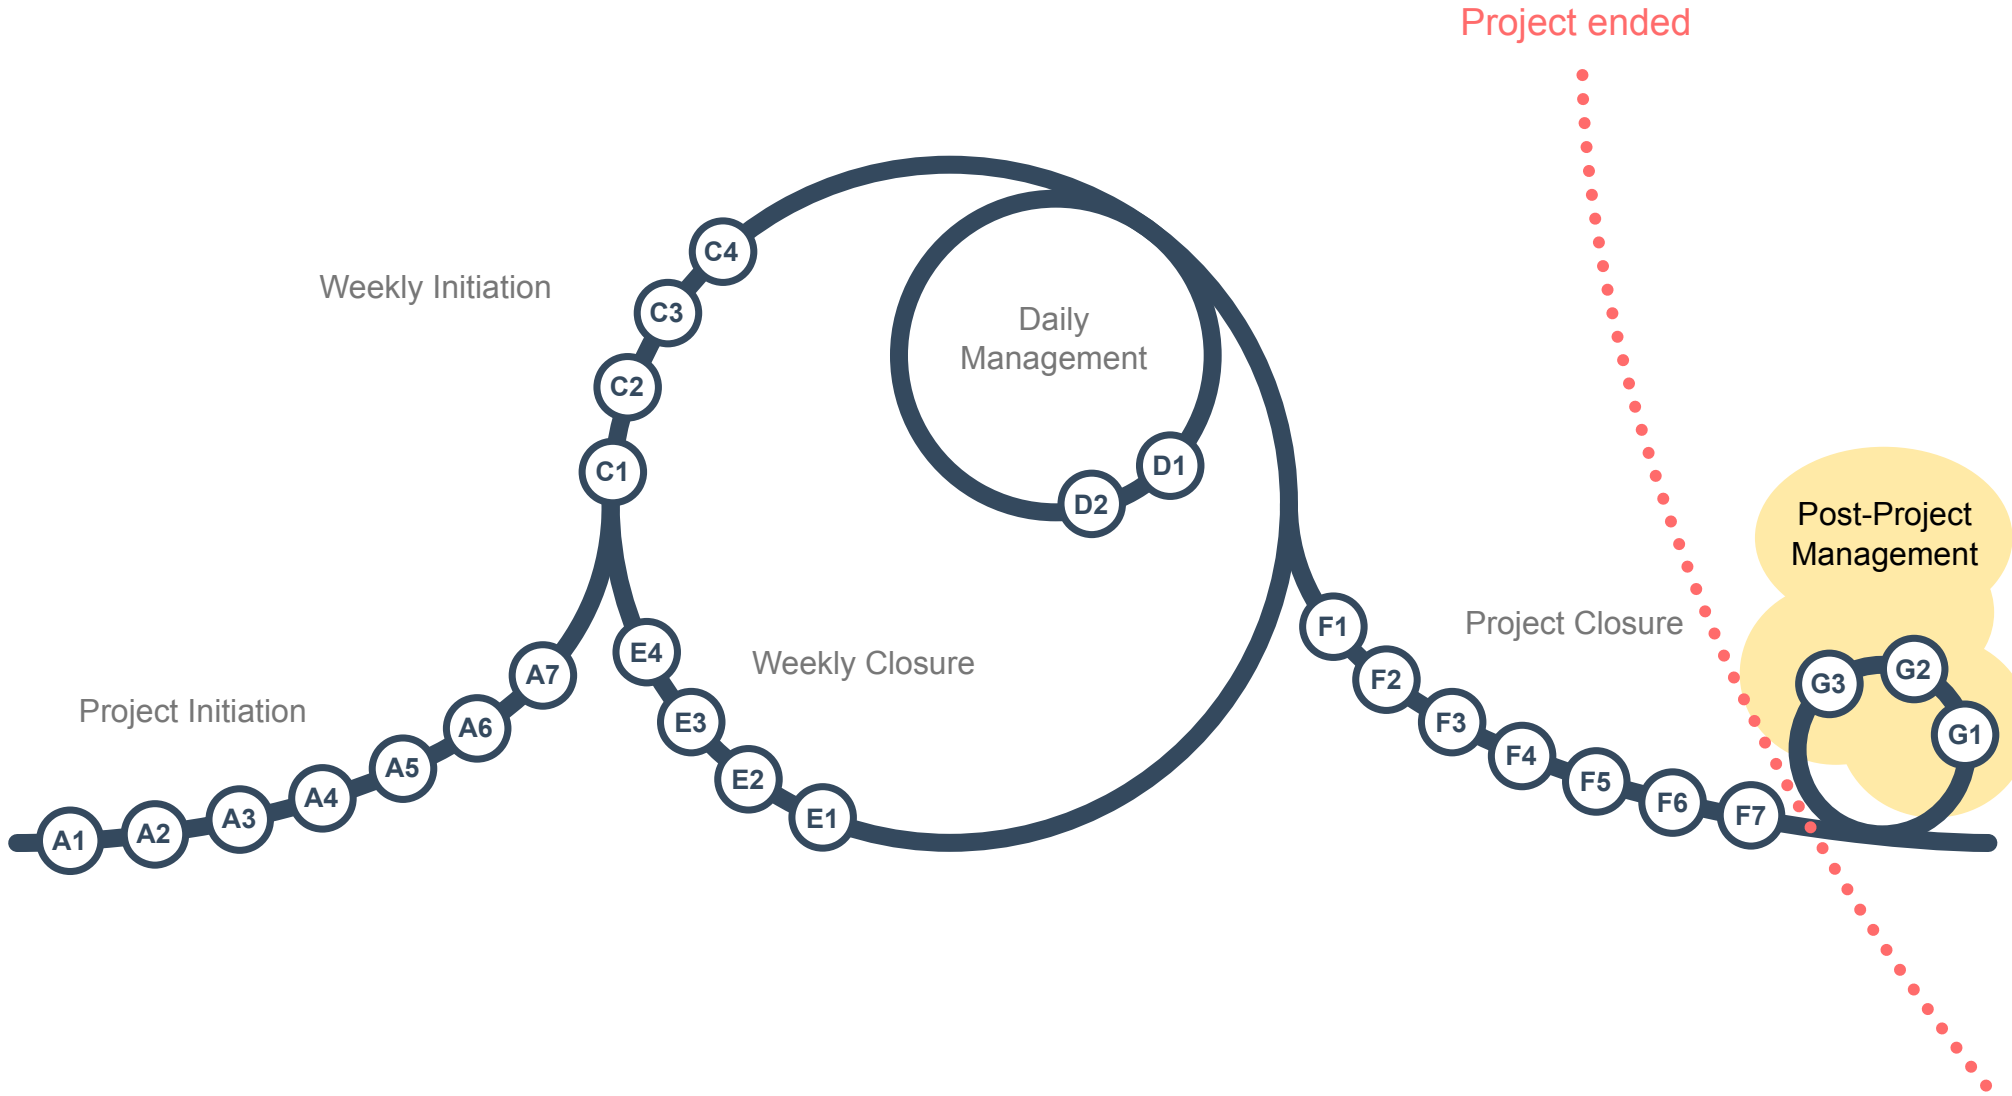

Weekly Initiation

Daily Management

Project ended

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E1

E2

E3

E4

F1

F2

F3

F4

F5


F6

F7

G3

G2

G1

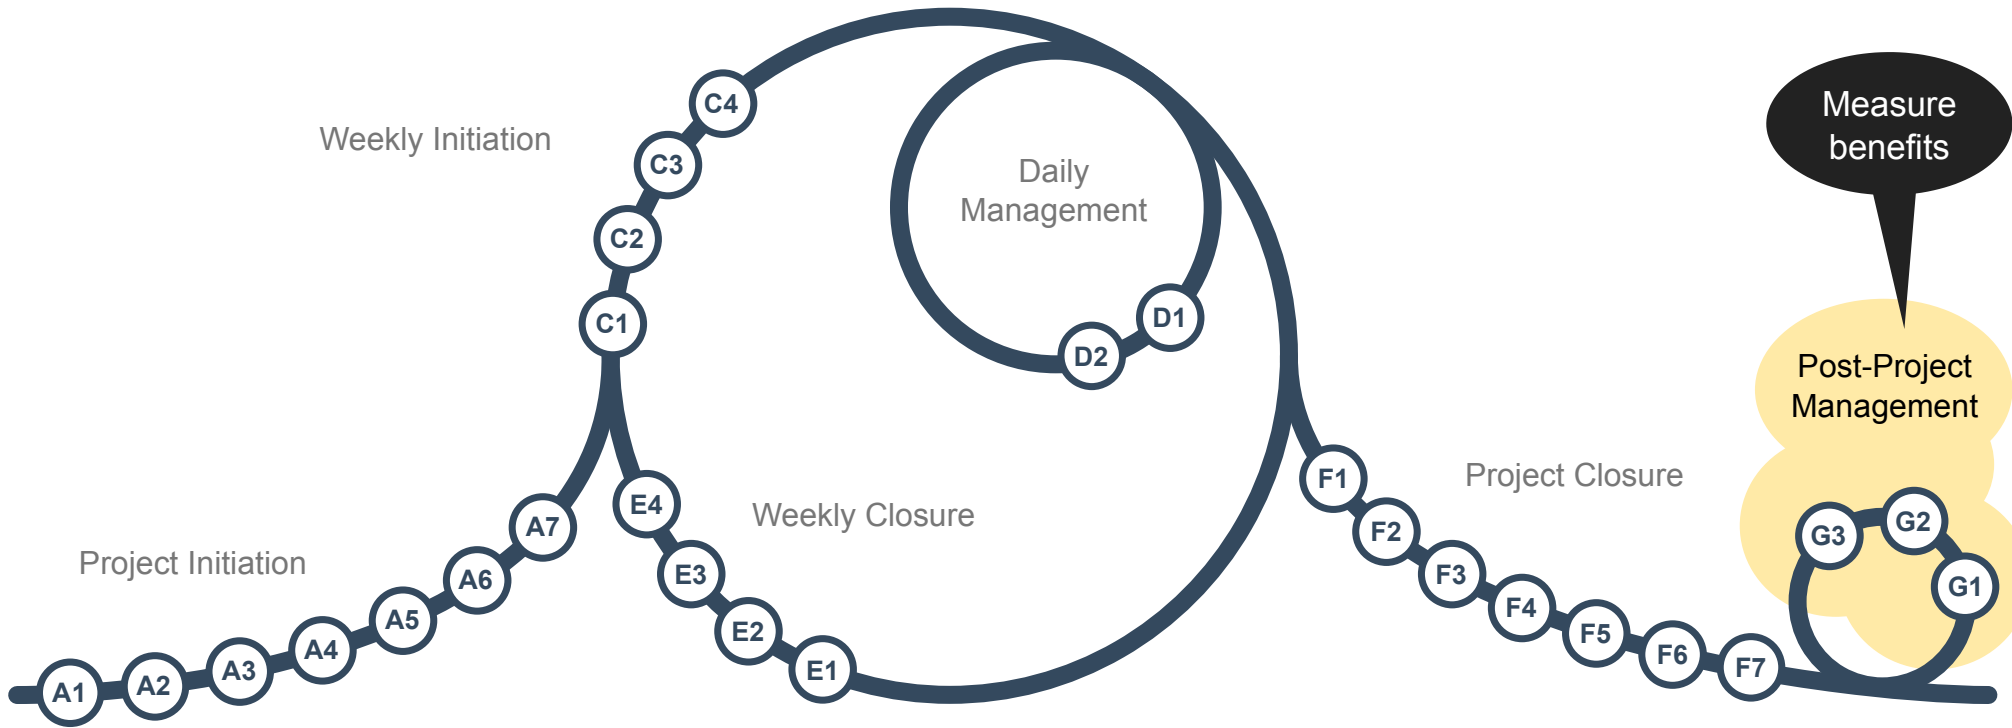

Measure benefits

Post-Project Management


Weekly Initiation

Daily Management

Weekly Closure

Project Initiation

Project Closure

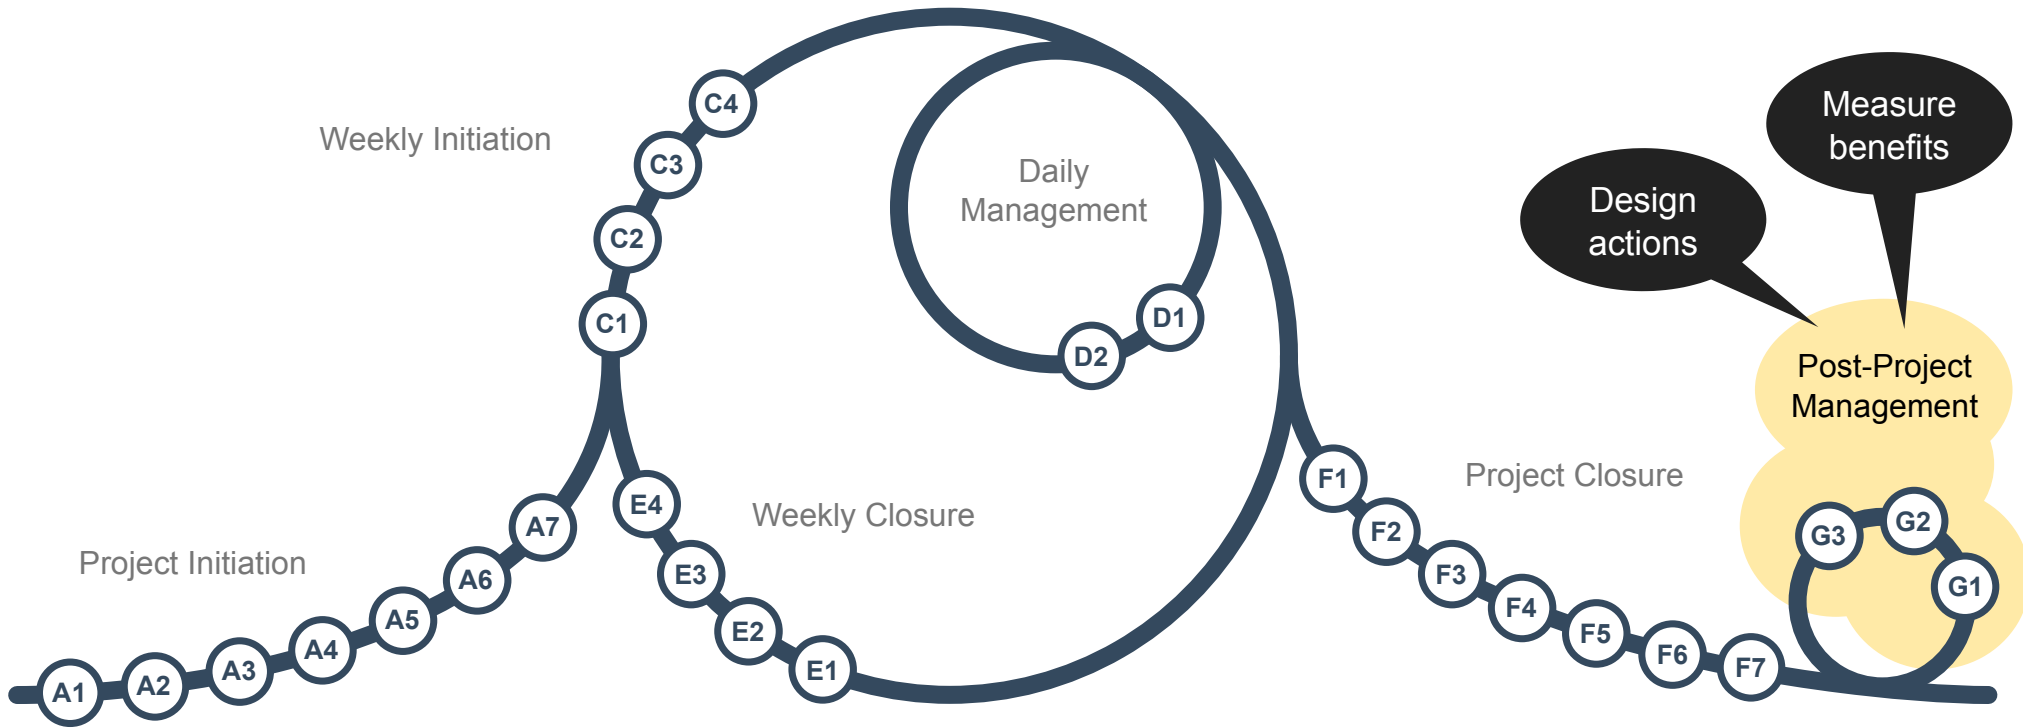

Project Initiation

Weekly Initiation

Daily Management

Weekly Closure

Project Closure

Post-Project Management

Design actions

Measure benefits

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

D2

D1

E1

E2

E3

E4

F1

F2

F3

F4

F5


F6

F7

G3

G2

G1

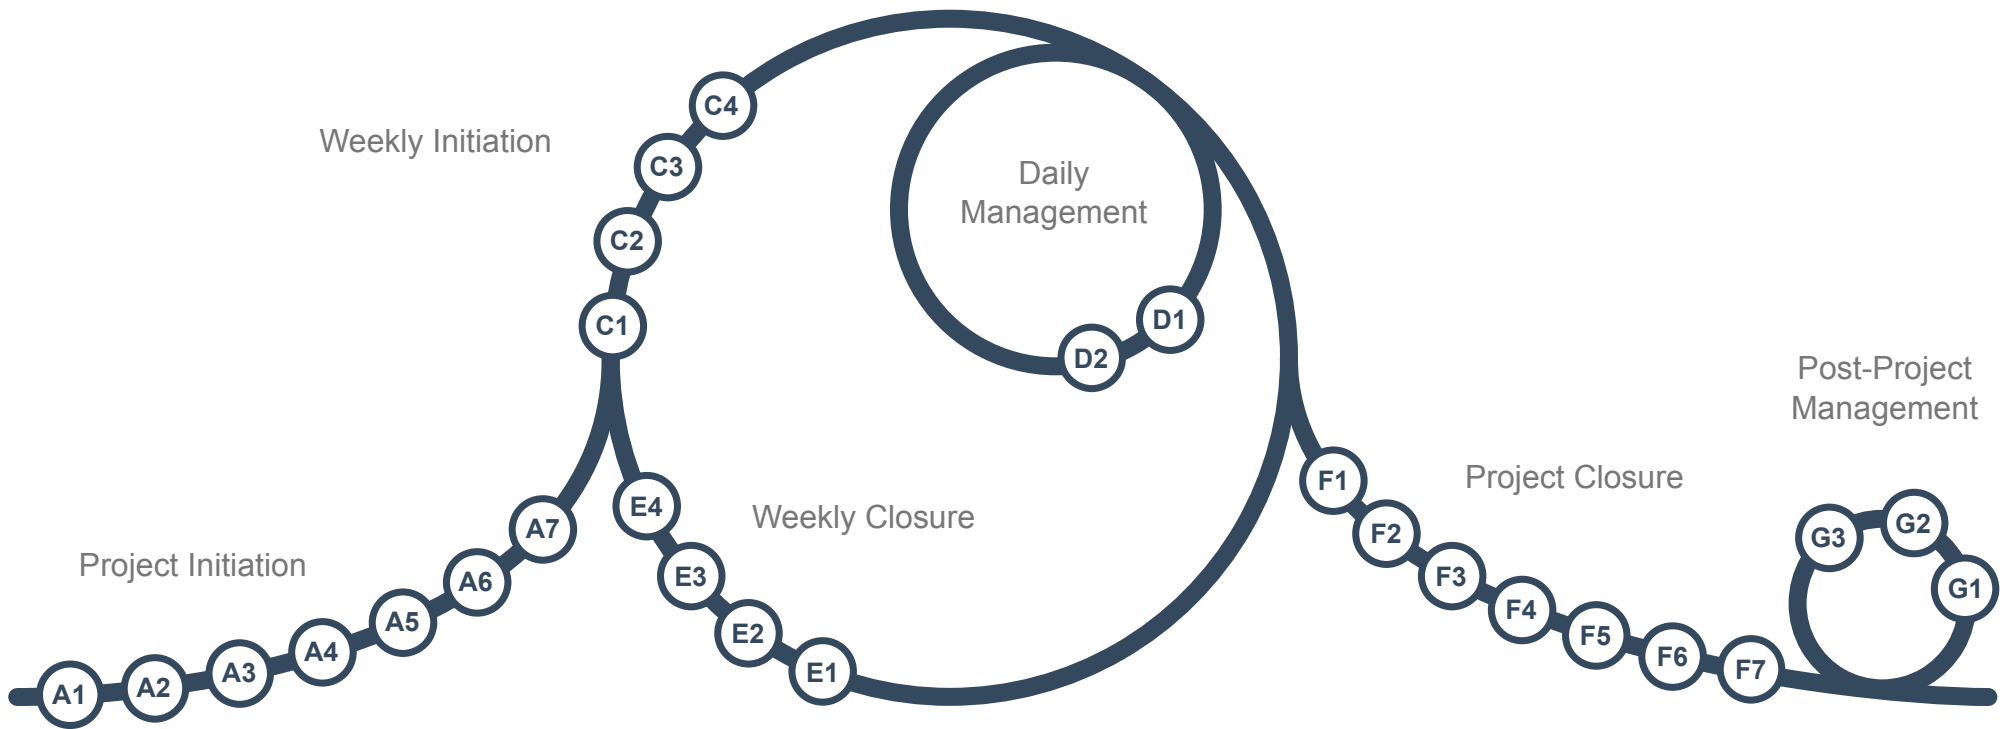


① High-level overview




② Full review


③ NUPP

④ Tailoring

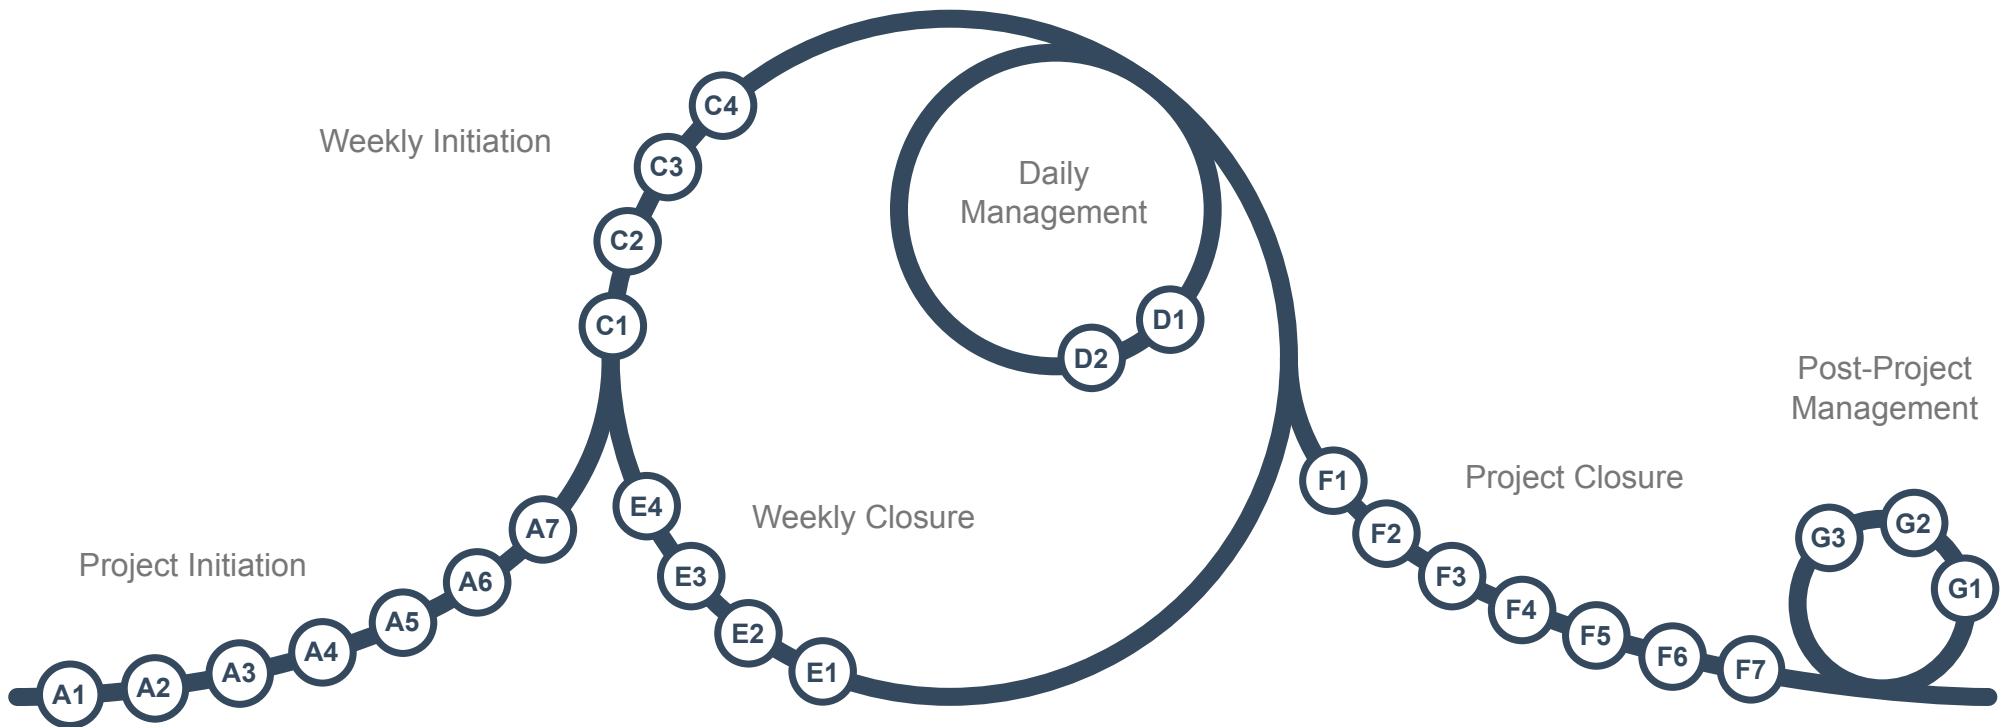


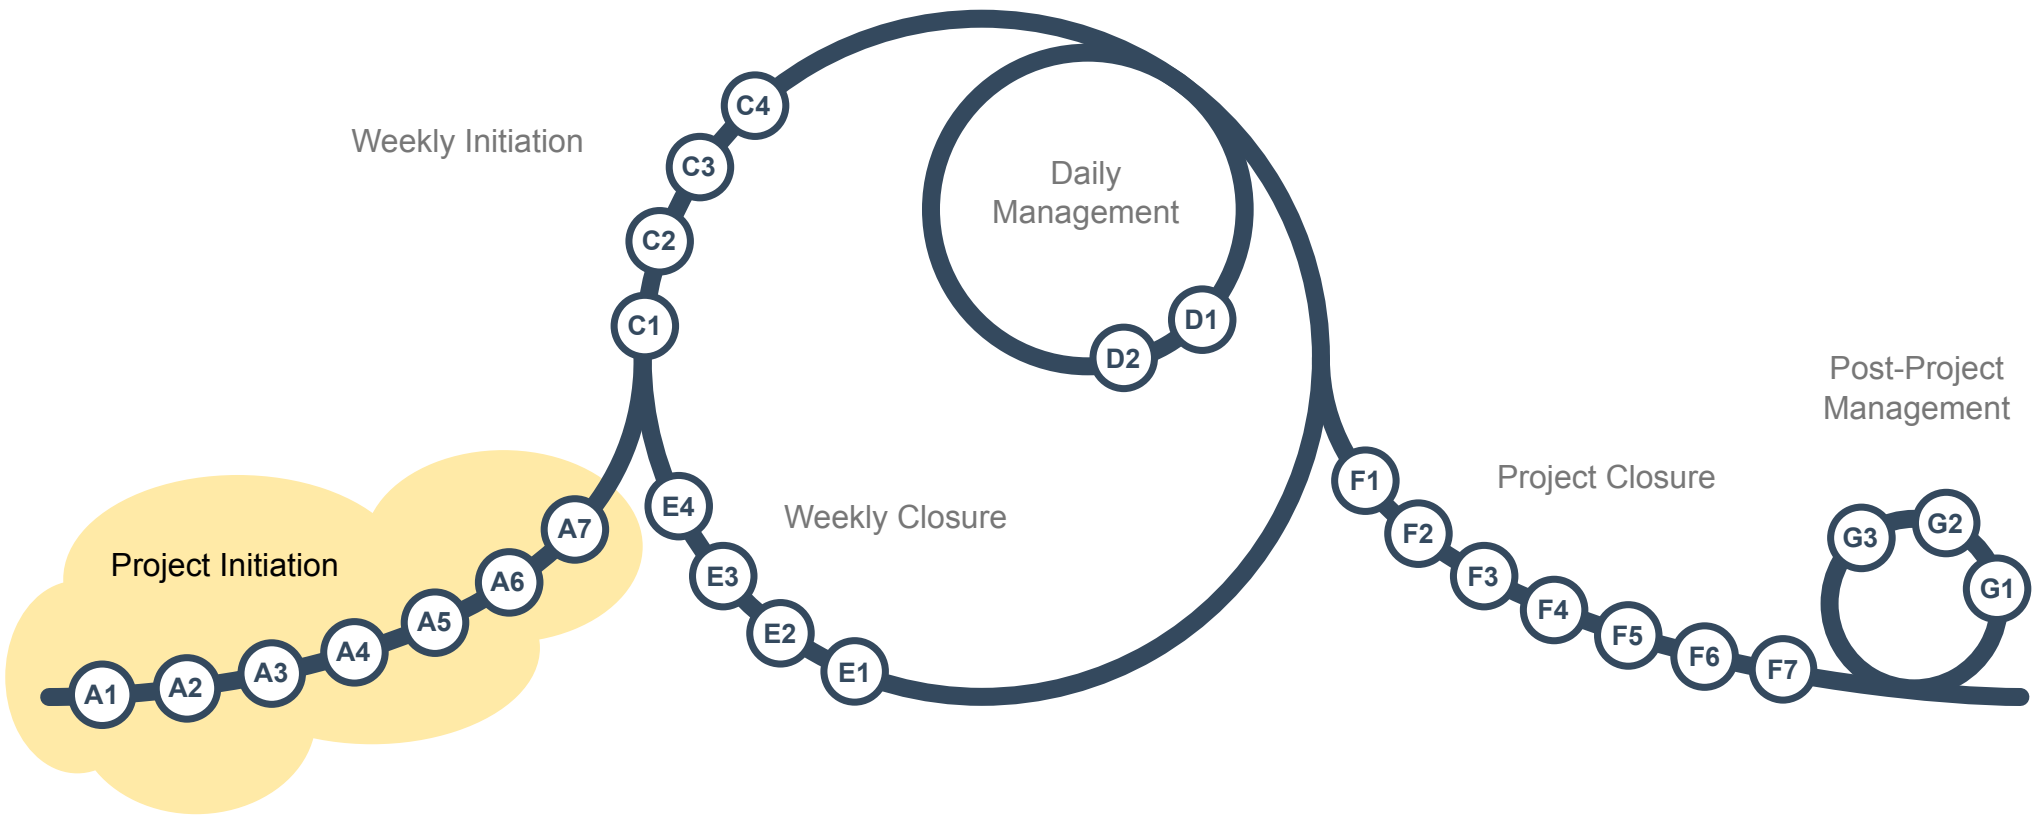


Identify the high-level decision maker(s)

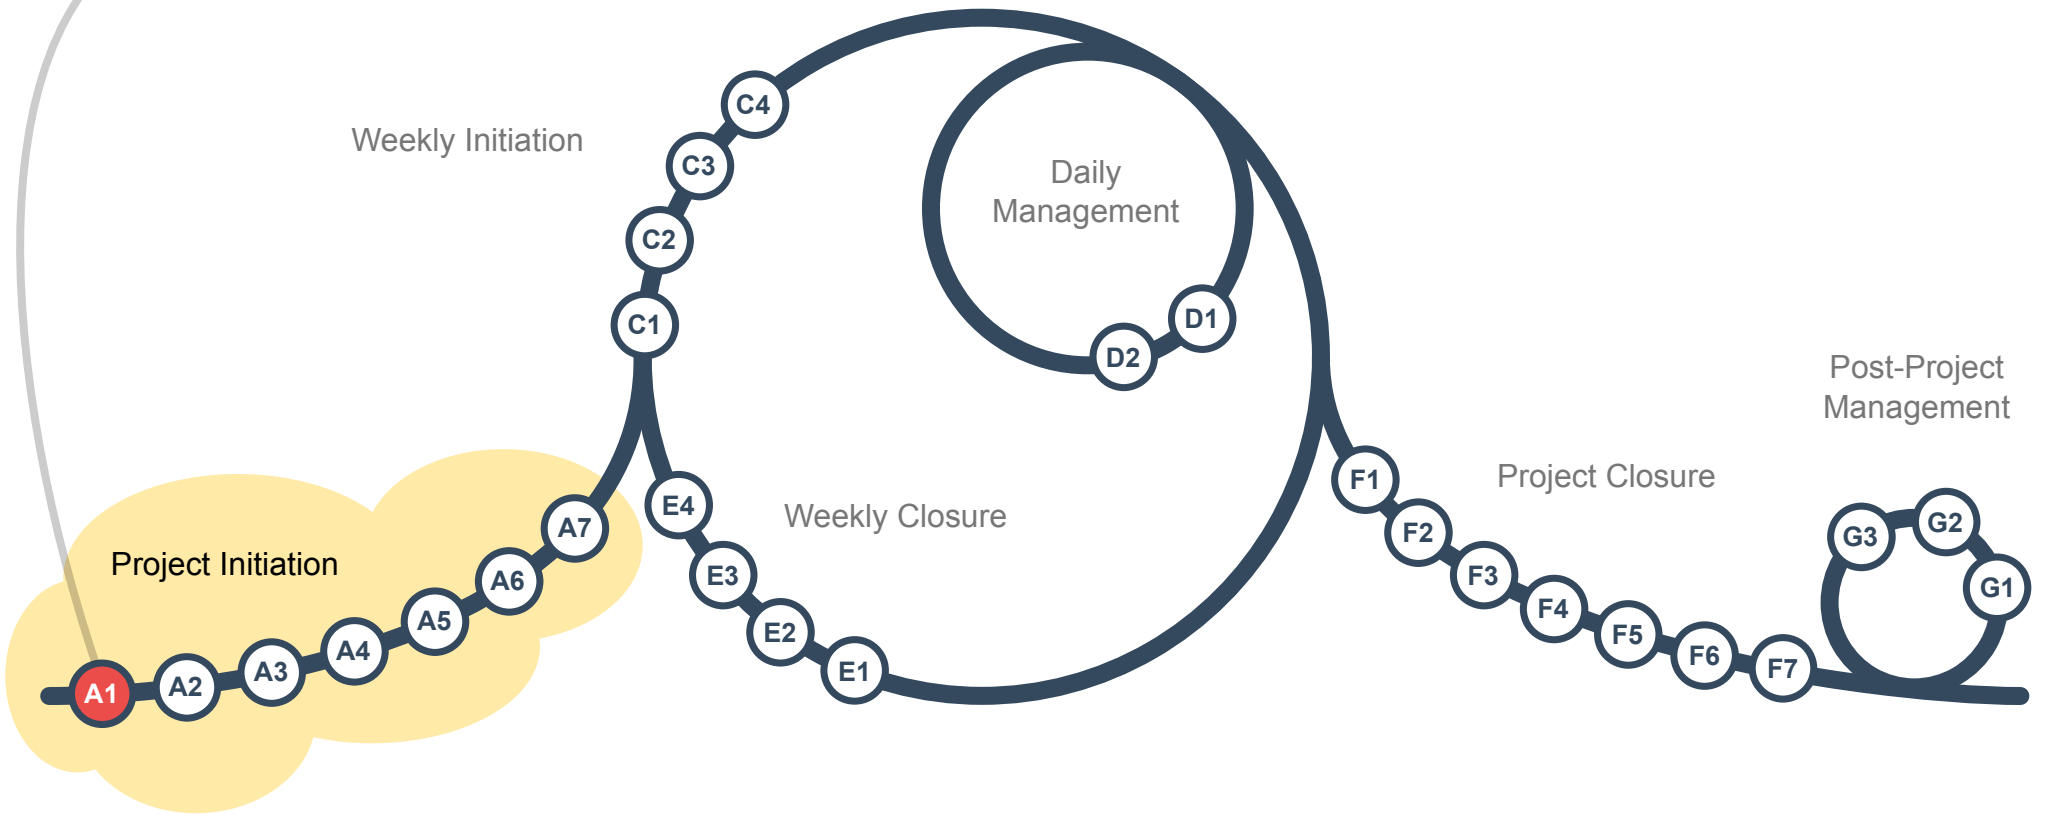

A1 - Identify the high-level decision maker(s)

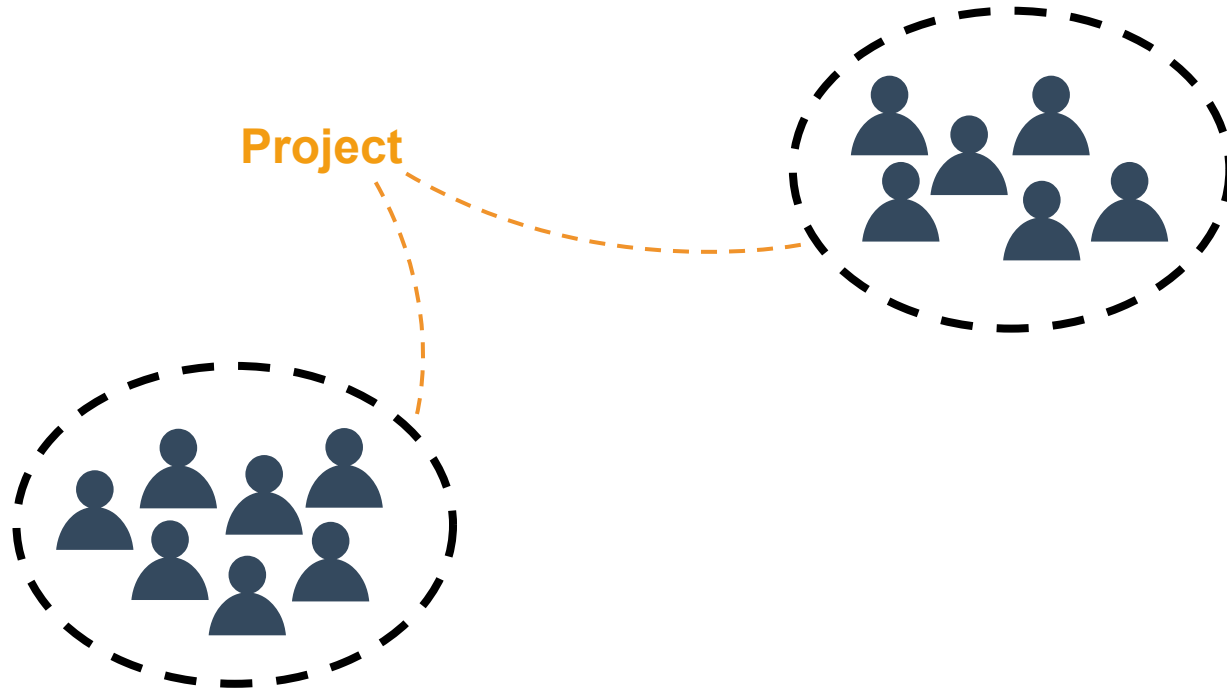

A1 - Identify the high-level decision maker(s)

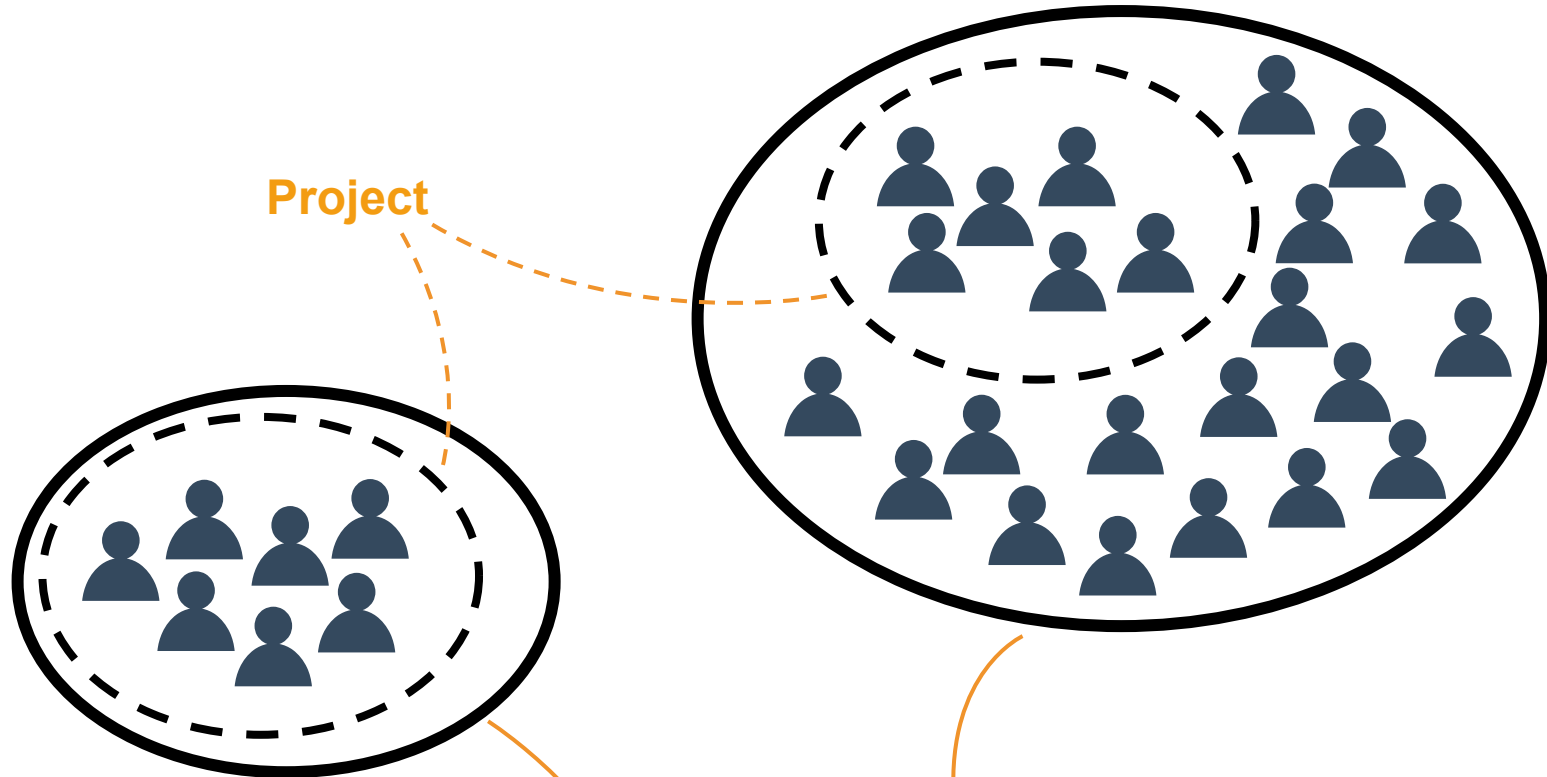


Project

Larger Organization

Micro-Organization

(More or less the same size as the project; e.g., a startup)

A1 - Identify the high-level decision maker(s)

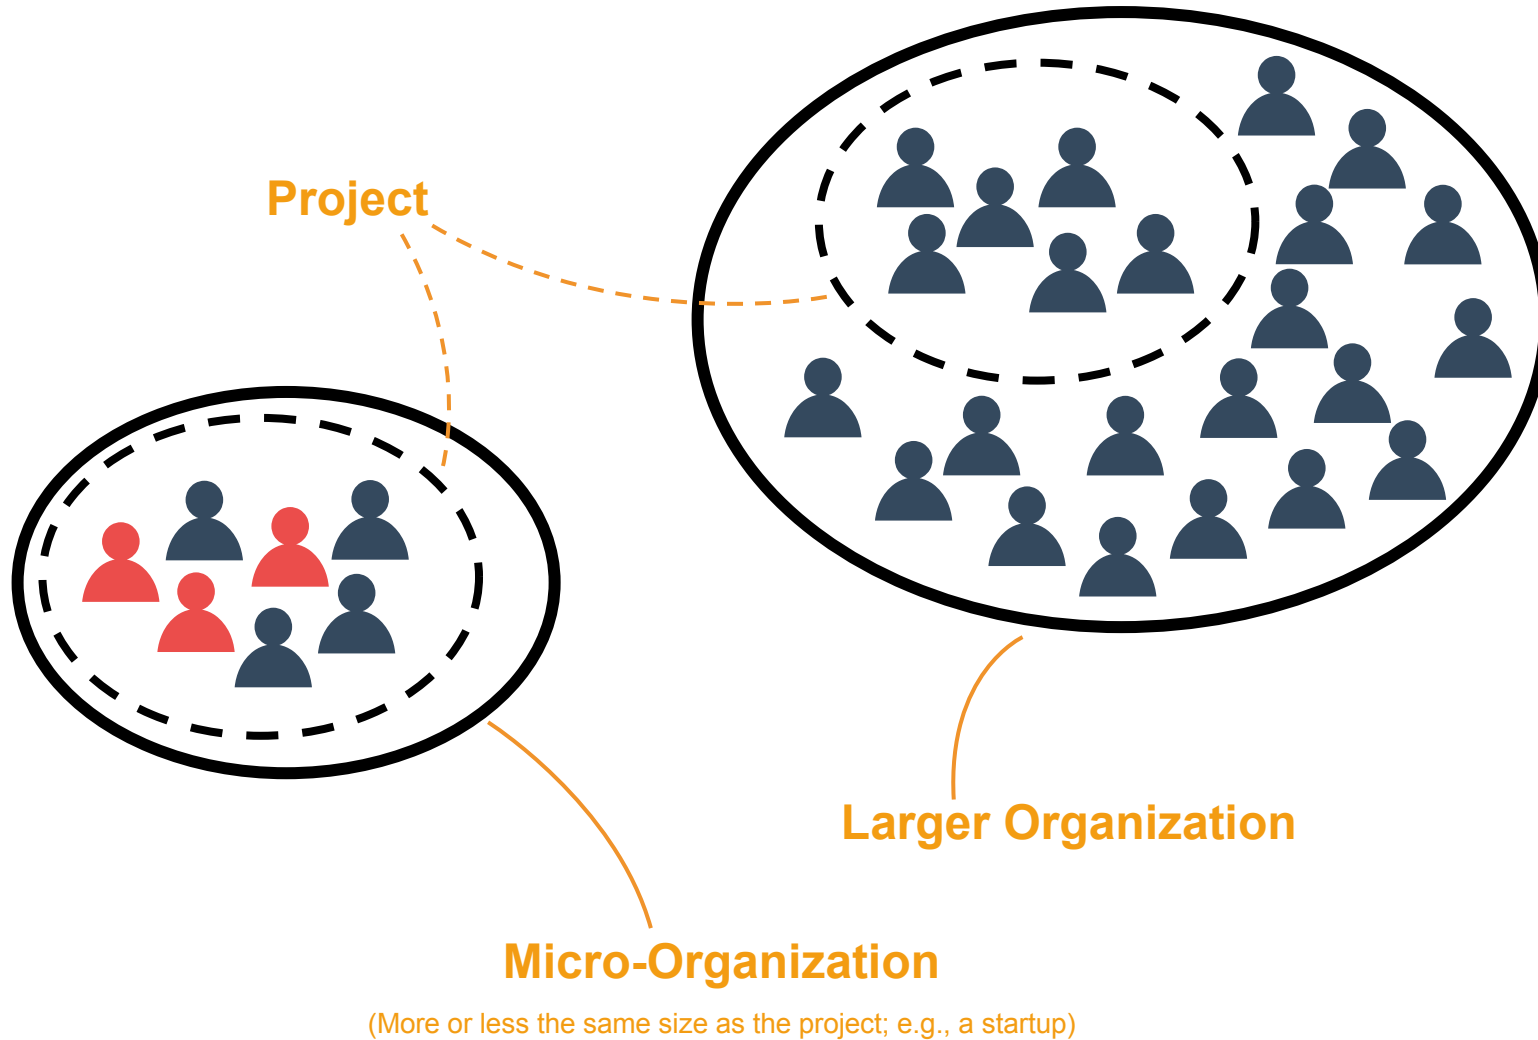


Project

Larger Organization


Micro-Organization

(More or less the same size as the project; e.g., a startup)

A1 - Identify the high-level decision maker(s)

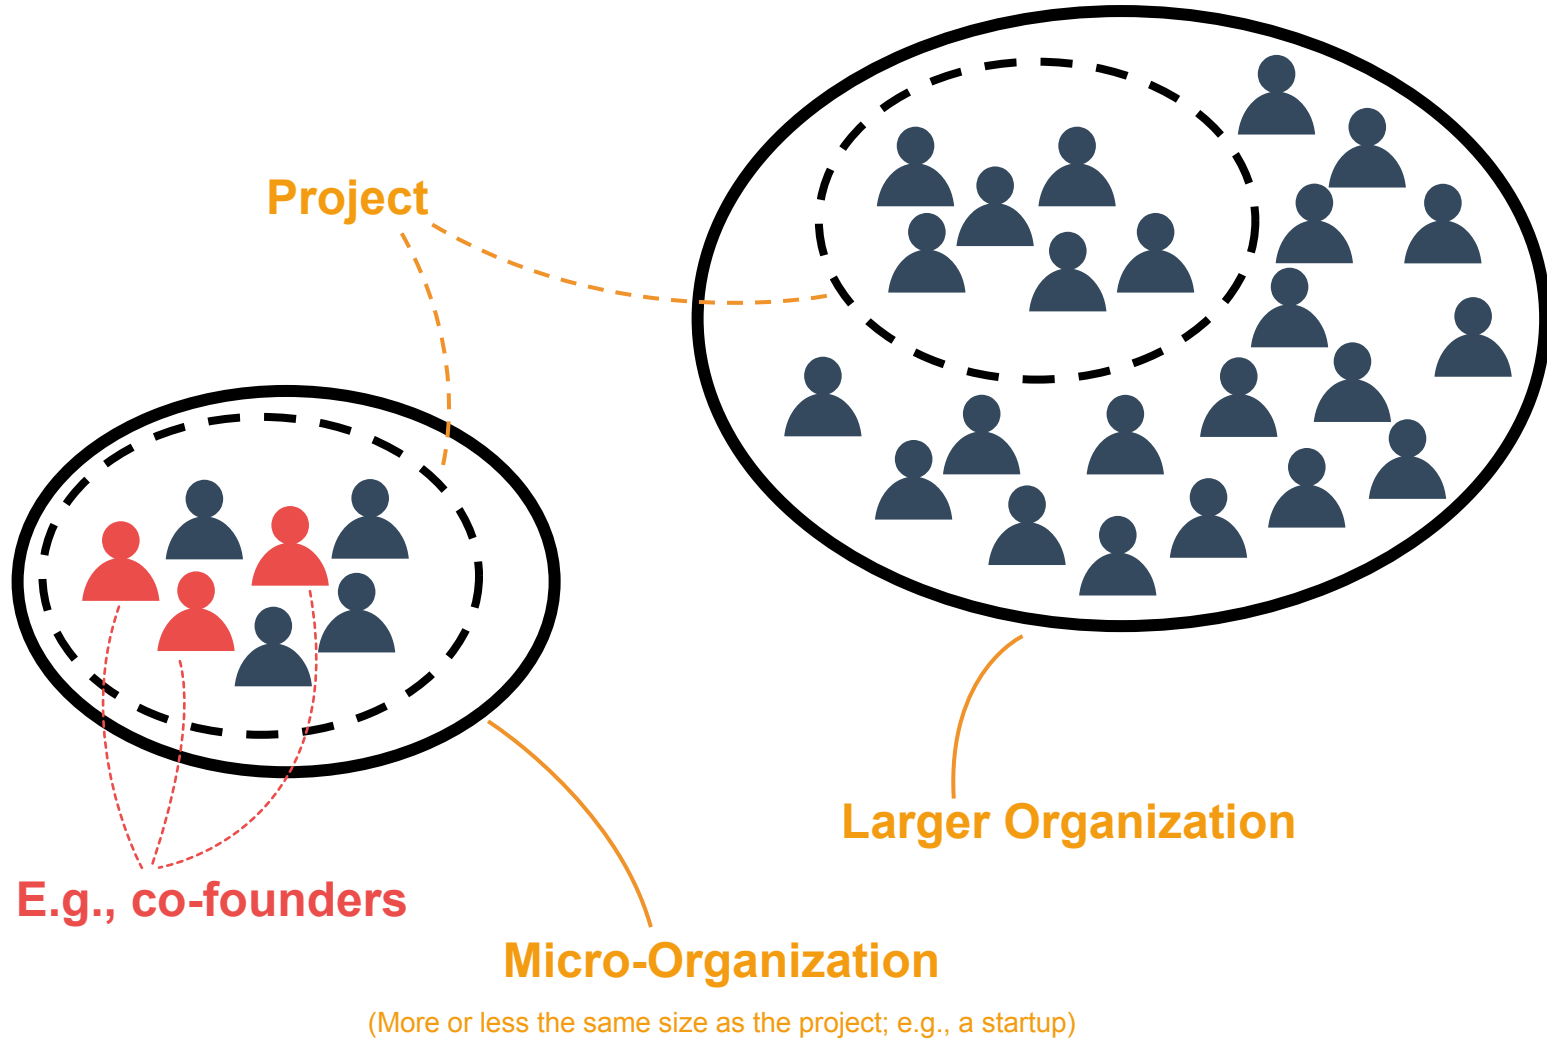


A1 - Identify the high-level decision maker(s)

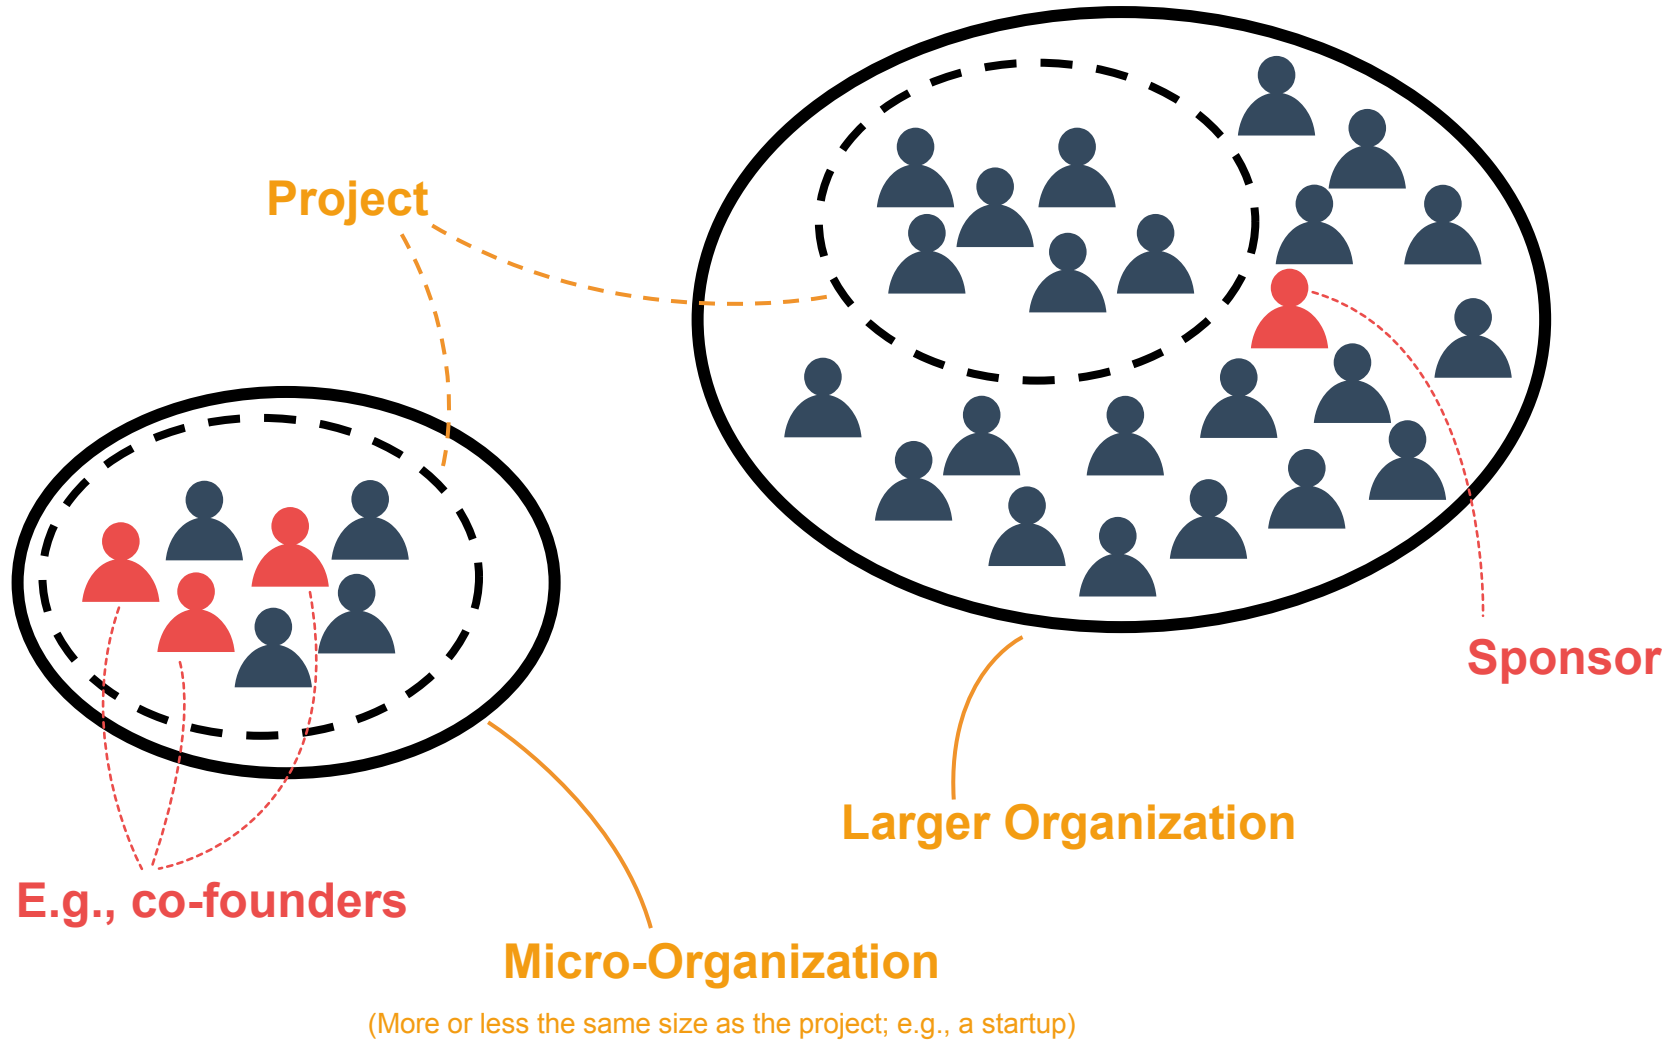


(More or less the same size as the project; e.g., a startup)

A1 - Identify the high-level decision maker(s)

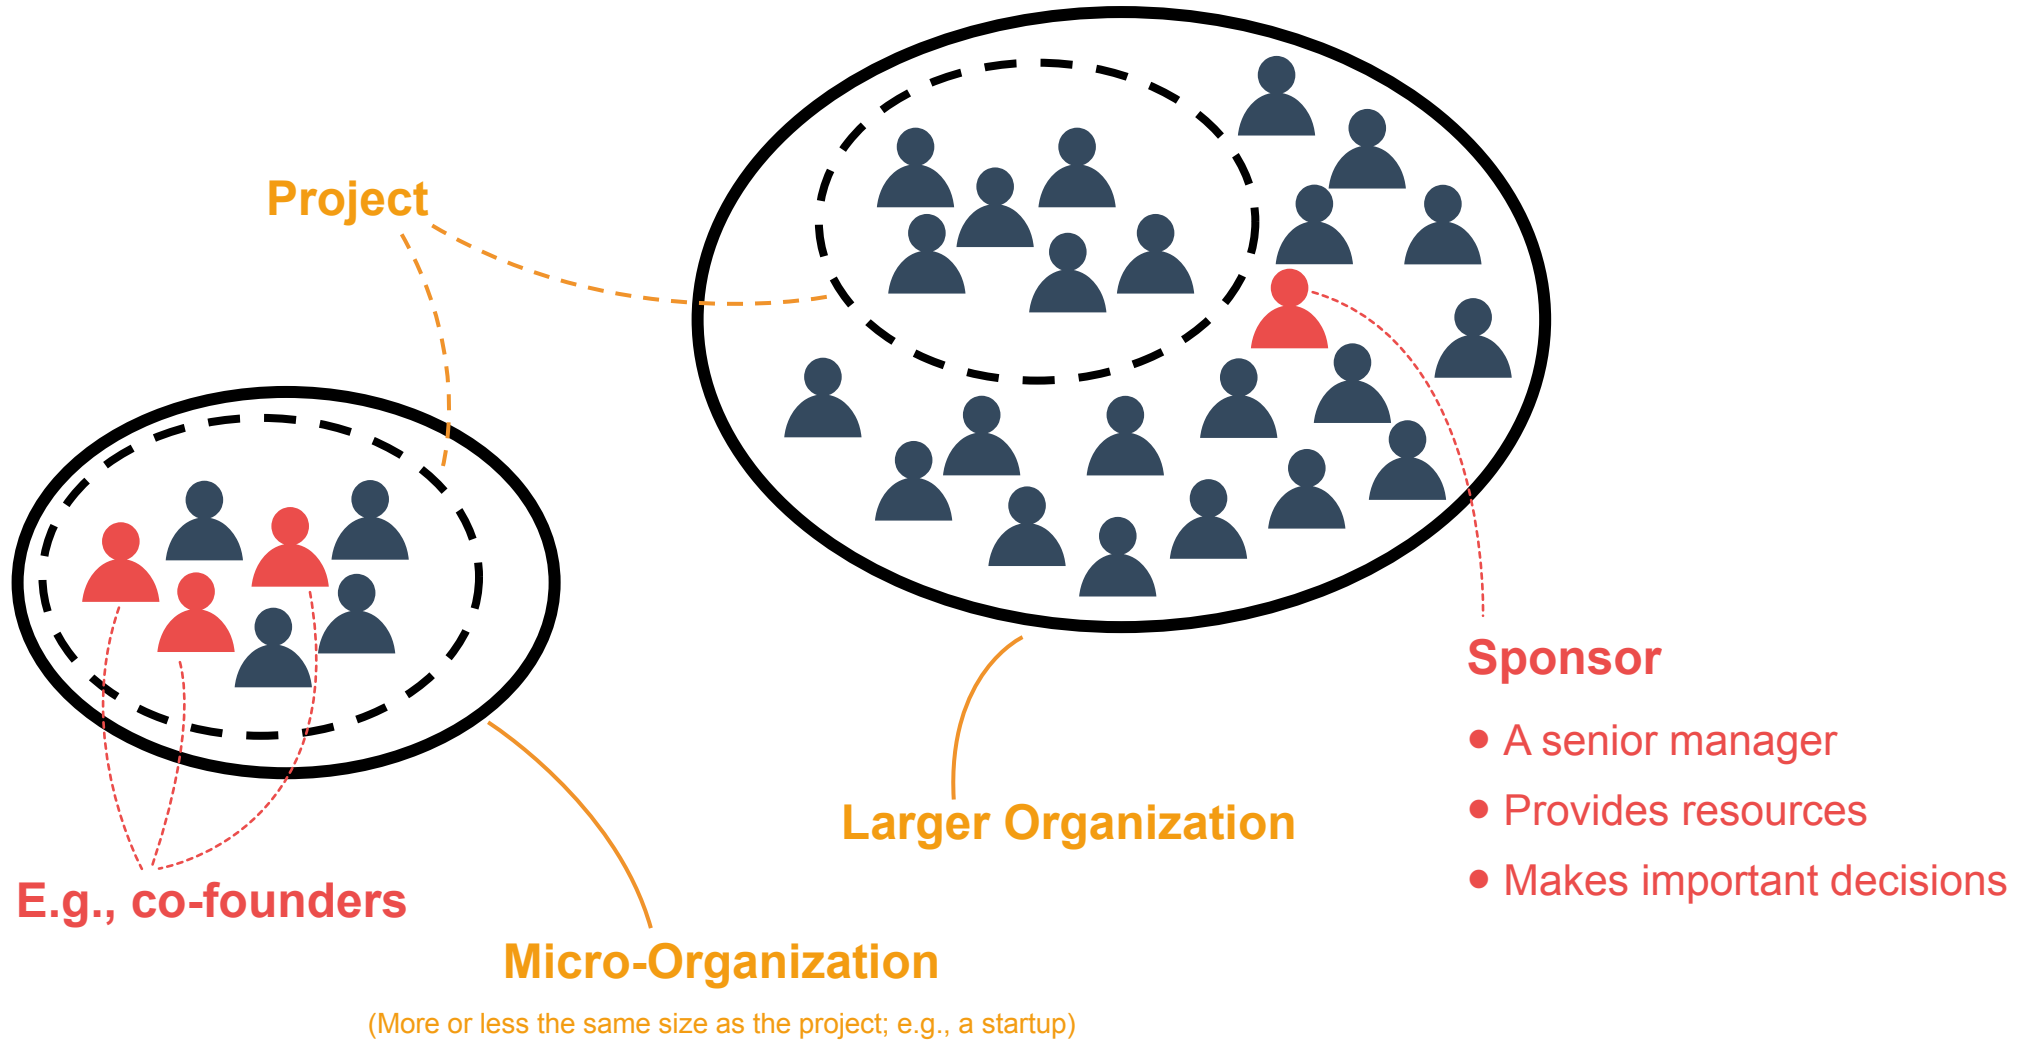


A1 - Identify the high-level decision maker(s)

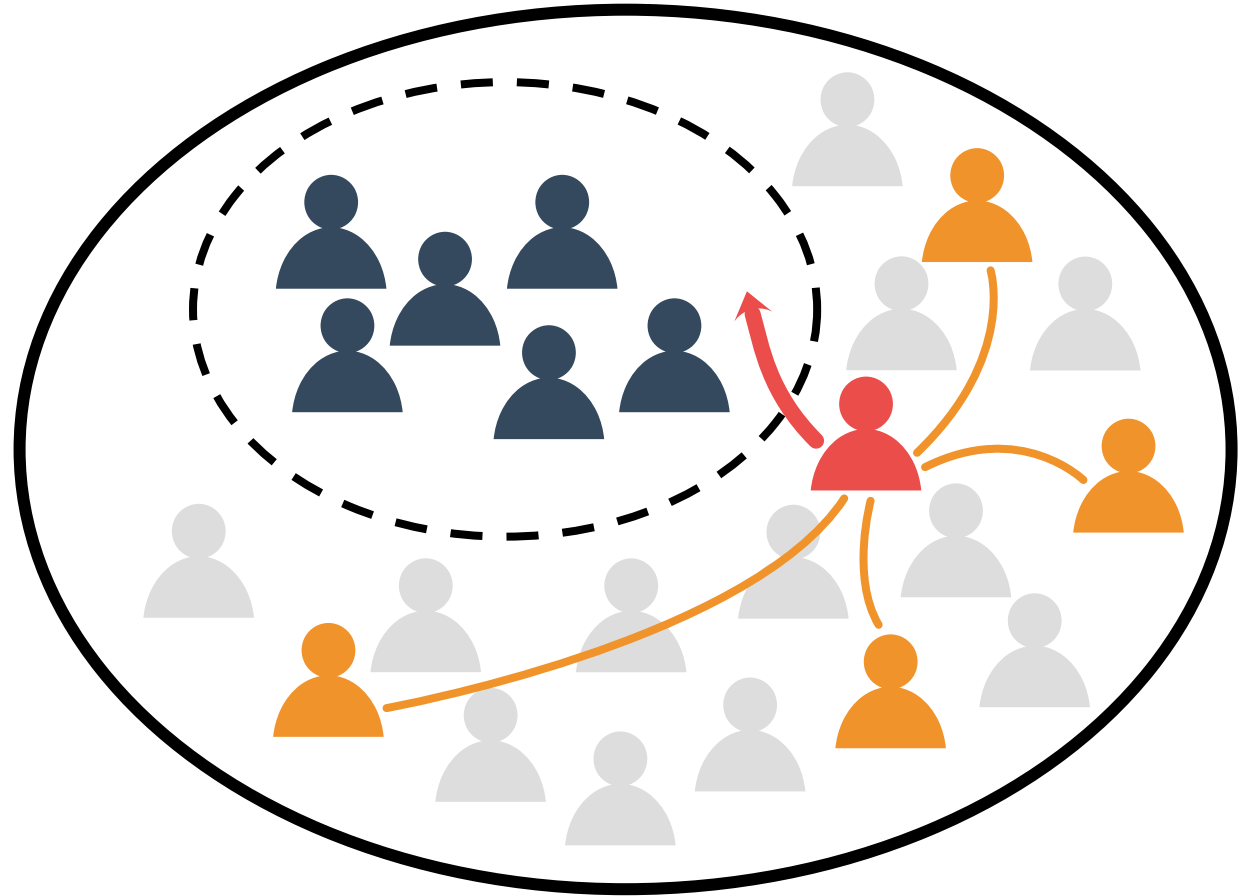

For decisions,
the team is only in touch with the sponsor.


(If more people should to be involved, the sponsor will take care of that.)

Identify the high-level decision maker(s)

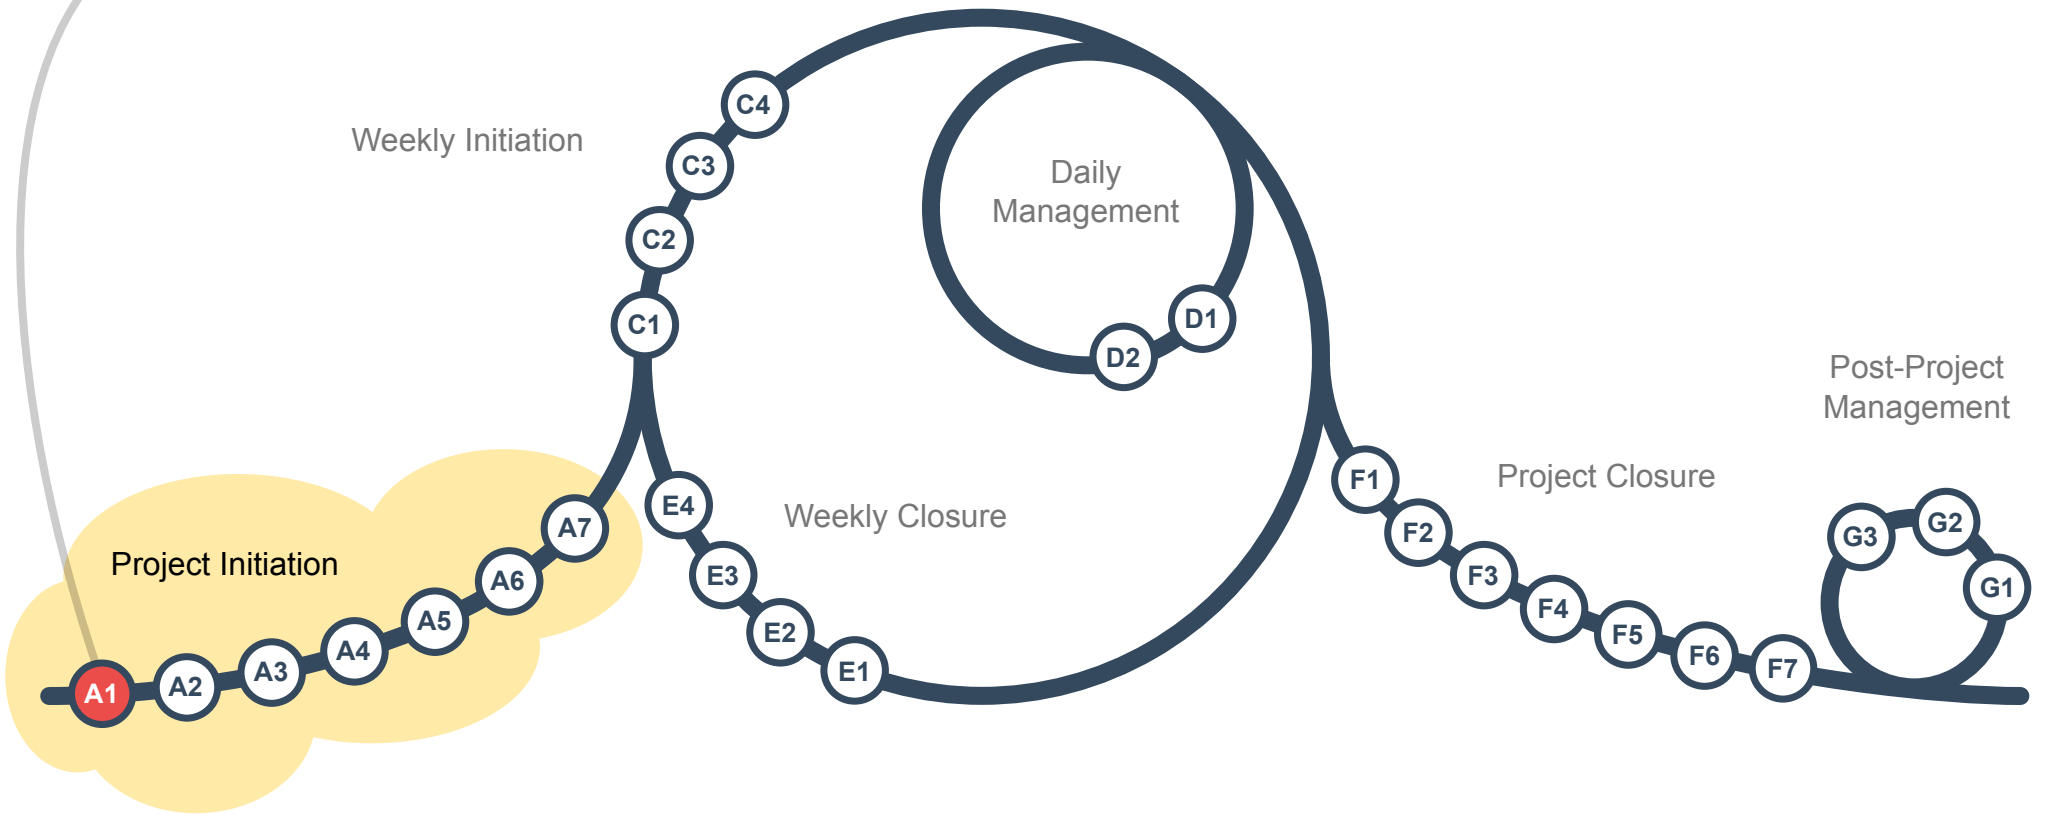



Identify the high-level decision maker(s)

Understand and distribute the hats

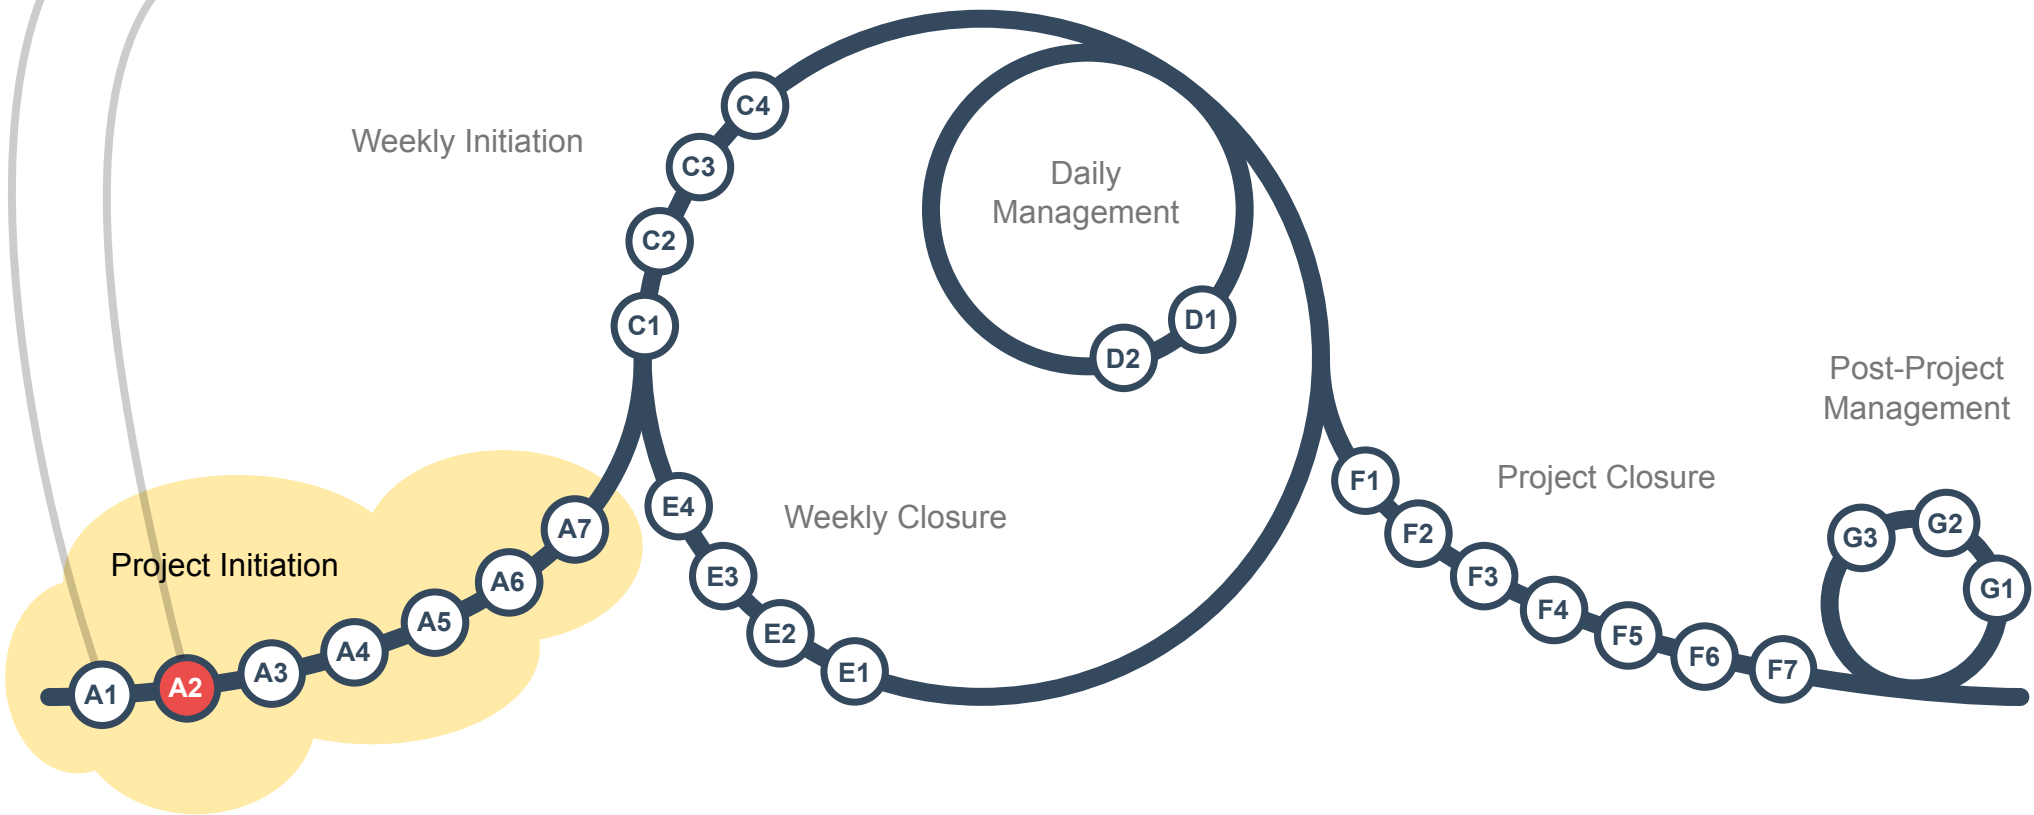

A2 - Understand and distribute the hats


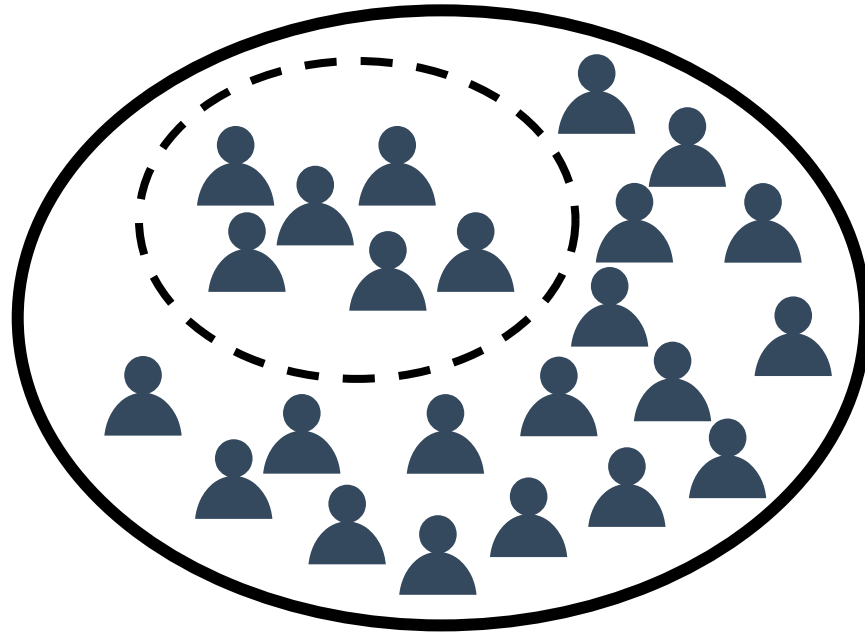


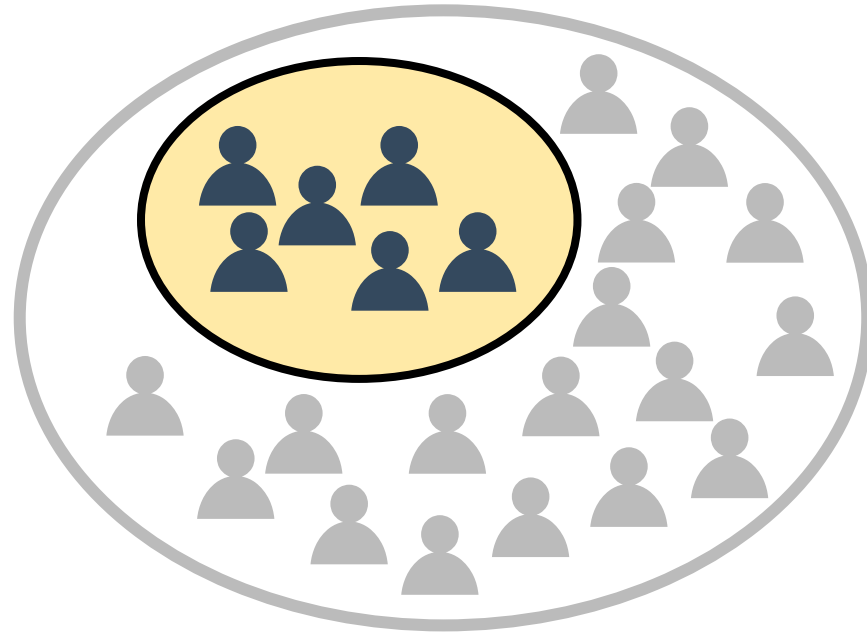



Team members should be officially appointed to the project.

(Instead of appointing tasks to departments)


A2 - Understand and distribute the hats




A2 - Understand and distribute the hats

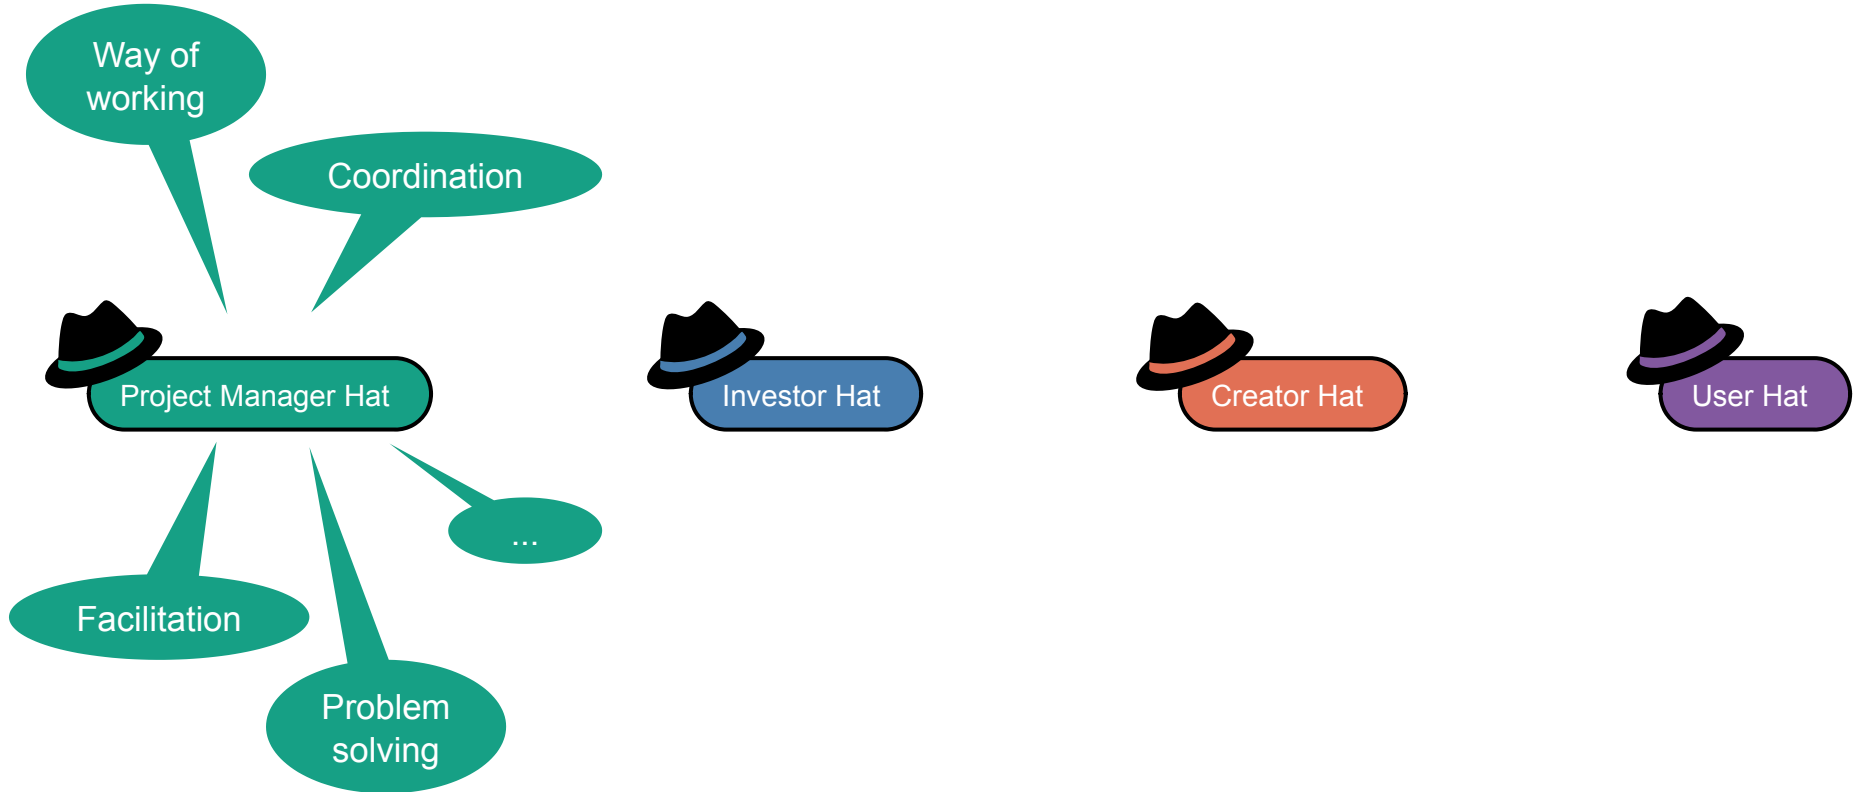


A2 - Understand and distribute the hats

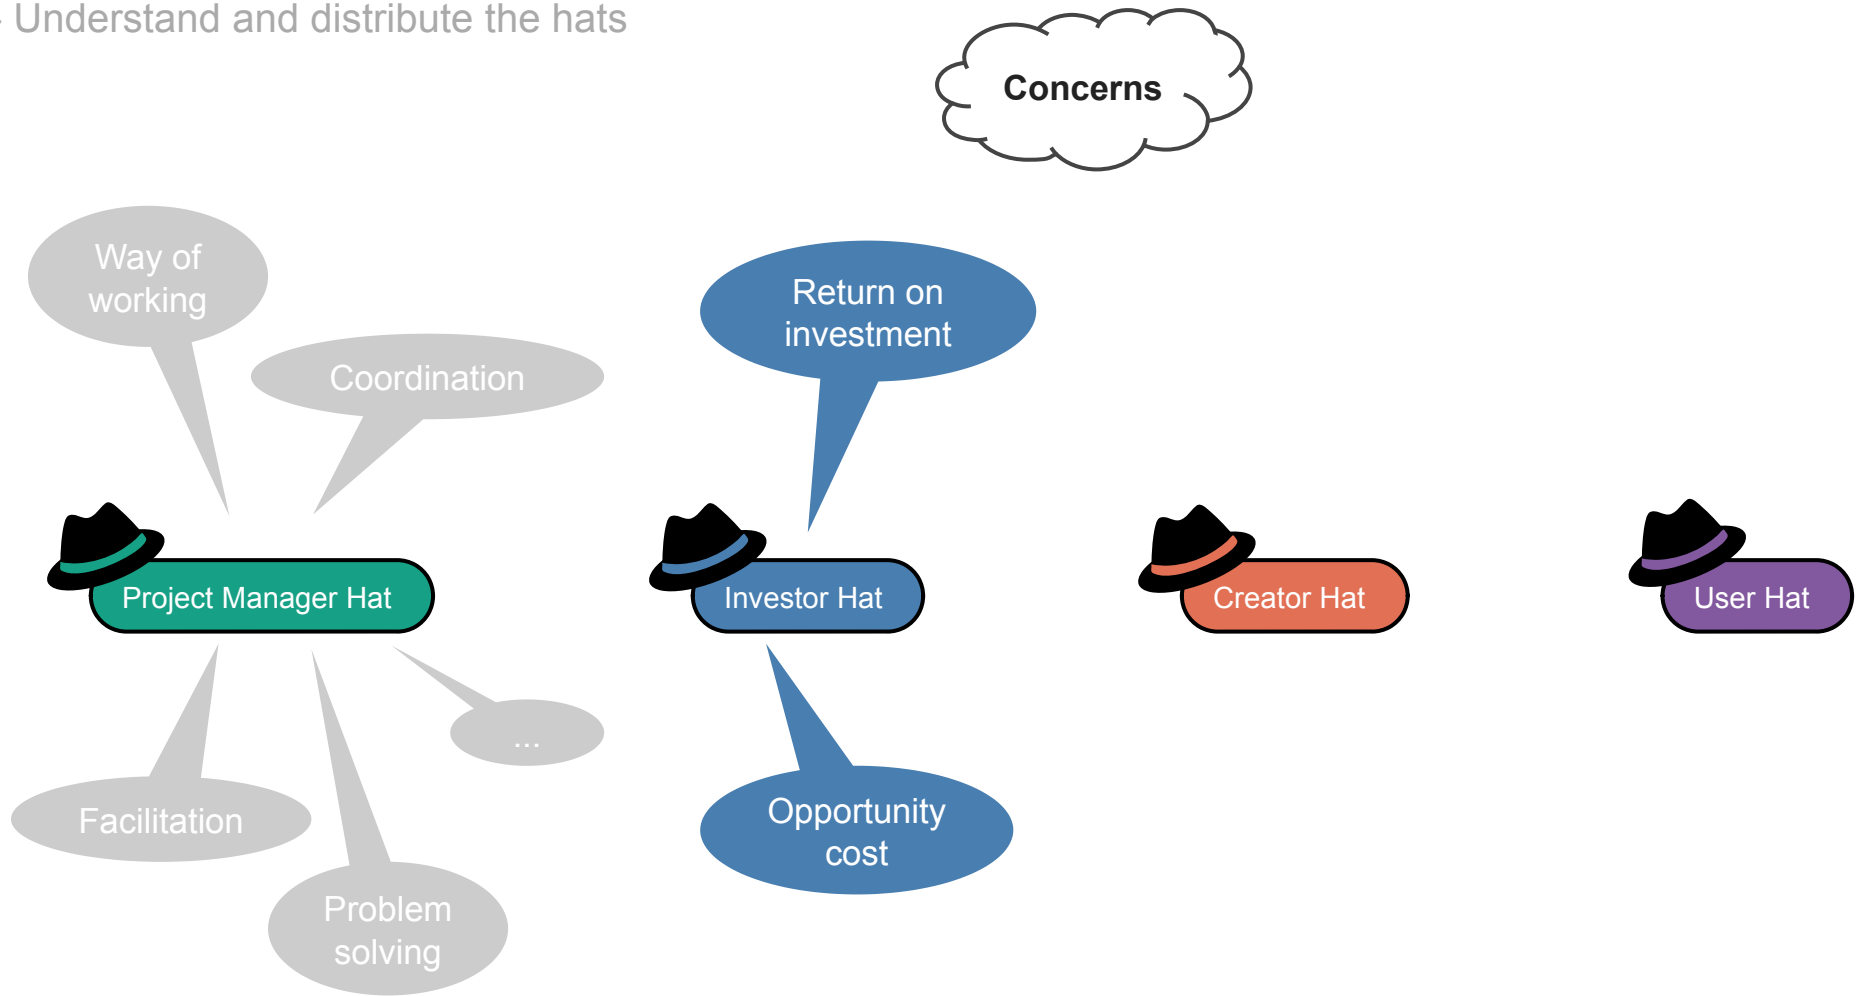


A2 - Understand and distribute the hats

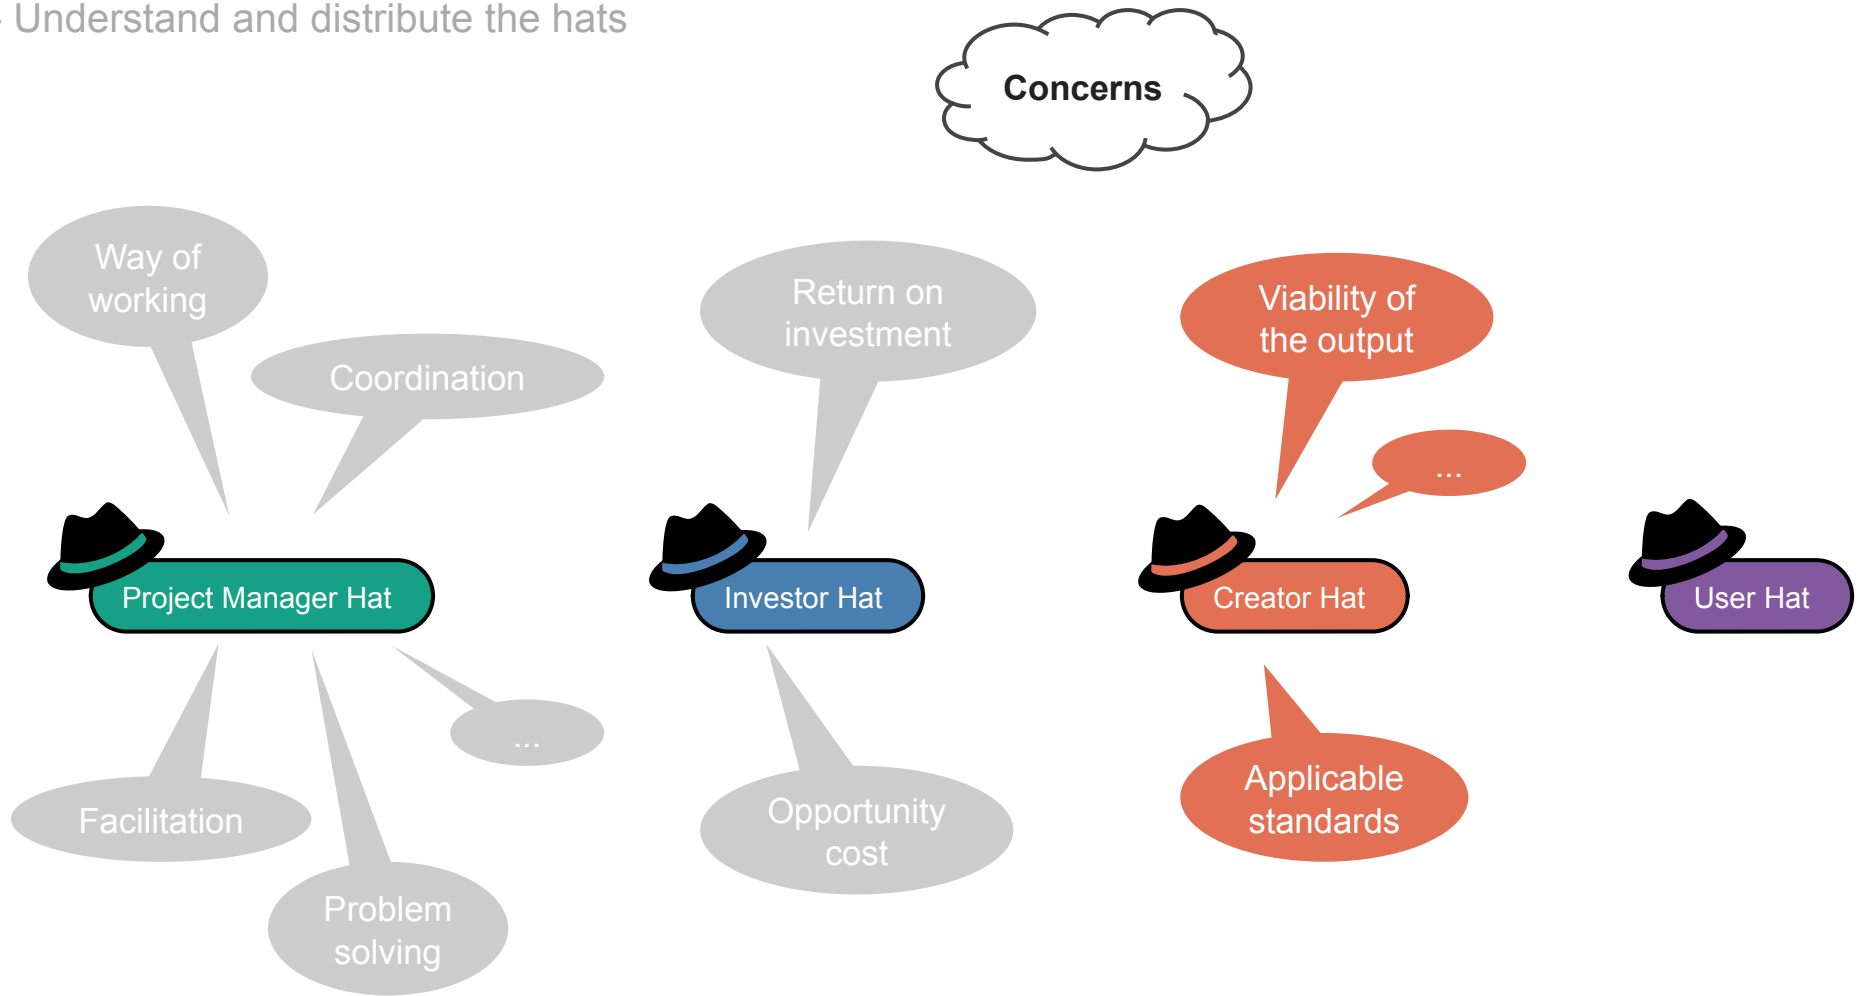

A2 - Understand and distribute the hats

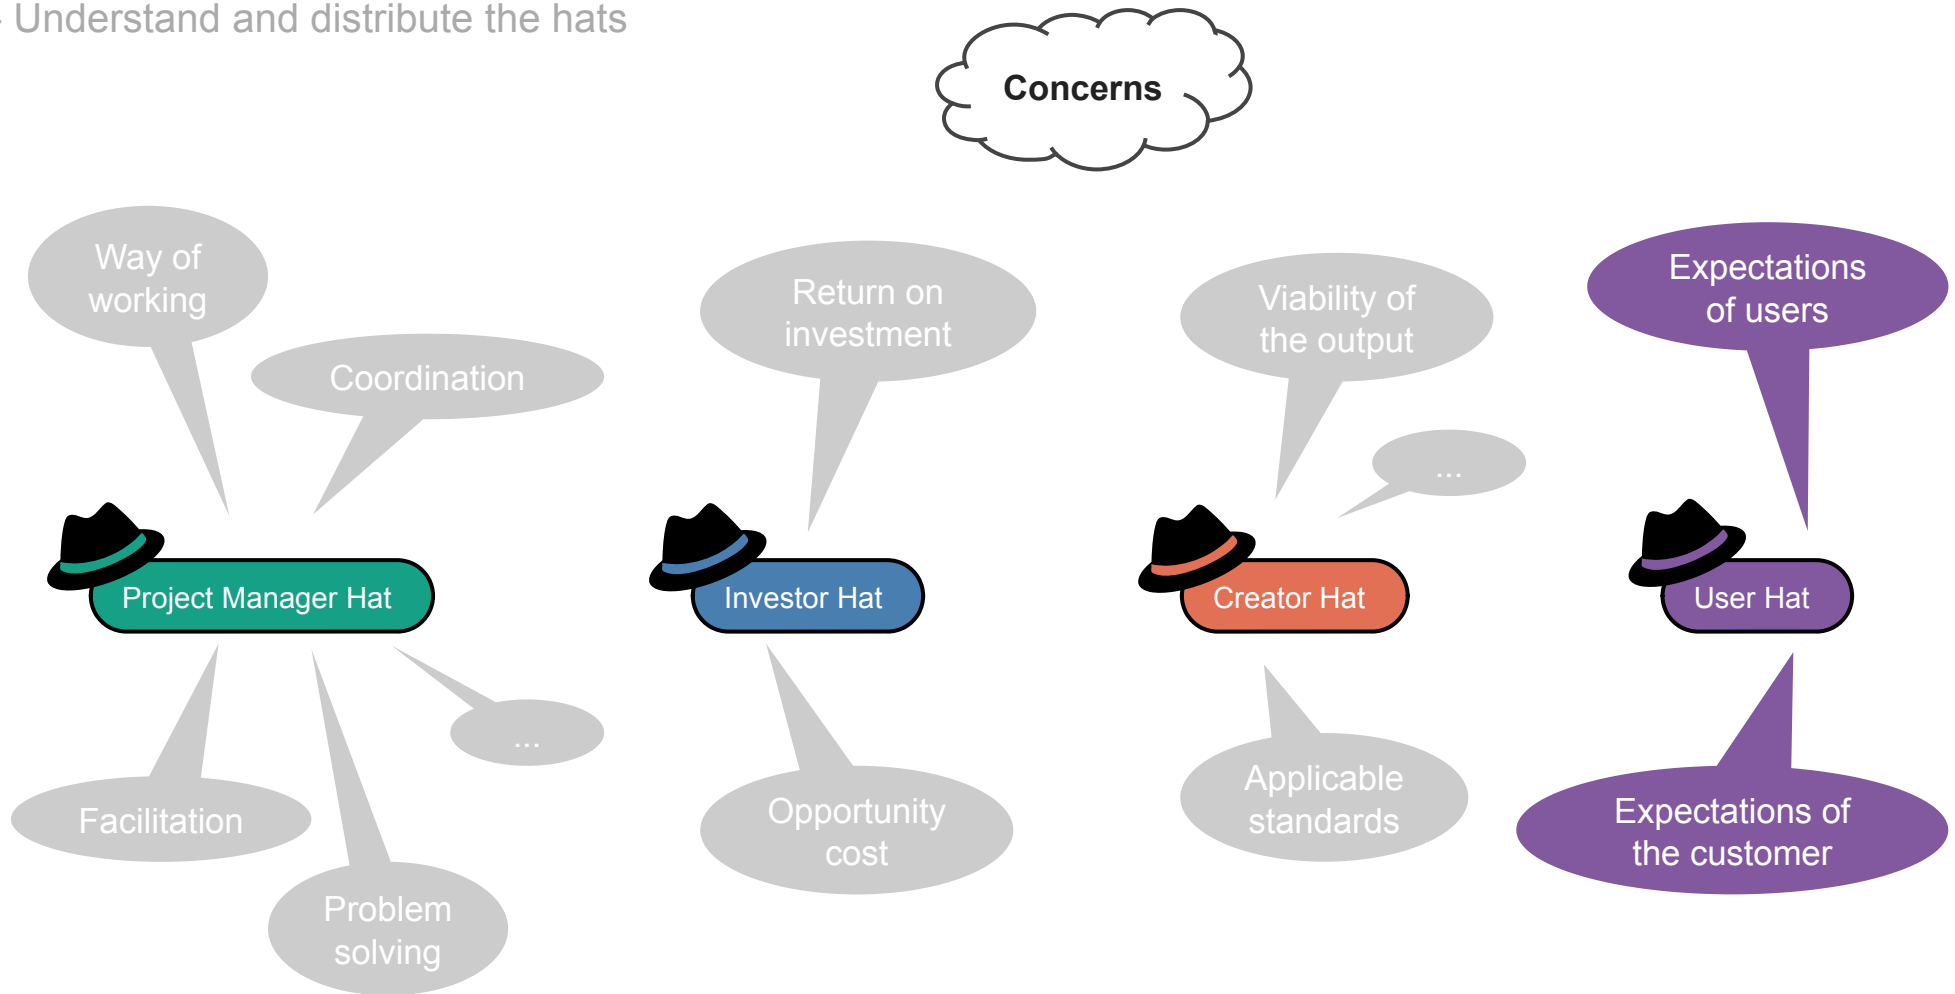

A2 - Understand and distribute the hats

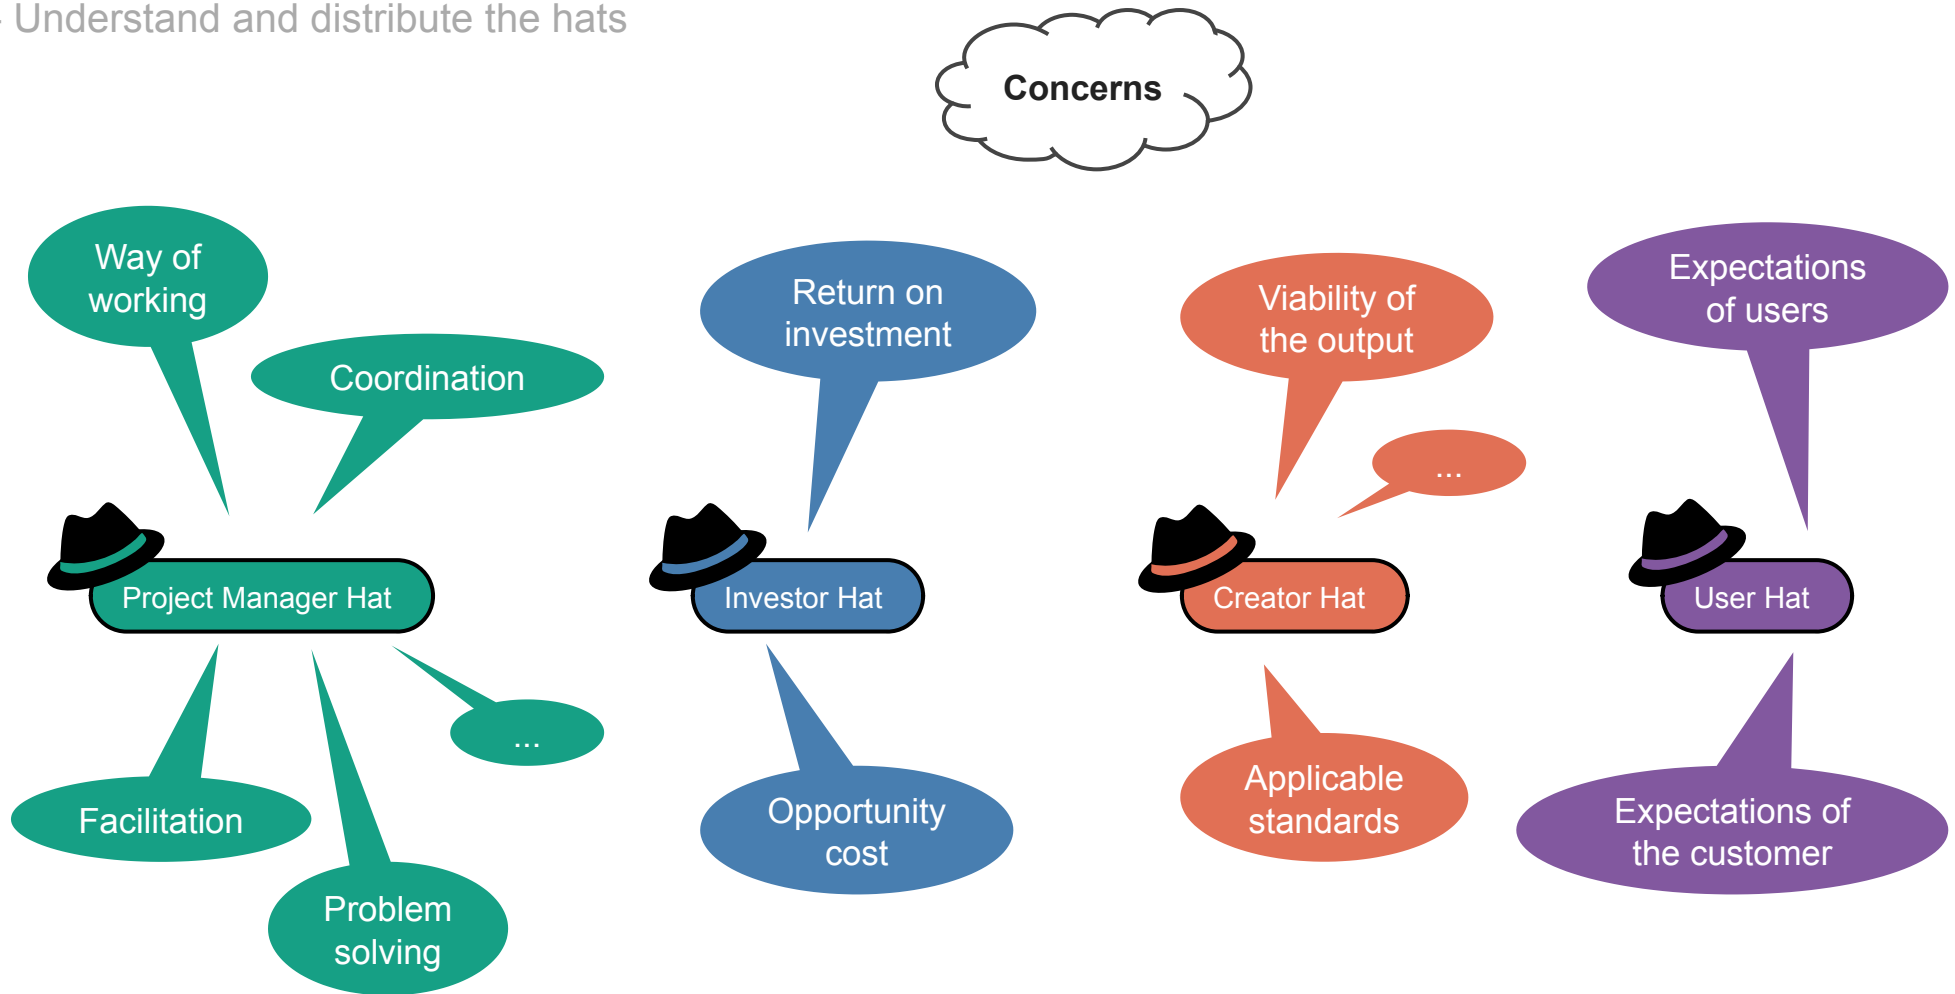




Expressing concerns

~~(Decision making) authority~~



✓ Making sure concerns are addressed

~~Addressing concerns~~




Only one person
wears the hat at any one time.



Only the team members
wear the hats


A2 - Understand and distribute the hats



Who is capable of and willing to wear each of the hats?


A2 - Understand and distribute the hats

Some people don't want to or can't wear any hats, and that's fine.




Who is capable of and willing to wear each of the hats?

A2 - Understand and distribute the hats

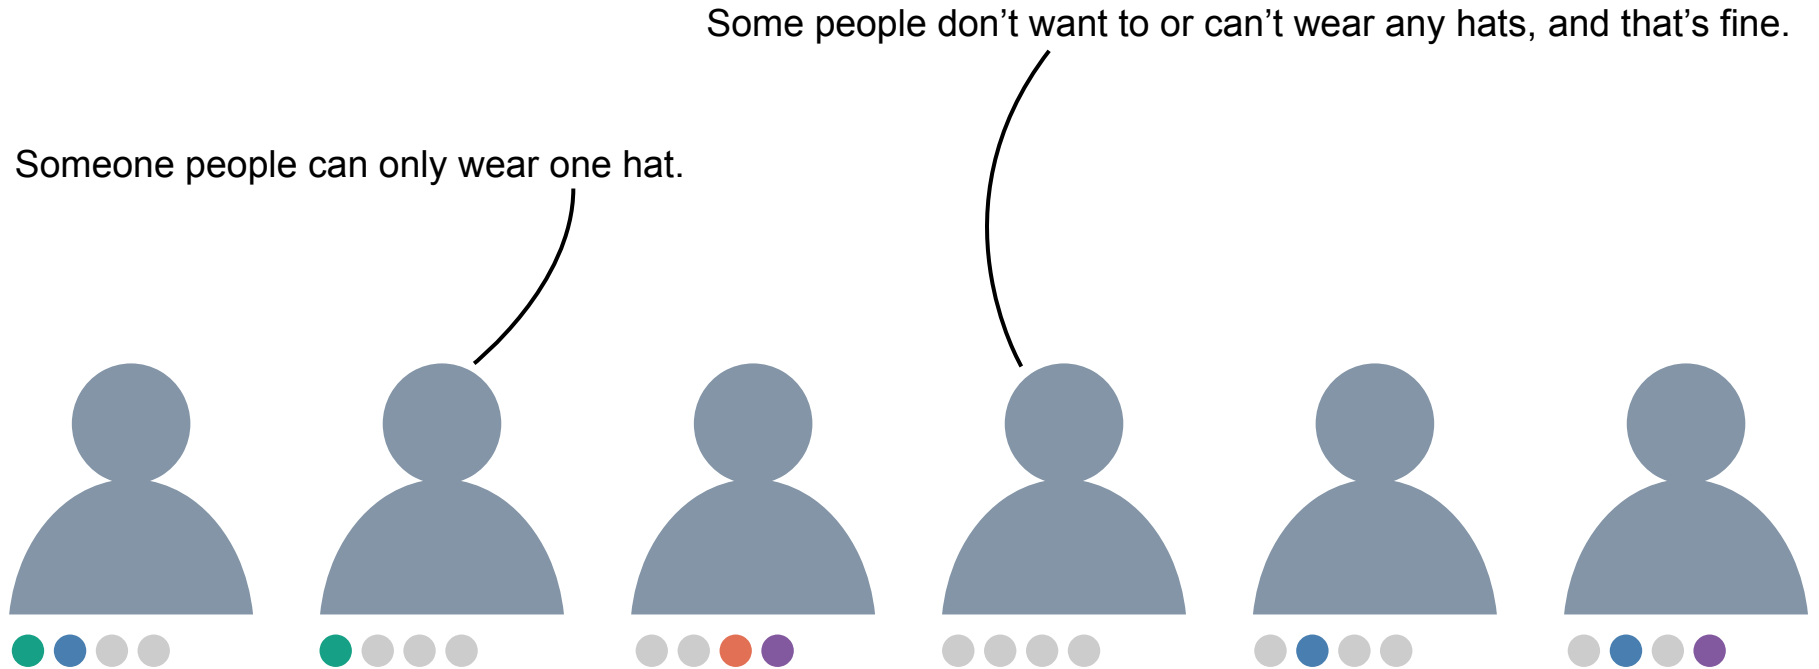


Who is capable of and willing to wear each of the hats?

A2 - Understand and distribute the hats

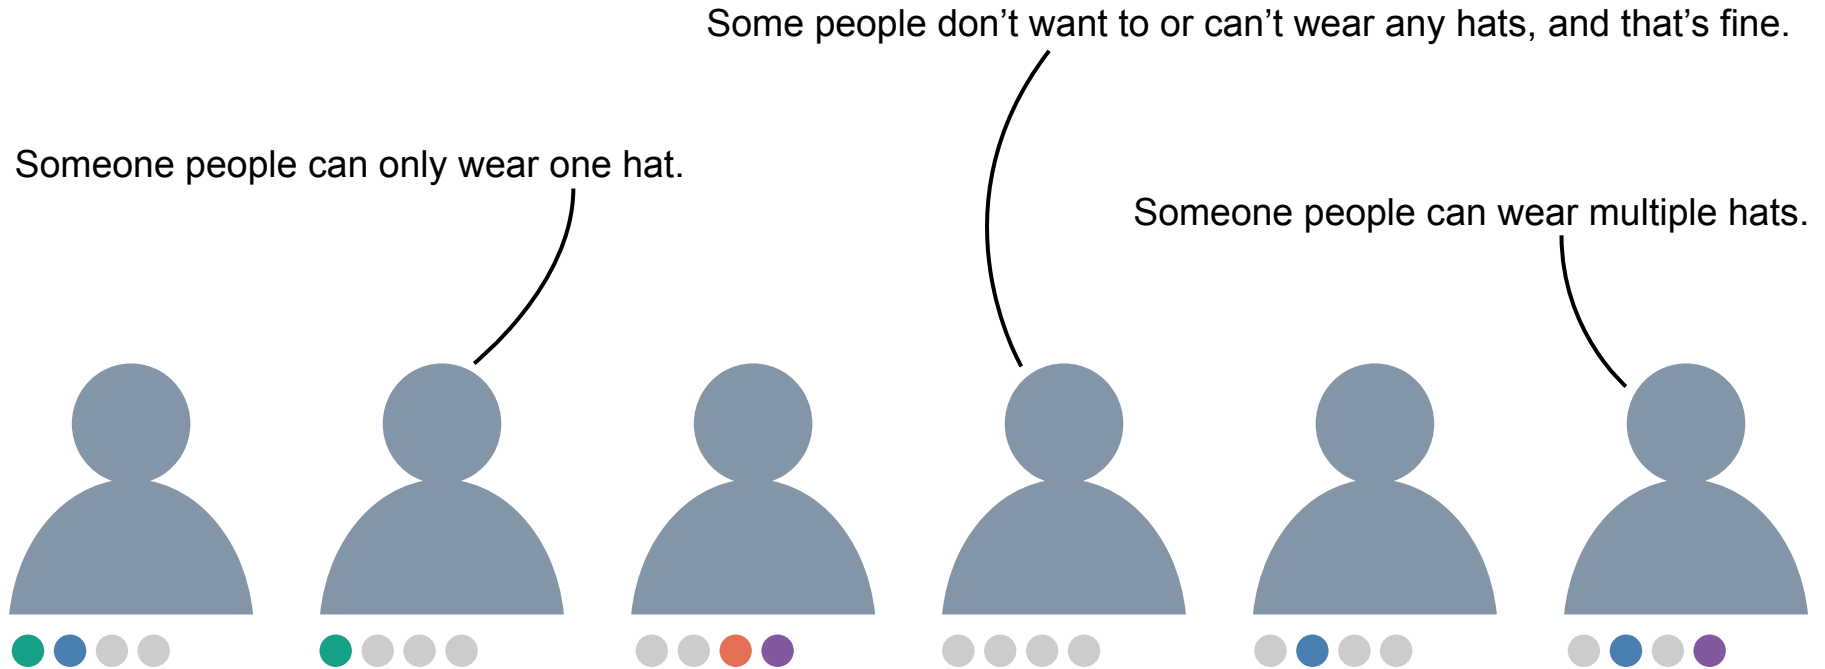

Who is capable of and willing to wear each of the hats?

A2 - Understand and distribute the hats



We prefer to swap hats frequently, if possible.

A2 - Understand and distribute the hats

Project Initiation




Cycle 1



Cycle 2




Time



A2 - Understand and distribute the hats




In a single-person project, the person has to wear all the hats...

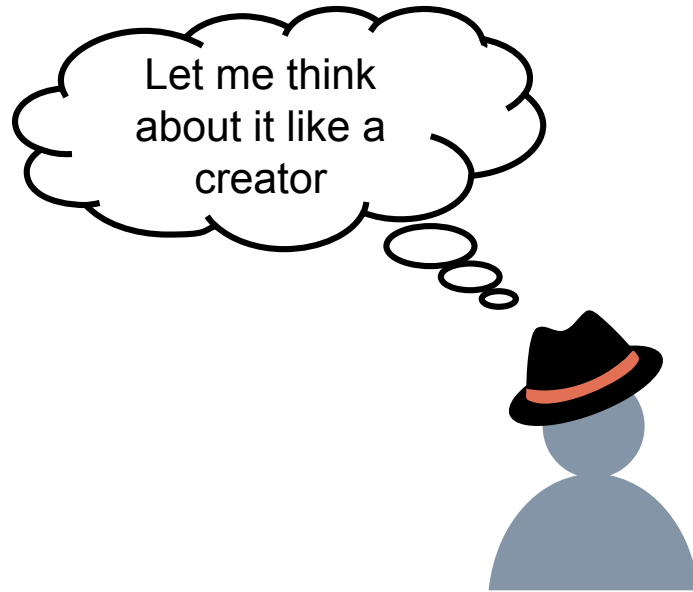

The single person should virtually switch hats all the time.

A2 - Understand and distribute the hats

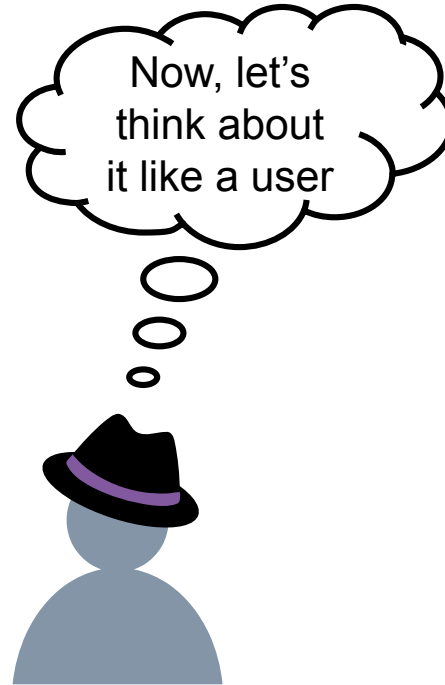

The single person should virtually switch hats all the time.



The single person should virtually switch hats all the time.




The single person should virtually switch hats all the time.

A2 - Understand and distribute the hats



Identify the high-level decision maker(s)

Understand and distribute the hats

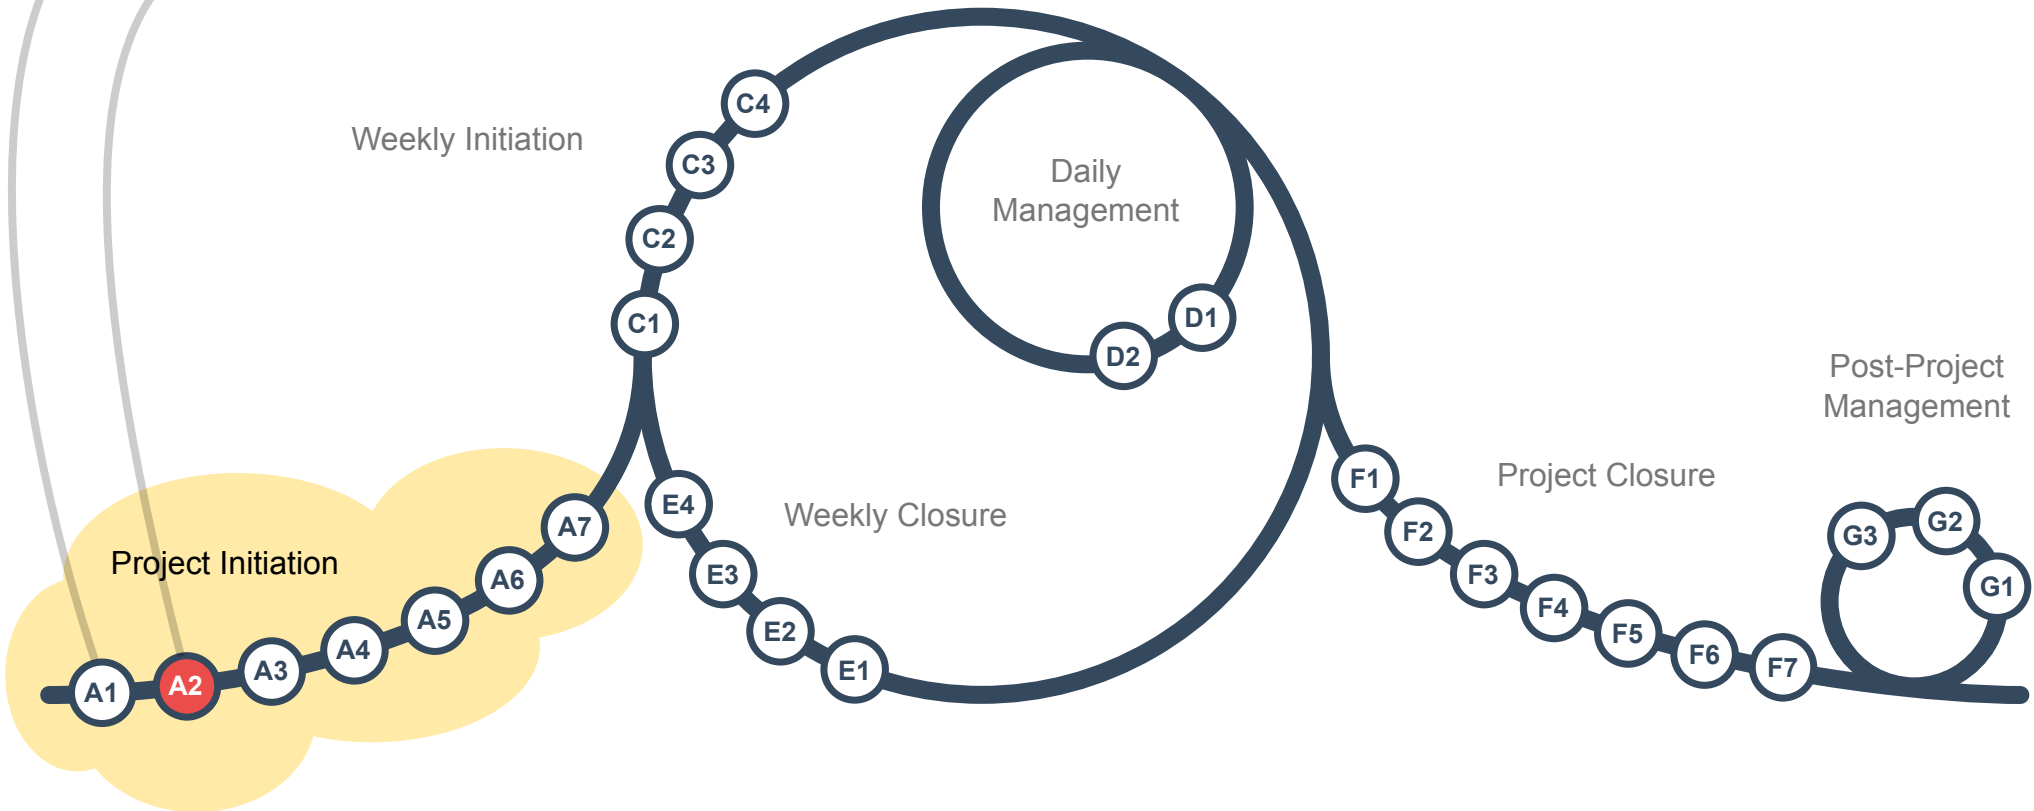

Project Initiation

Weekly Initiation

Daily Management

Weekly Closure

Project Closure

Post-Project Management

A1

A2

A3

A4

A5

A6

A7

C1

C2

C3

C4

E4

E3

E2

E1

D2

D1

F1

F2

F3

F4

F5

F6

F7

G3


G2

G1

Identify the high-level decision maker(s)

Understand and distribute the hats


Select tools and create a project repository

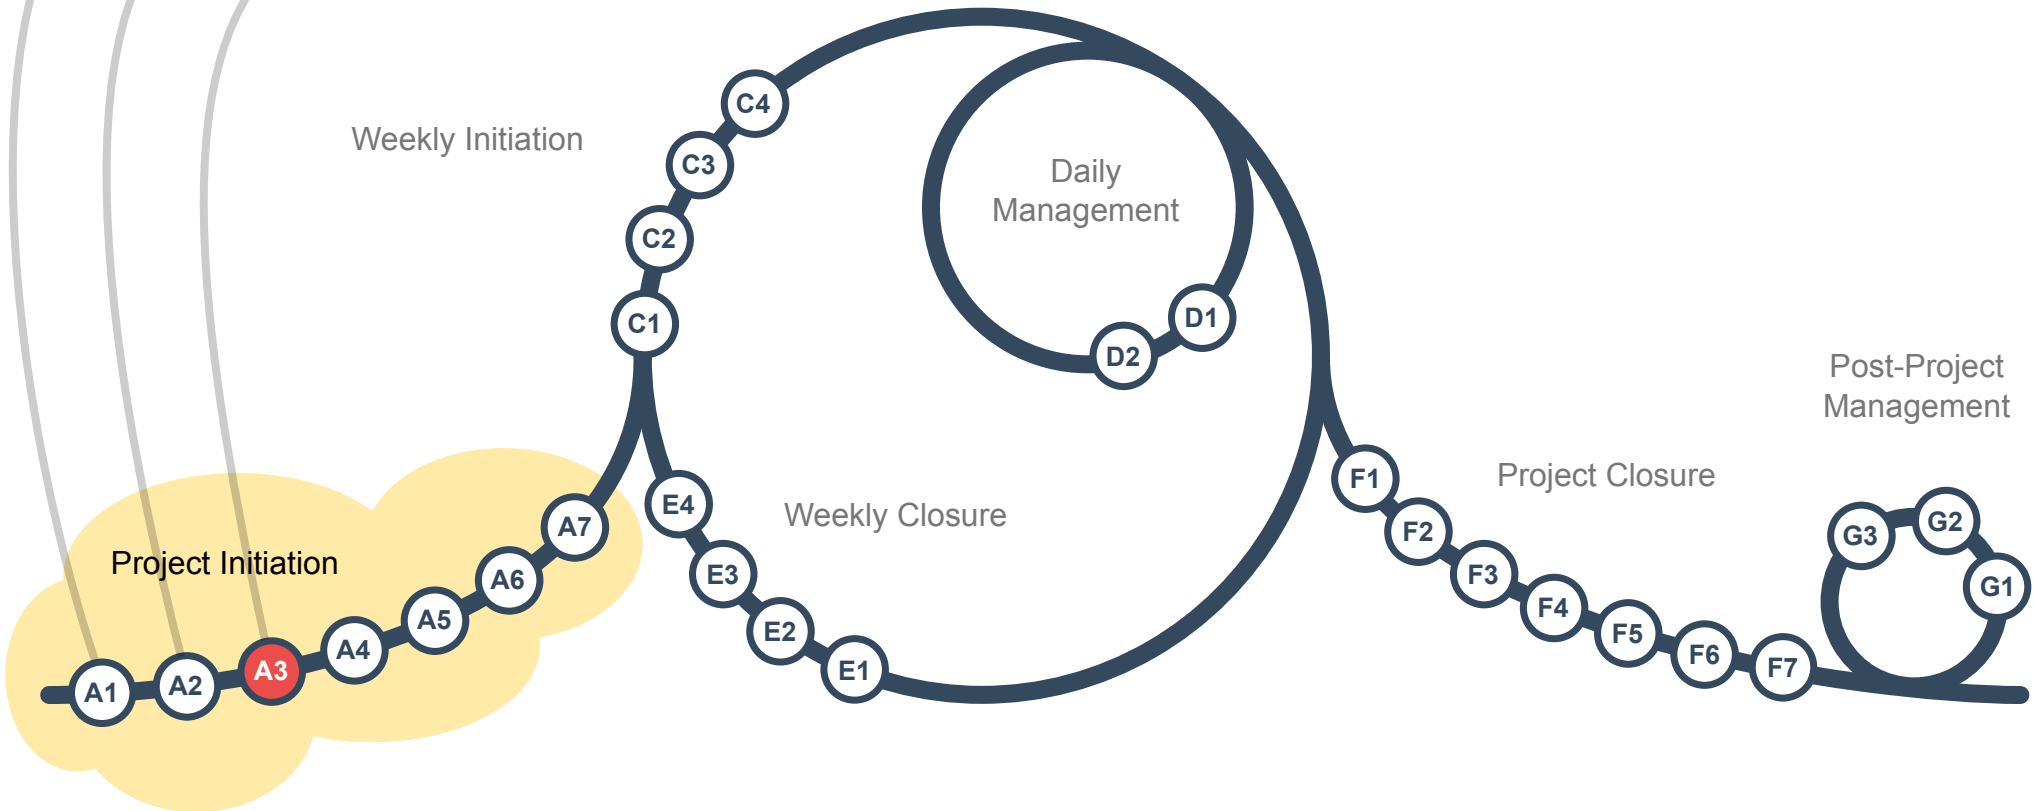


What concerns do you think each hat should have
in this management activity?




A3 - Select tools and create a project repository

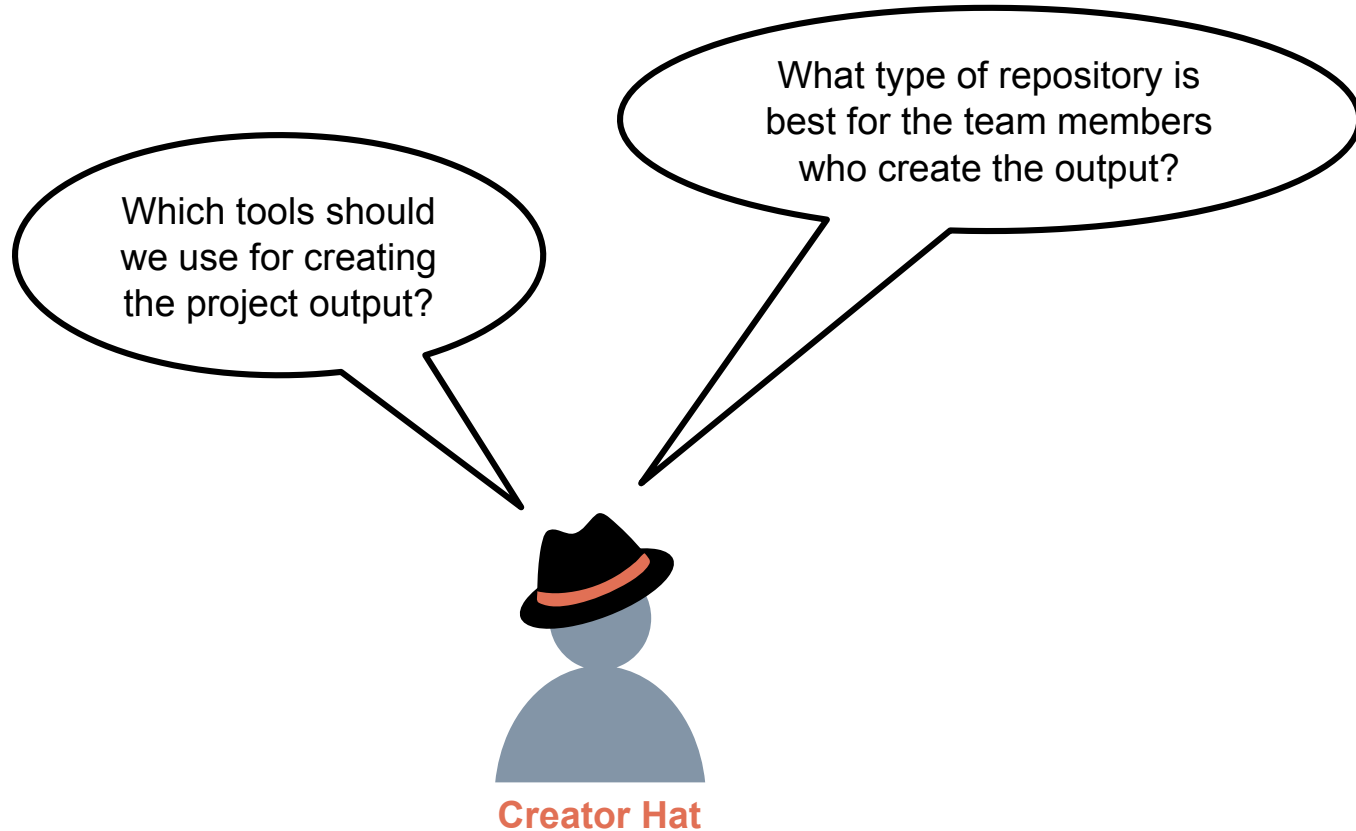

A3 - Select tools and create a project repository

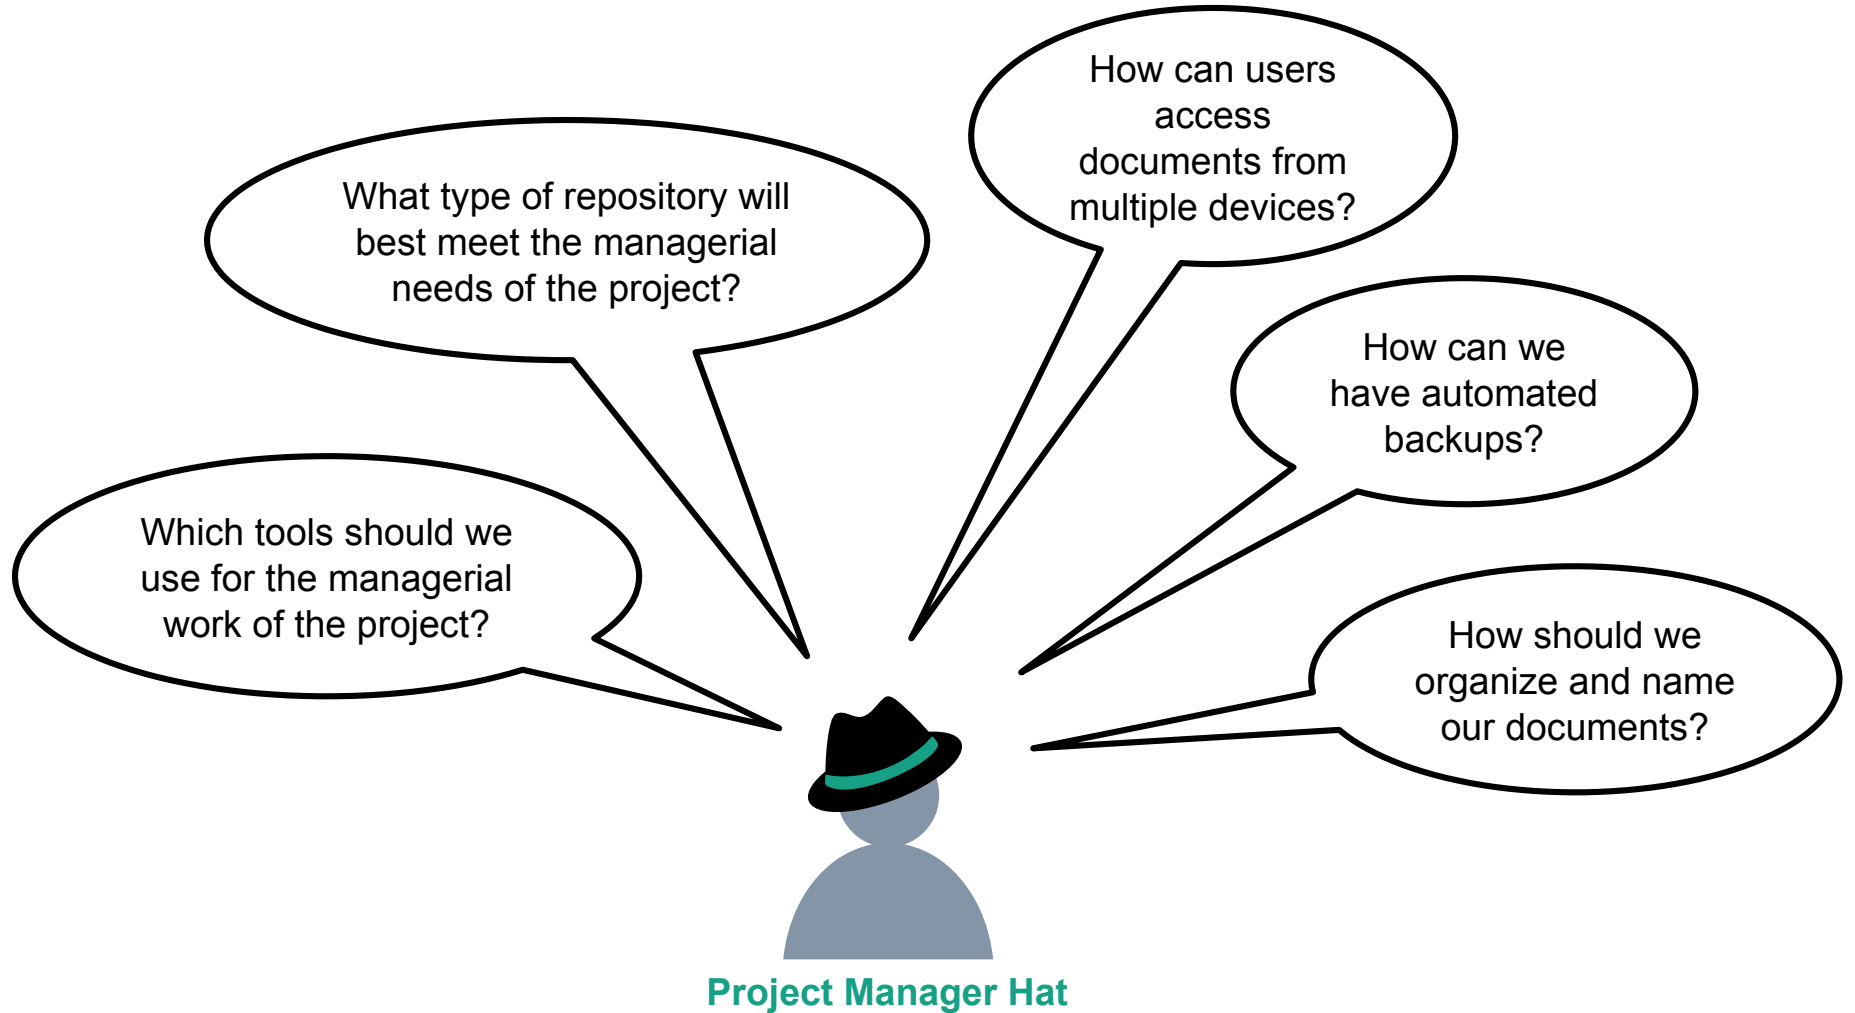

A3 - Select tools and create a project repository



A3 - Select tools and create a project repository




A3 - Select tools and create a project repository



Identify the high-level decision maker(s)

Understand and distribute the hats

Select tools and create a project repository

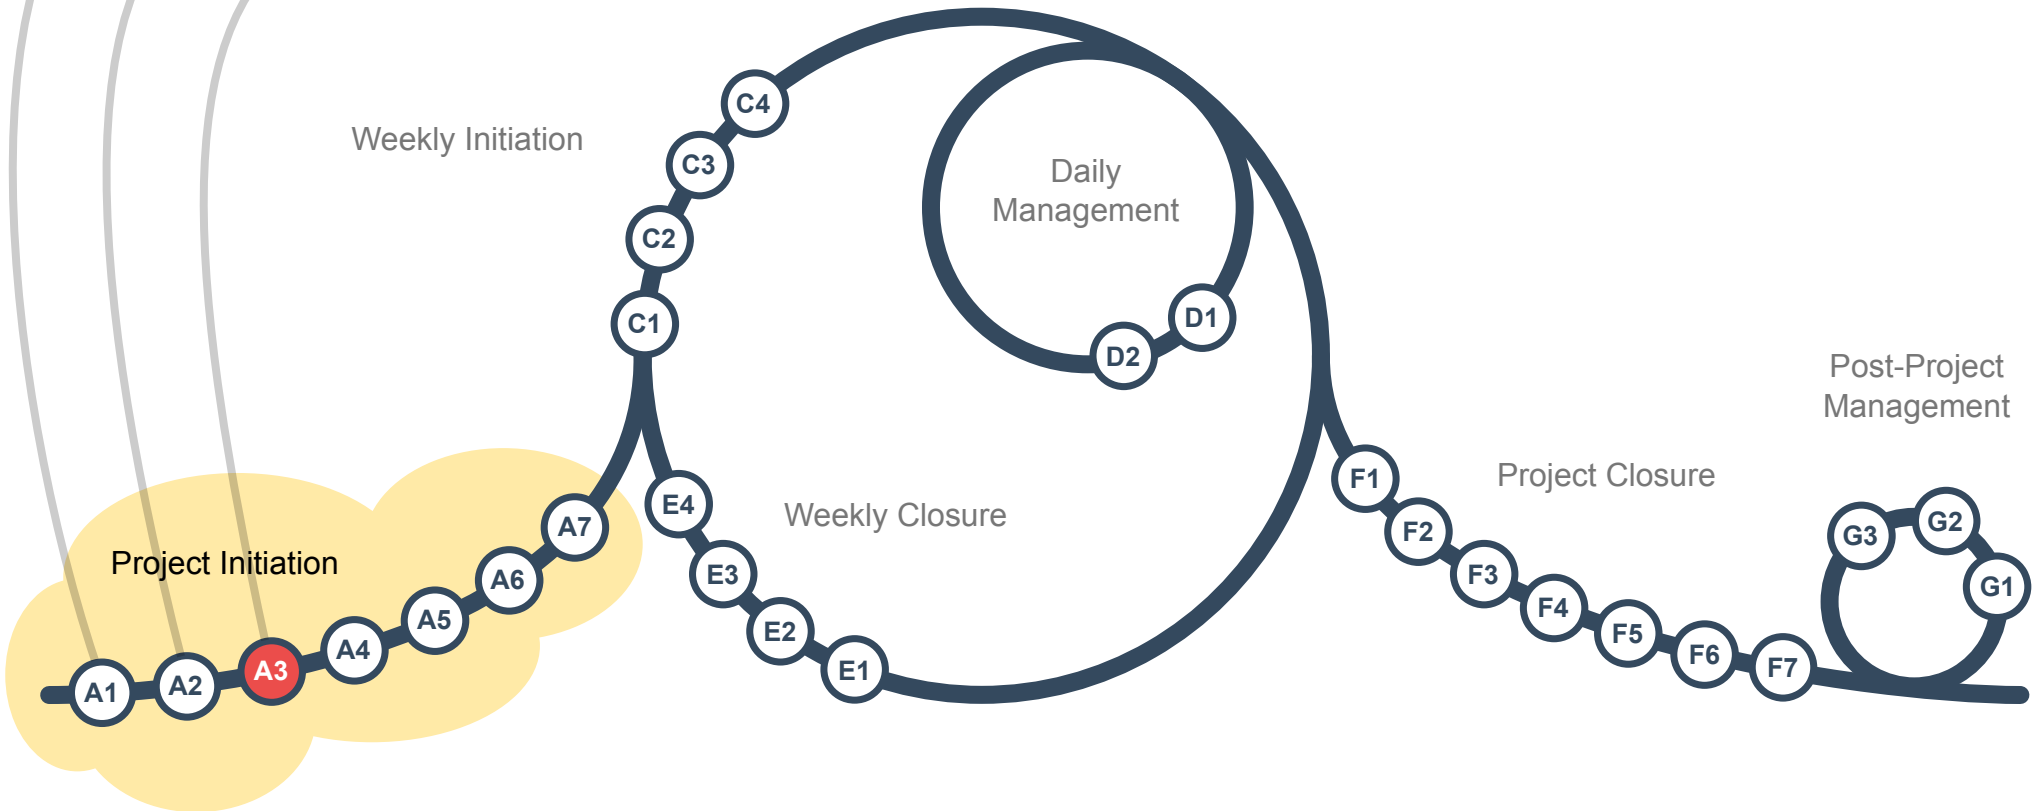


Identify the high-level decision maker(s)


Understand and distribute the hats

Select tools and create a project repository

Create a common understanding

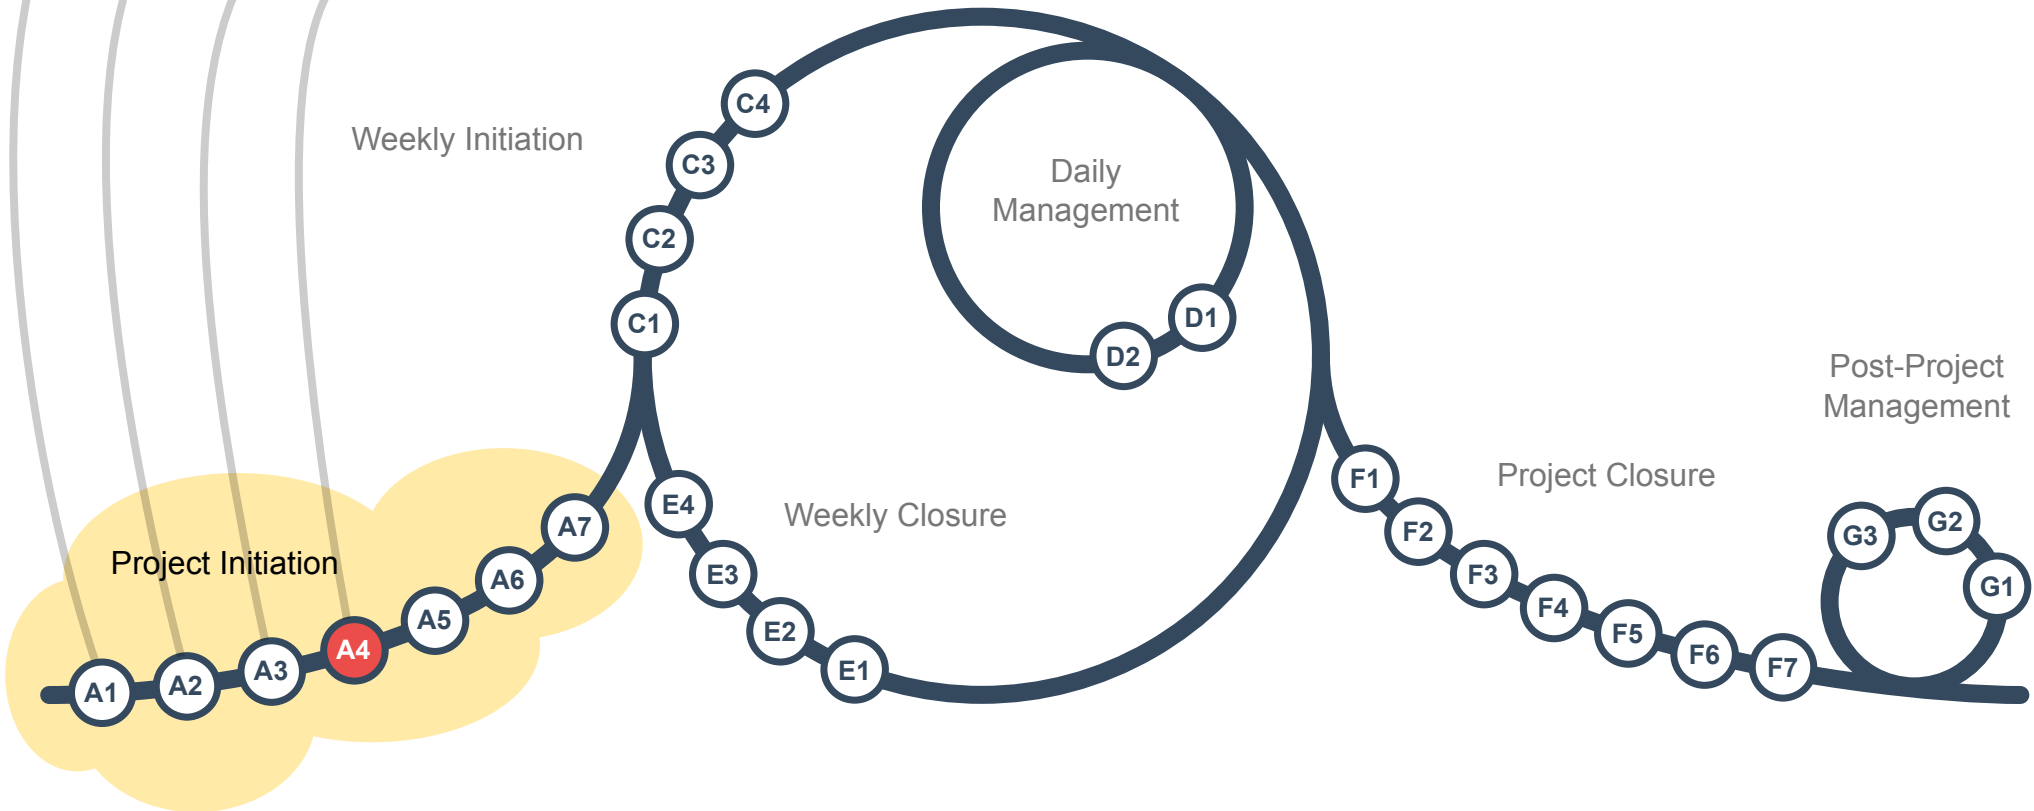


A4 - Create a common understanding

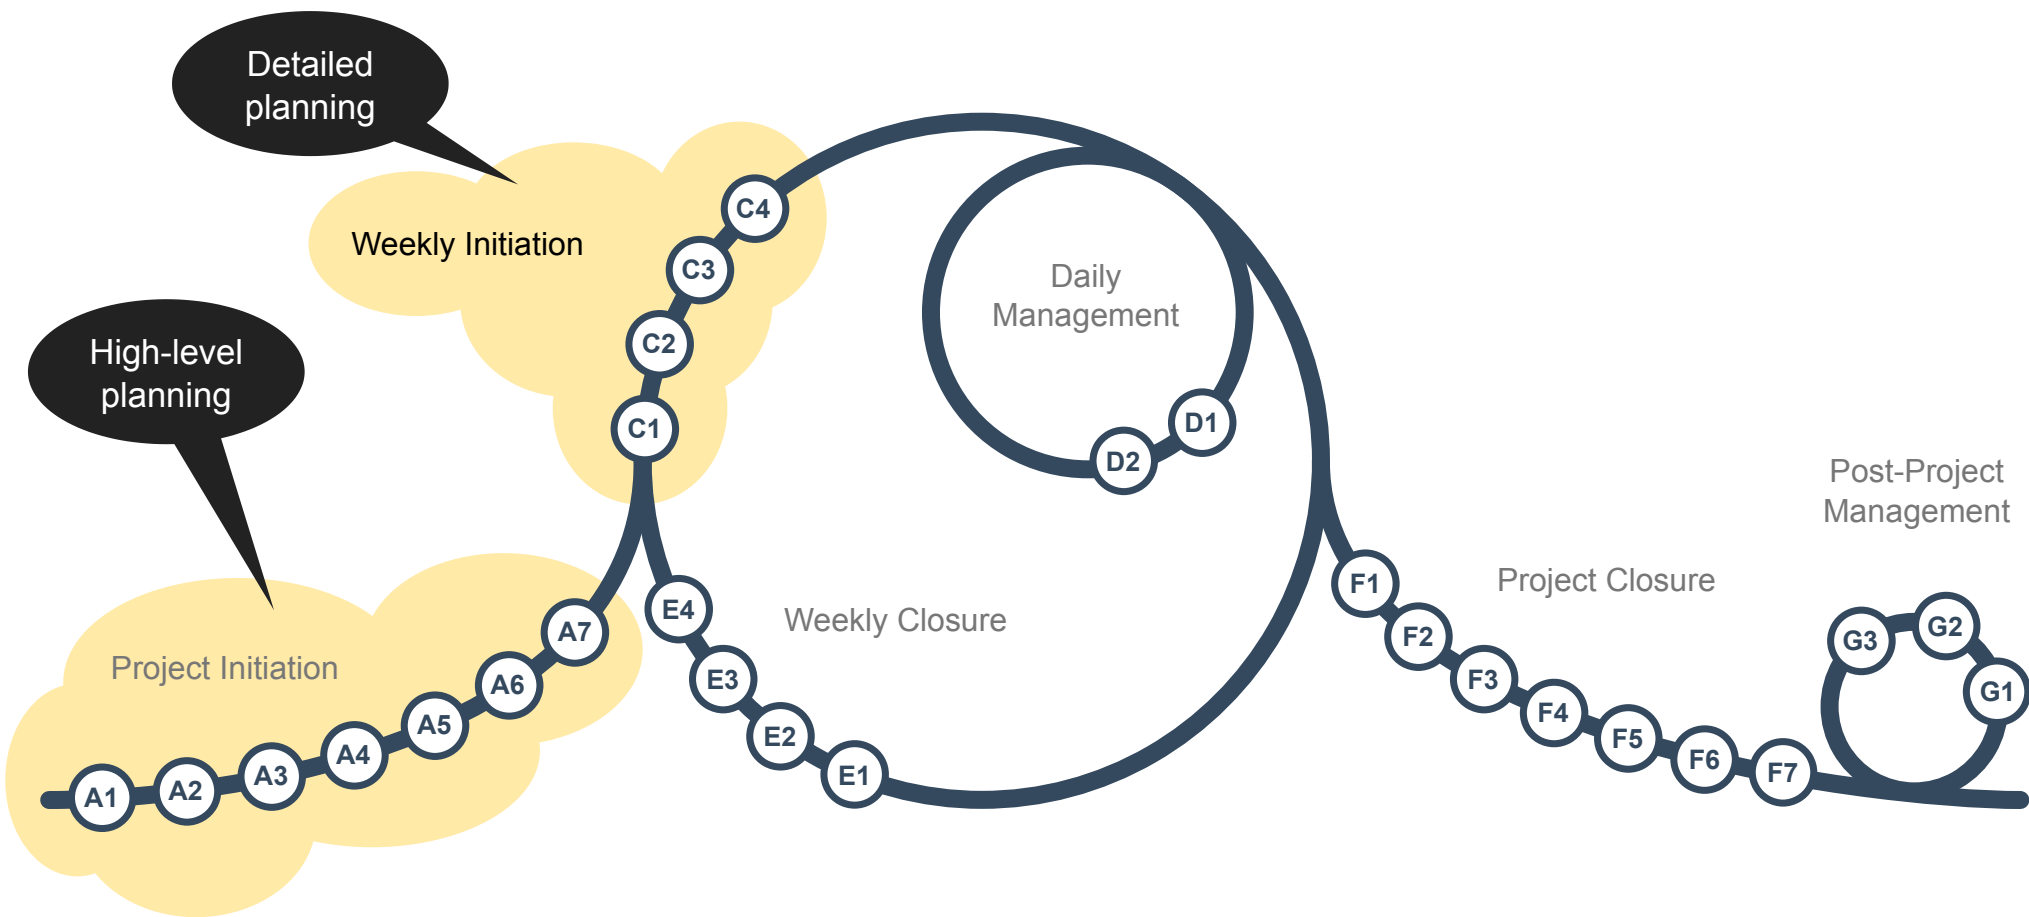


Integrated Project Board

A digital or physical board

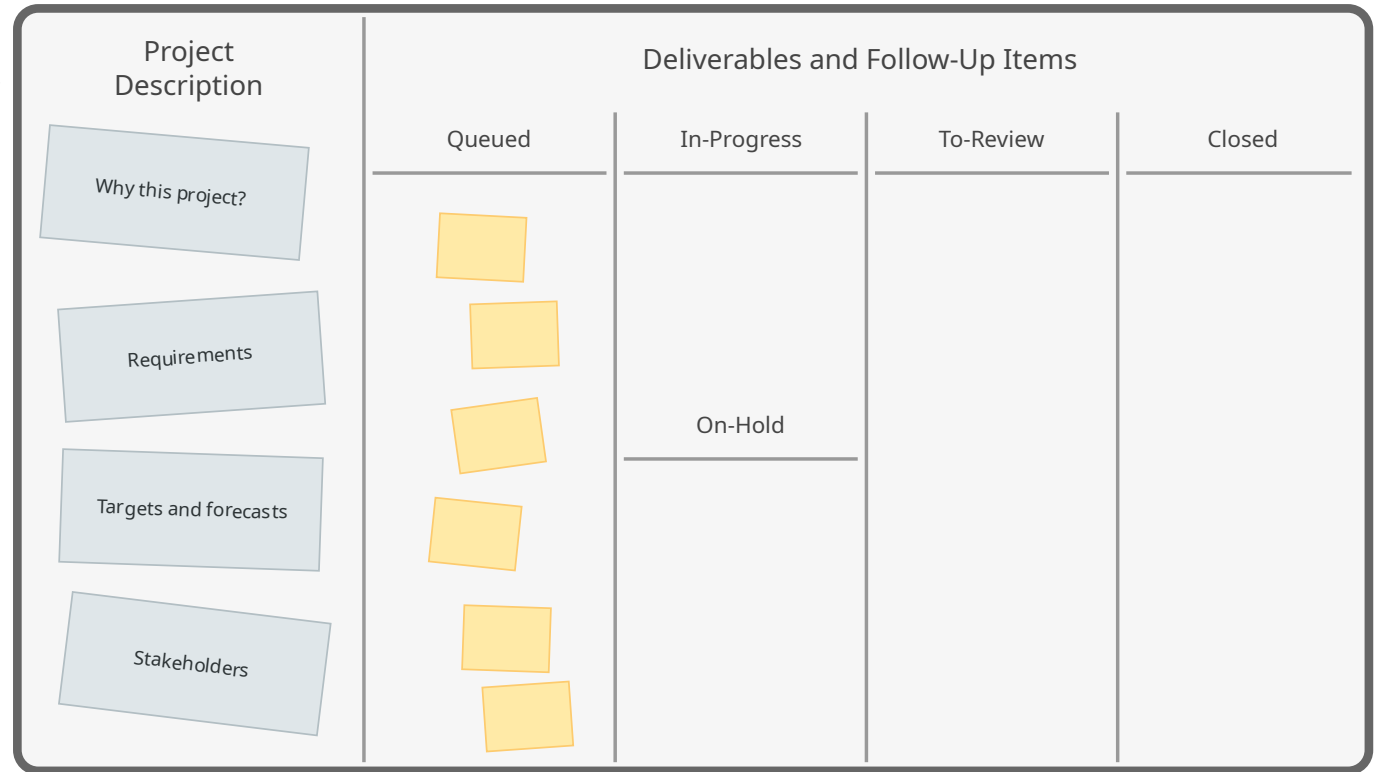

Integrated Project Board

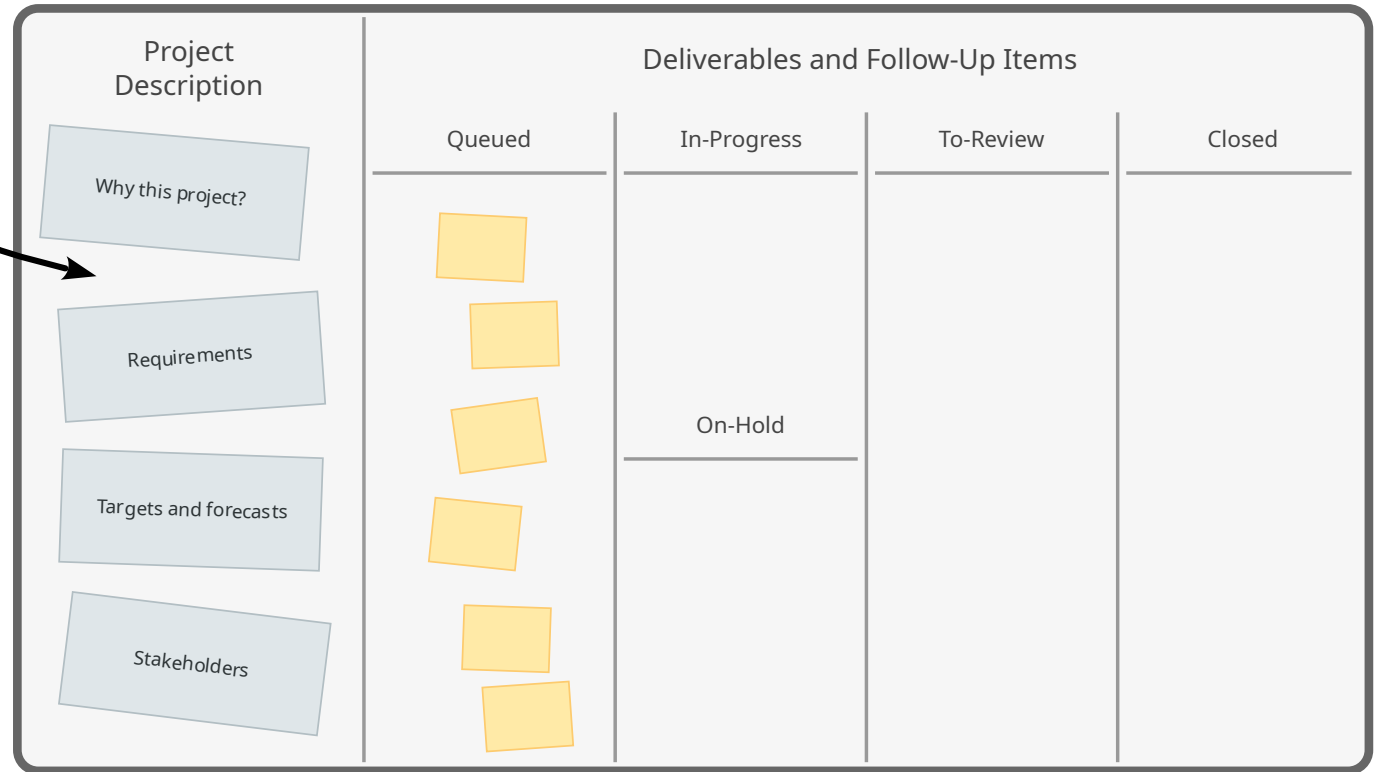

Meta-cards



Remain in the first column


Updated during the project

Integrated Project Board

Why this project?

Example:

our website can gradually grown and has more elements than before, but still has the old structure that was suitable to a simple website, which makes it difficult for people to use it. By rebuilding the website and using a better structure, we can improve user interactions, and ultimately, sales.

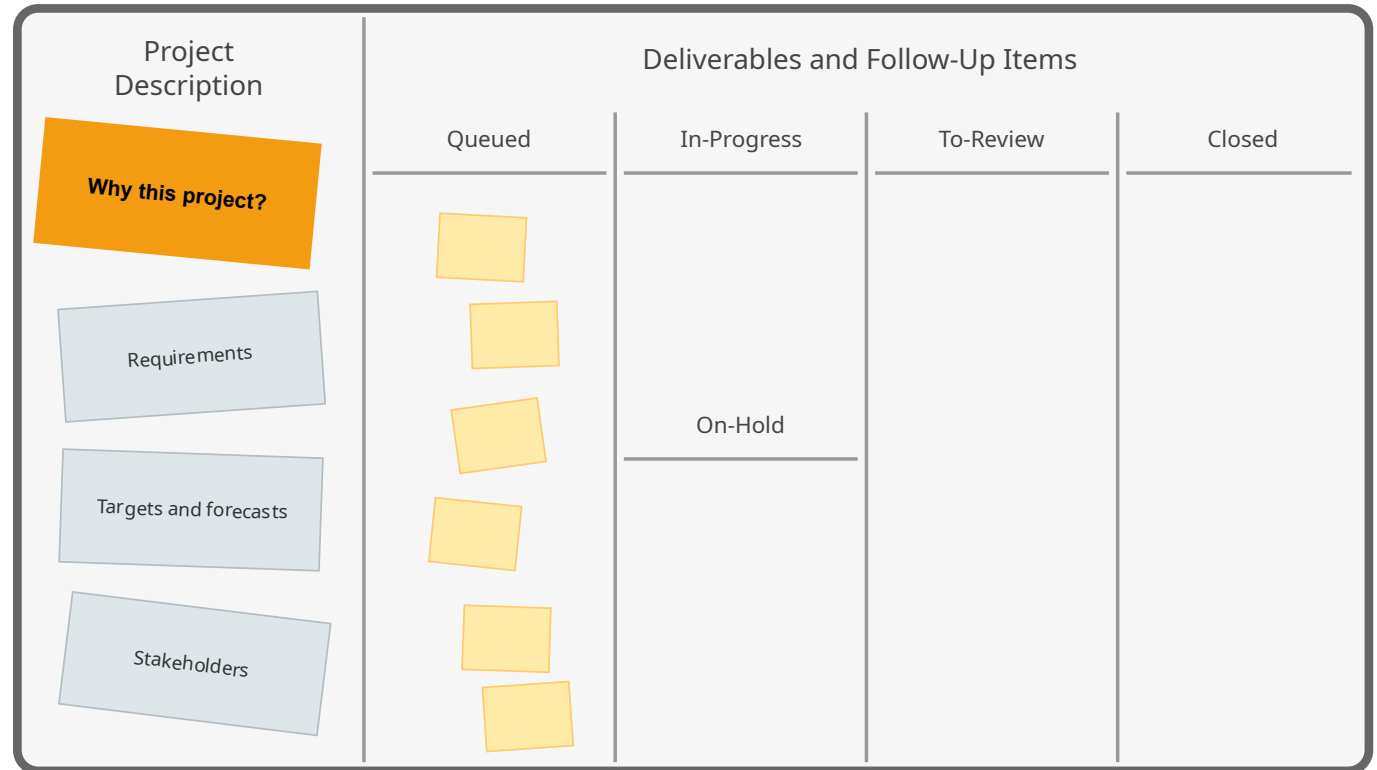


Integrated Project Board

Requirements

Example:

- It should be search engine optimized.
- It should be easy for all users to navigate.
- It should enable cross-sales.
- It should look premium.
- ...

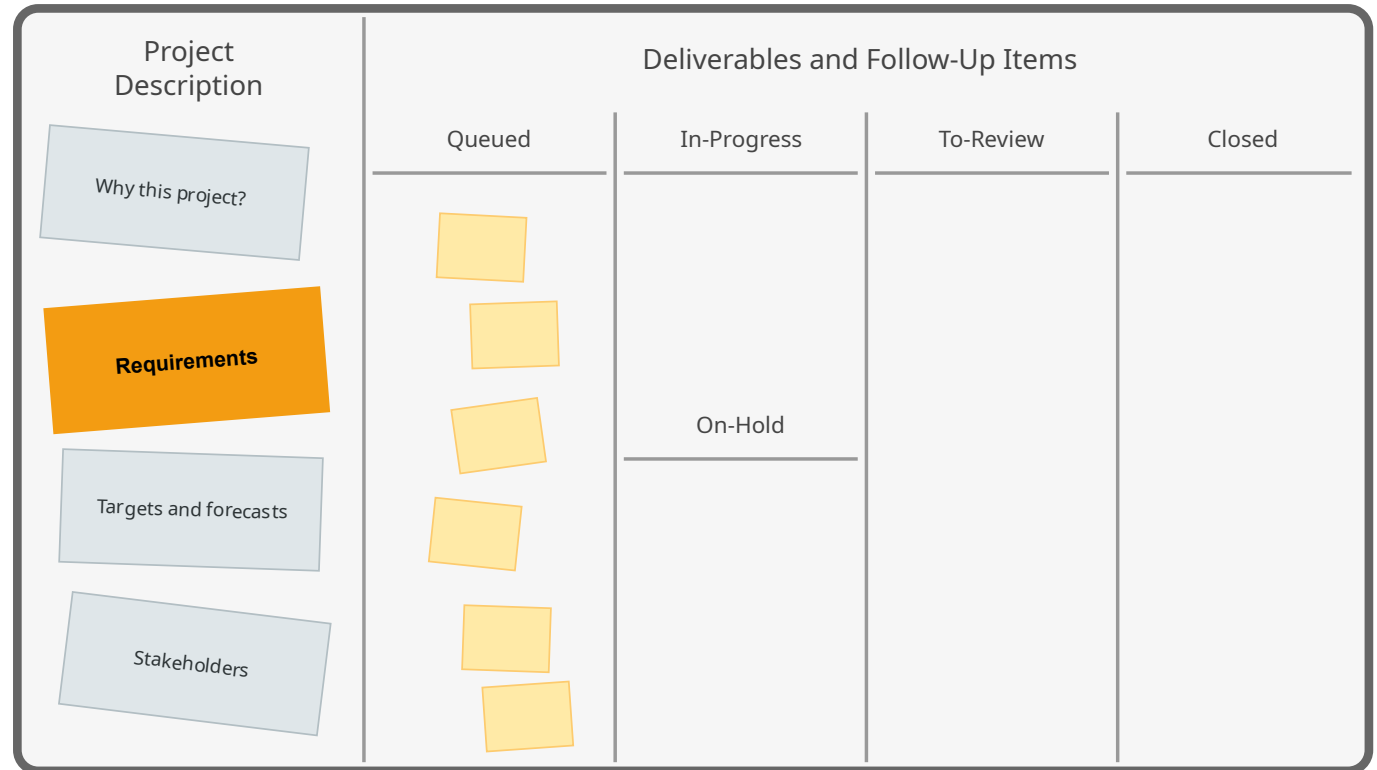


Integrated Project Board

Targets and forecasts


Example:

It should be finished before the New Year sales.

The work will be done by internal people, but we can spend up to €10k for graphic design and other outsourced aspects.

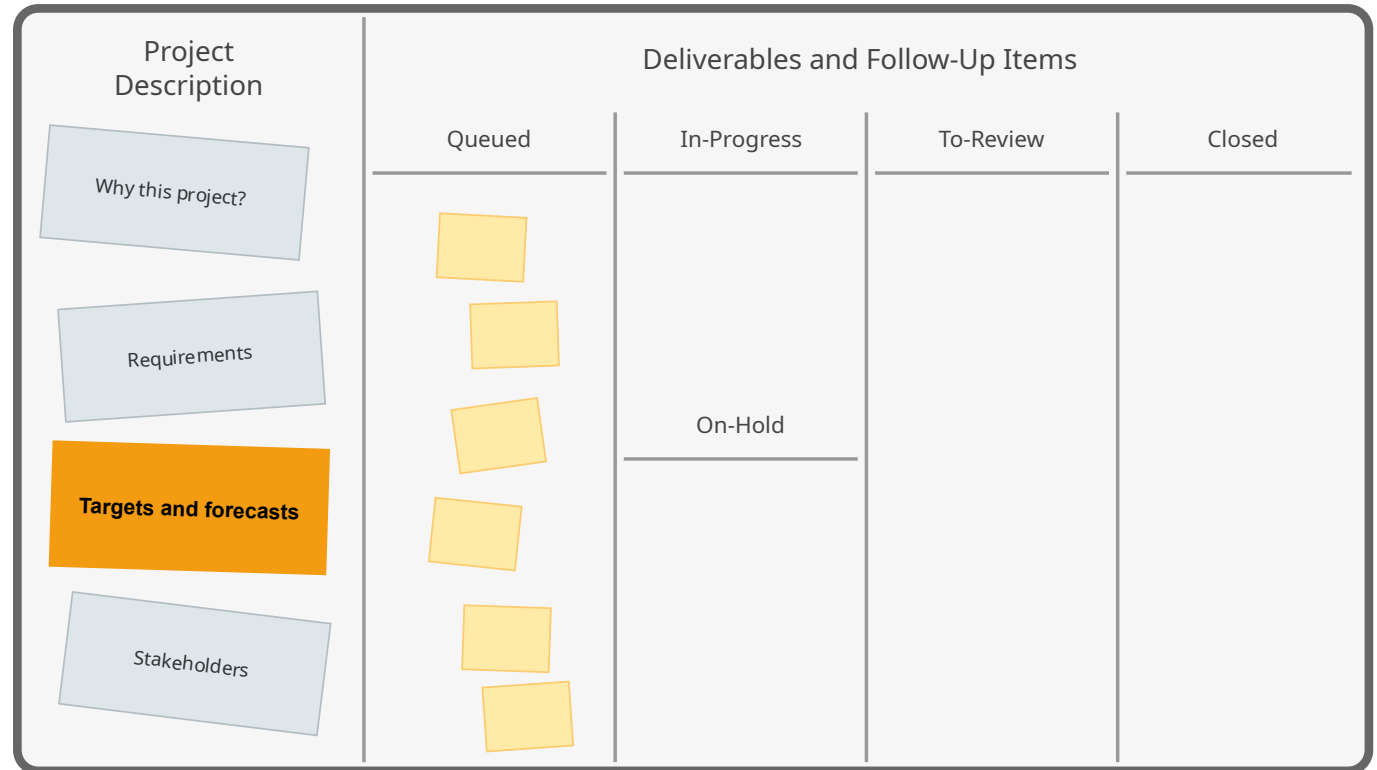

Integrated Project Board

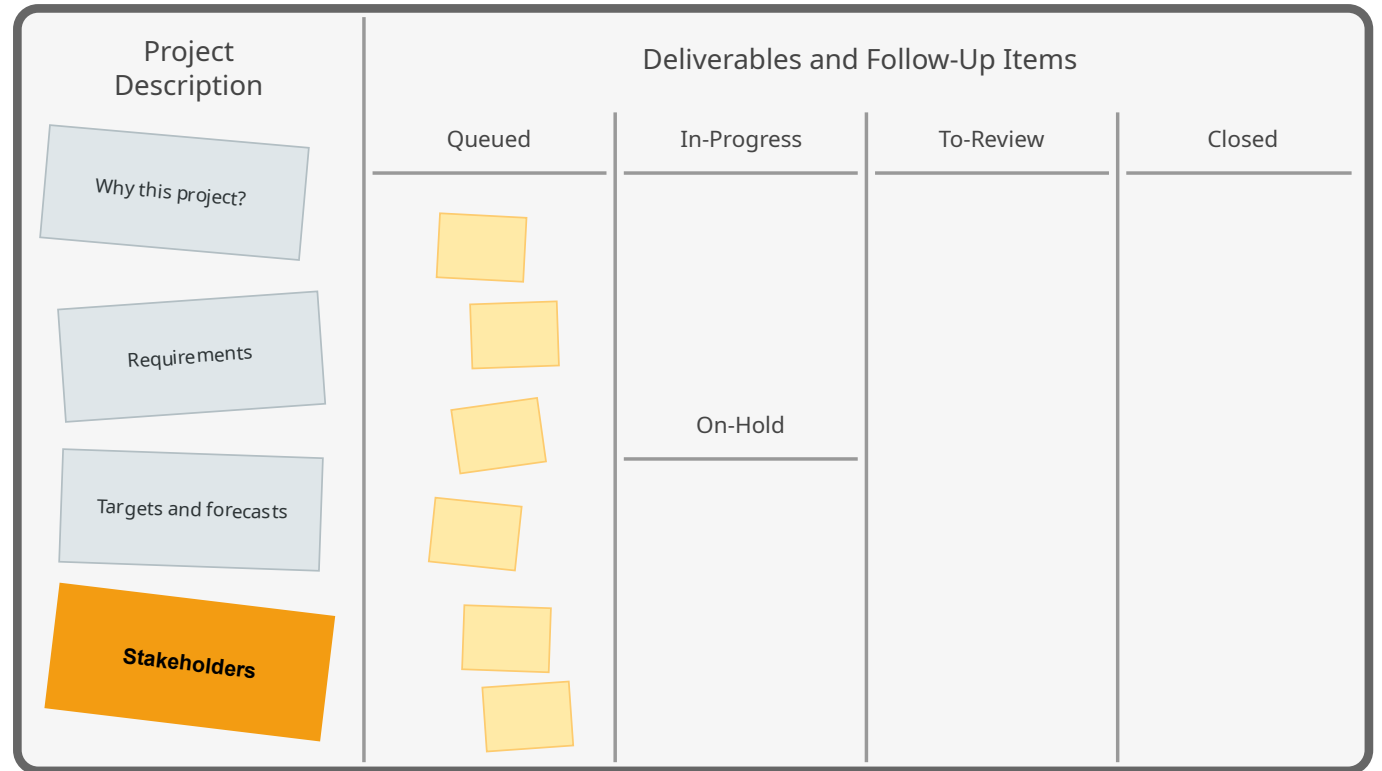

Stakeholder:


Anyone who has an interest in the project and can impact it.

Integrated Project Board

Stakeholders


Example:

- Monet, the CEO
- Fede, the COO & sponsor
- Kyung, account manager
- Jehan, our biggest competitor
- Mirai, our main supplier
- GDPR authority
- Customer Protection Agency
- ...

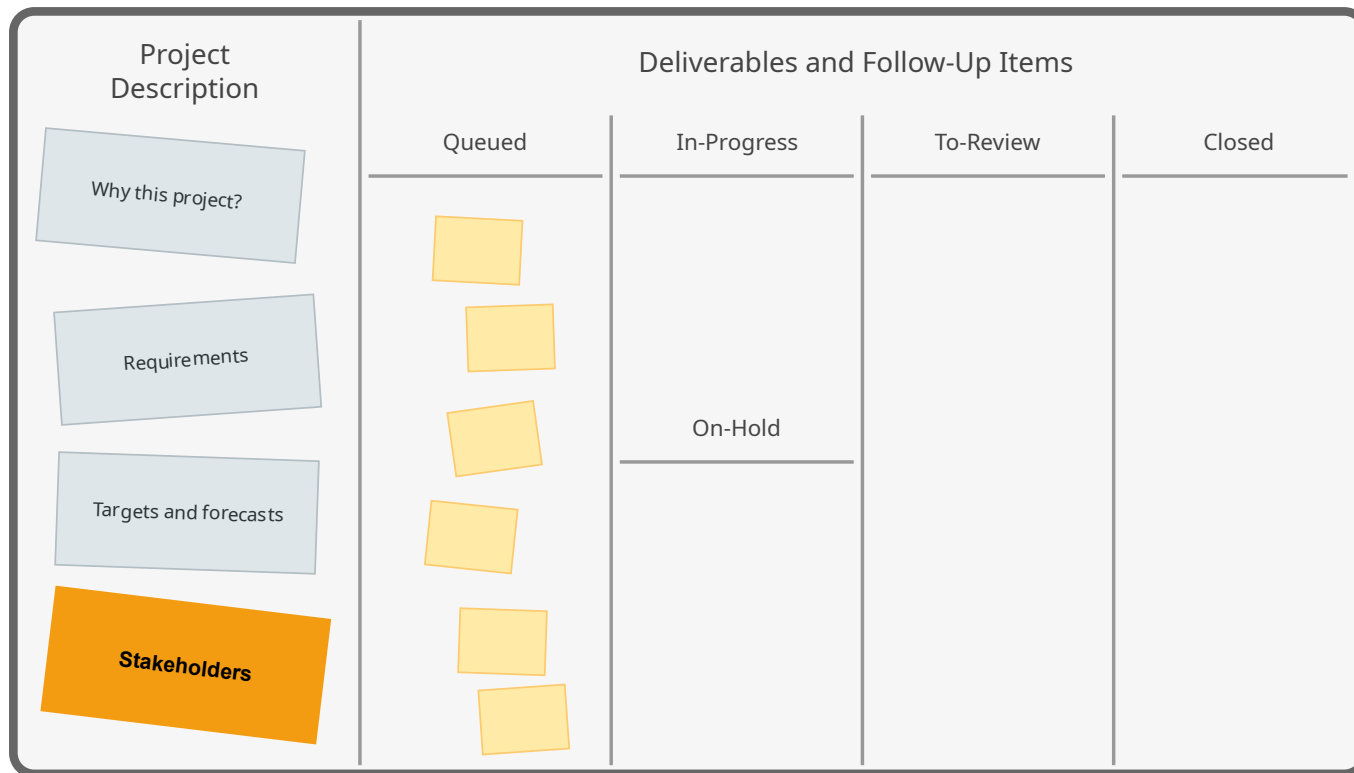


Integrated Project Board

Meta-cards

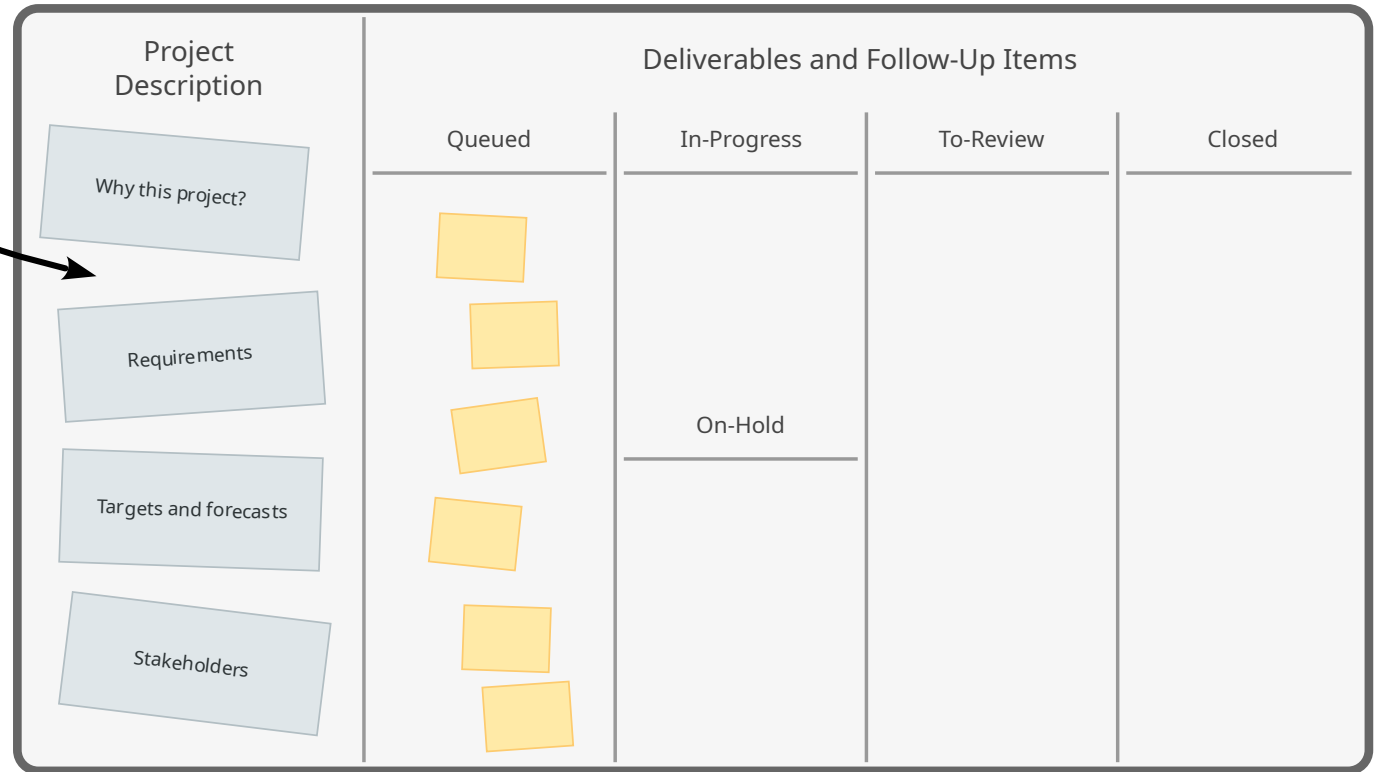

Integrated Project Board

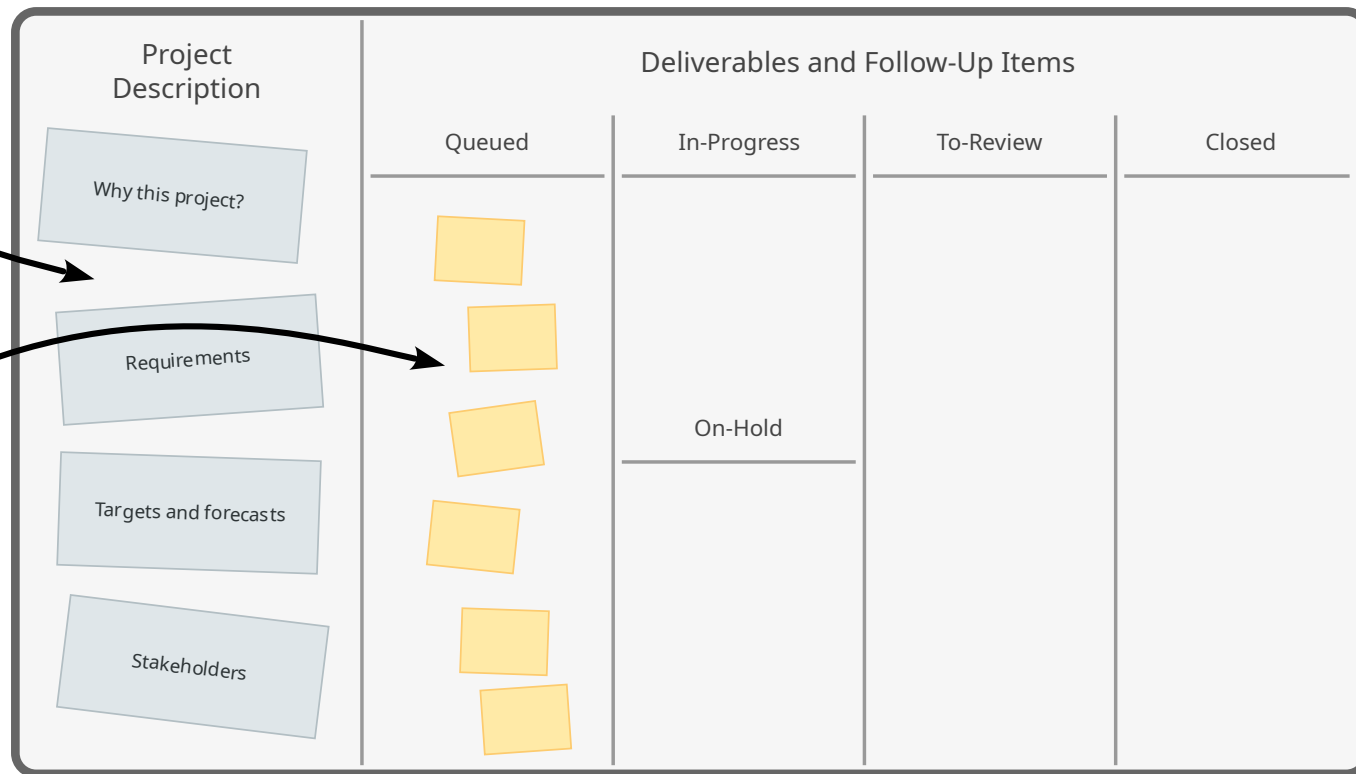

Meta-cards

Remain in the first column

Cards


Should ultimately move to the "closed" column.

Integrated Project Board

Meta-cards

Cards

(Deliverables & follow-up items)

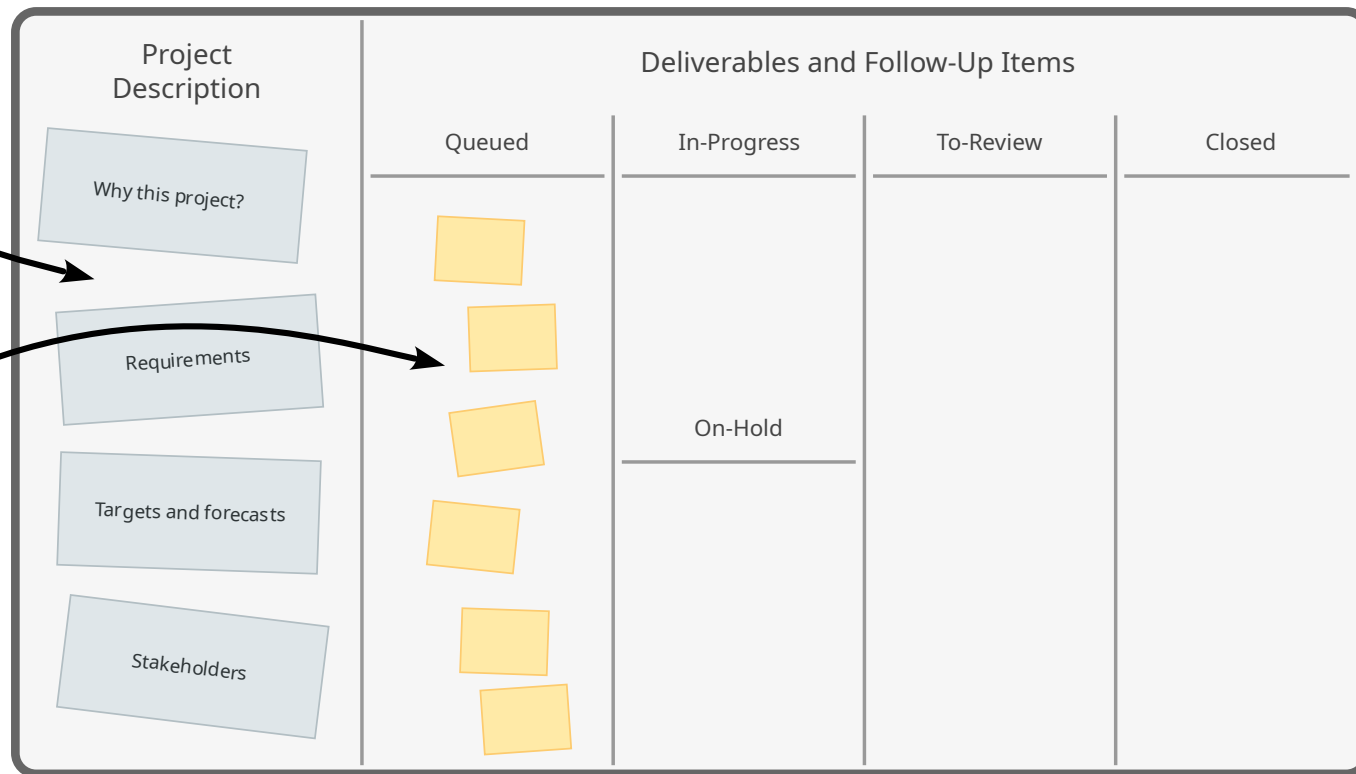

Integrated Project Board


Meta-cards

Cards


(Deliverables & follow-up items)

Deliverables examples:

- Payment gateways
- Discount coupons
- ...

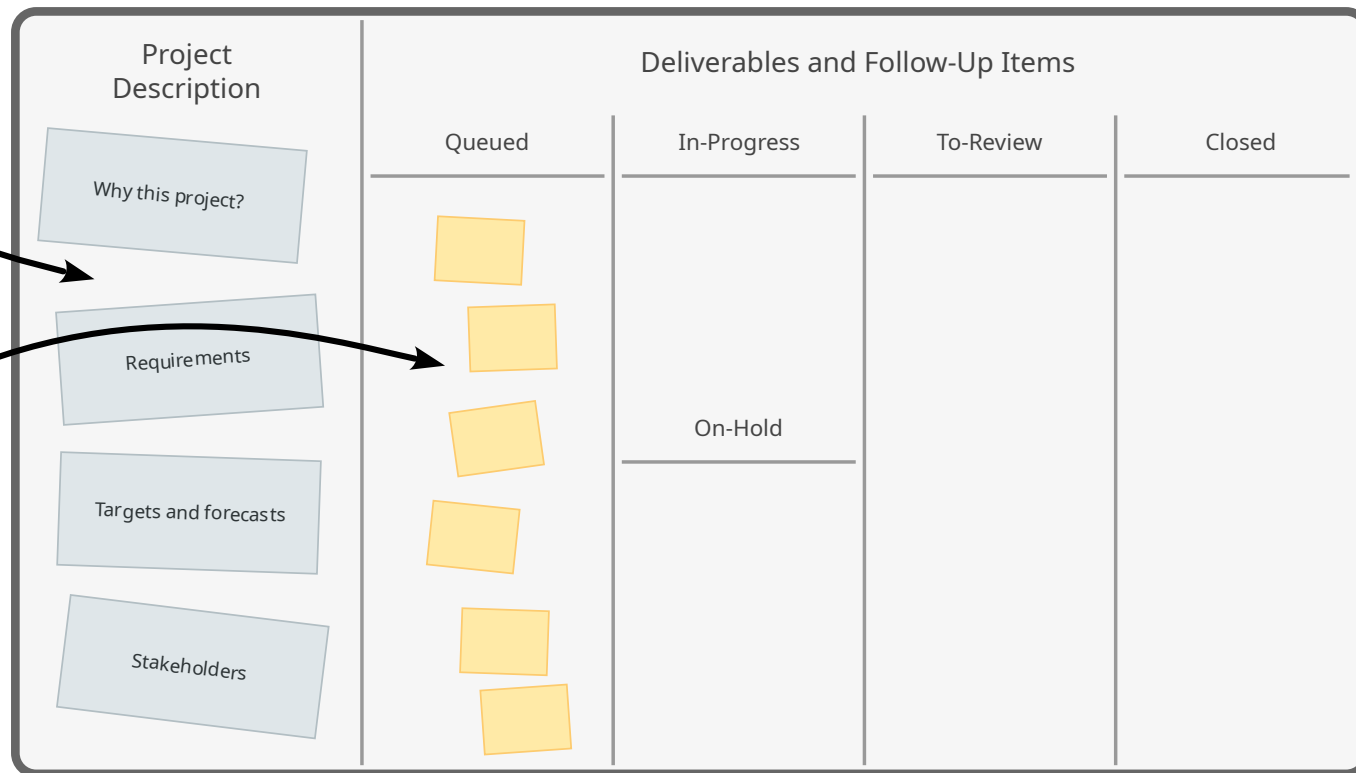

Integrated Project Board

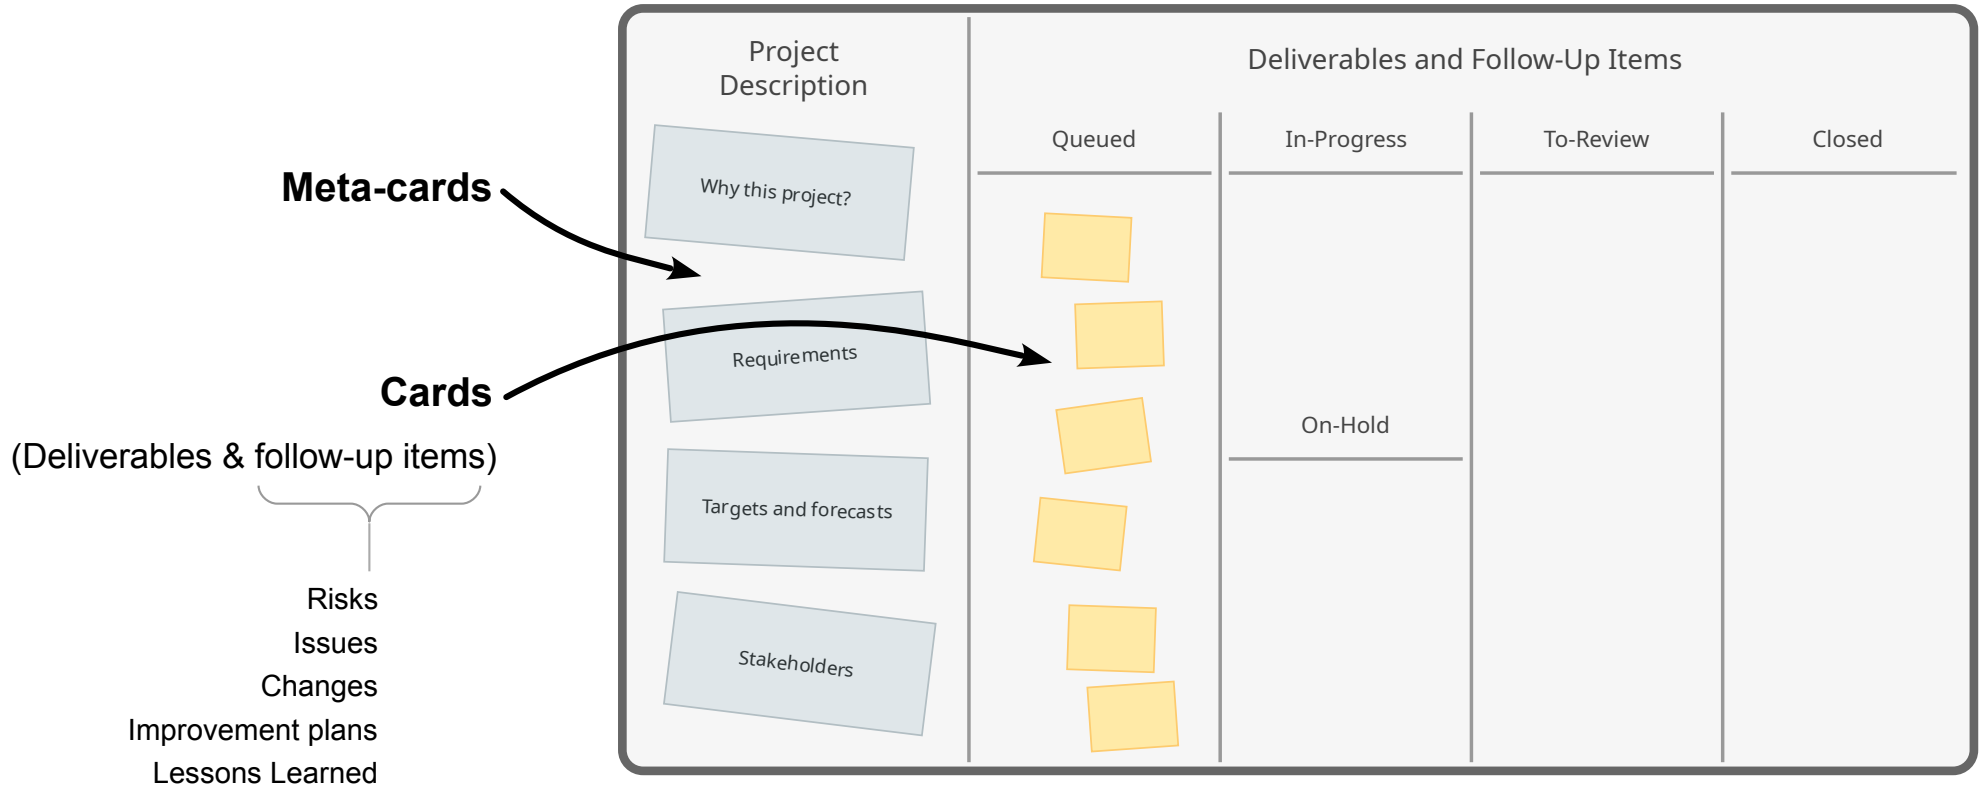

Integrated Project Board


Meta-cards

Cards

(Deliverables & follow-up items)

Follow-up example:


Some people may forget to enter their VAT number when placing their order and later ask for a correction.

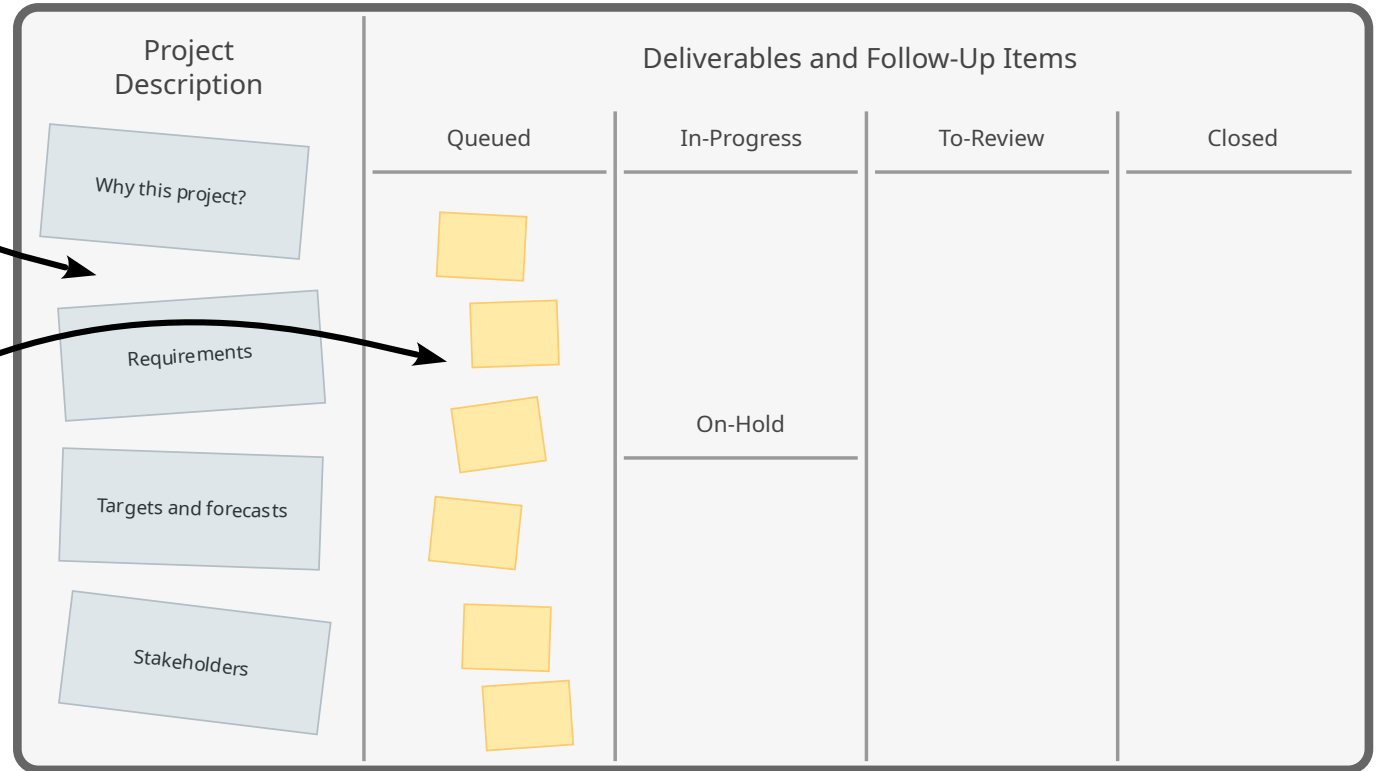


What concerns do you think each hat should have
in this management activity?




A4 - Create a common understanding

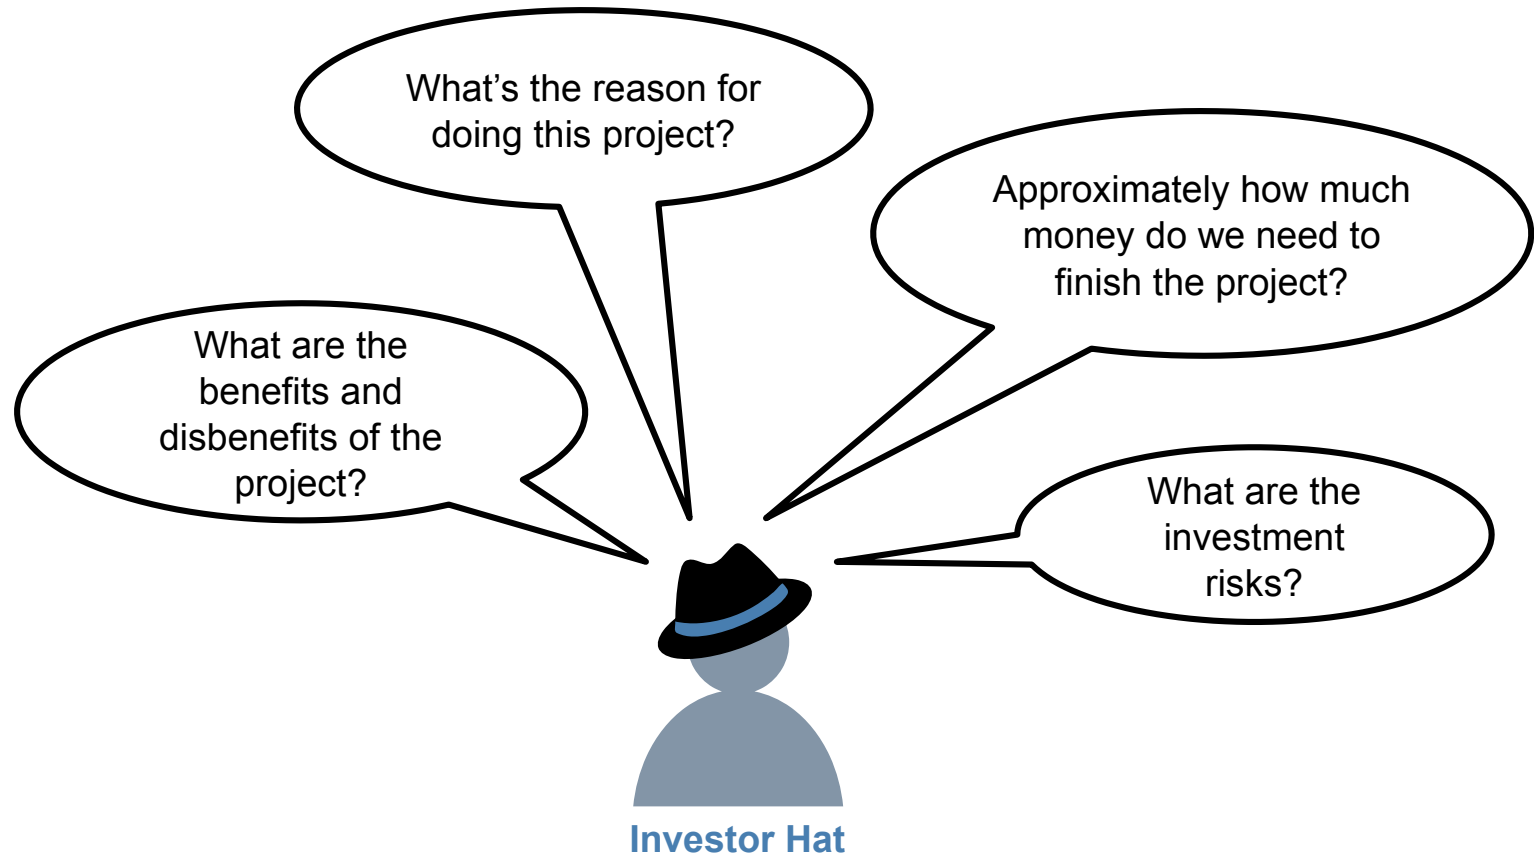

A4 - Create a common understanding

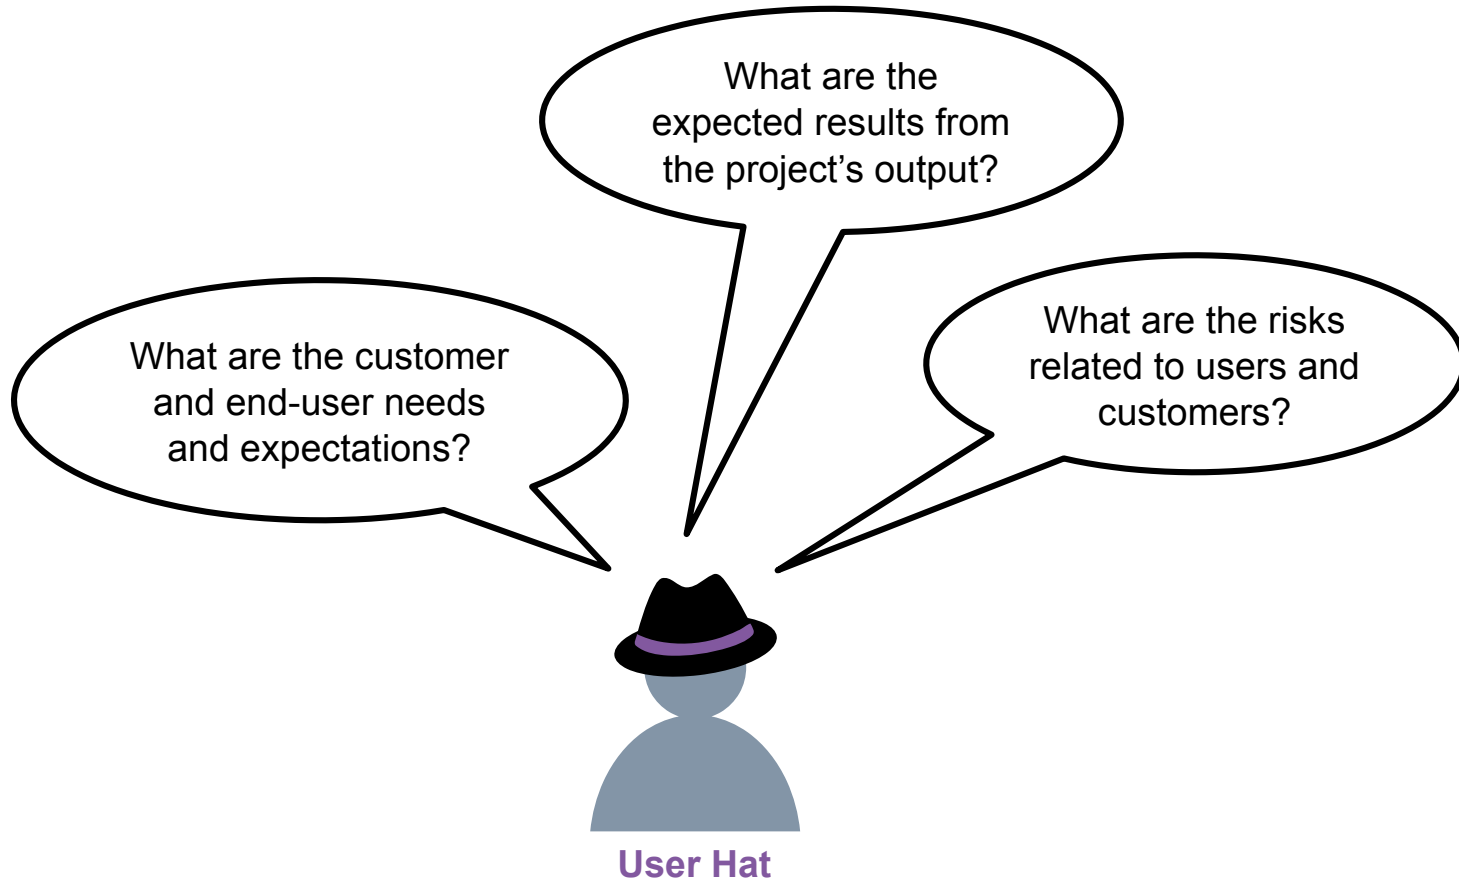


A4 - Create a common understanding

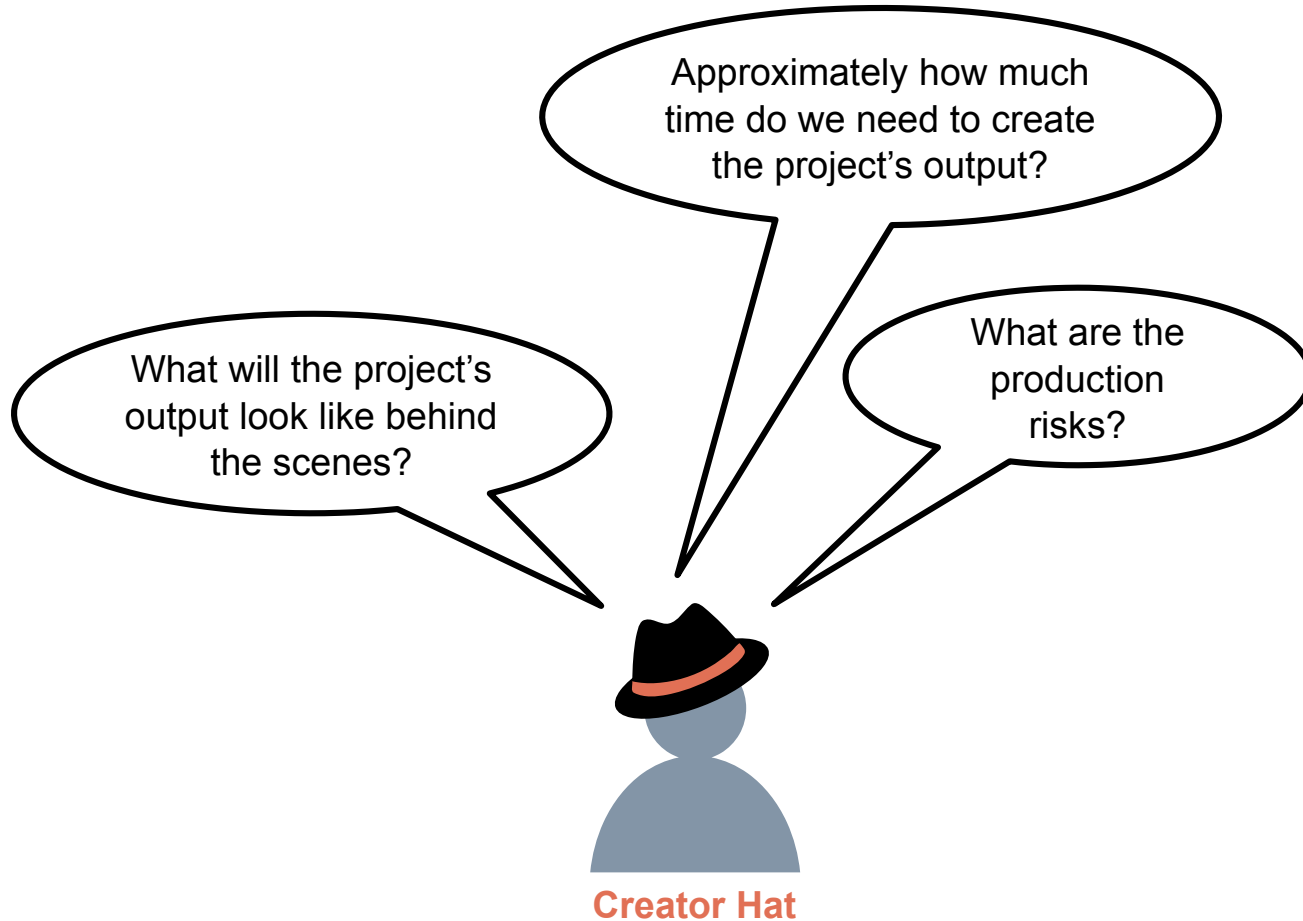

A4 - Create a common understanding



A4 - Create a common understanding



**Are the documents
clear and easy to
understand?**


Project Manager Hat

Identify the high-level decision maker(s)

Understand and distribute the hats

Select tools and create a project repository

Create a common understanding

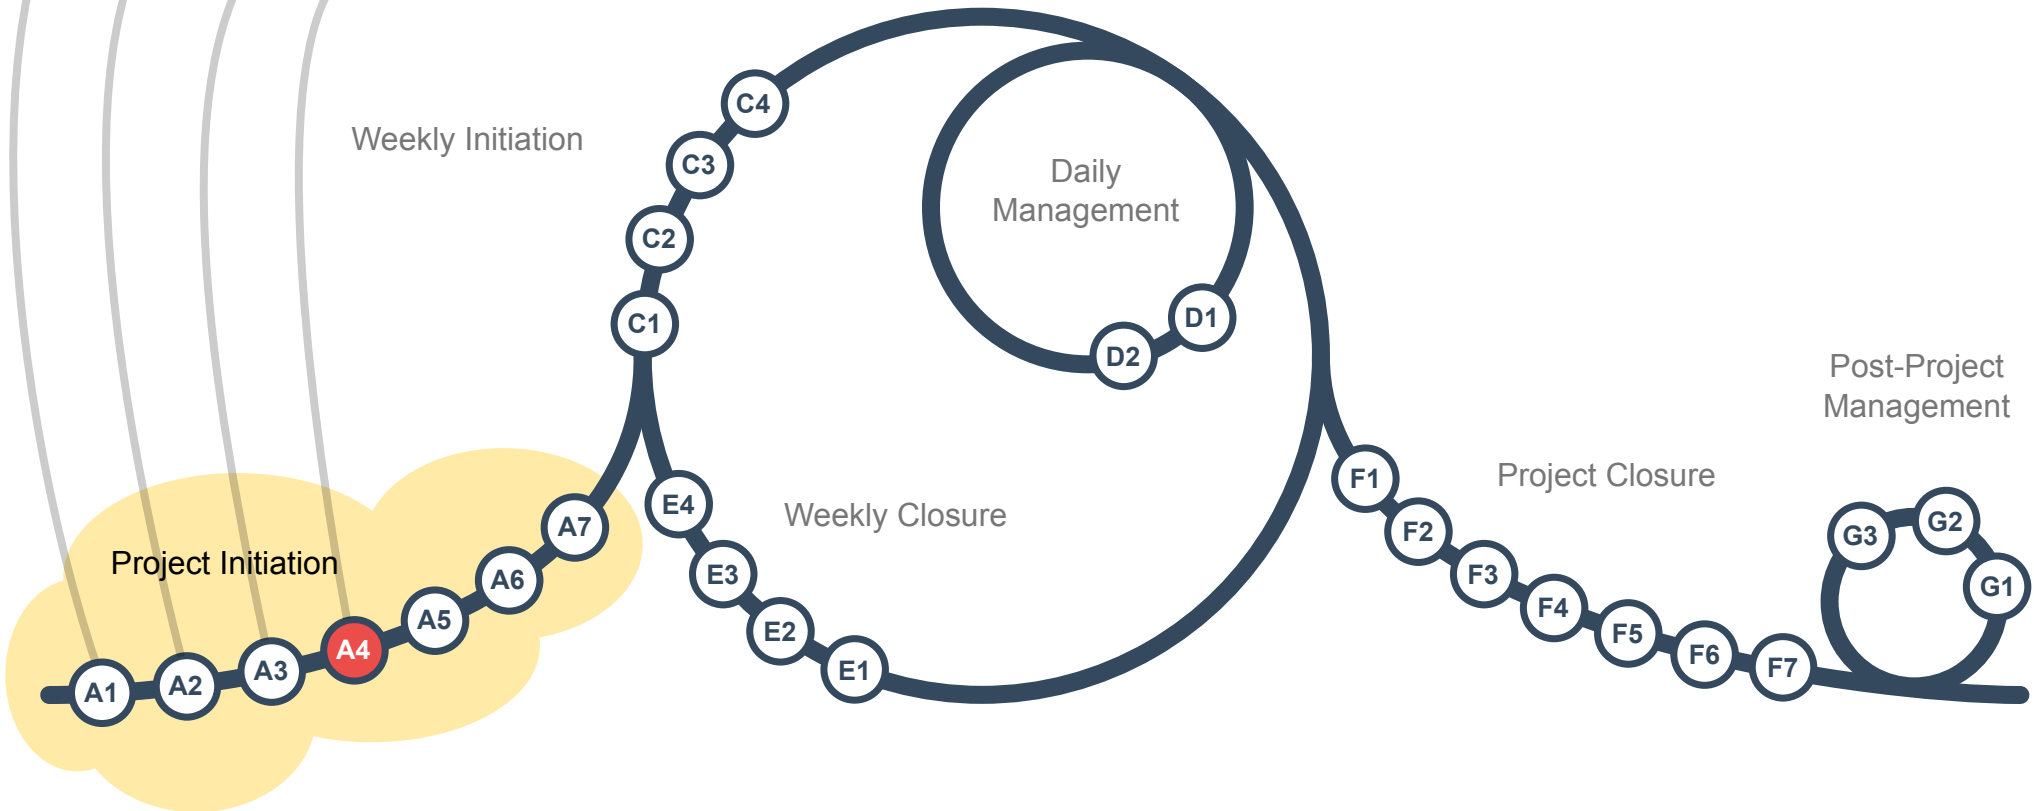

Project Initiation

Weekly Initiation

Daily Management

Weekly Closure

Project Closure

Post-Project Management

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C1

C2

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6

F7

G3


G2

G1

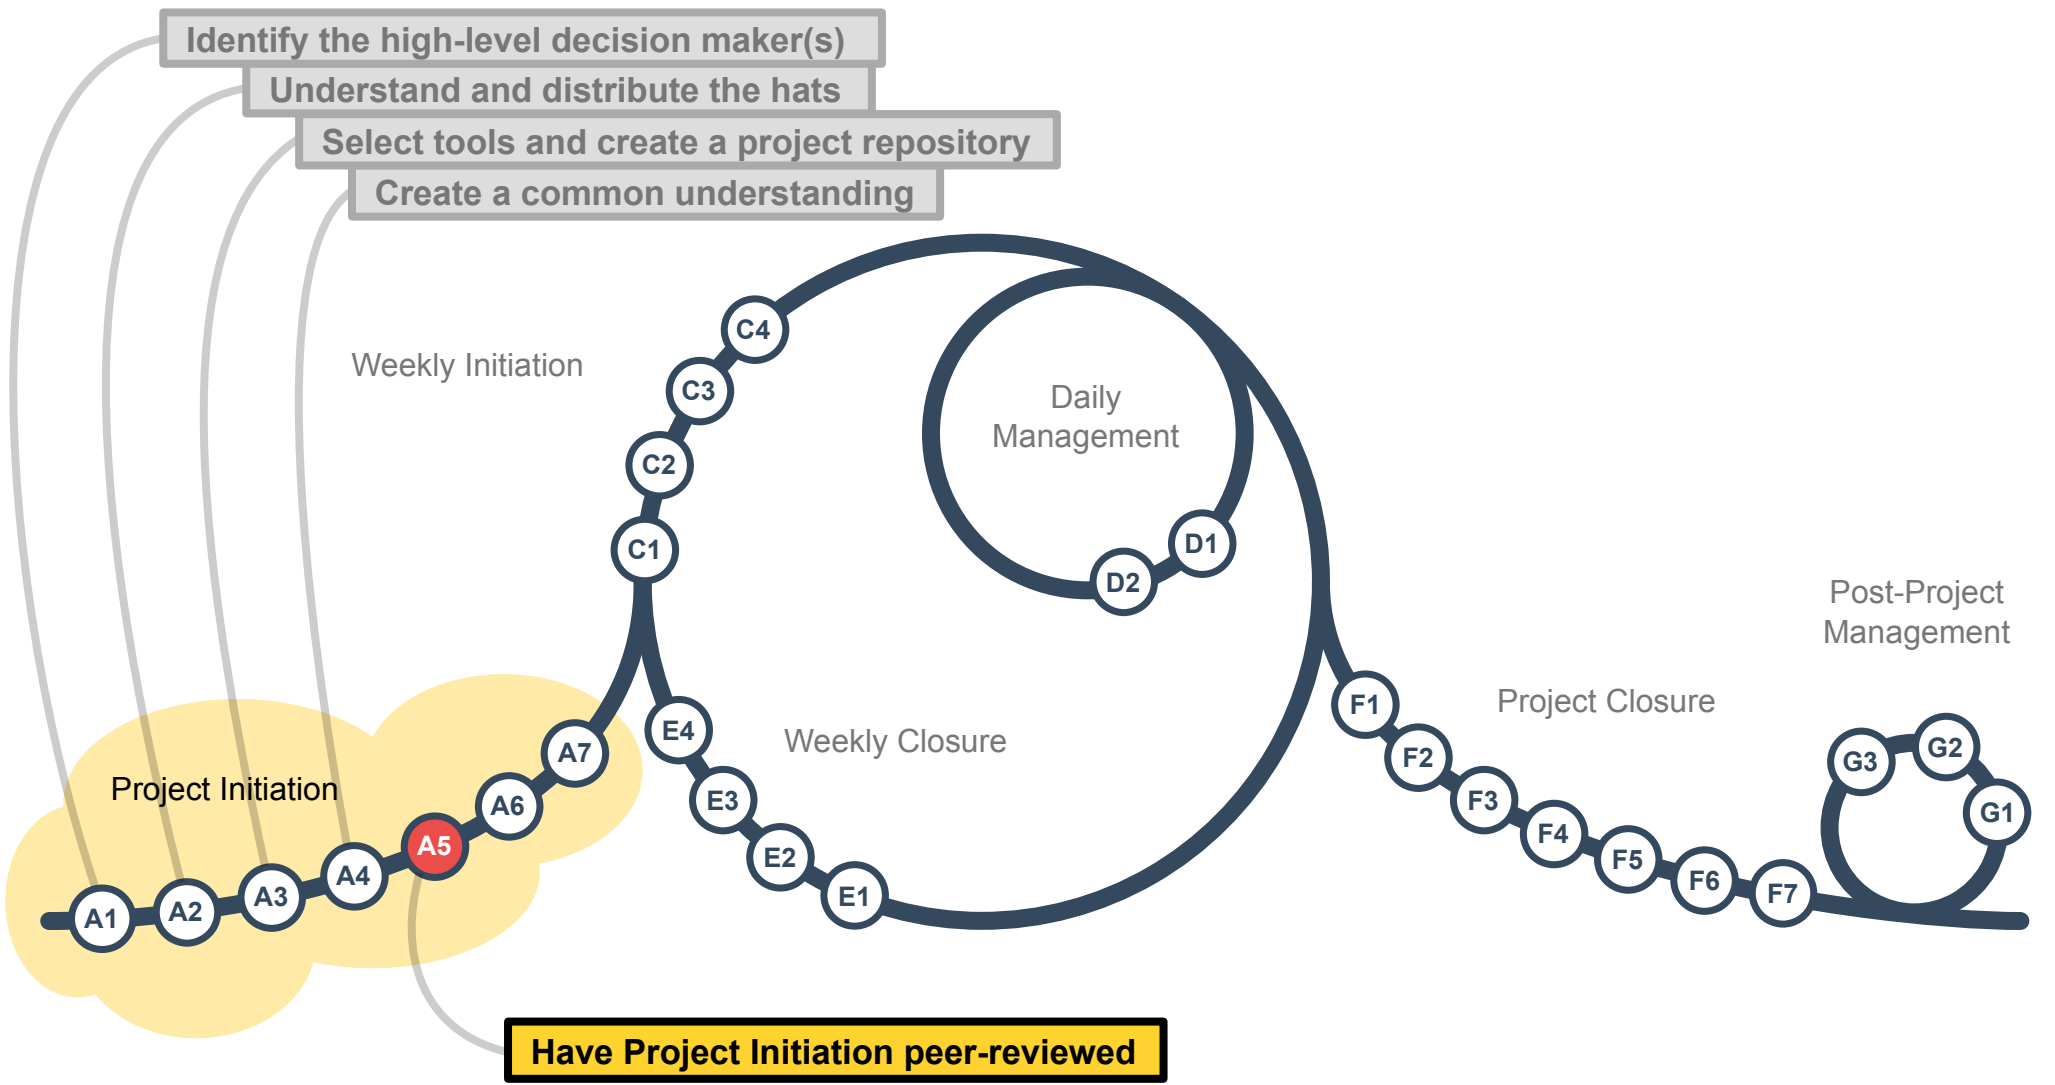


Have Project Initiation peer-reviewed

A5 - Have project initiation peer-reviewed

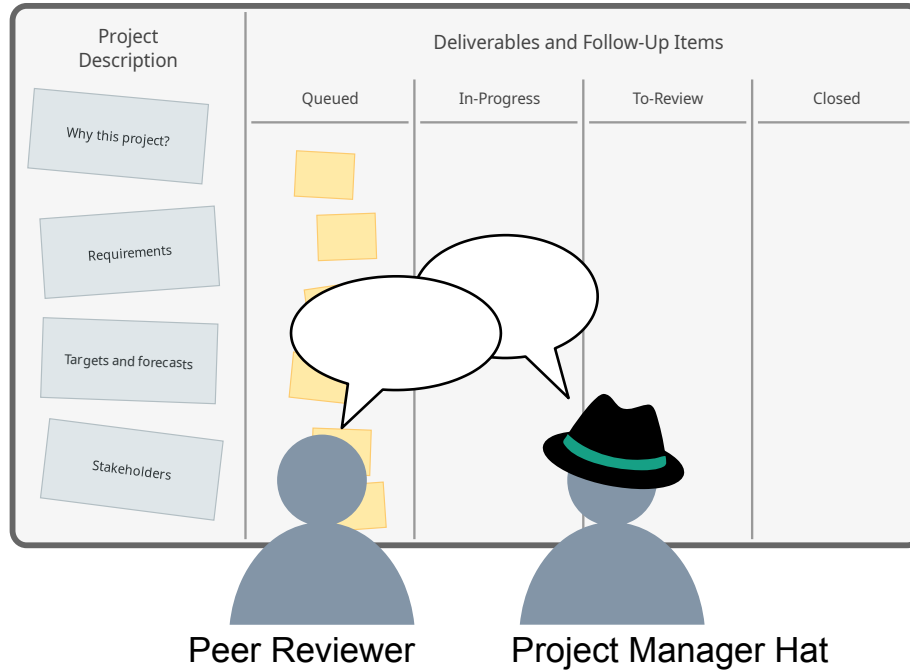


A5 - Have project initiation peer-reviewed

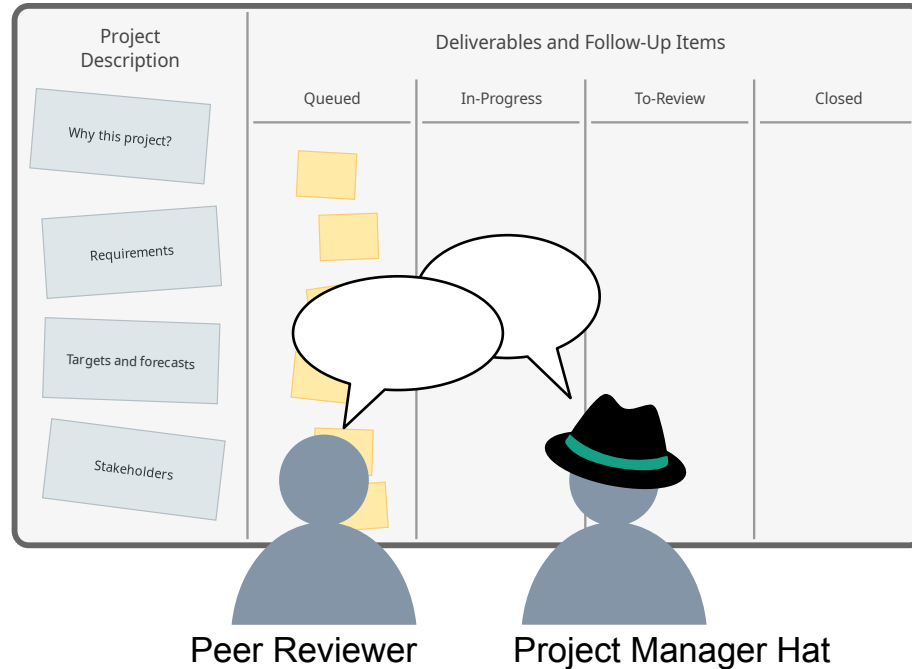

External to the project
Expert in project management
(A different person each time)


A5 - Have project initiation peer-reviewed

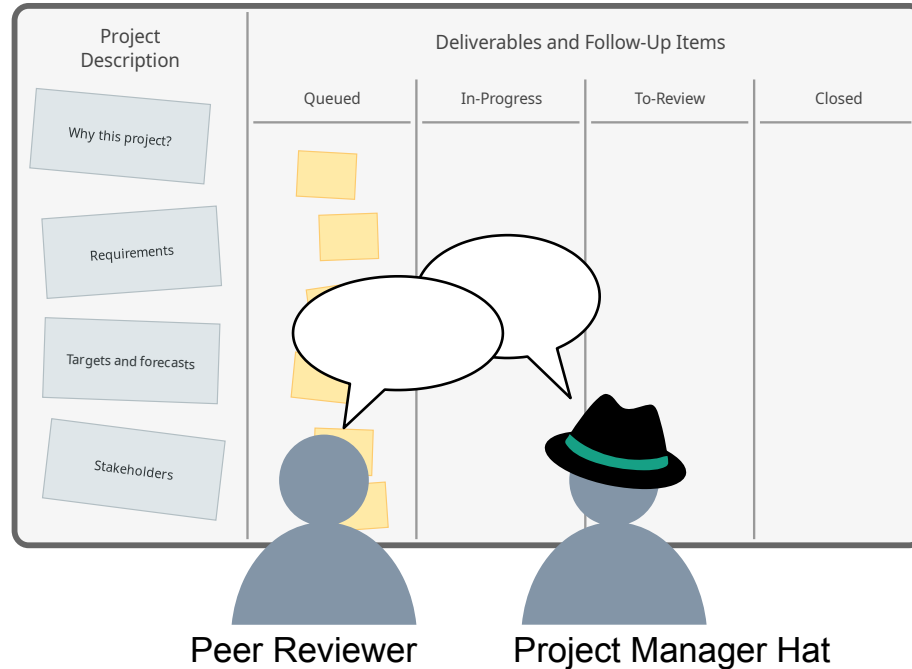

★ Helps find mistakes

★ Both learn from each other

A5 - Have project initiation peer-reviewed

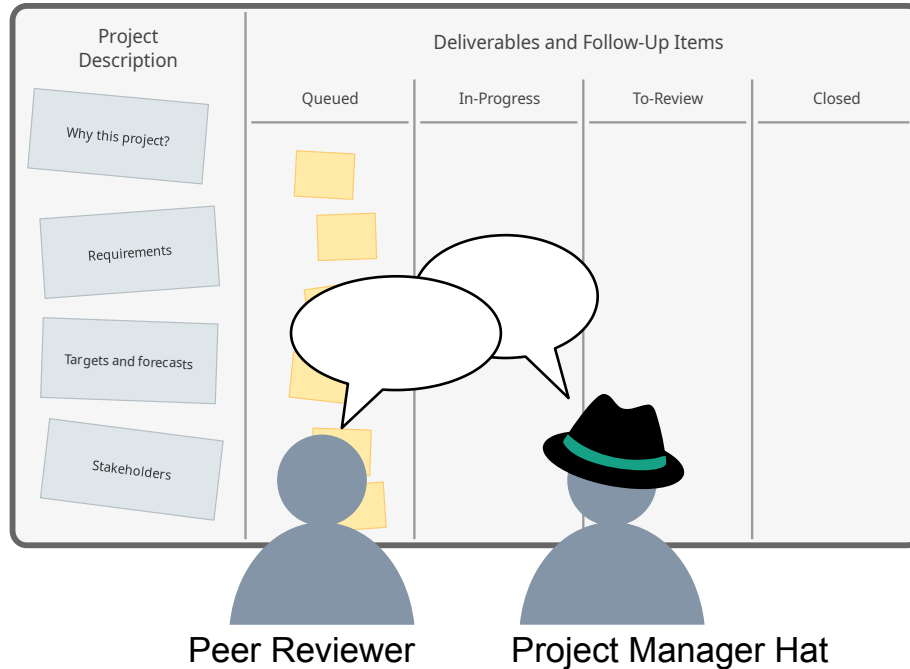


External to the project
Expert in project management
(A different person each time)

- ★ Helps find mistakes
- ★ Both learn from each other




Do other hats need peer-reviews as well?


A5 - Have project initiation peer-reviewed

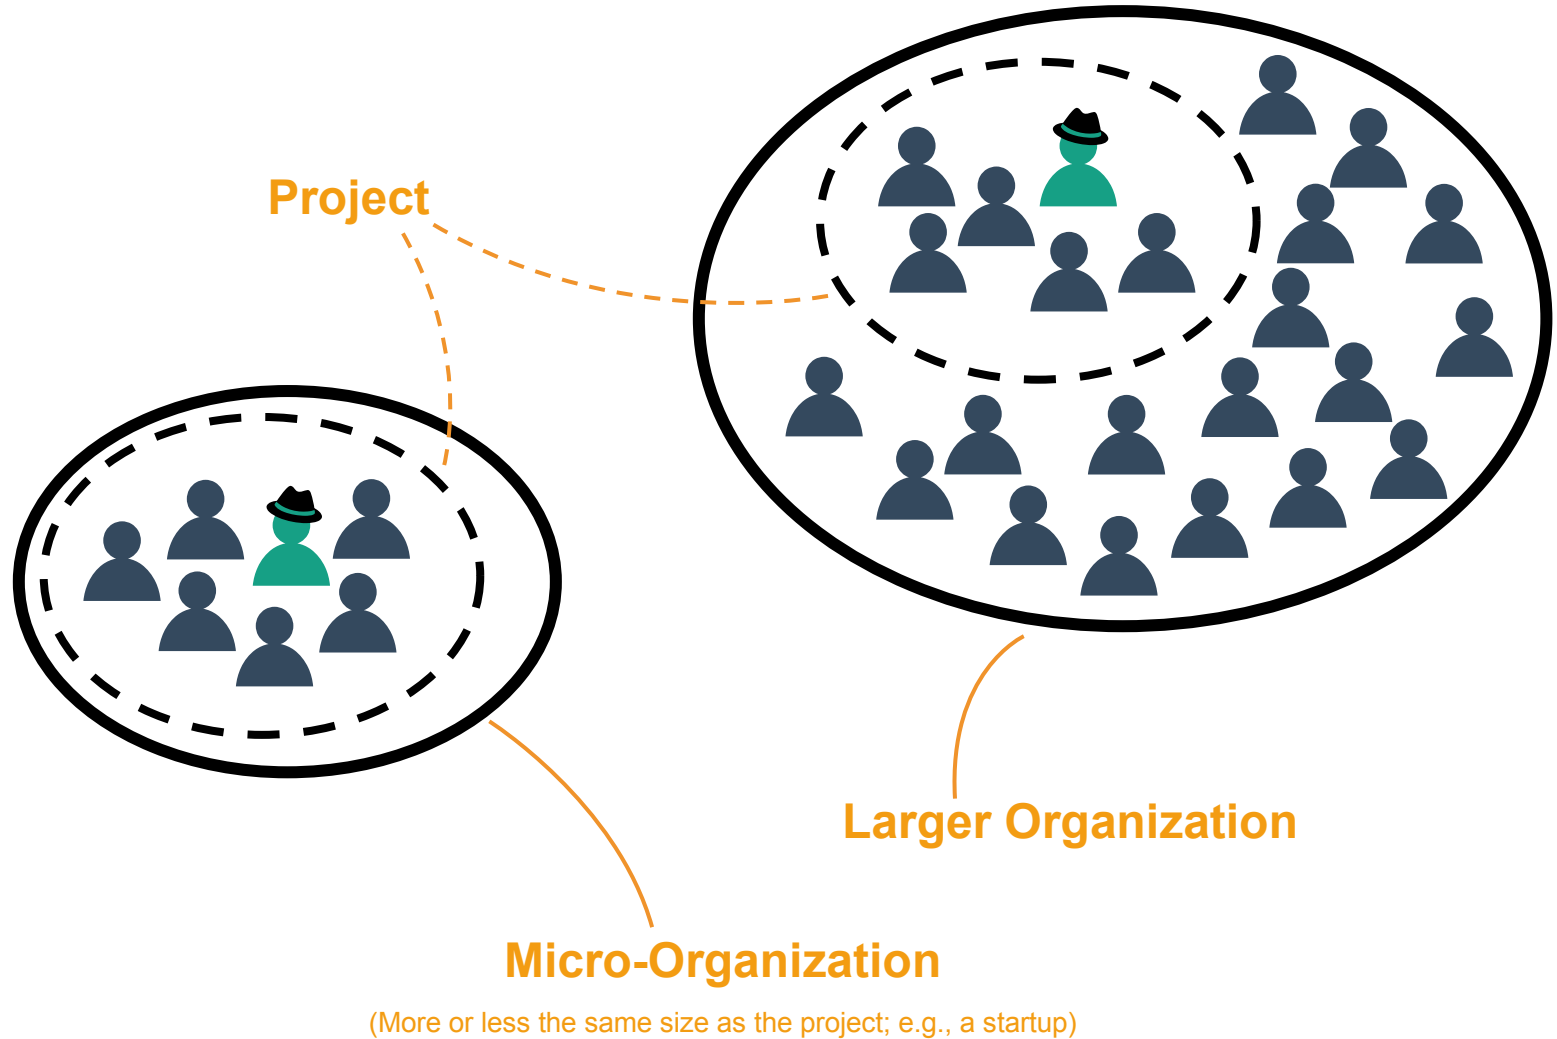


A5 - Have project initiation peer-reviewed

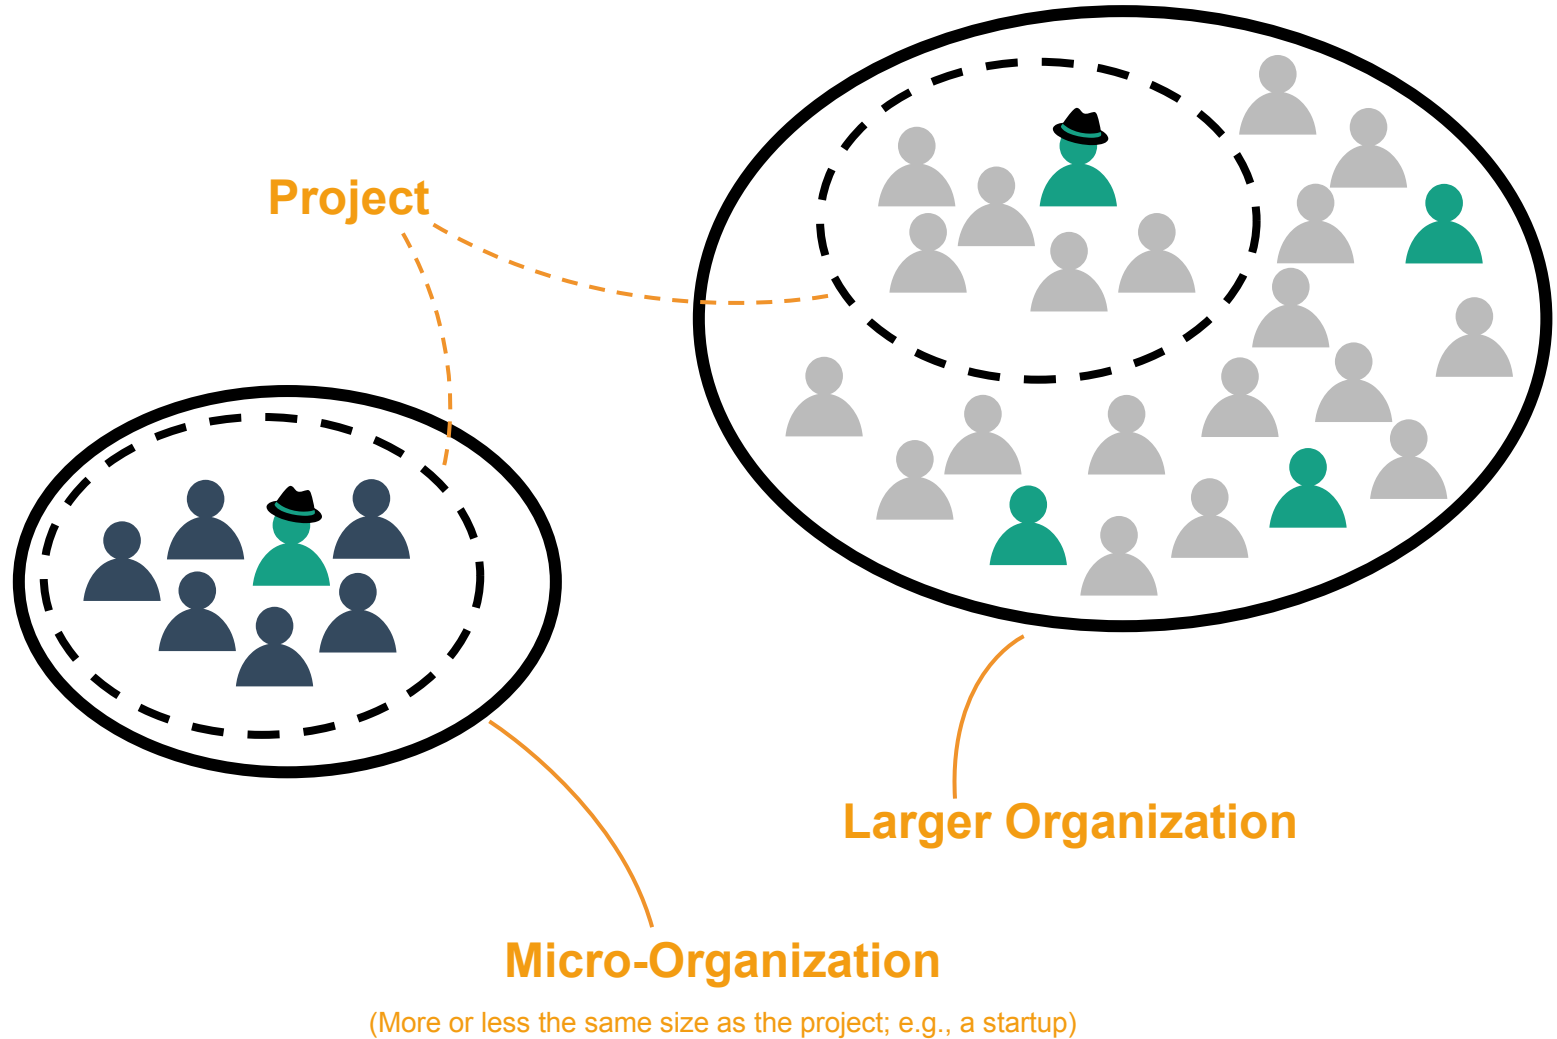


A5 - Have project initiation peer-reviewed

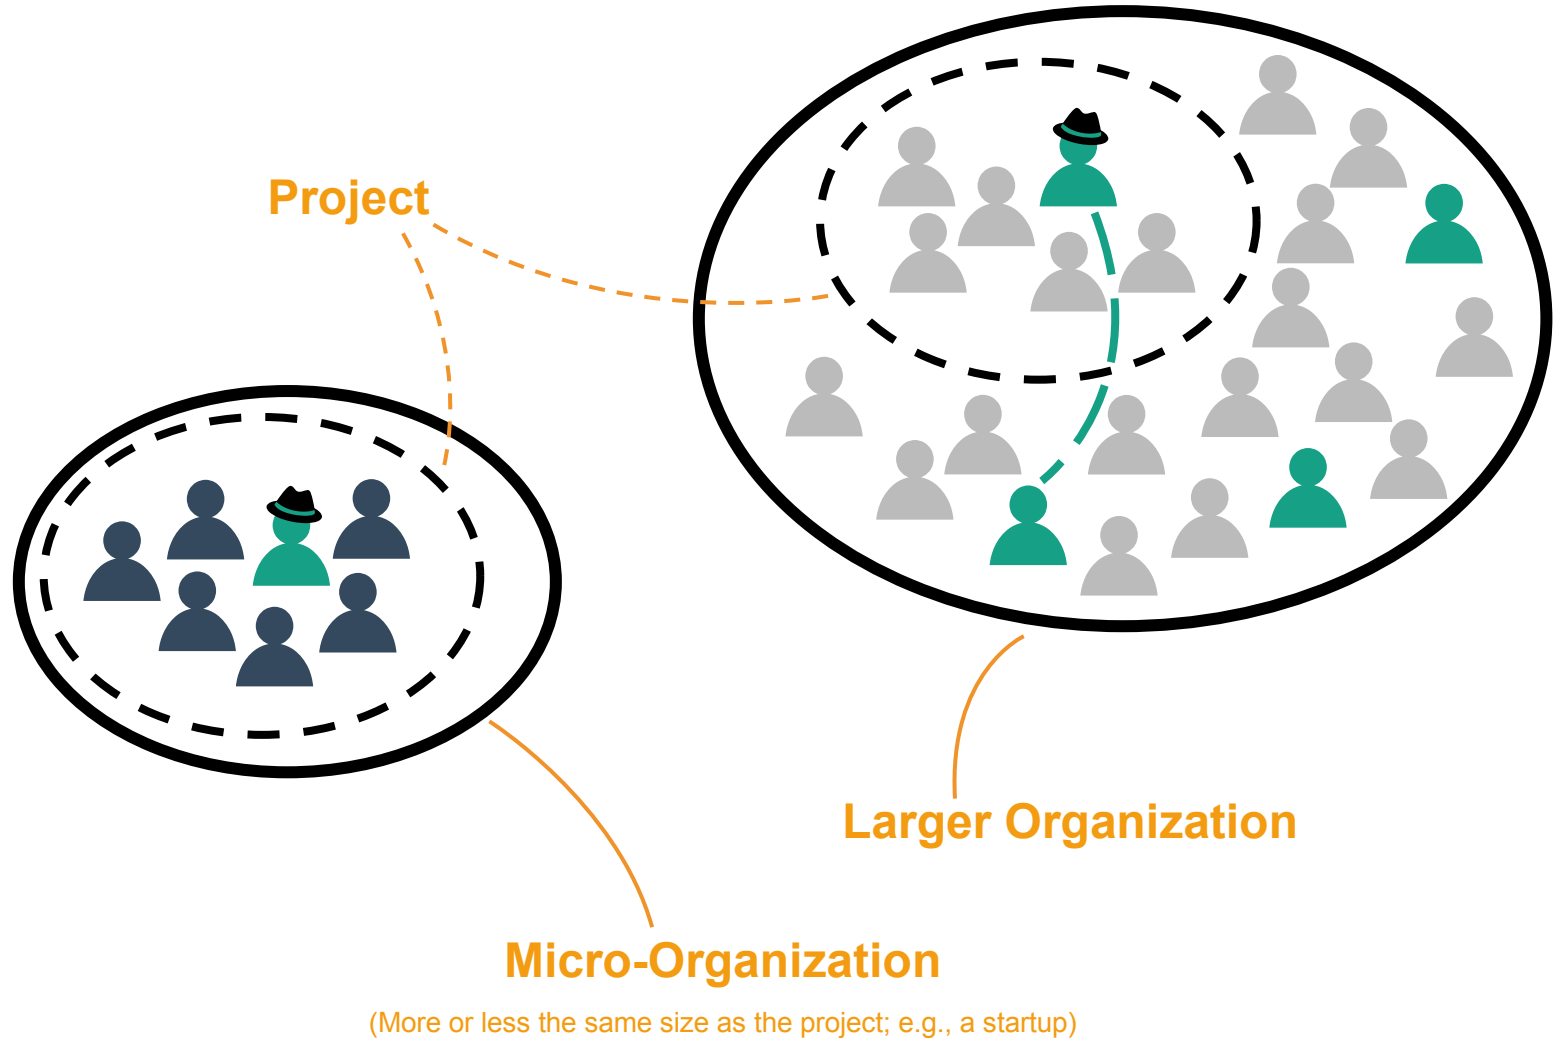


A5 - Have project initiation peer-reviewed

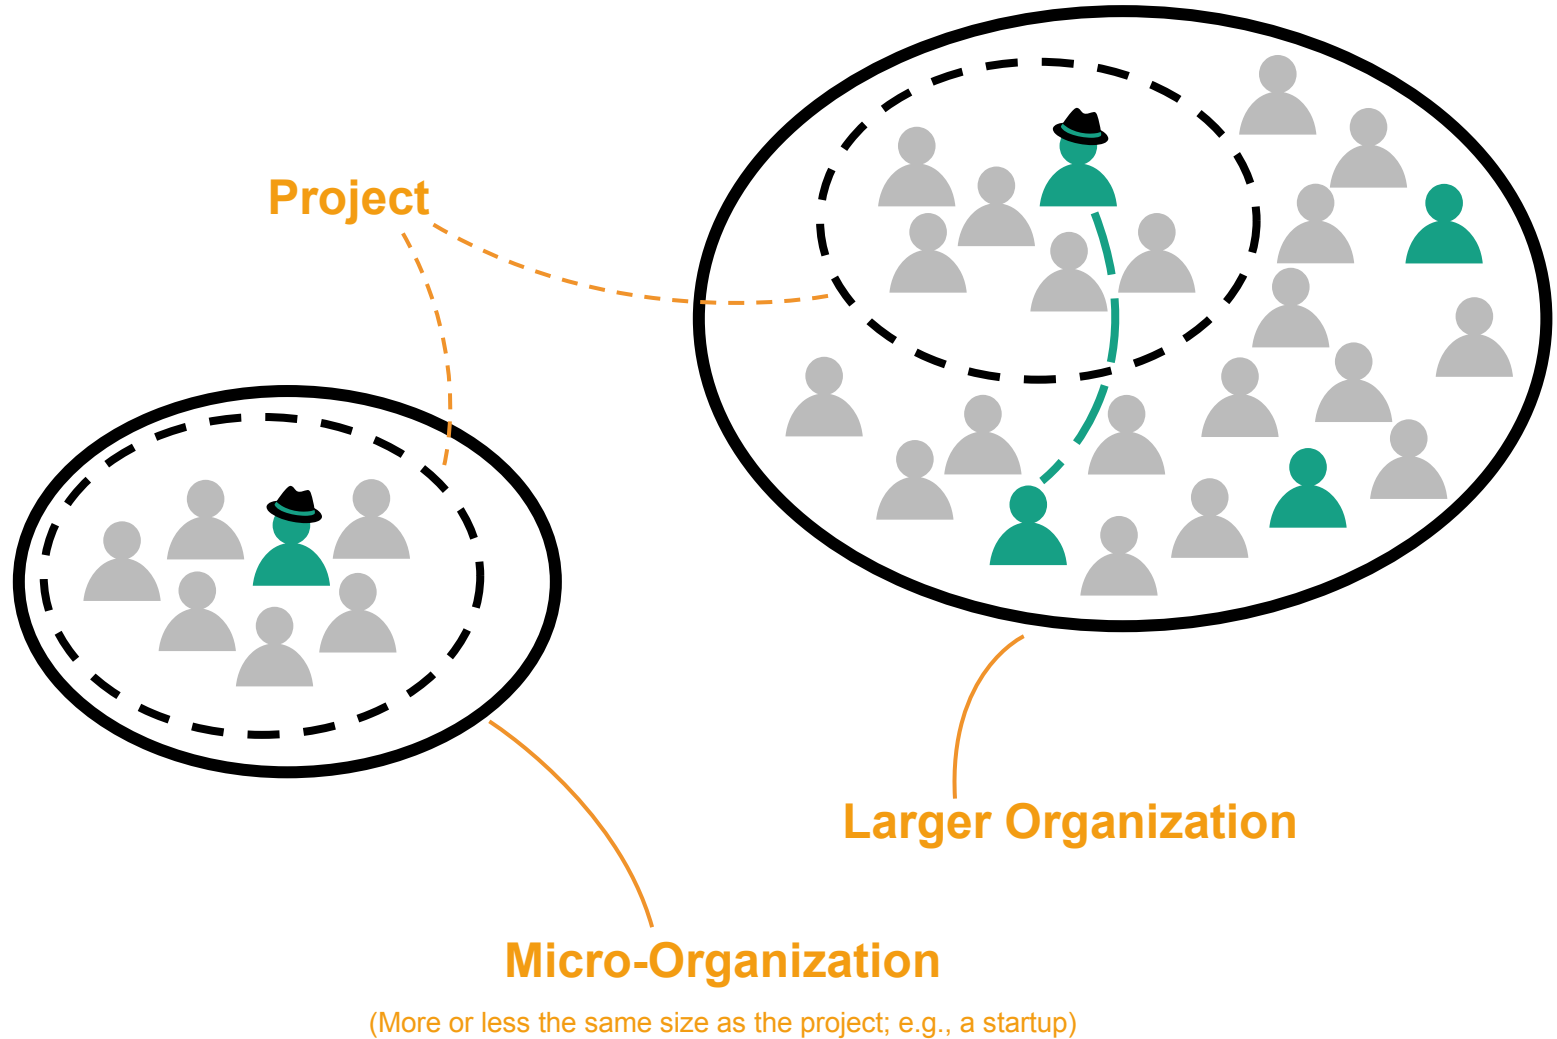


A5 - Have project initiation peer-reviewed

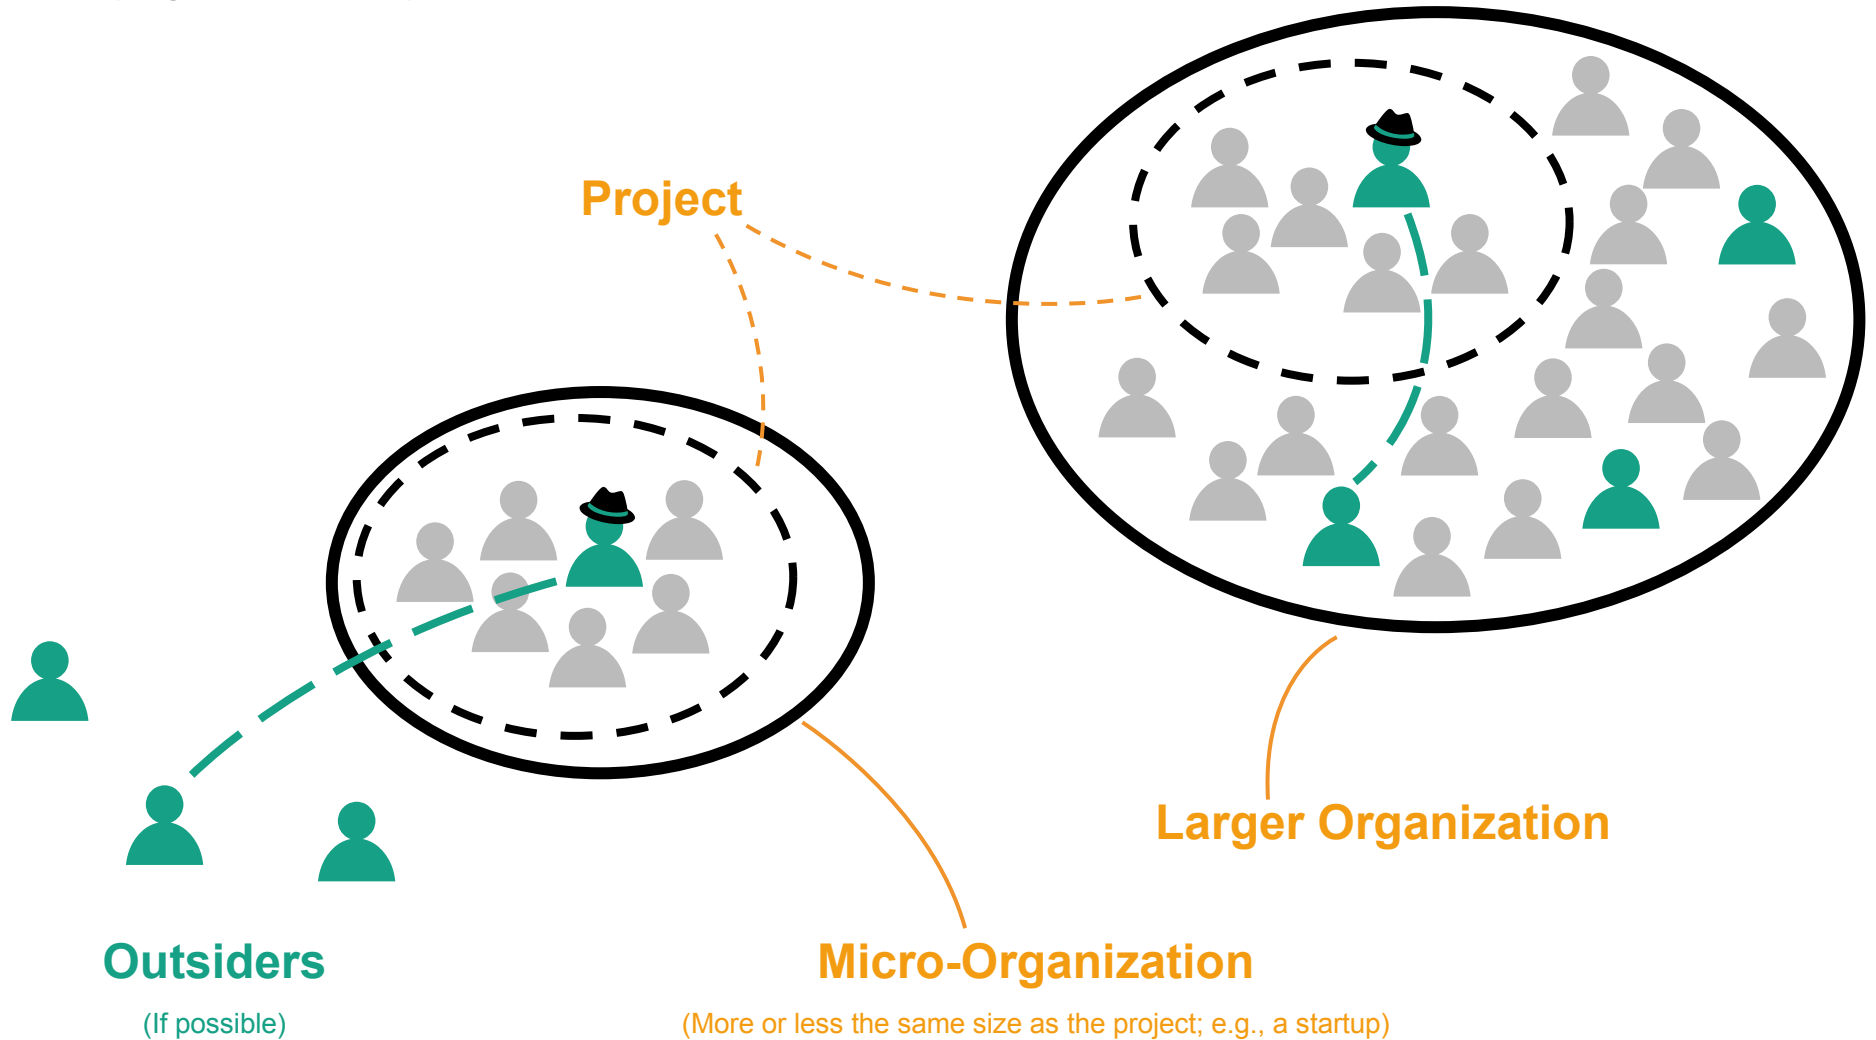

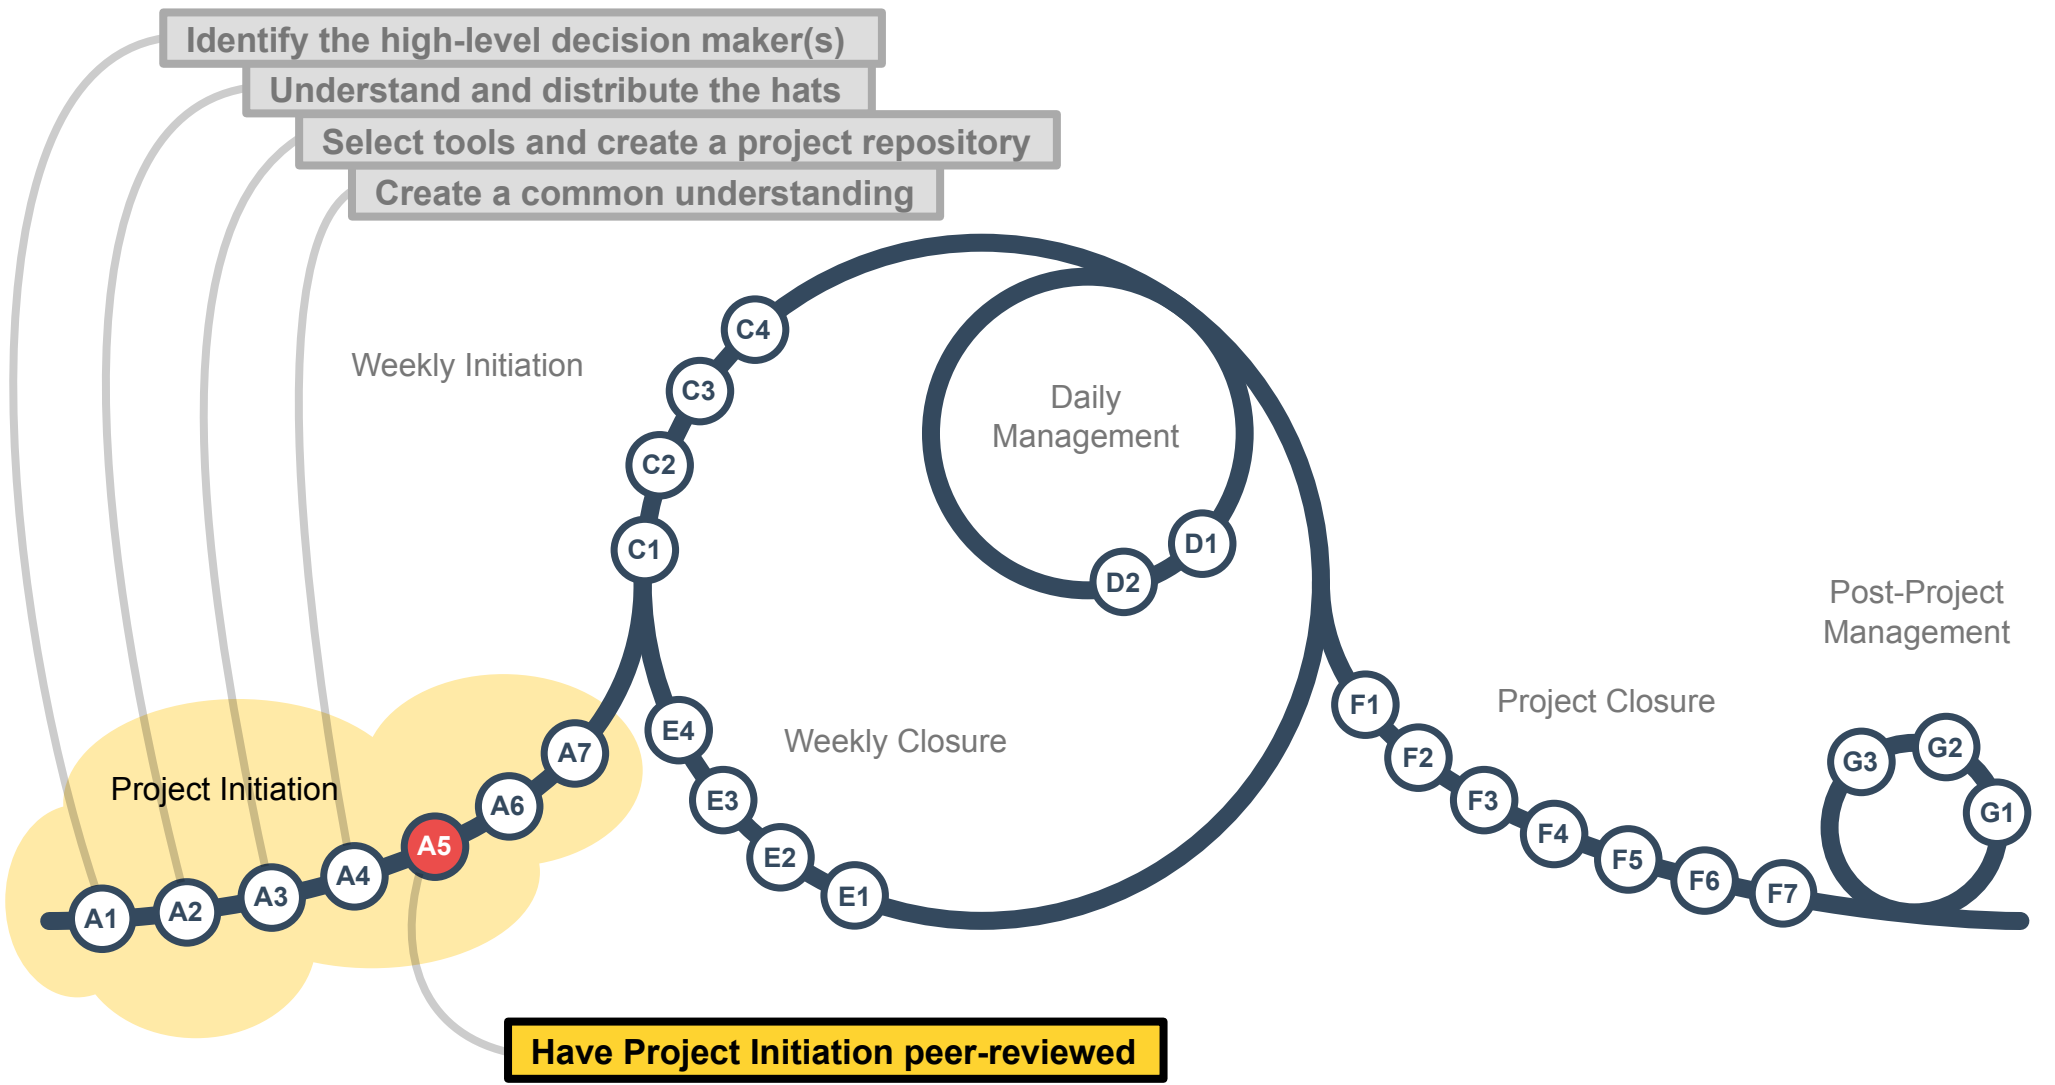

Have Project Initiation peer-reviewed

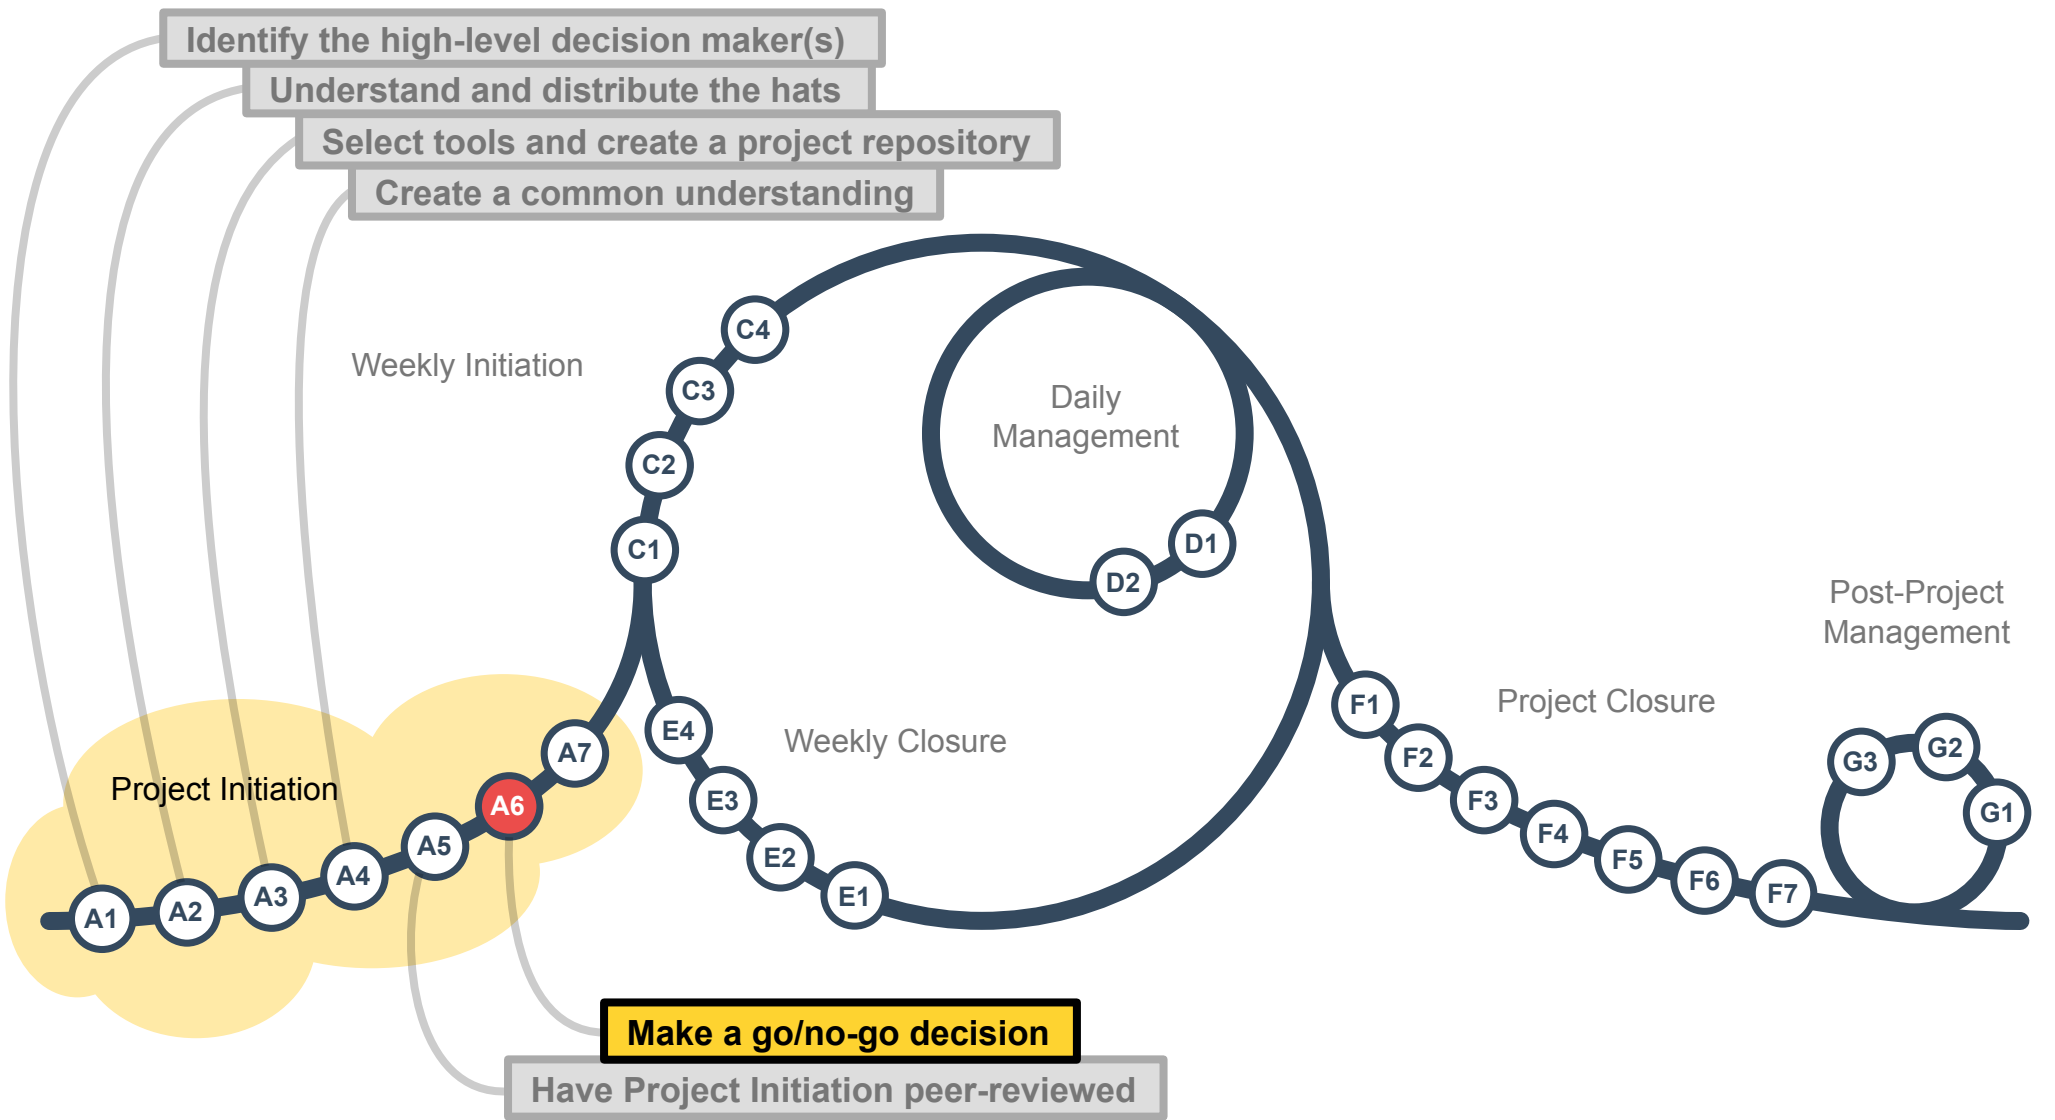

Identify the high-level decision maker(s)

Understand and distribute the hats

Select tools and create a project repository

Create a common understanding

Weekly Initiation

Daily Management

Post-Project Management

Project Closure

Project Initiation

Weekly Closure


Make a go/no-go decision

Have Project Initiation peer-reviewed

What concerns do you think each hat should have in this management activity?



A6 - Make a go/no-go decision




Project Manager Hat

A6 - Make a go/no-go decision




A6 - Make a go/no-go decision




User Hat


A6 - Make a go/no-go decision

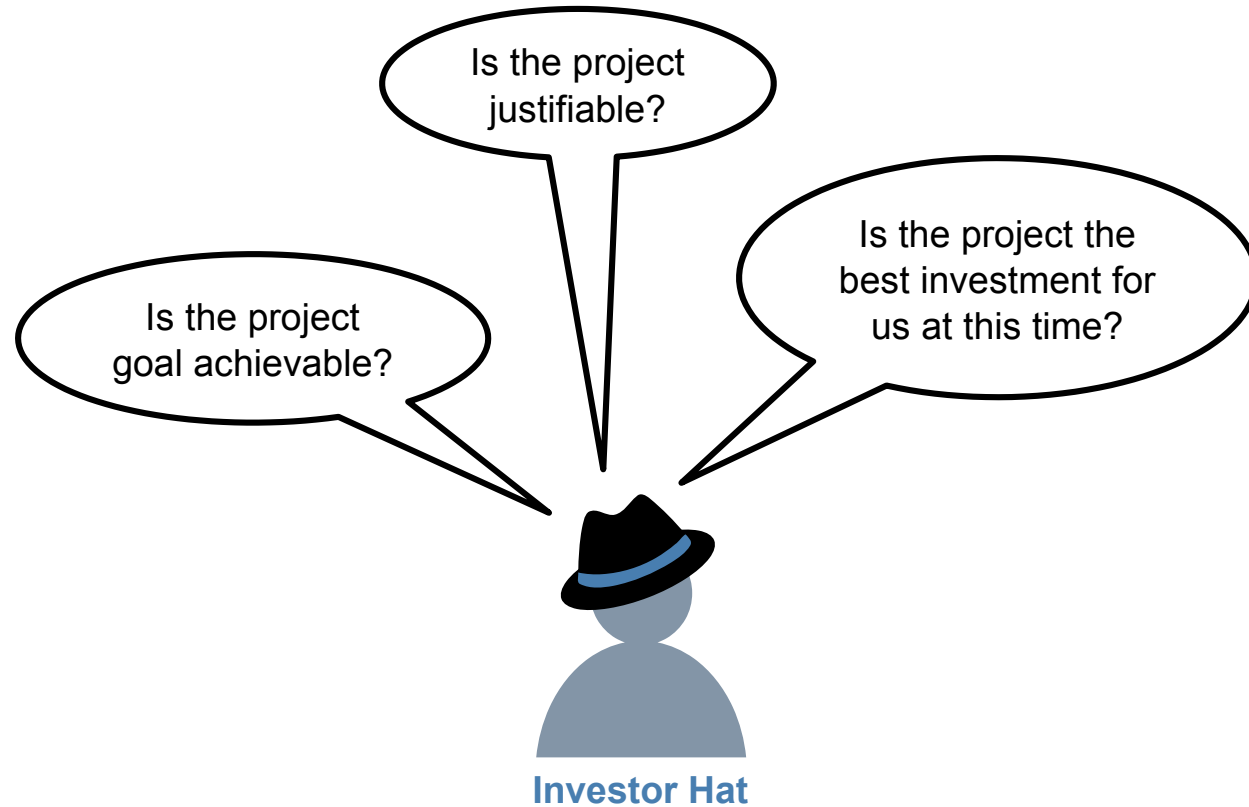

A6 - Make a go/no-go decision

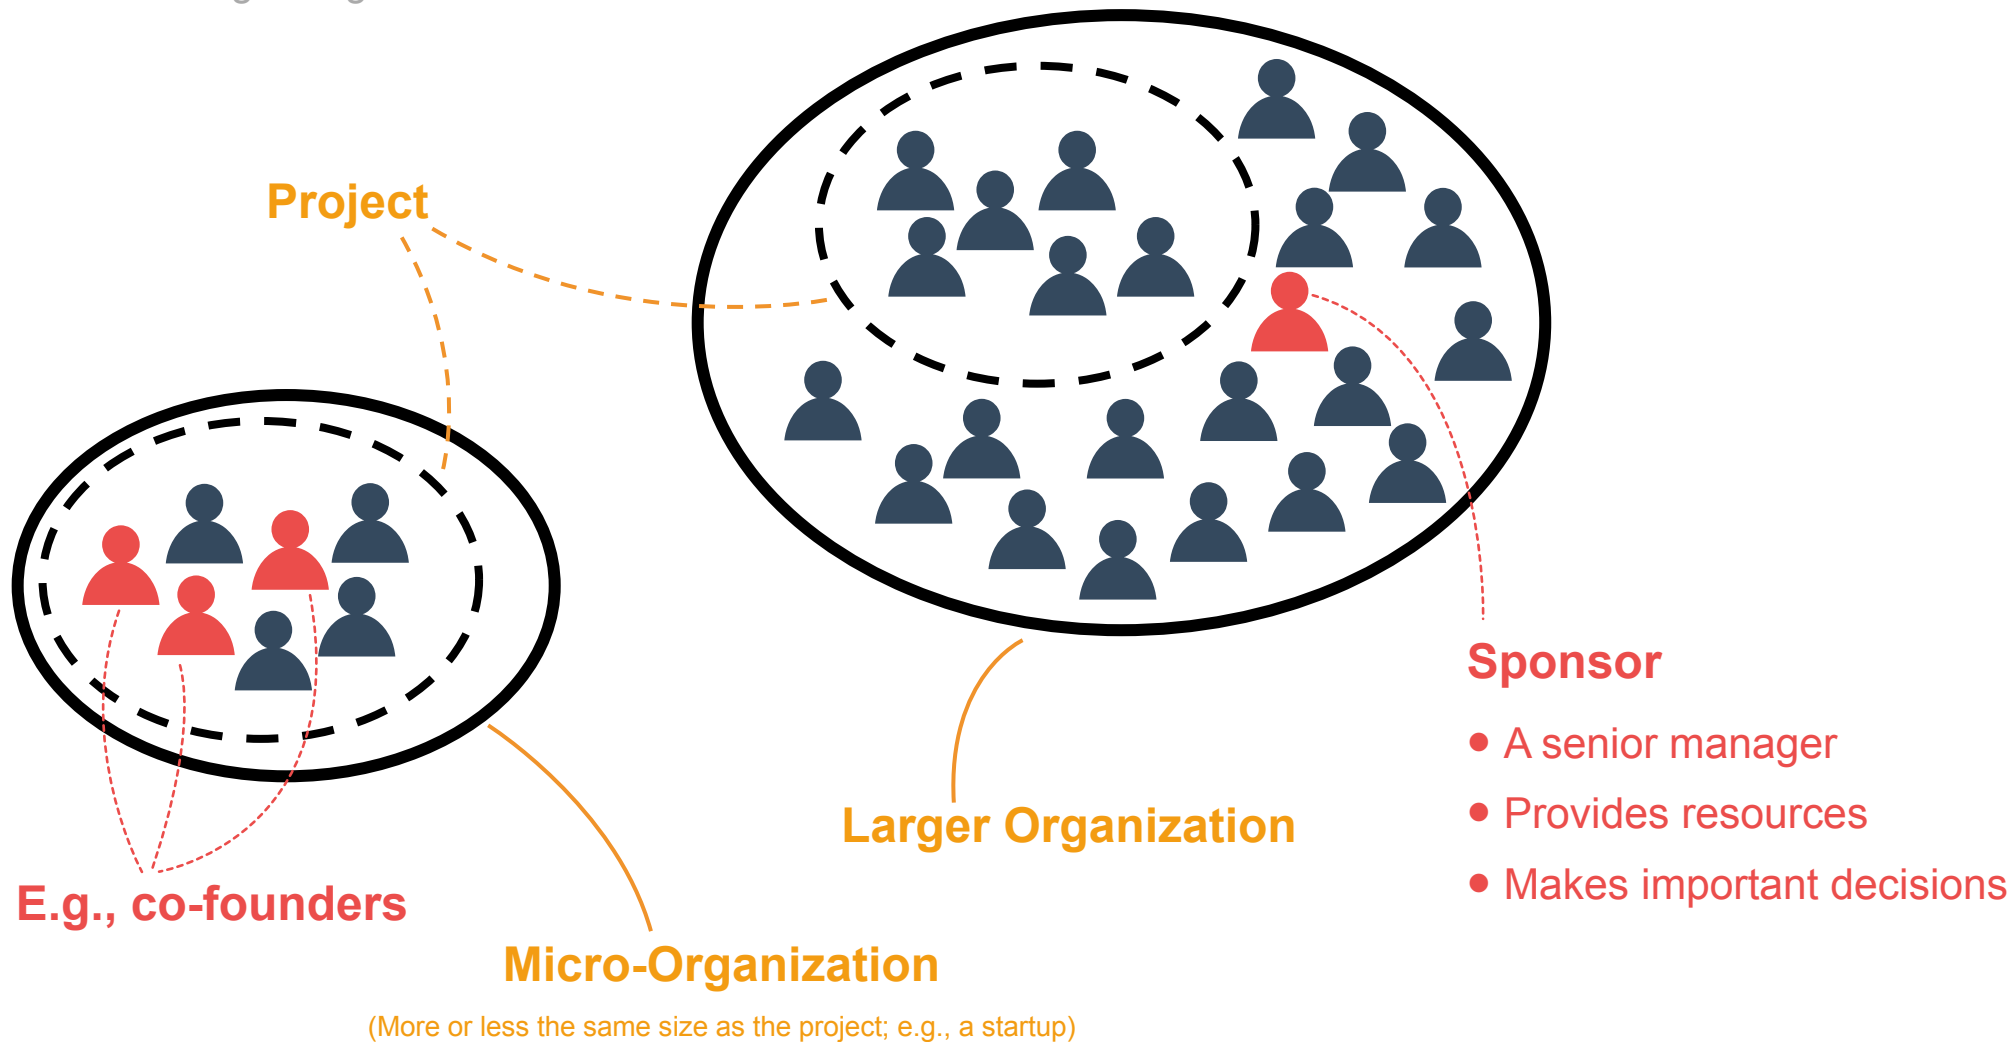



Integrated Project Board

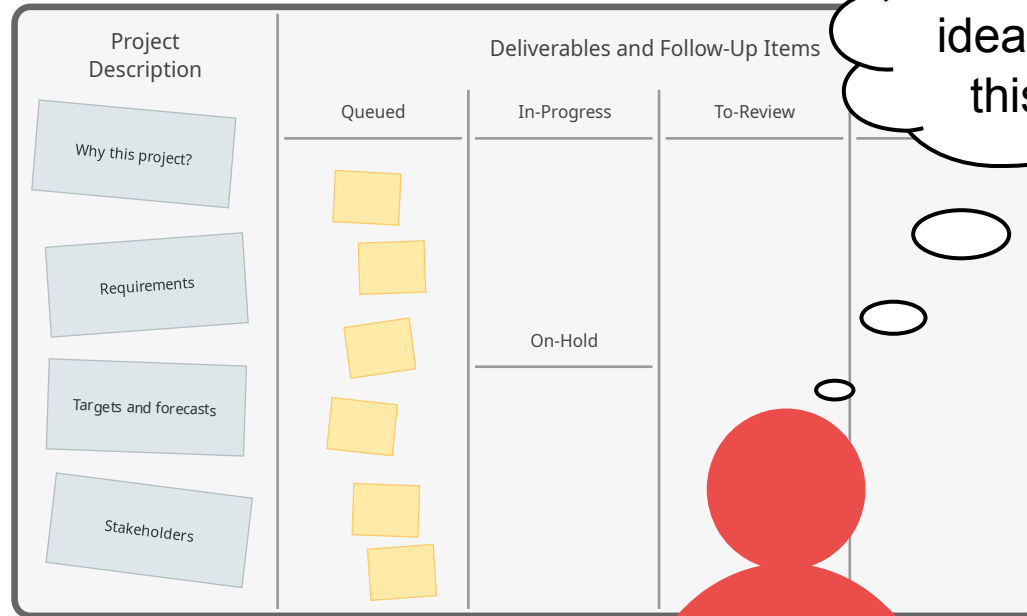

The high-level decision maker(s)
(e.g., the Sponsor)

A6 - Make a go/no-go decision

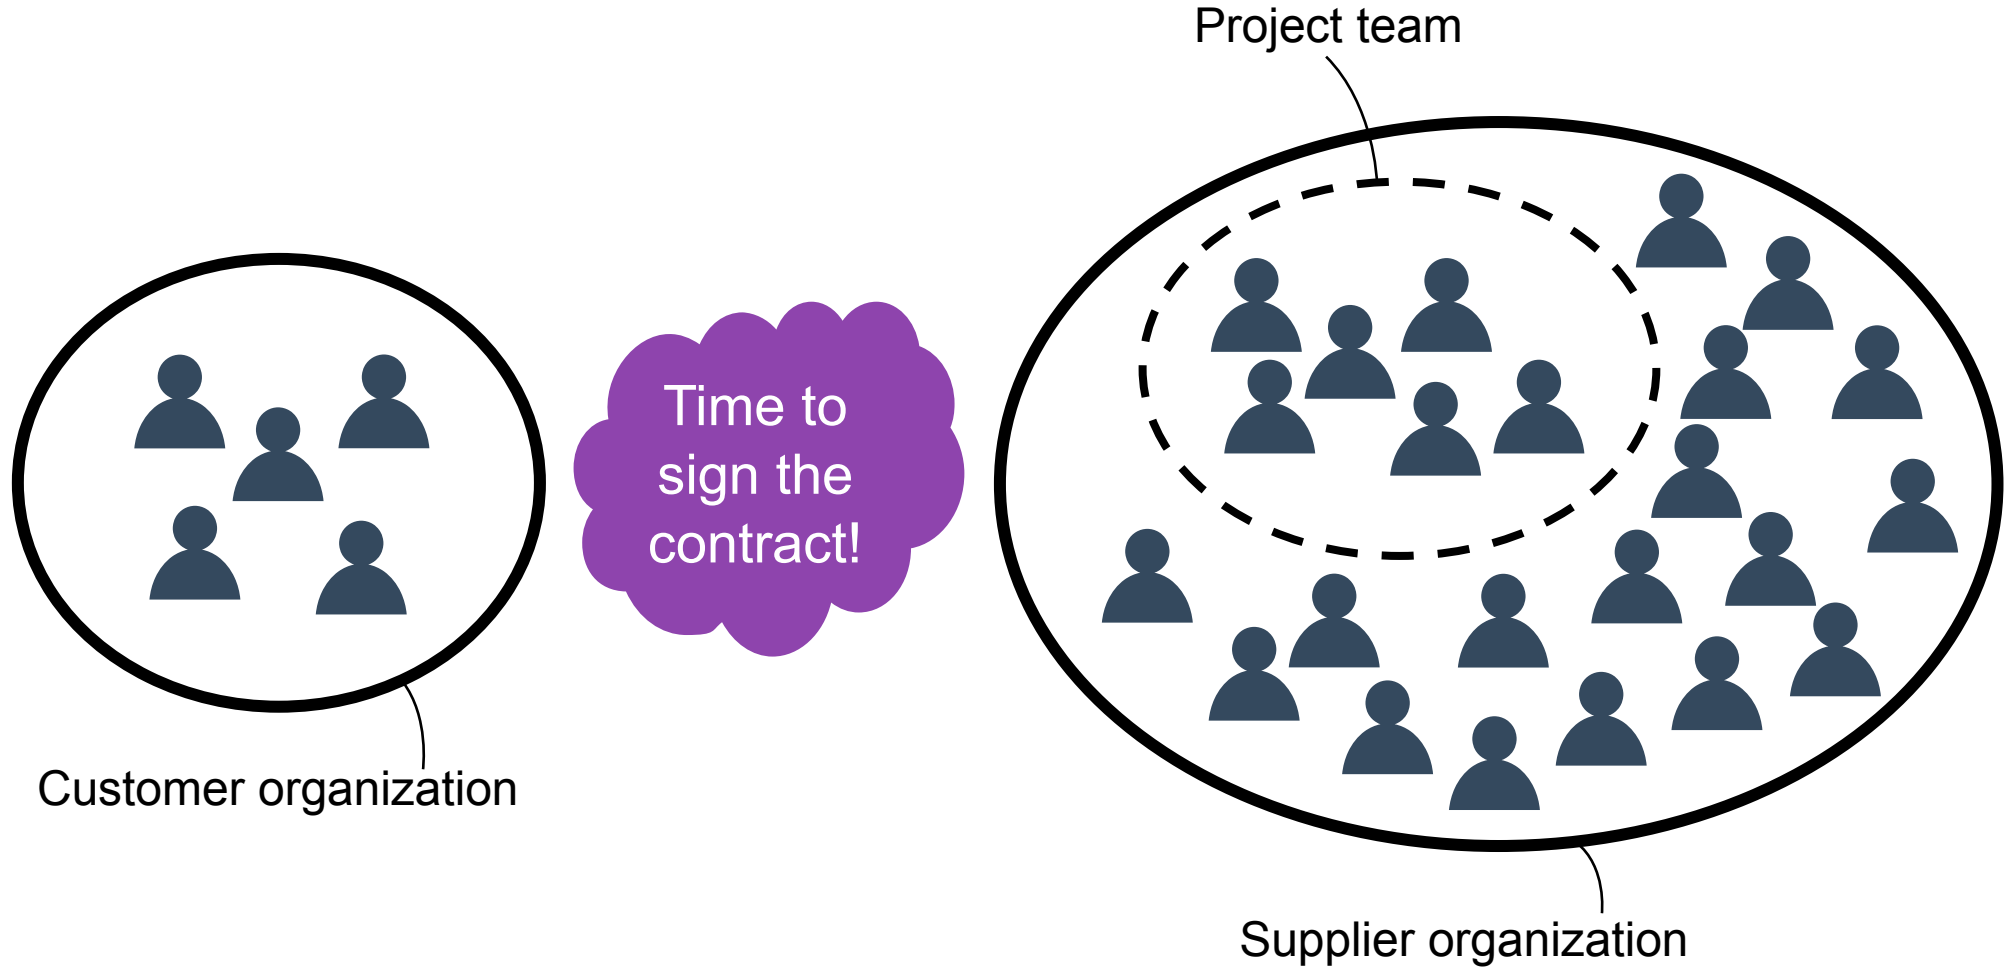

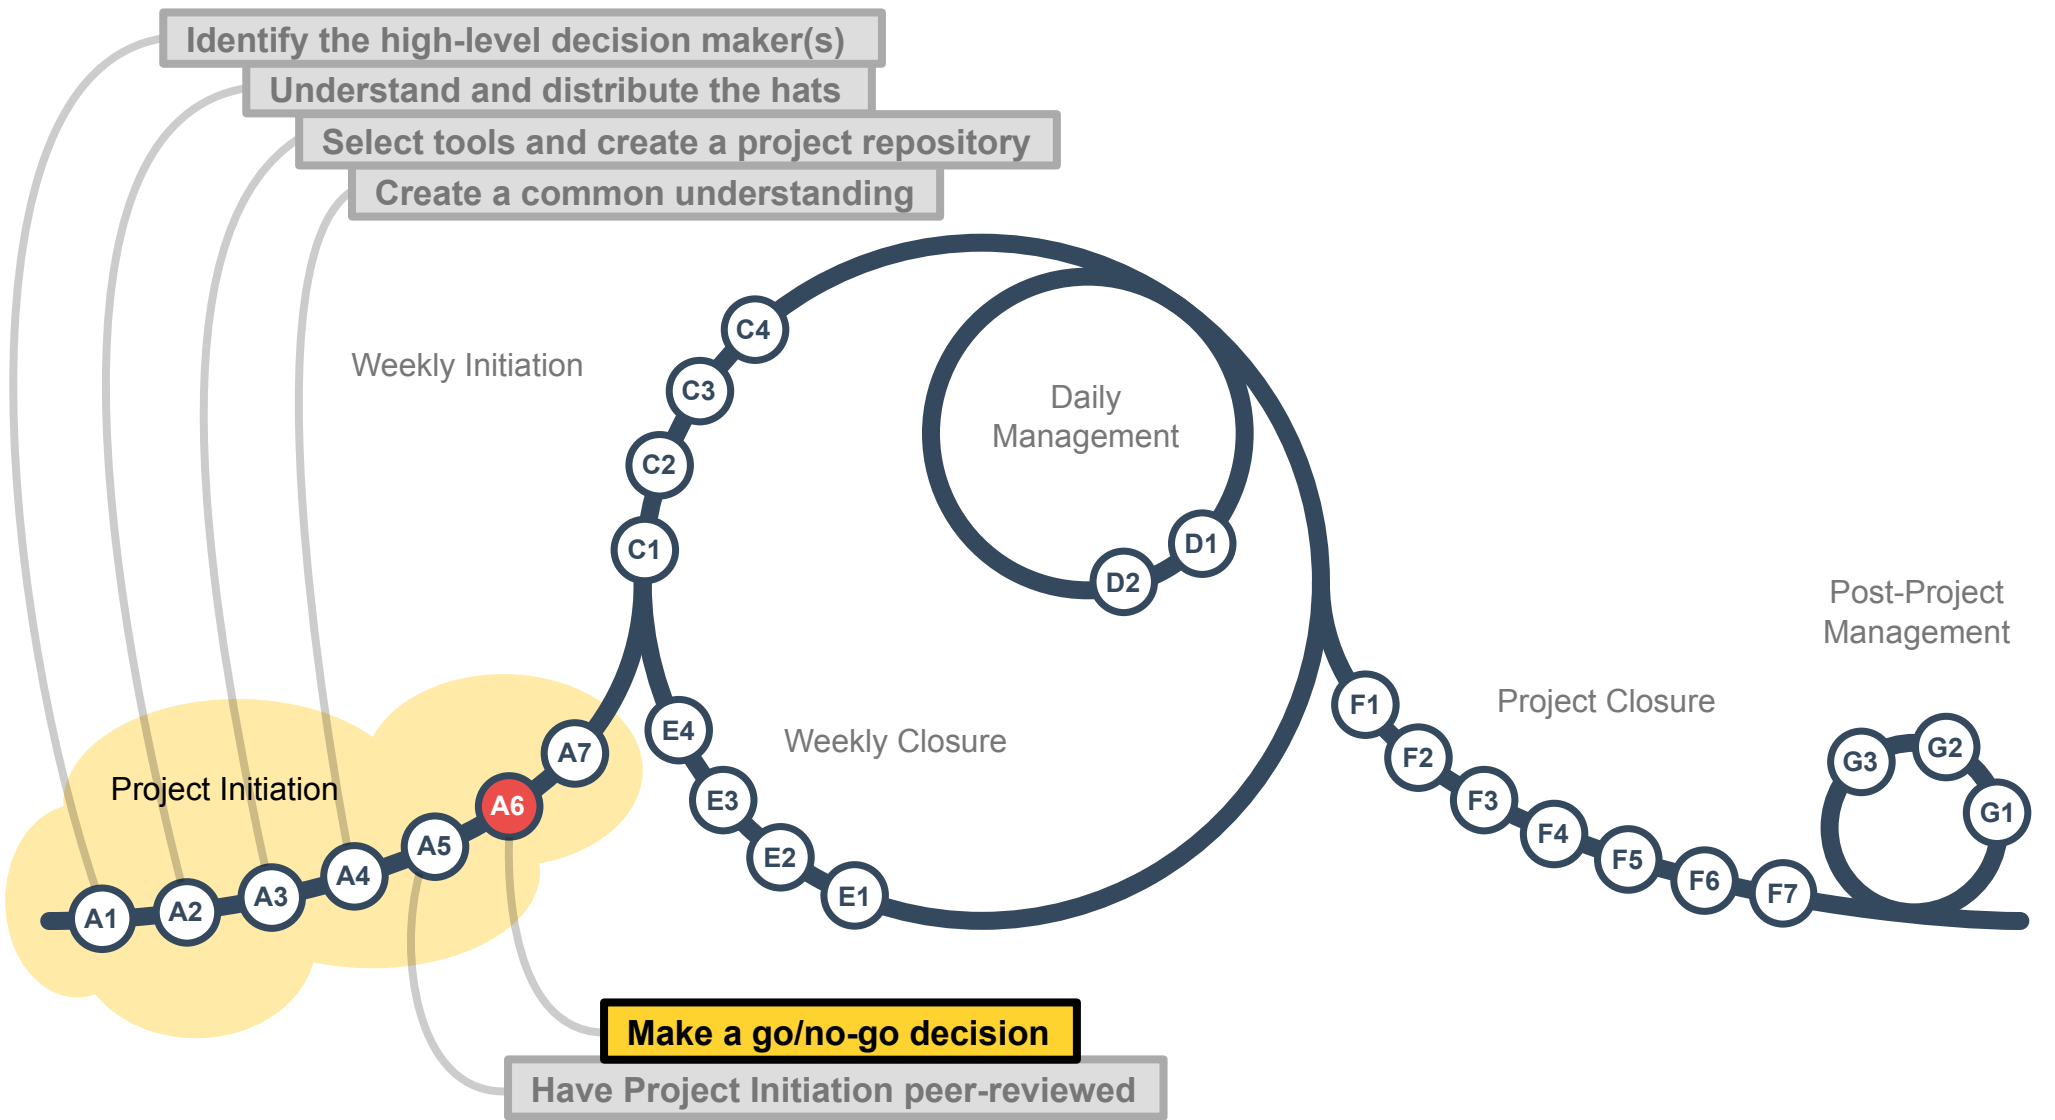

Identify the high-level decision maker(s)

Understand and distribute the hats

Select tools and create a project repository

Create a common understanding

Weekly Initiation

Daily Management

Post-Project Management


Project Closure

Project Initiation

Weekly Closure

Make a go/no-go decision


Have Project Initiation peer-reviewed

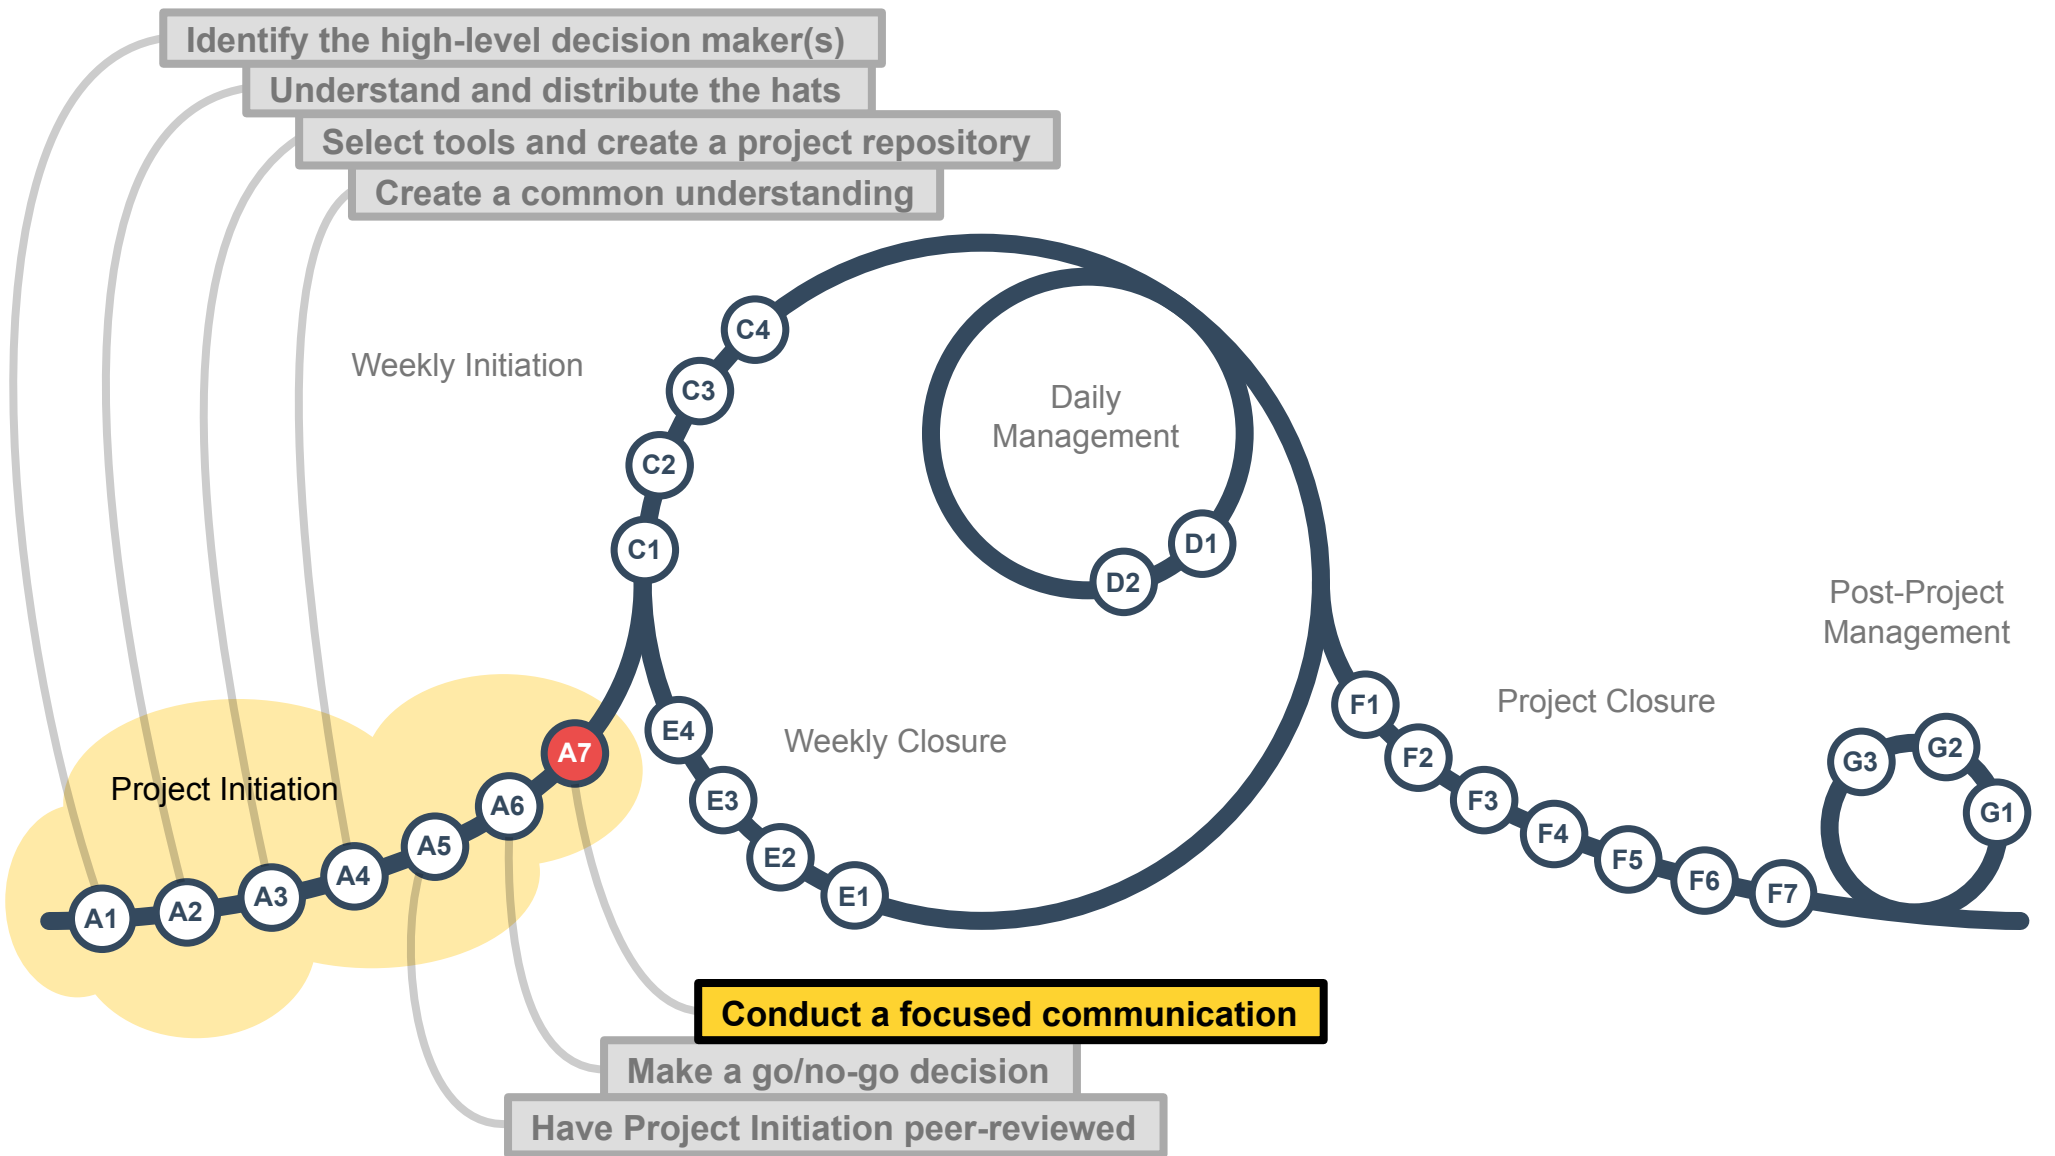


What are the advantages of informing everyone in the organization that we're going to start working on a new project?




A7 - Conduct a focused communication

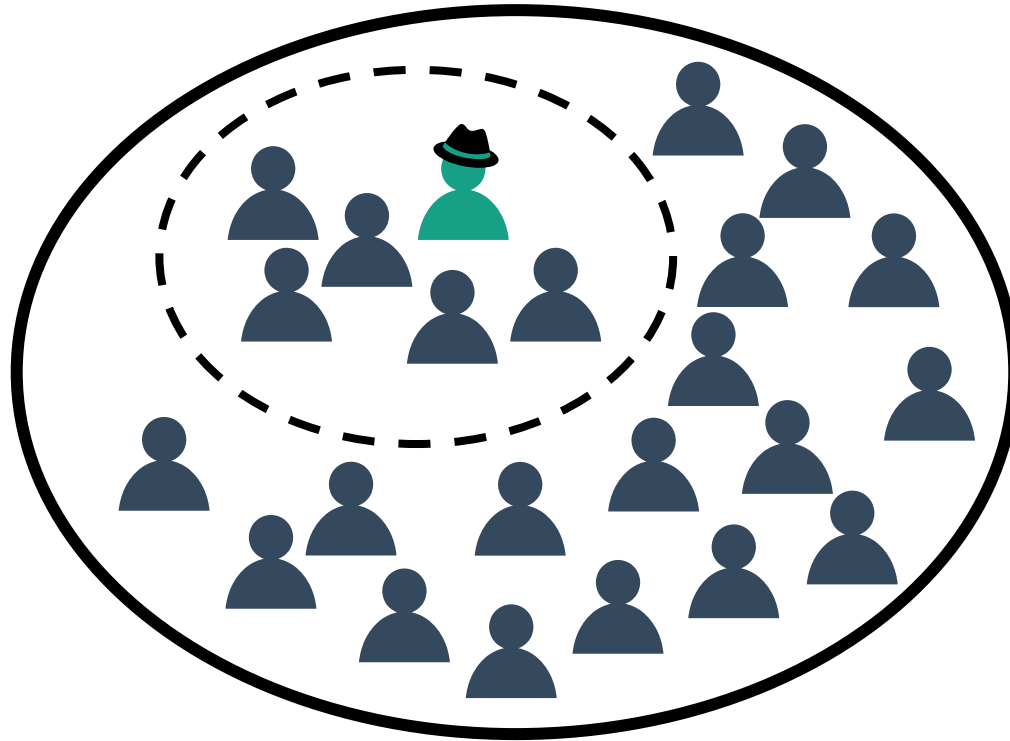


A7 - Conduct a focused communication

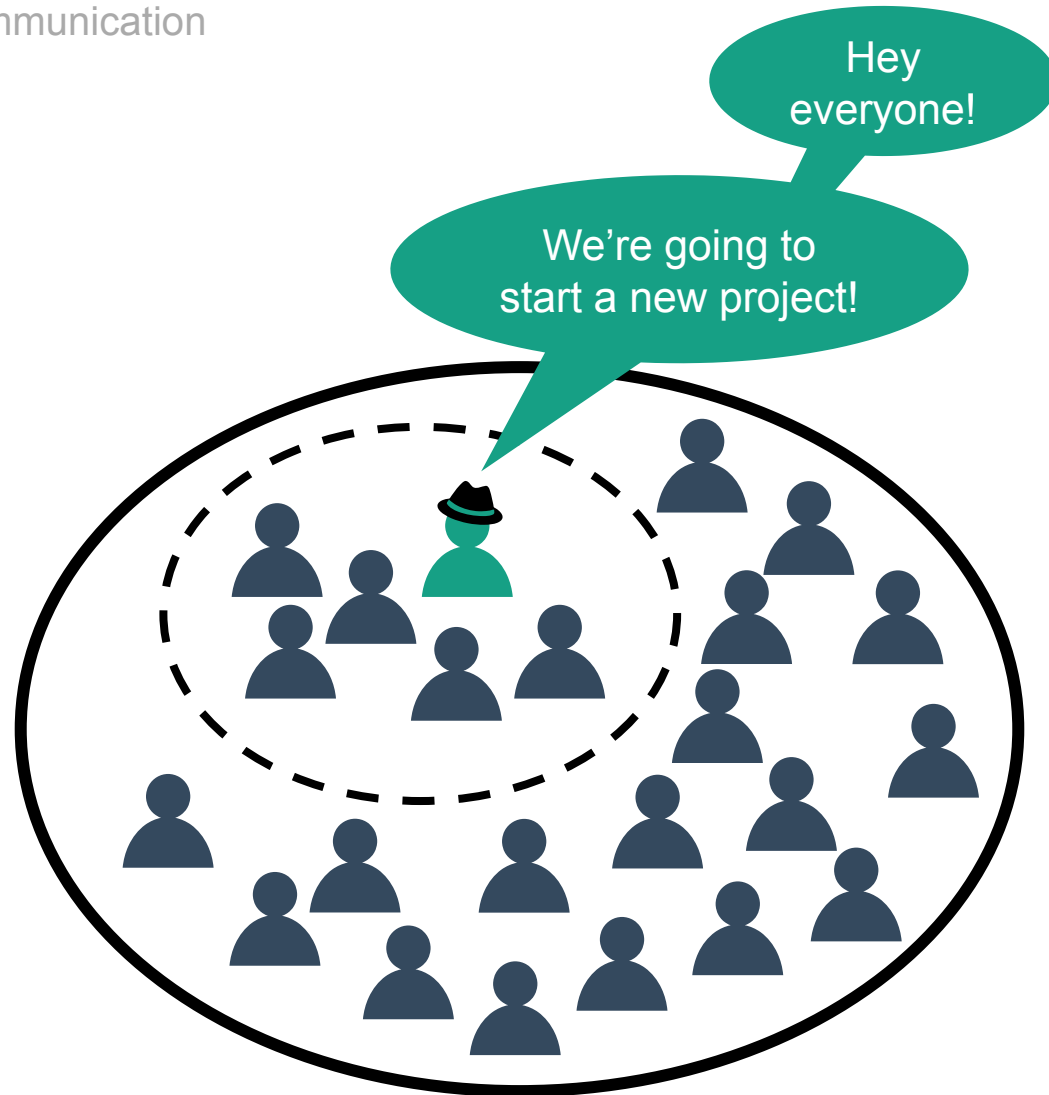



A7 - Conduct a focused communication




A7 - Conduct a focused communication

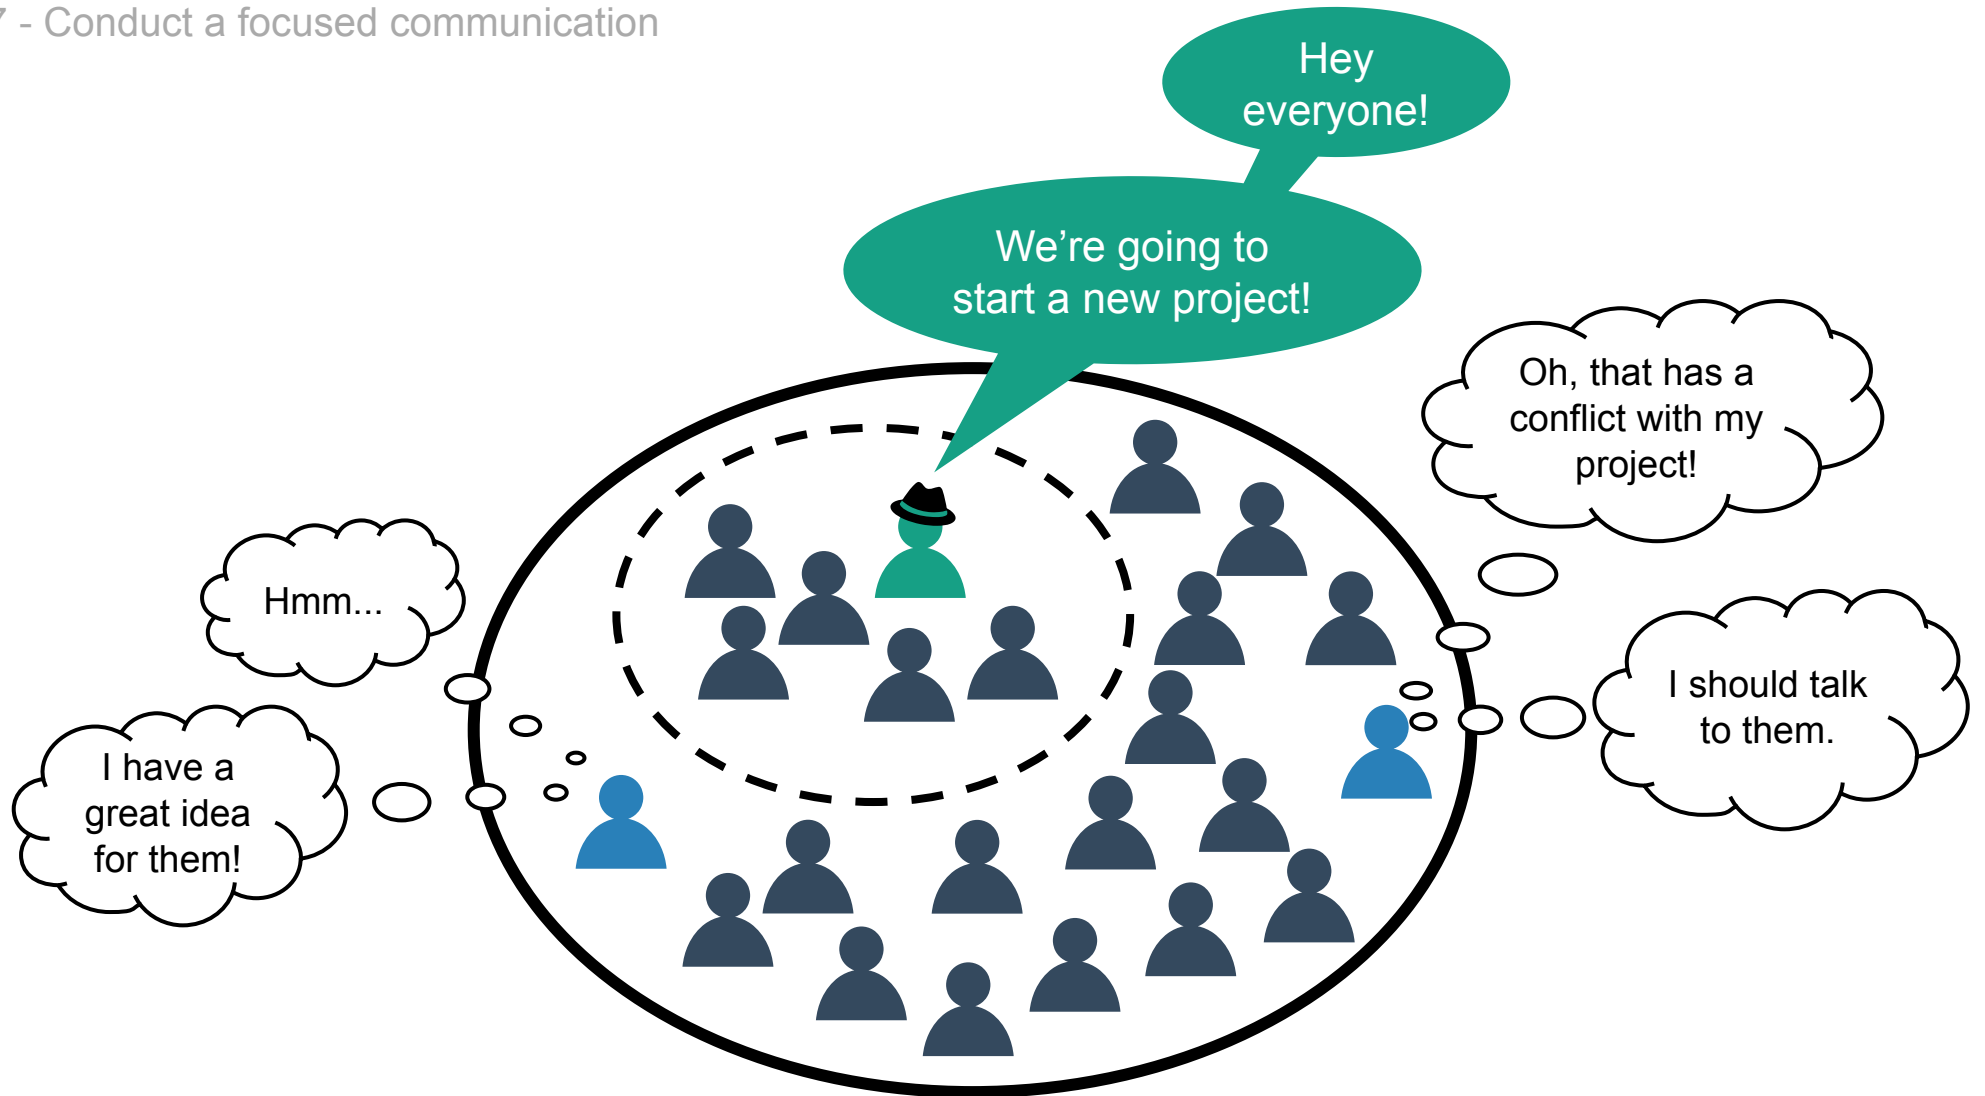

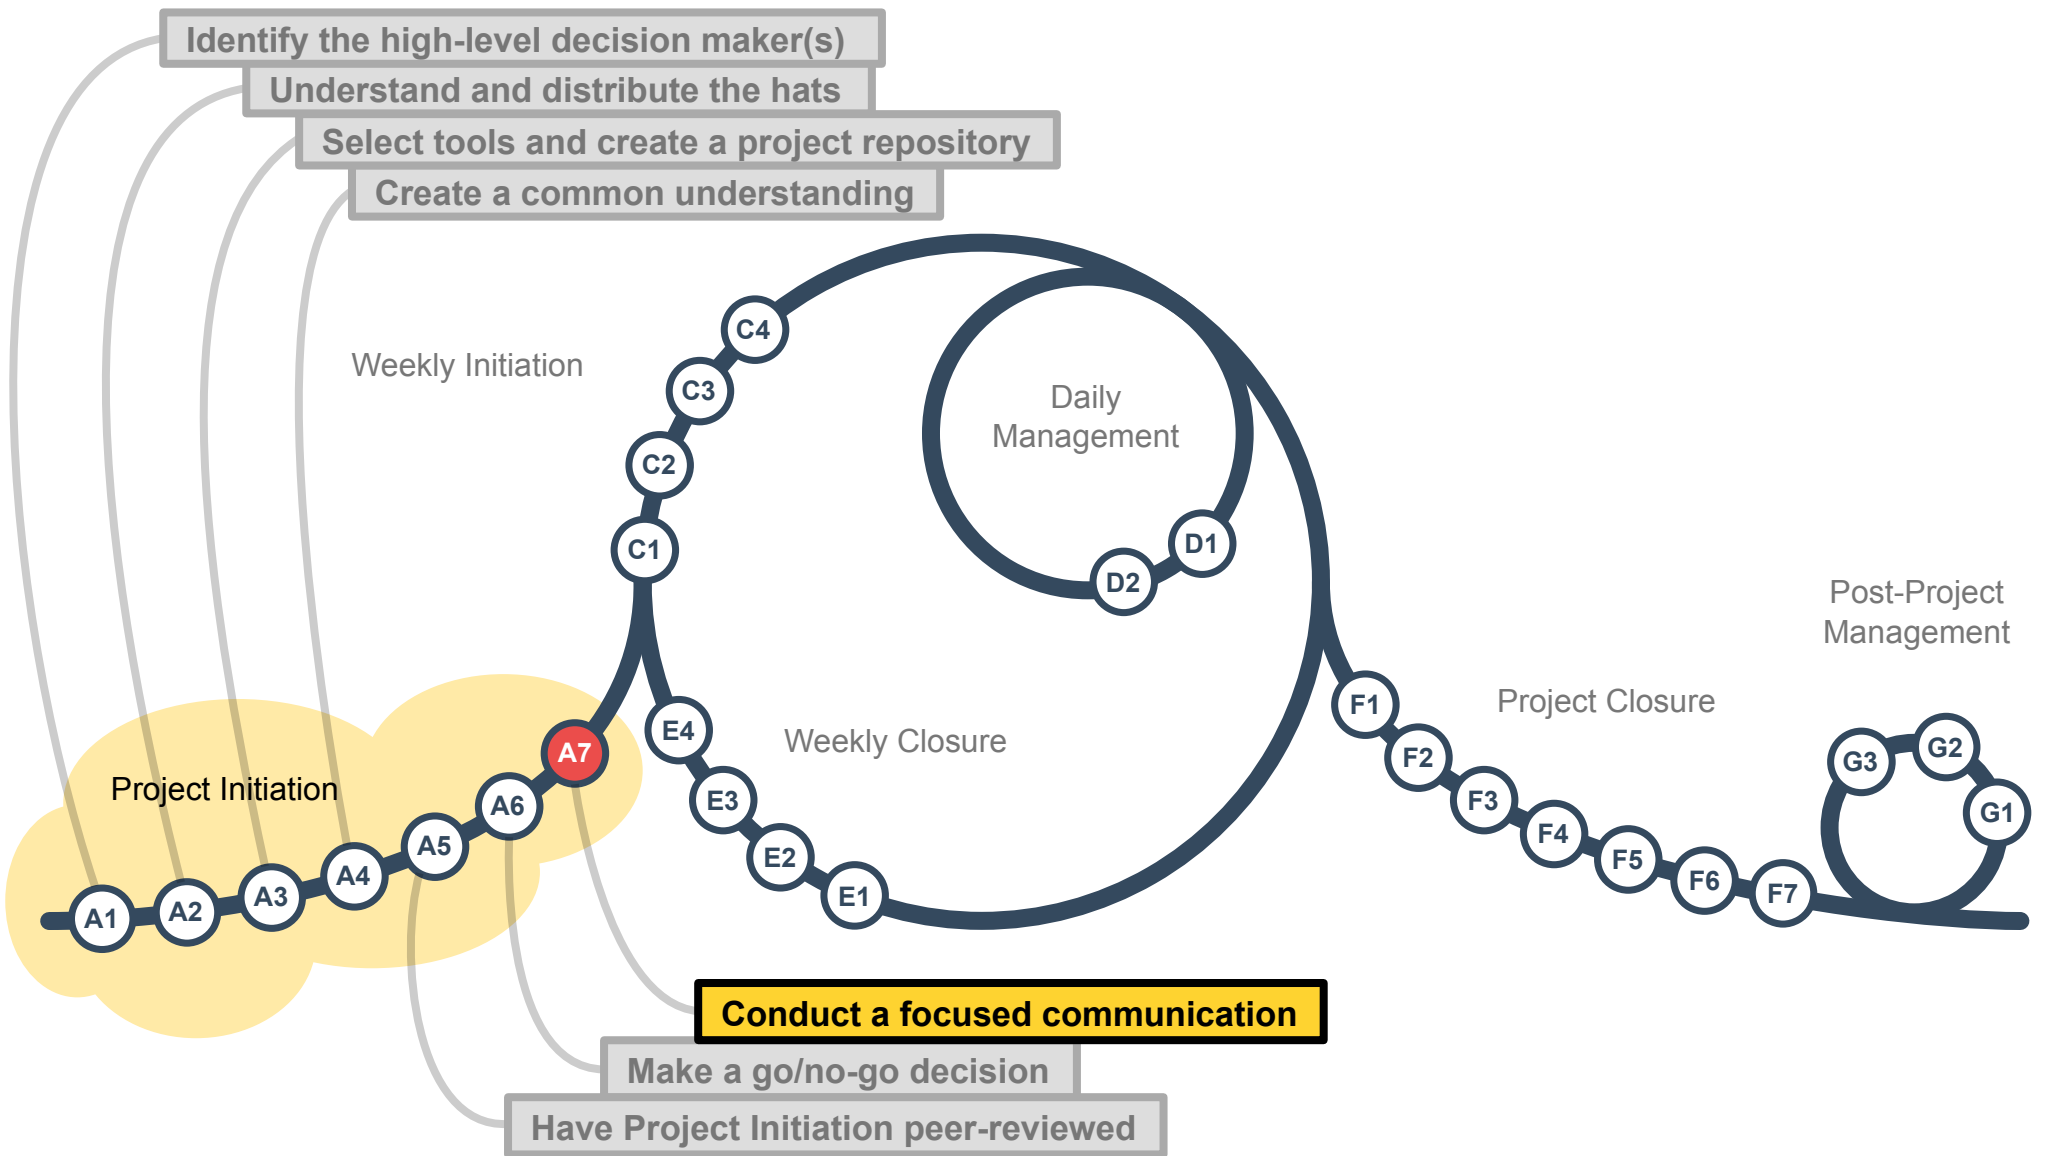

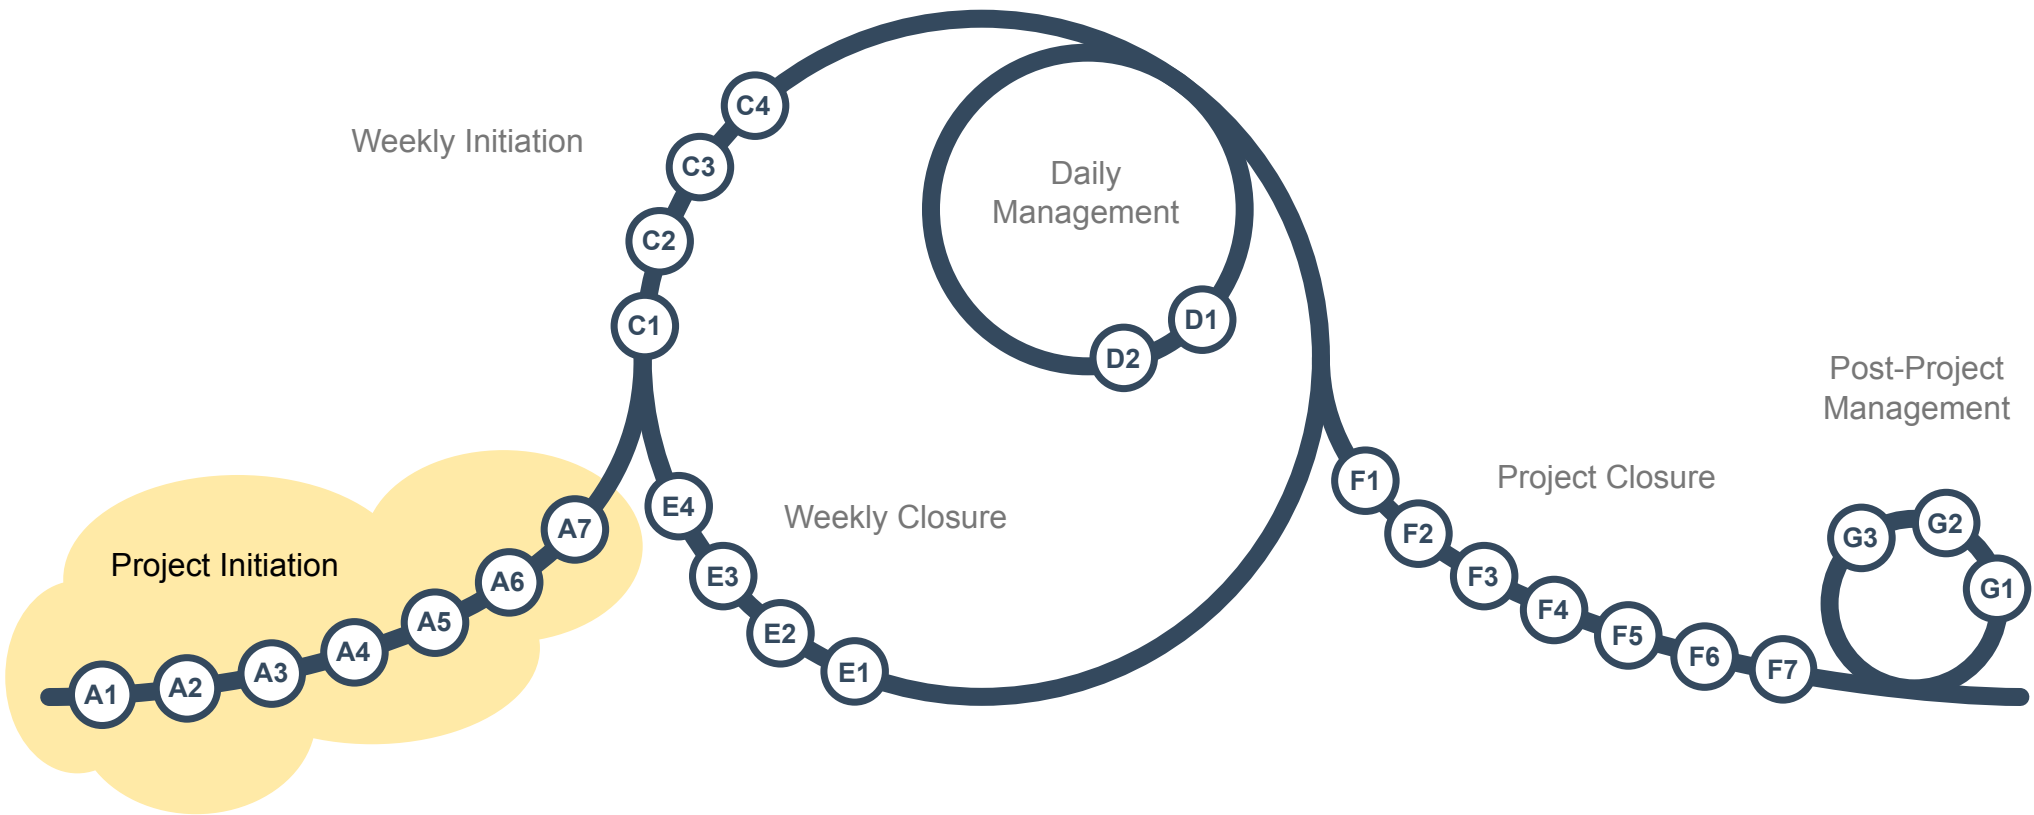

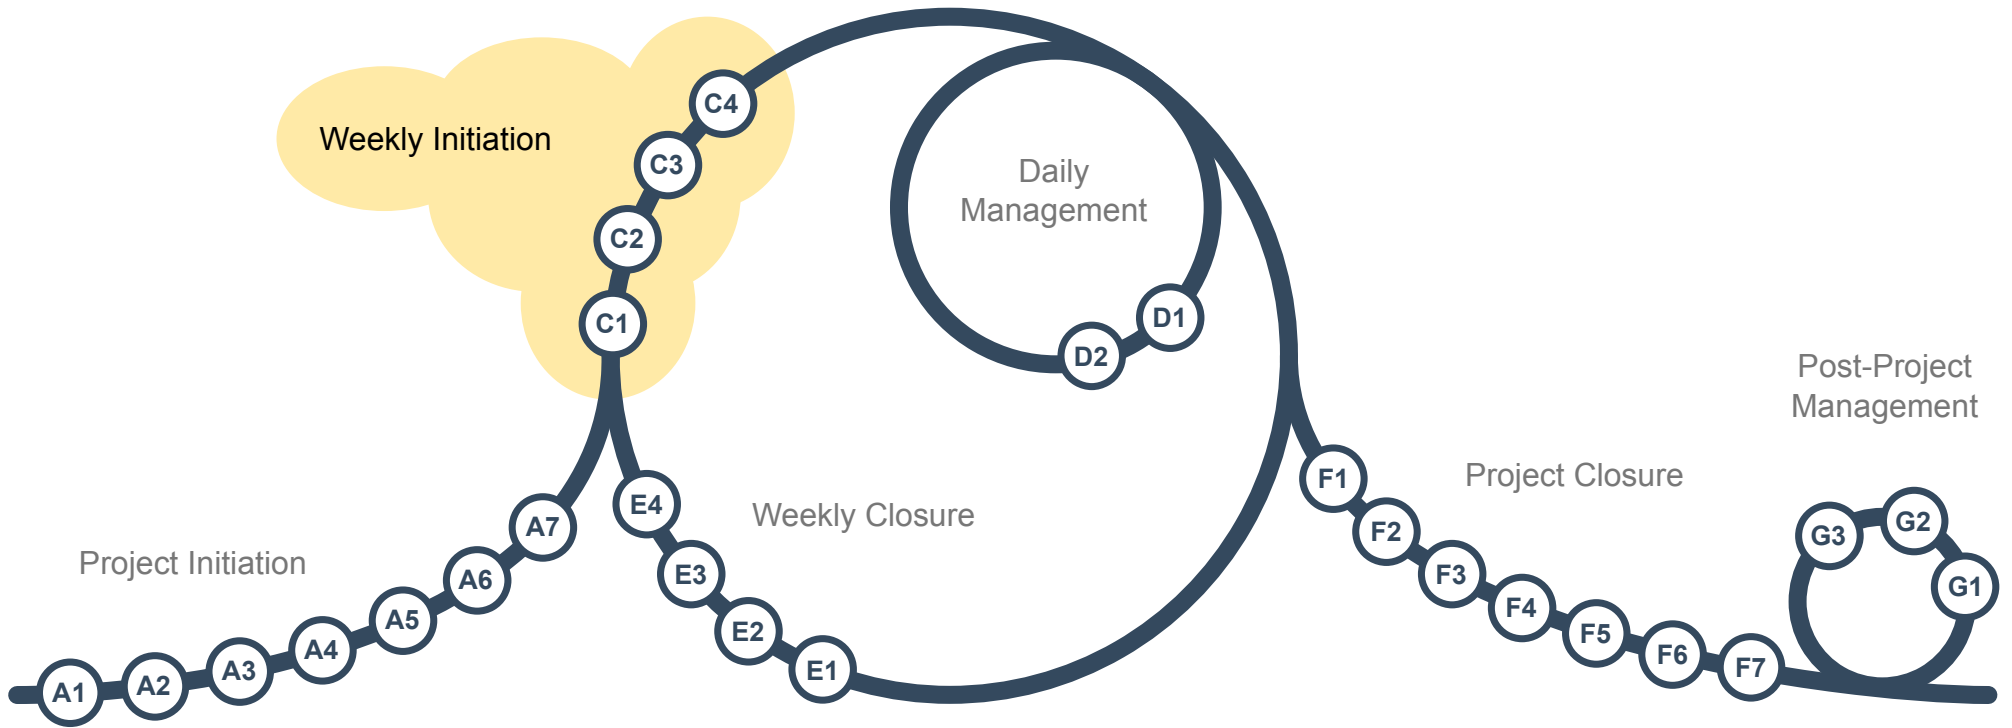

Weekly Initiation


Daily Management

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

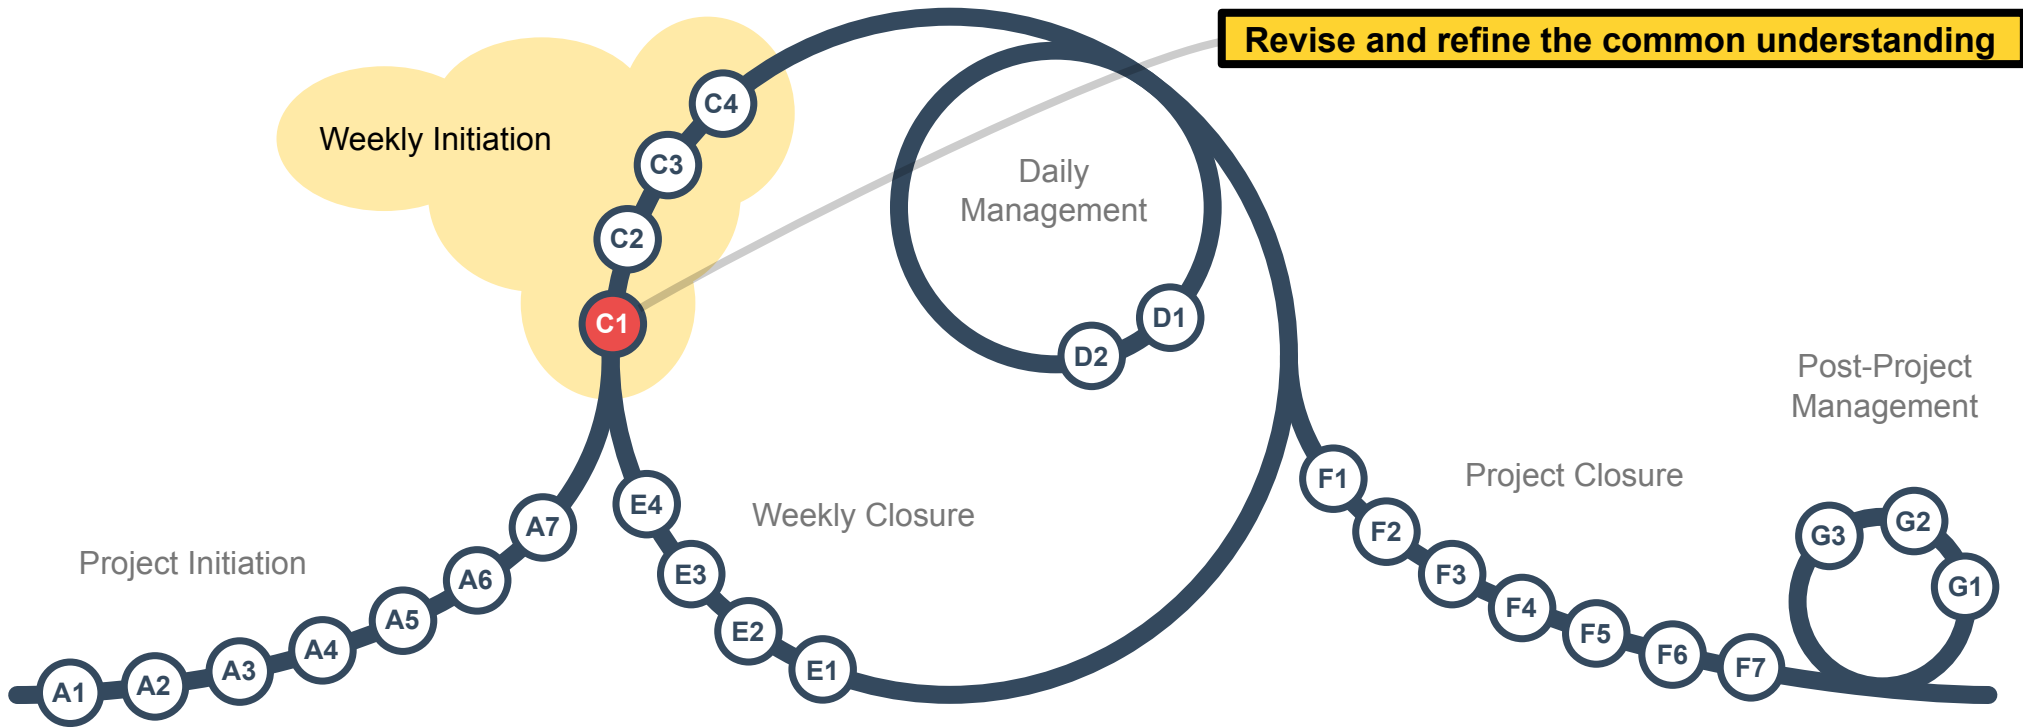

Revise and refine the common understanding

Weekly Initiation

Daily Management


Post-Project Management

Project Initiation


Weekly Closure

Project Closure

C1 - Revise and refine the common understanding

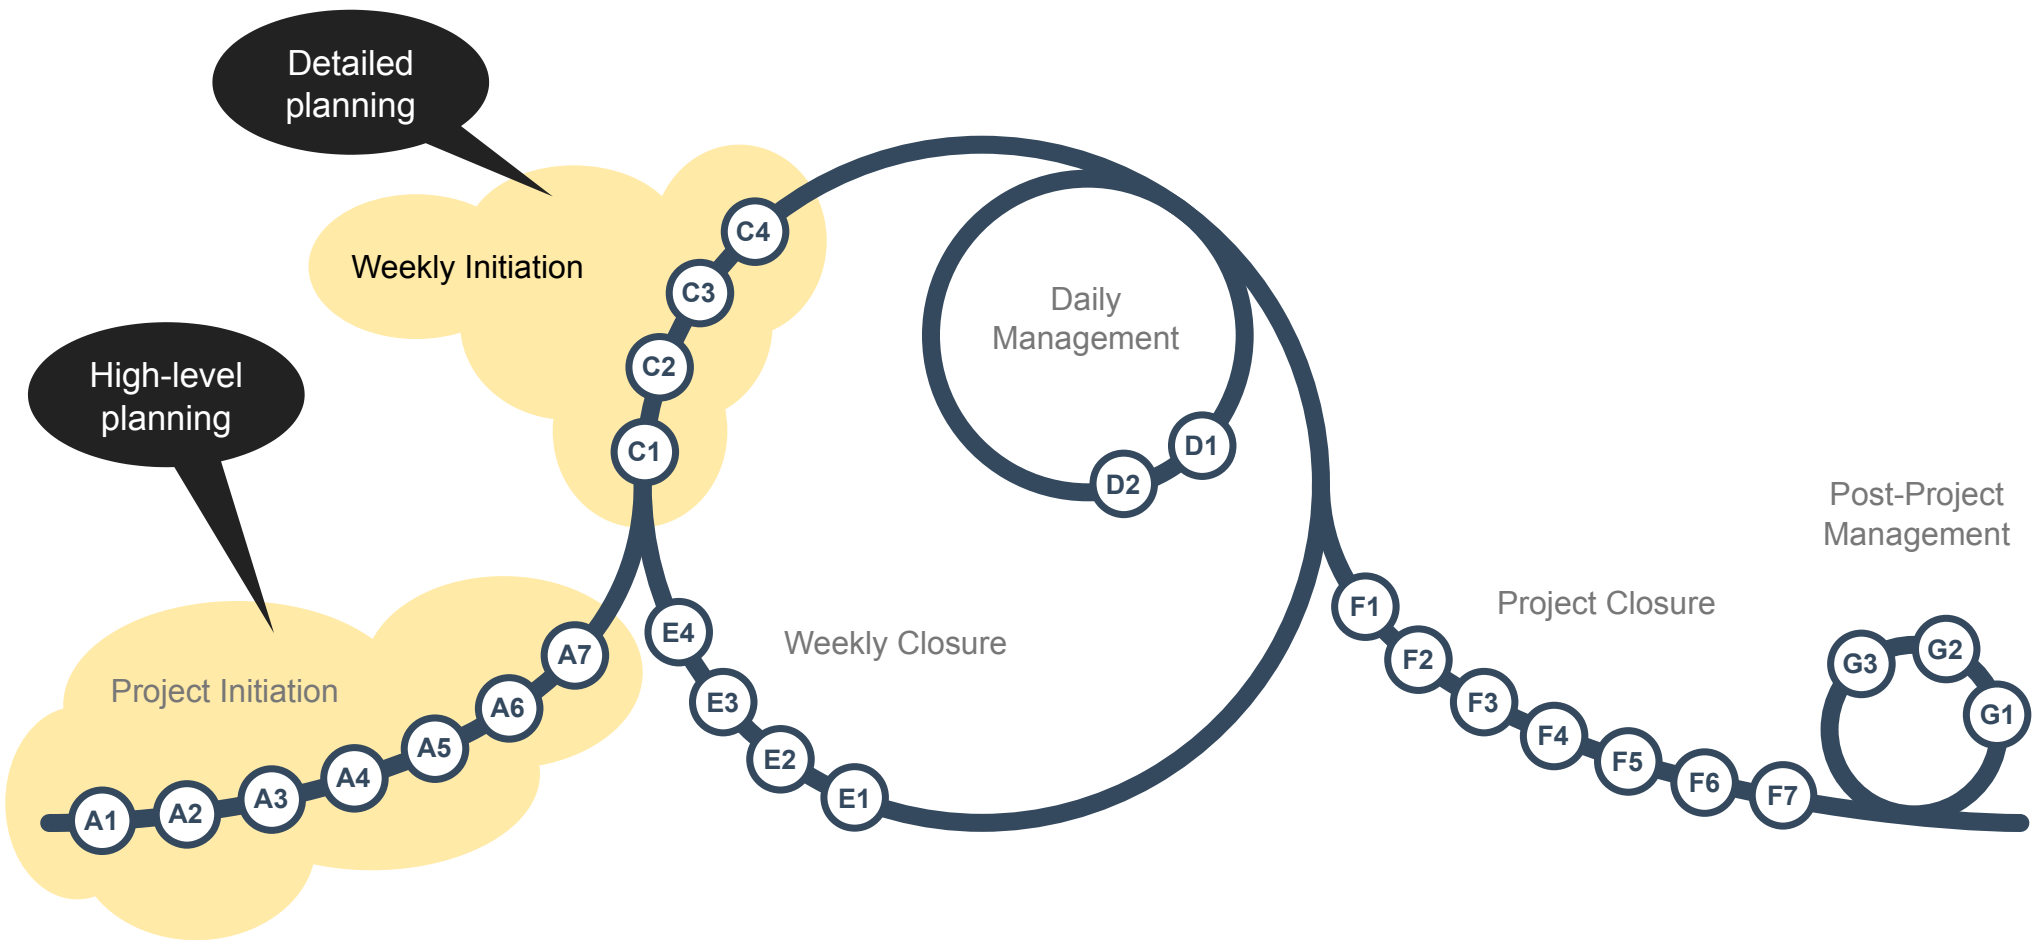


Integrated Project Board

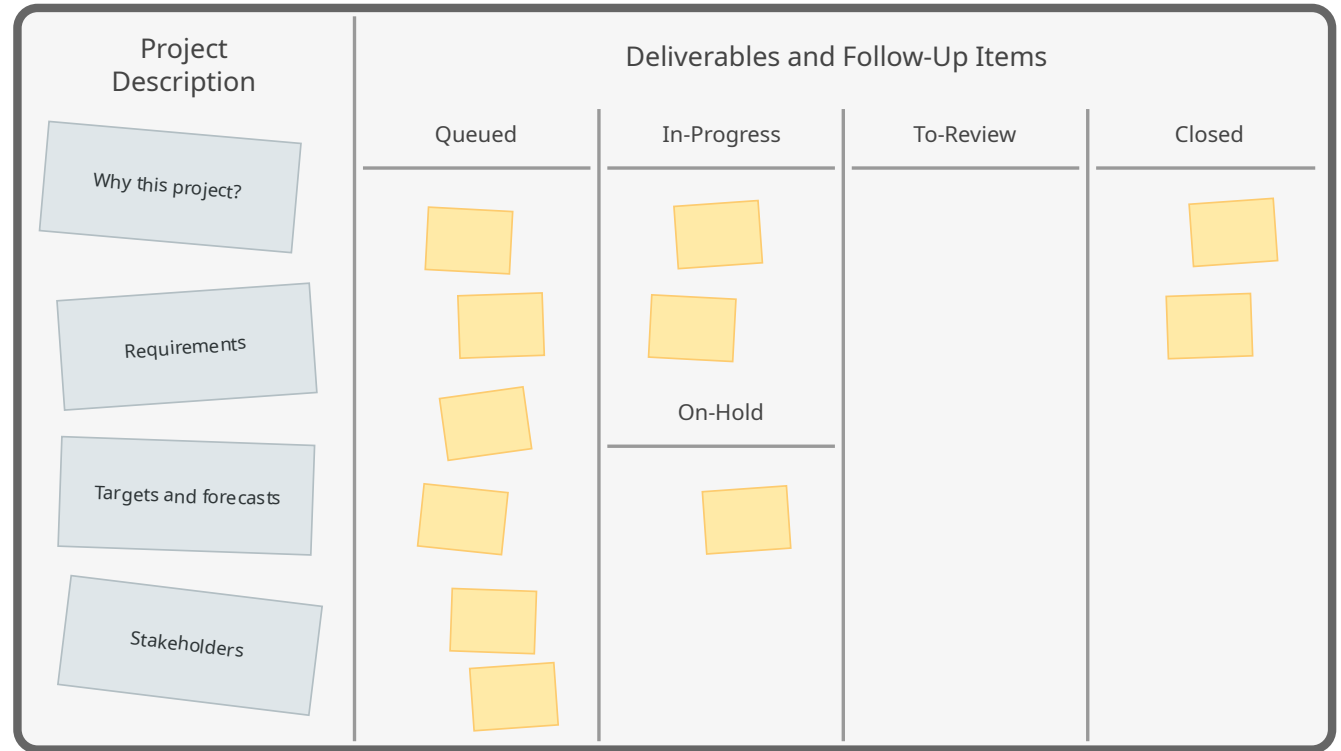


Integrated Project Board


- 1 Adding new cards
- 2 Revising the sequence

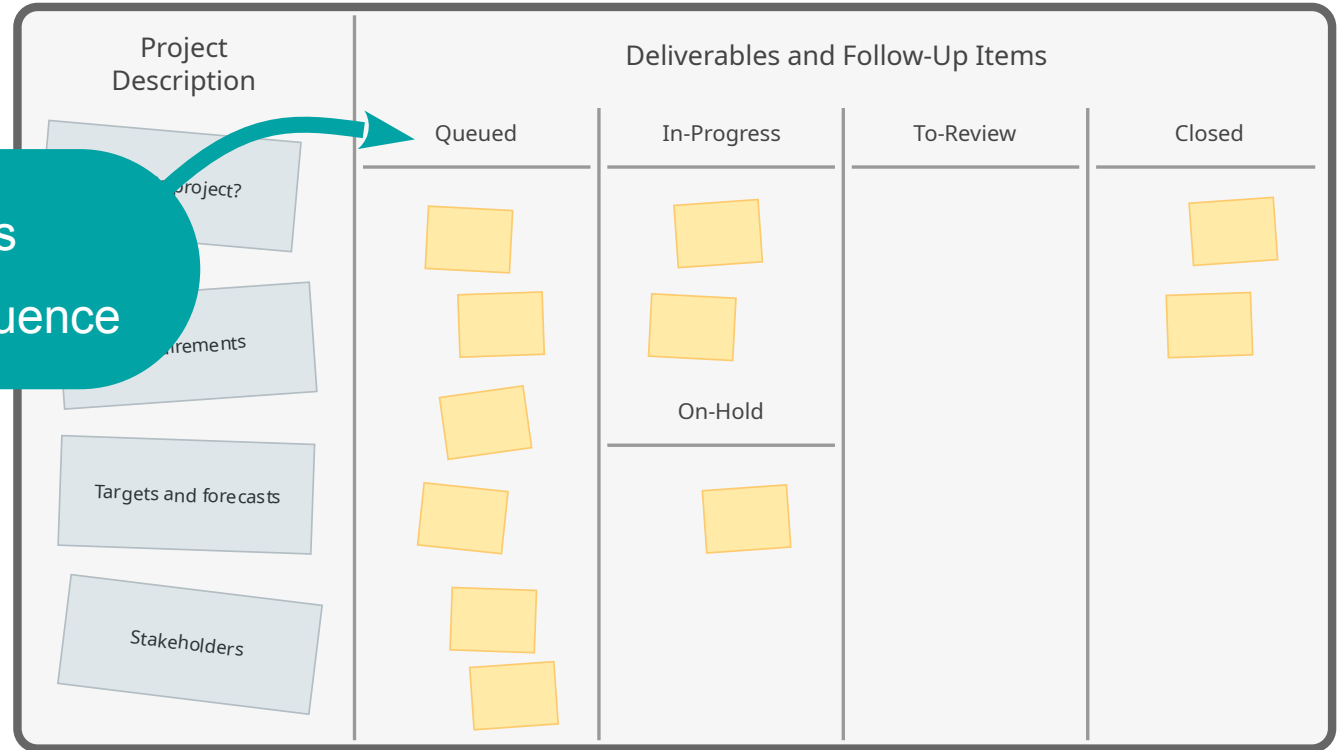

Integrated Project Board

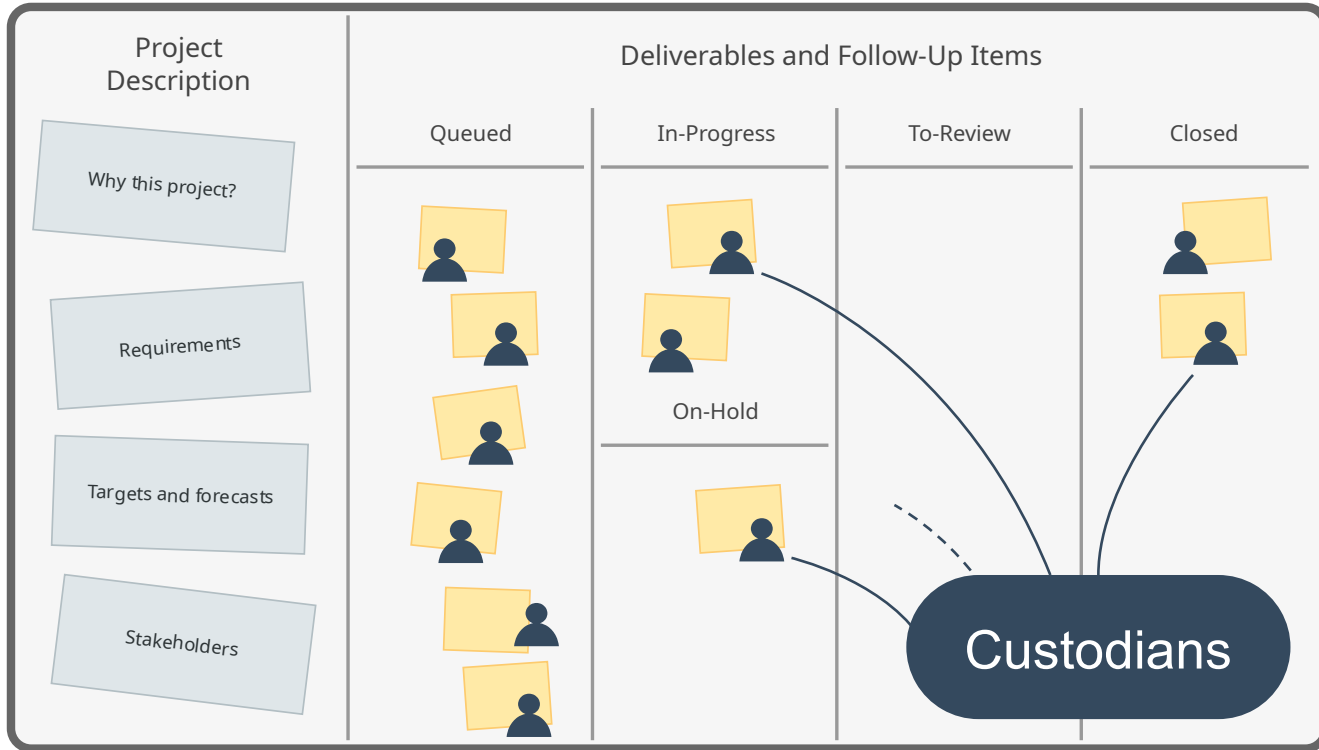

Integrated Project Board

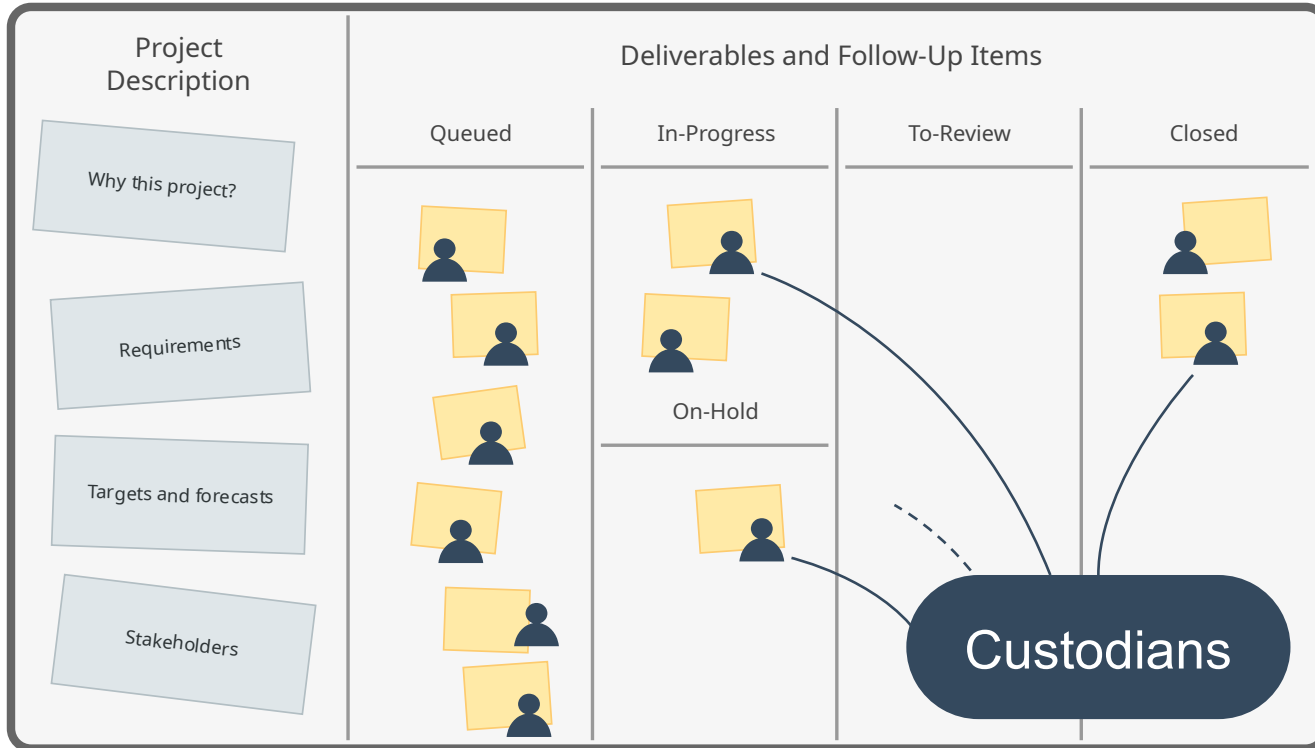


- Adding comments
- Updating status
- Following up


What concerns do you think each hat should have
in this management activity?




C1 - Revise and refine the common understanding

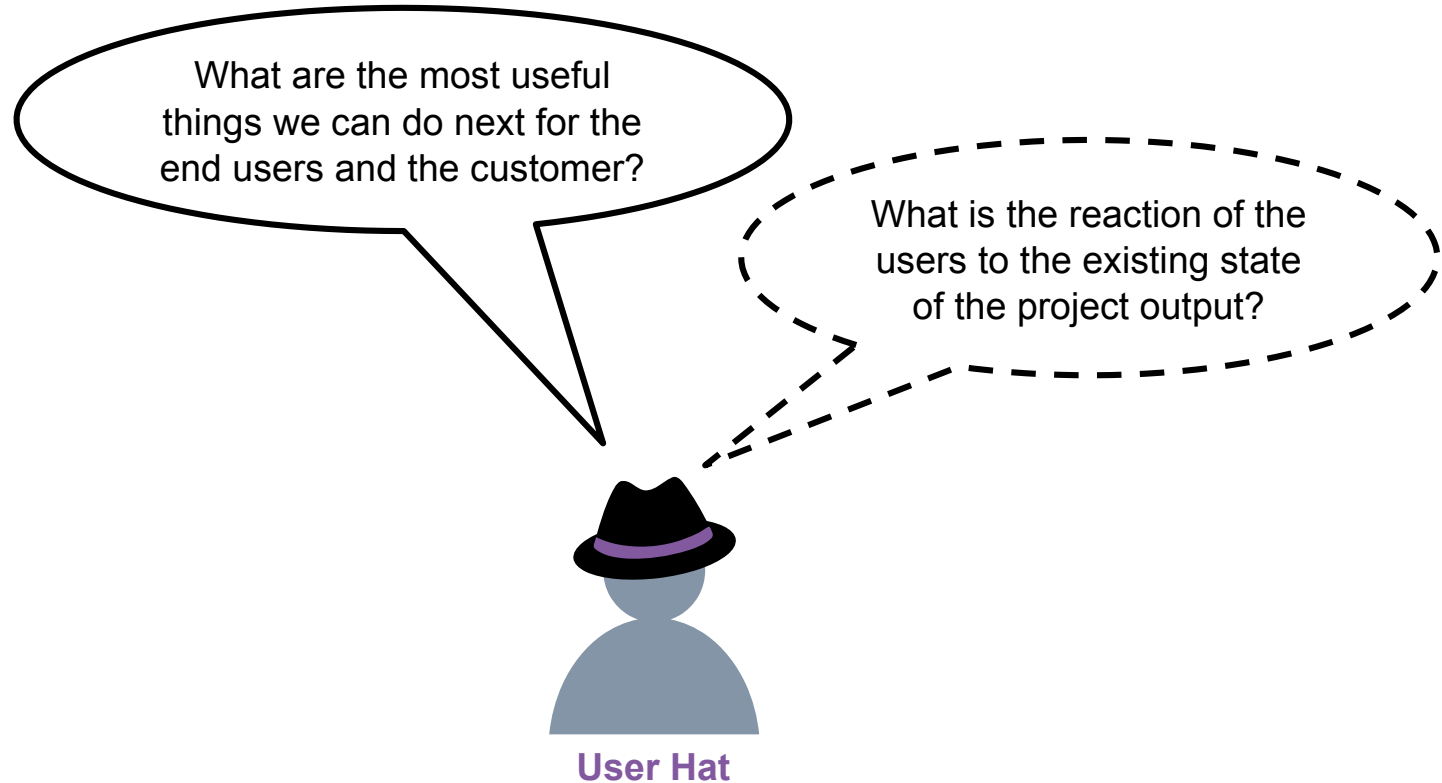


C1 - Revise and refine the common understanding

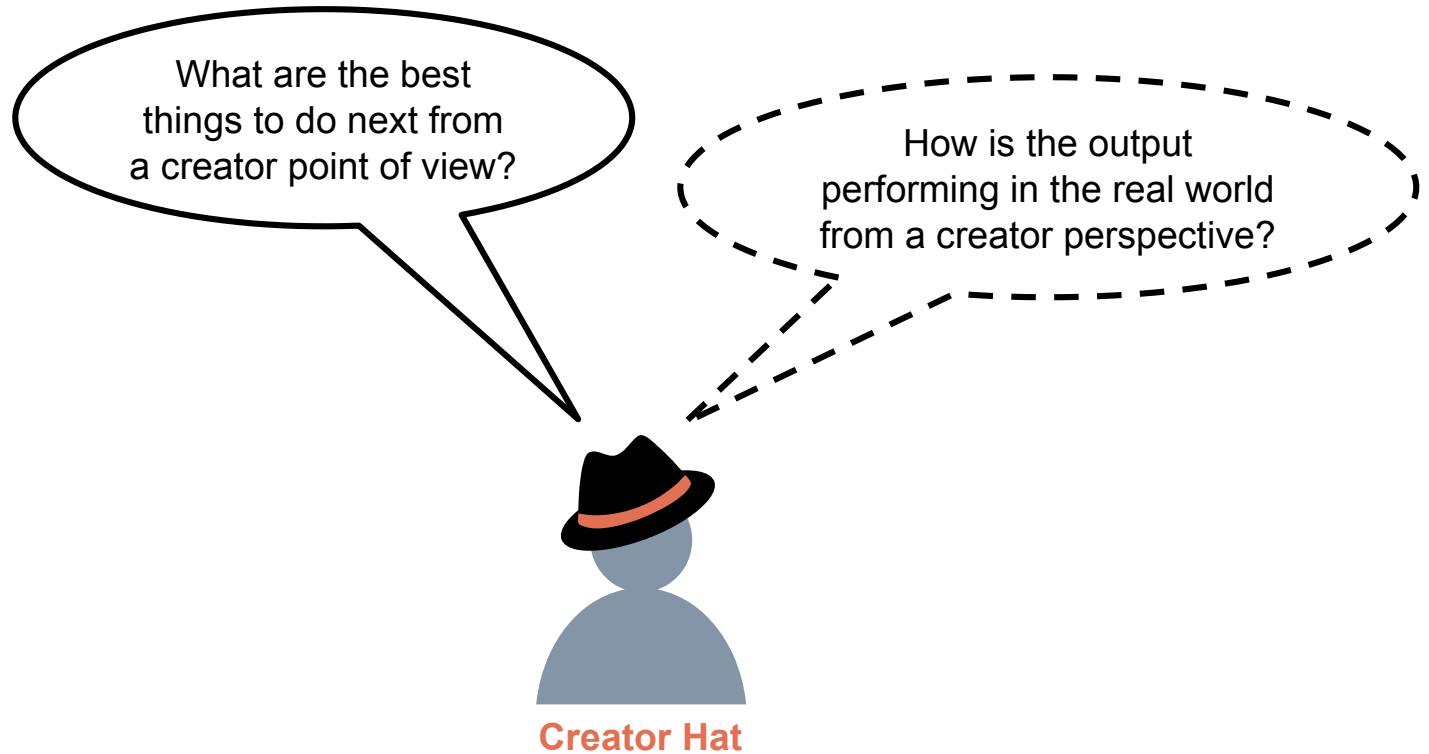


C1 - Revise and refine the common understanding



C1 - Revise and refine the common understanding

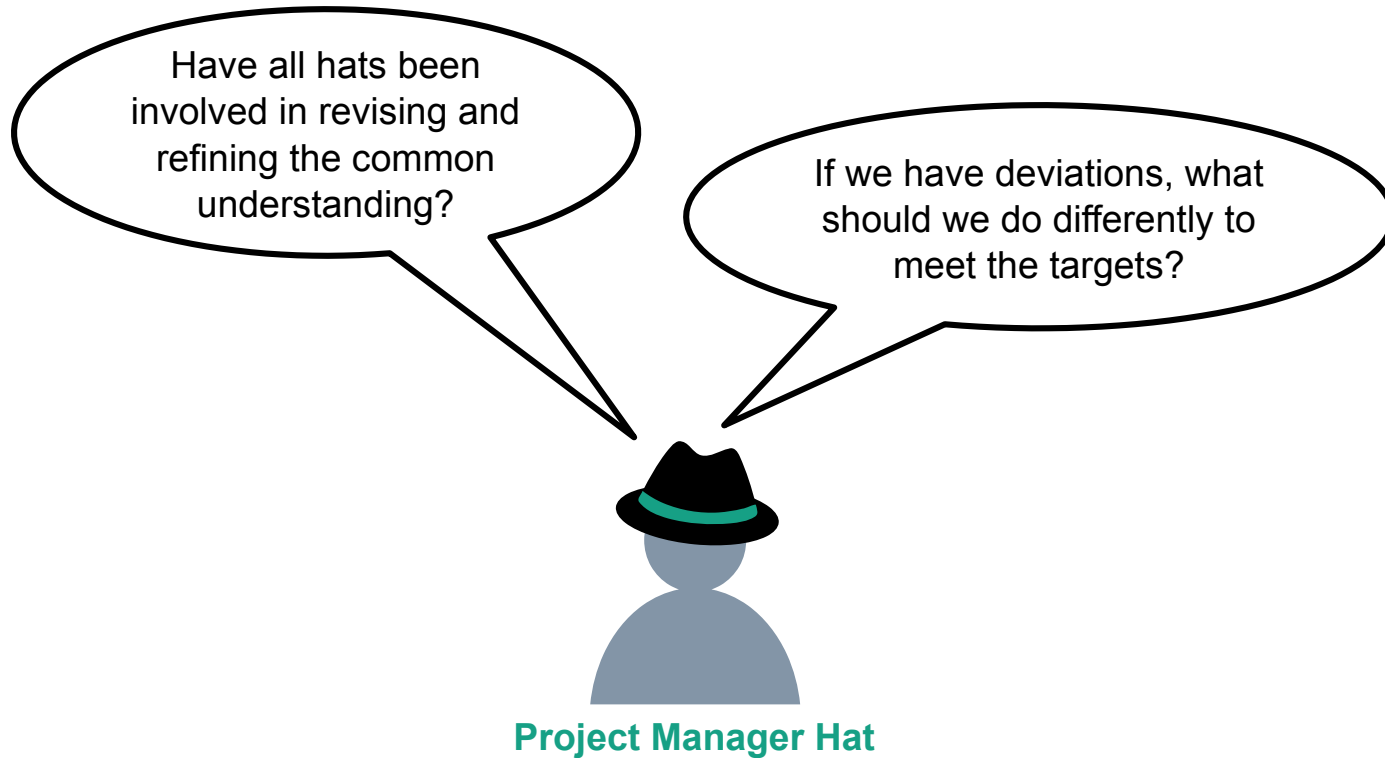


C1 - Revise and refine the common understanding



**Are the documents
clear and easy to
understand?**

Project Manager Hat

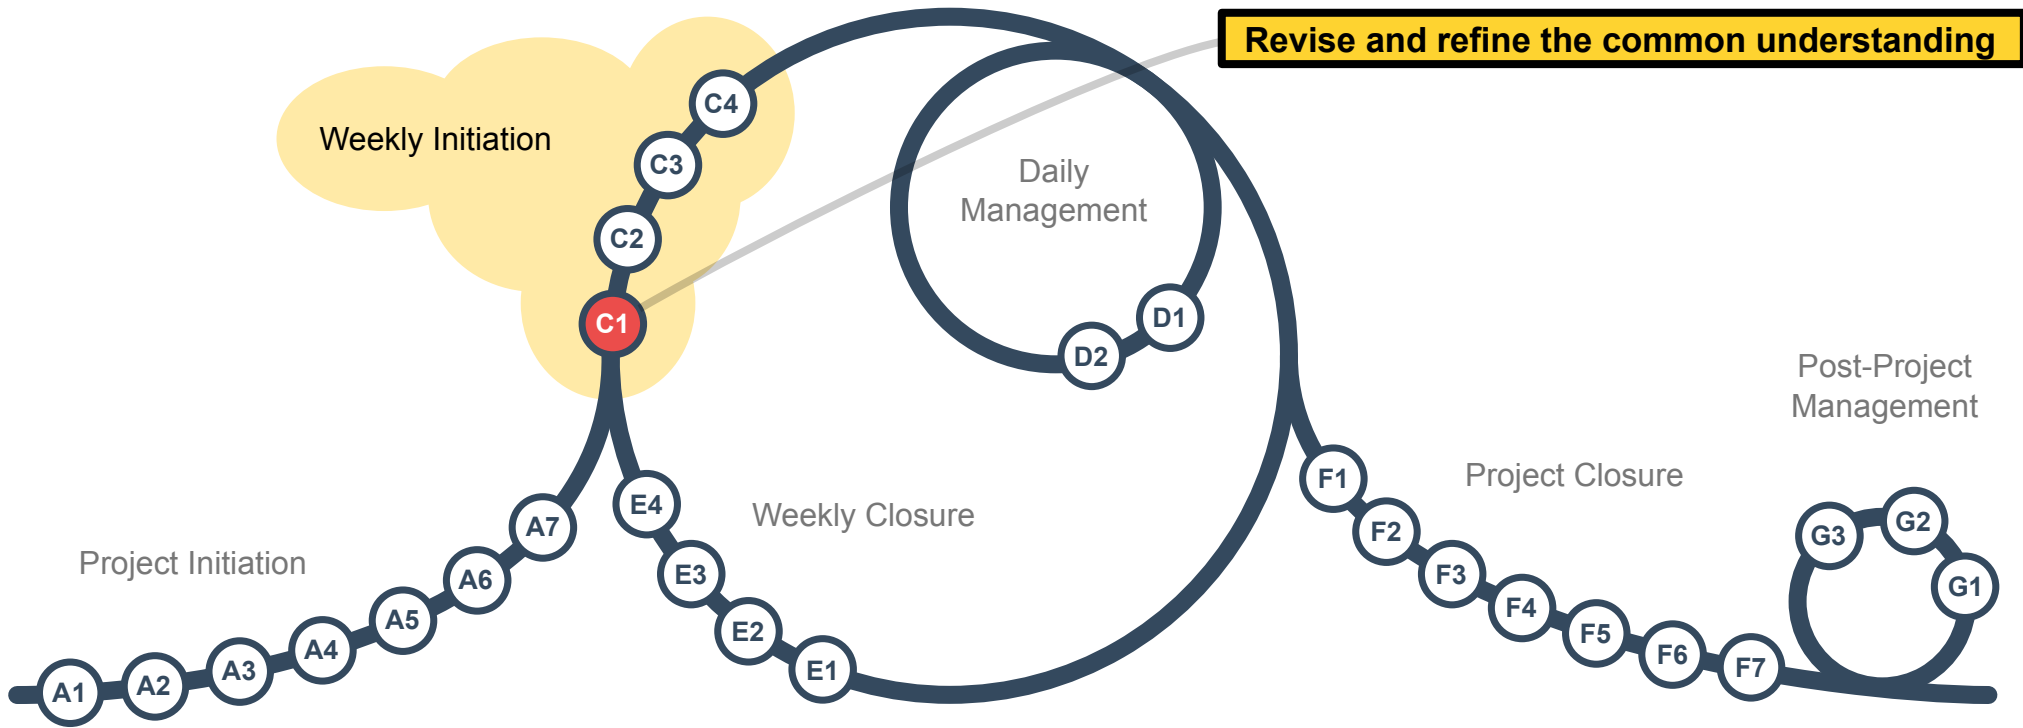

Weekly Initiation

Revise and refine the common understanding


Daily Management

Post-Project Management

Project Closure

Weekly Closure

Project Initiation

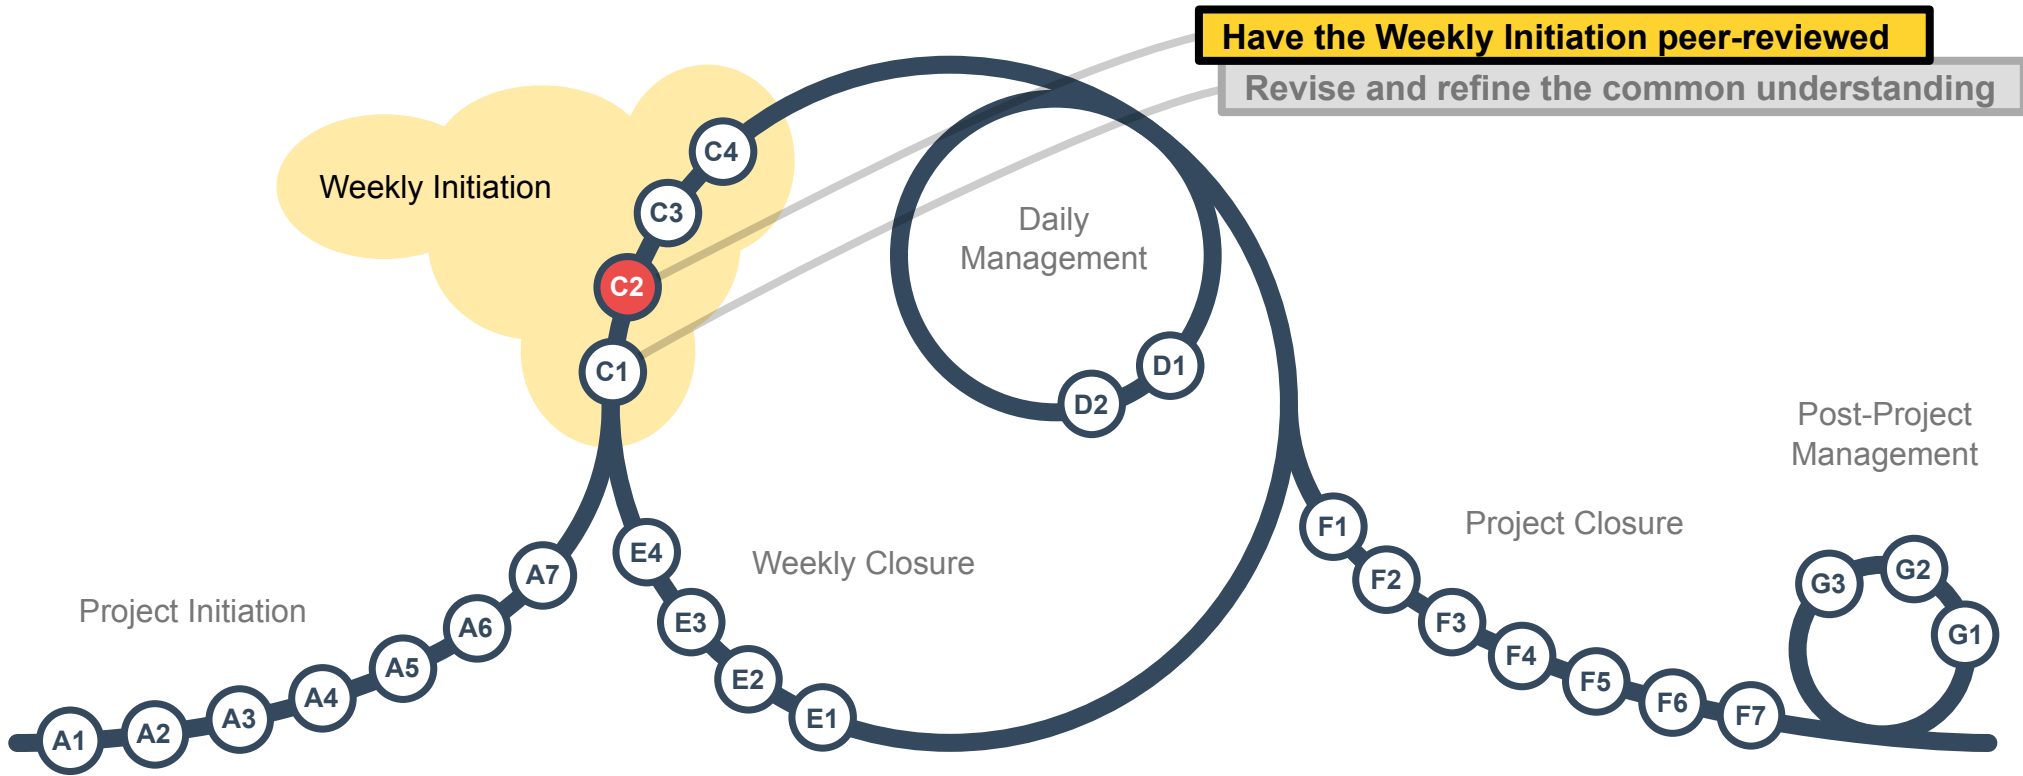


C2 - Have the Weekly Initiation peer-reviewed




- ★ Helps find mistakes
- ★ Both learn from each other



Do other hats need peer-reviews as well?

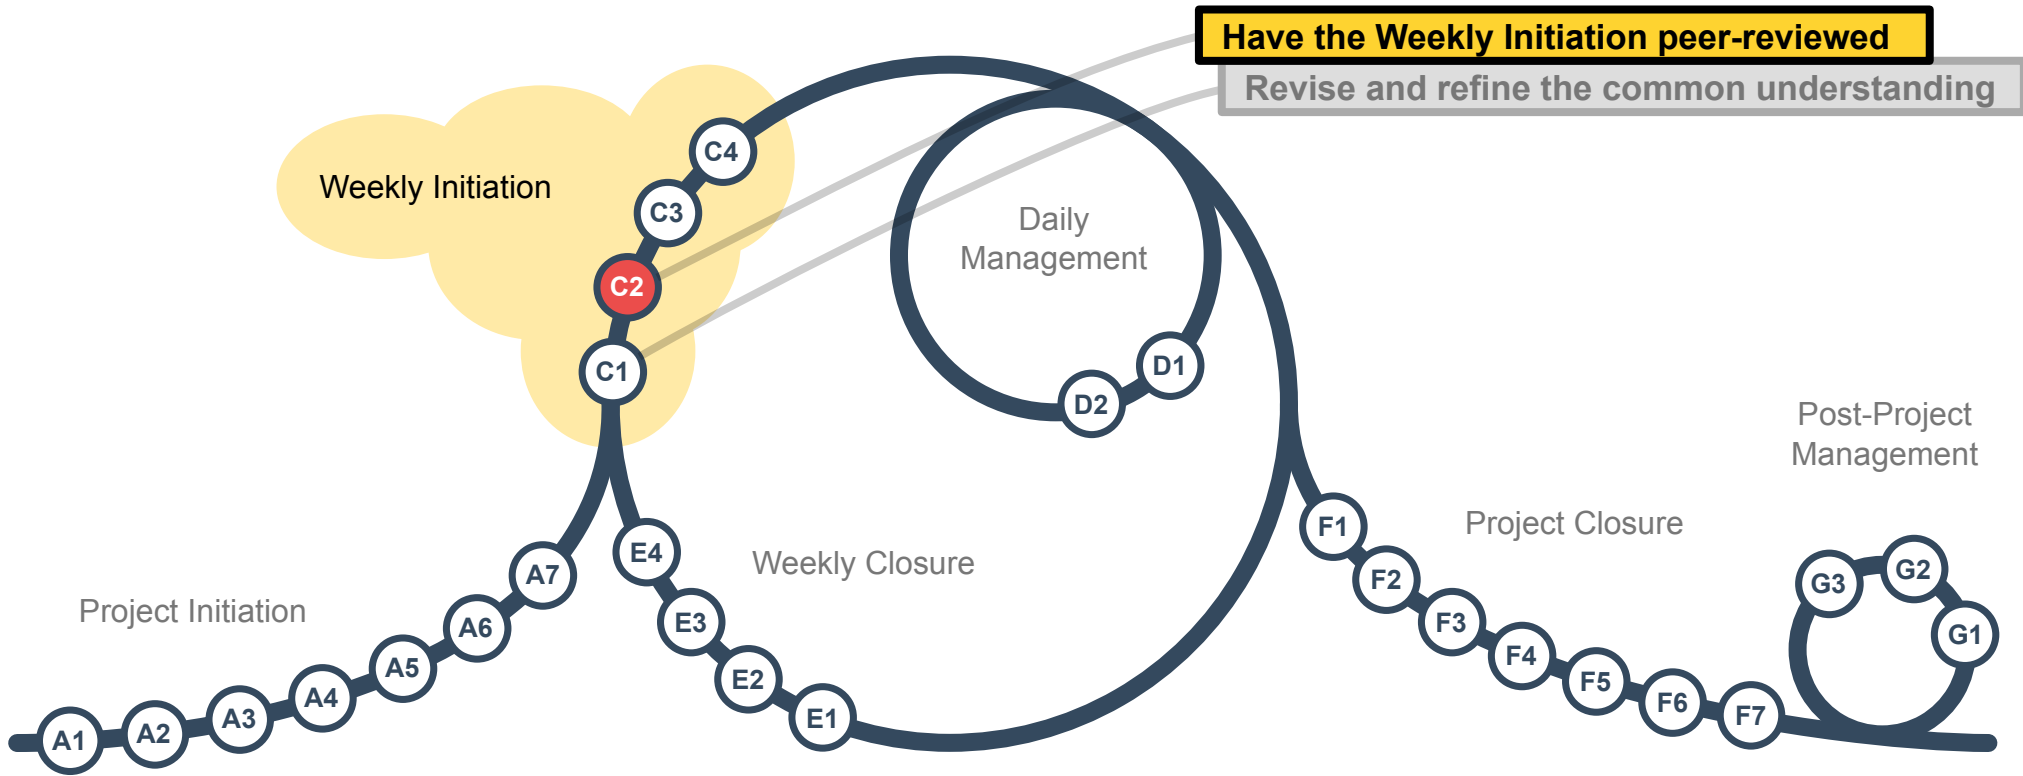

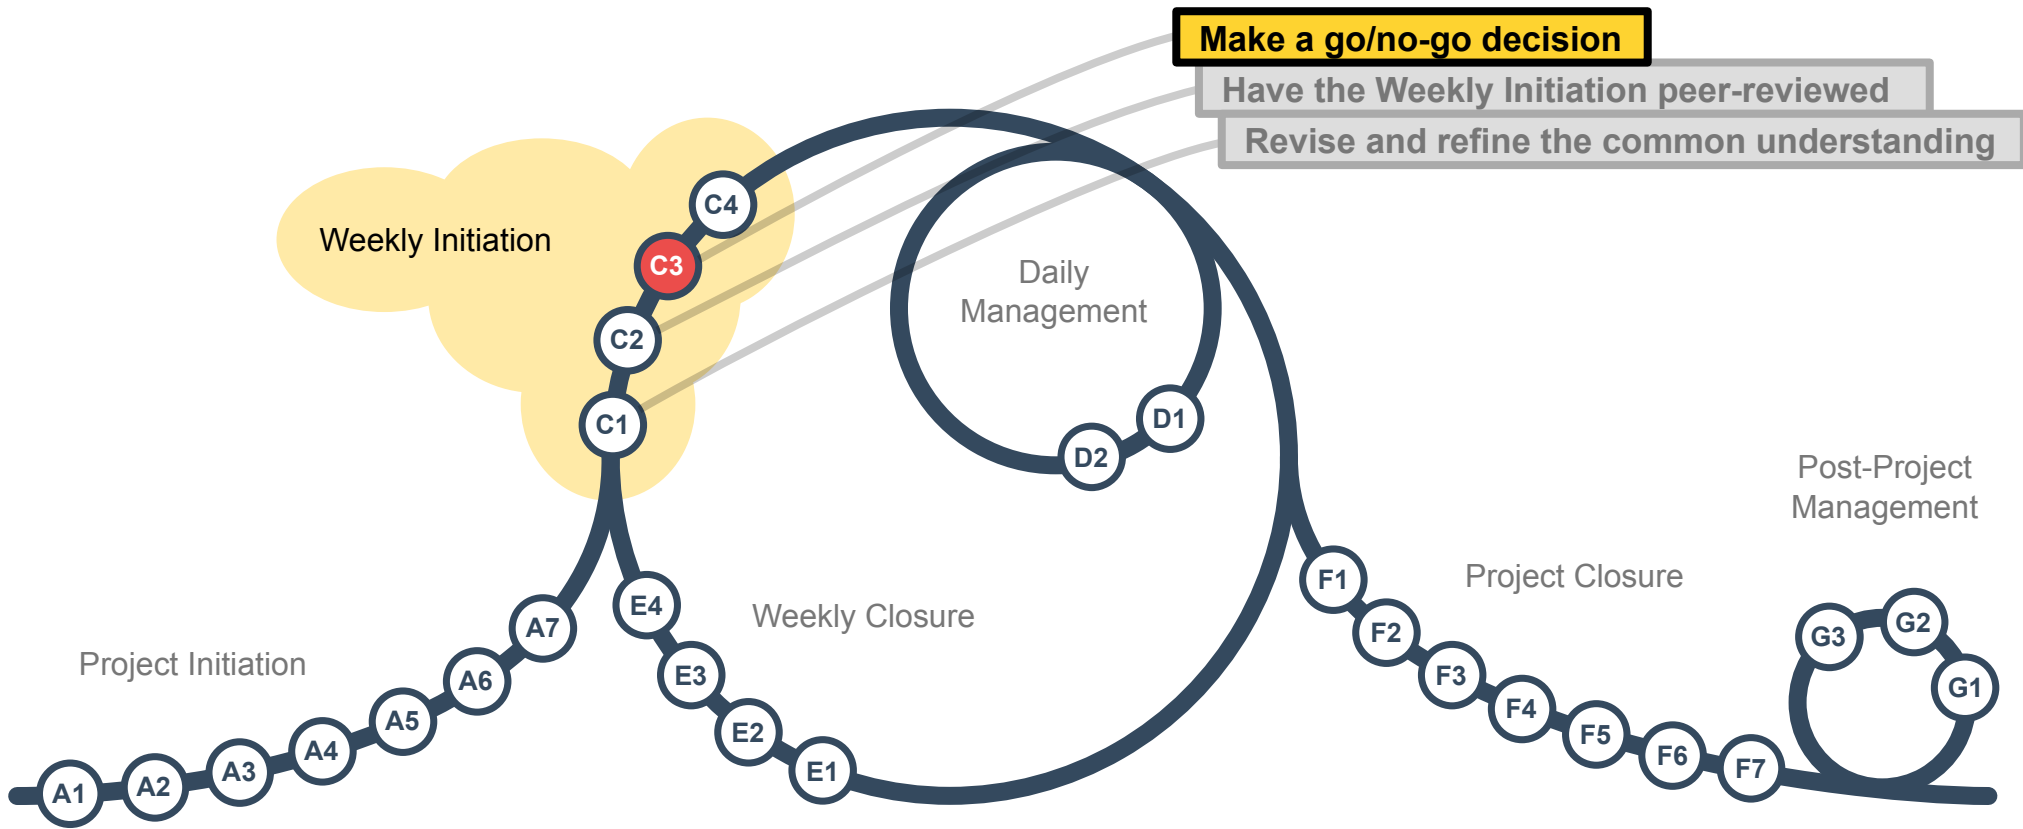


What concerns do you think each hat should have
in this management activity?




C3 - Make a go/no-go decision




C3 - Make a go/no-go decision

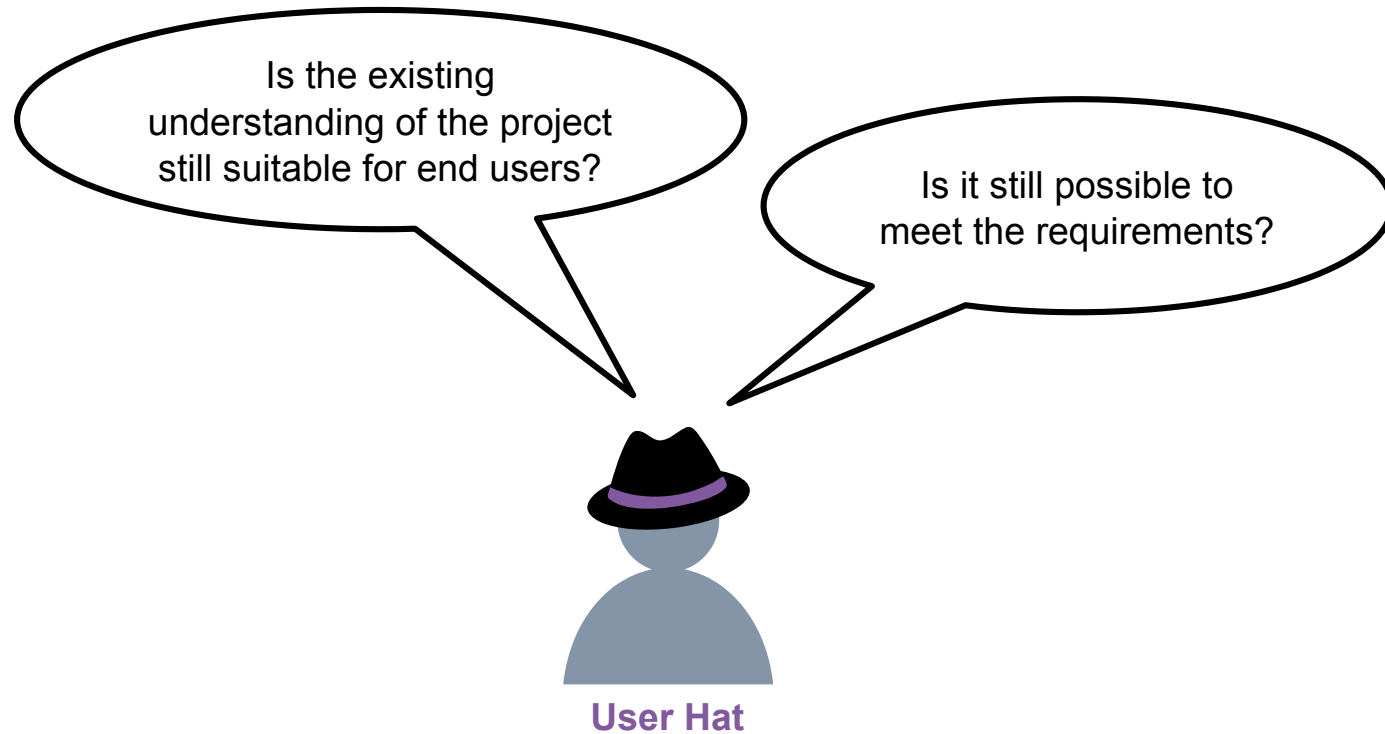


C3 - Make a go/no-go decision

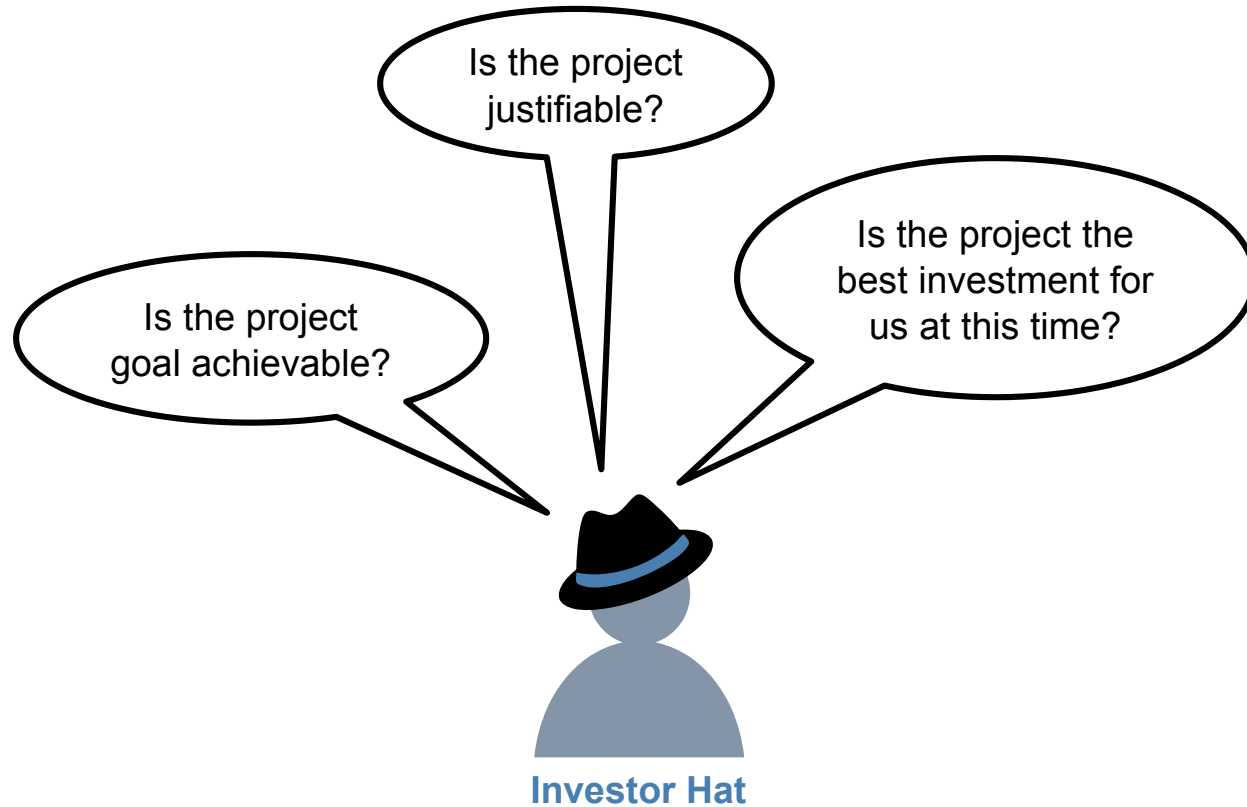


C3 - Make a go/no-go decision

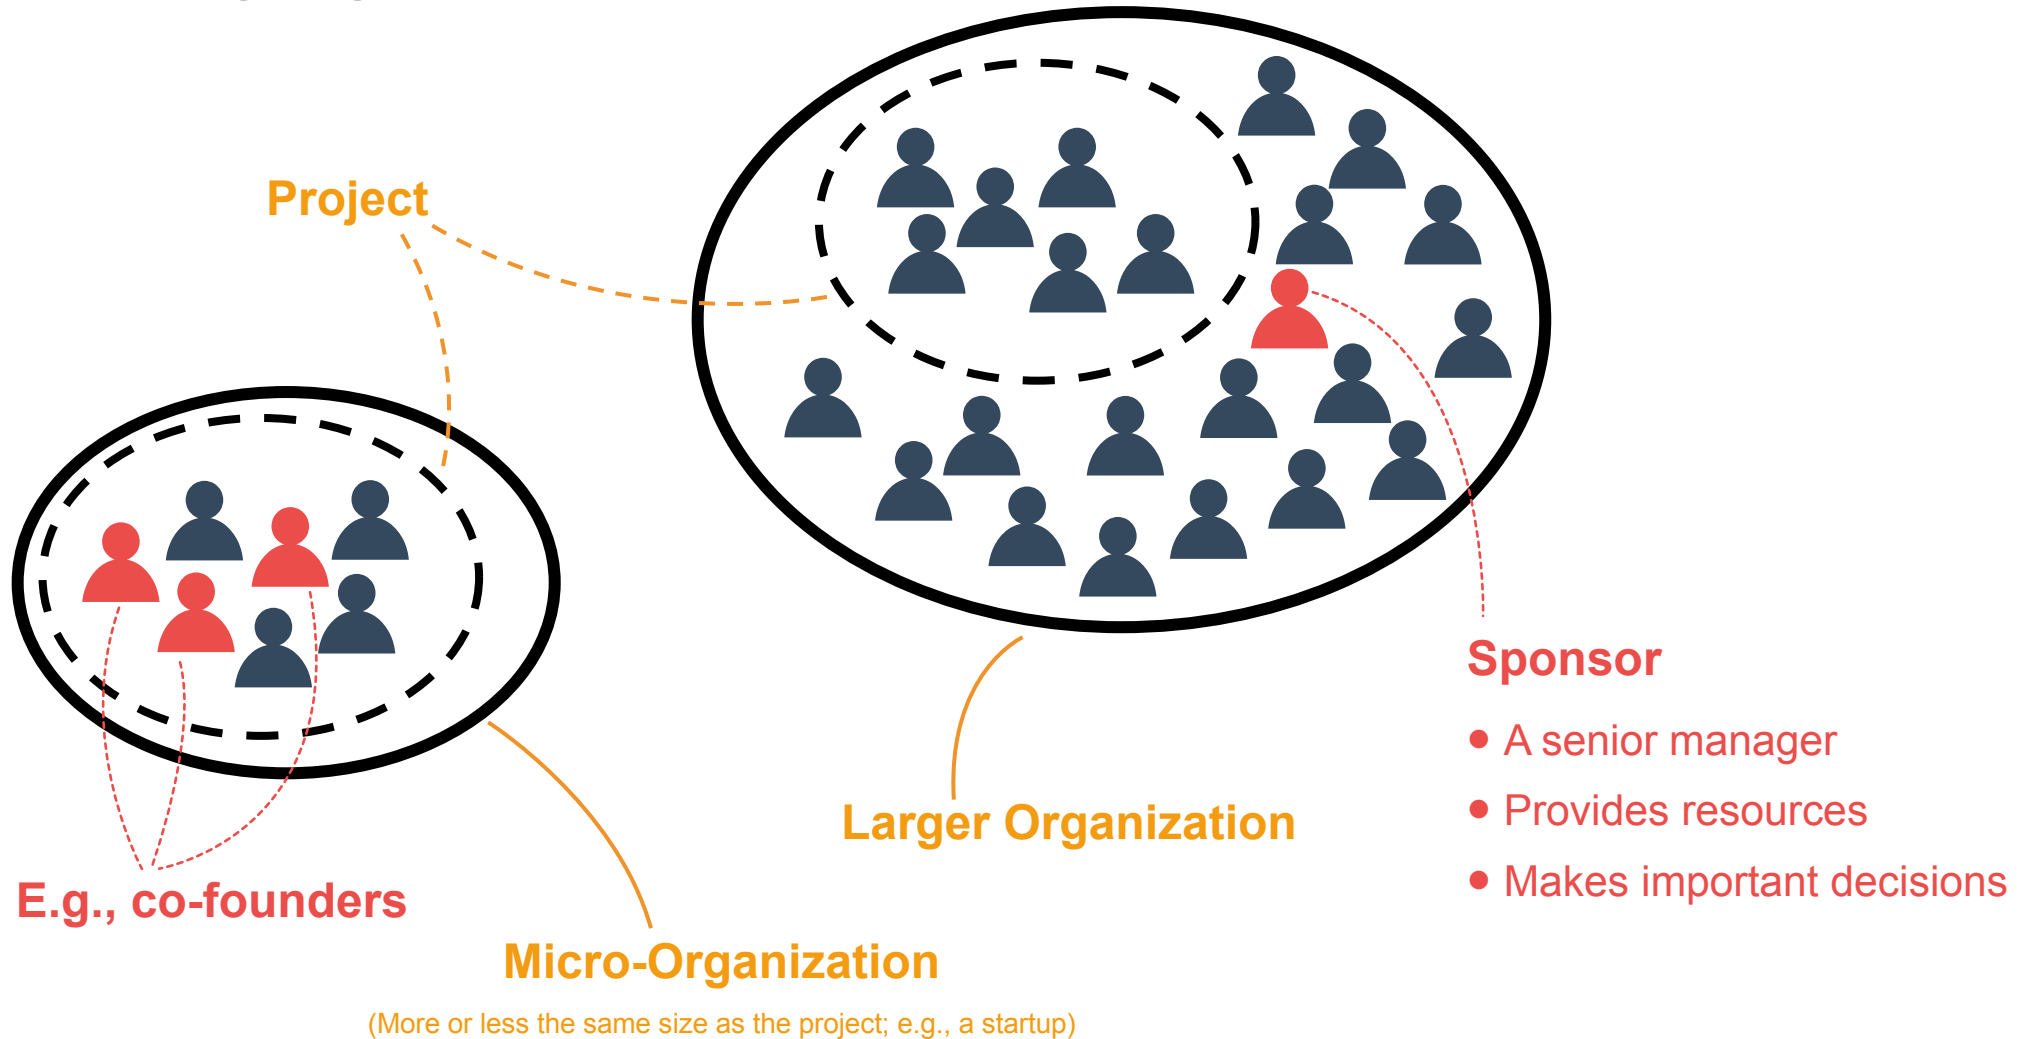

Integrated Project Board

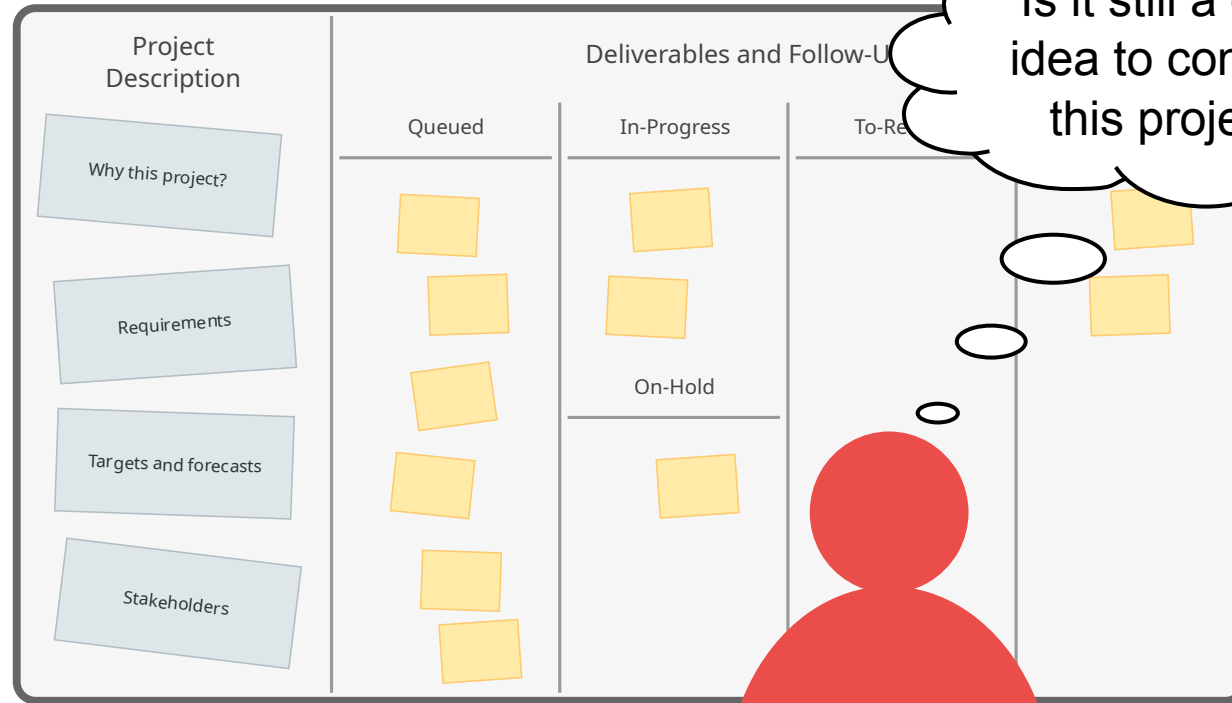

The high-level decision maker(s)
(e.g., the Sponsor)

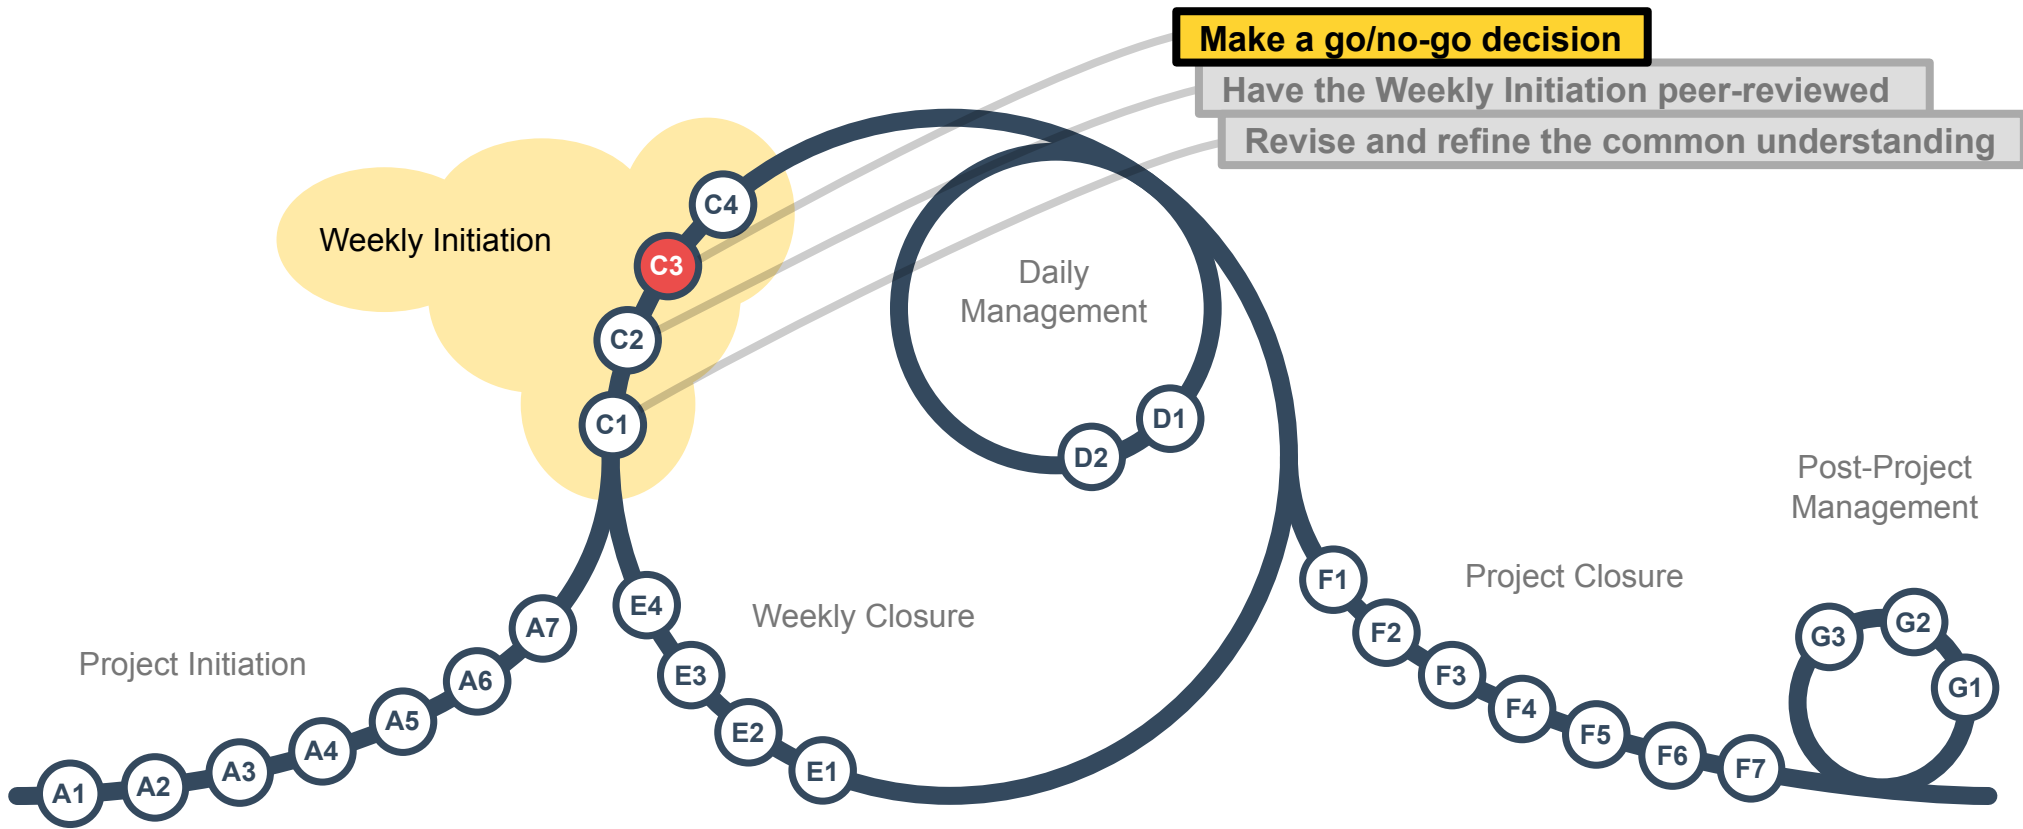

Make a go/no-go decision

Have the Weekly Initiation peer-reviewed

Revise and refine the common understanding

Weekly Initiation

Daily Management

Weekly Closure

Project Initiation

Project Closure

Post-Project Management

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C2

C1

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6

F7

G3

G2


G1

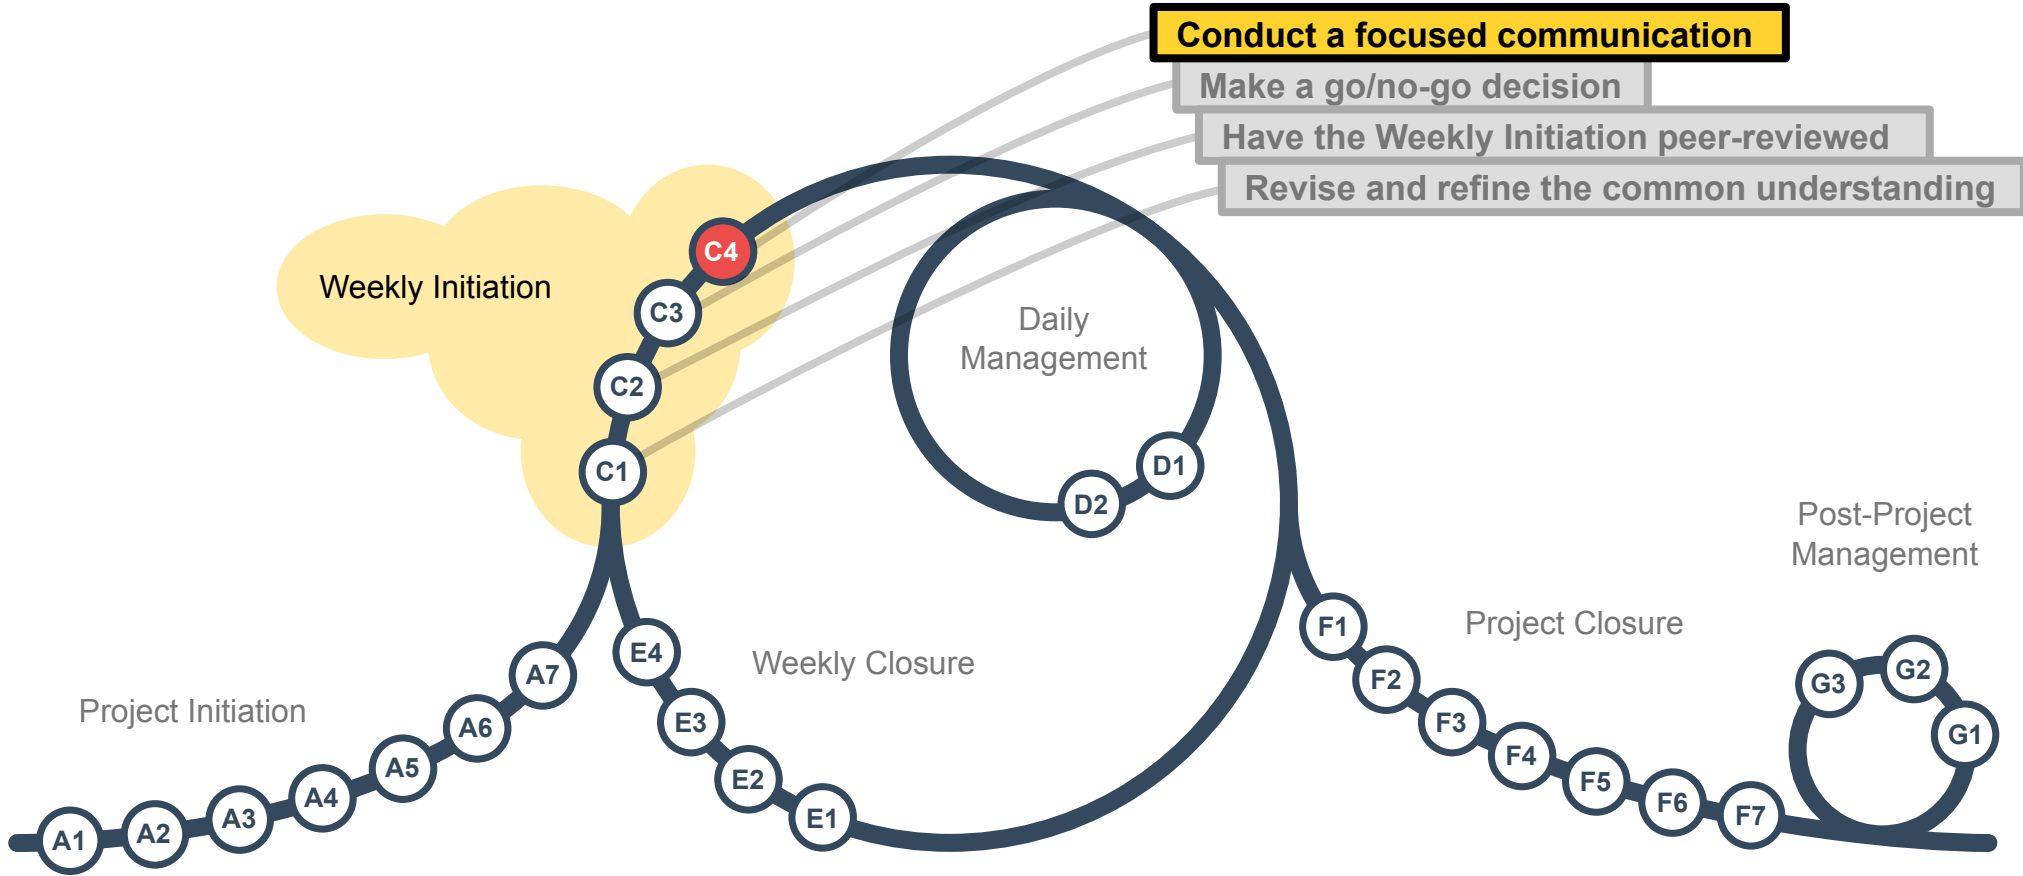


What are the advantages of telling the status of the project to everyone in the organization?




C4 - Conduct a focused communication

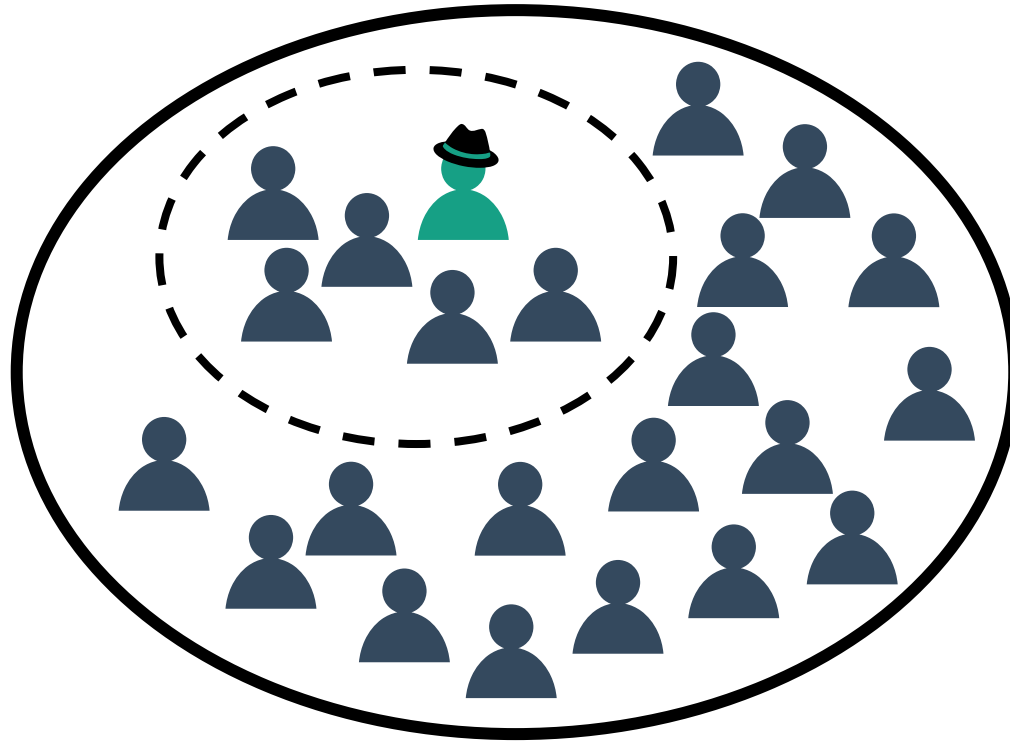


C4 - Conduct a focused communication

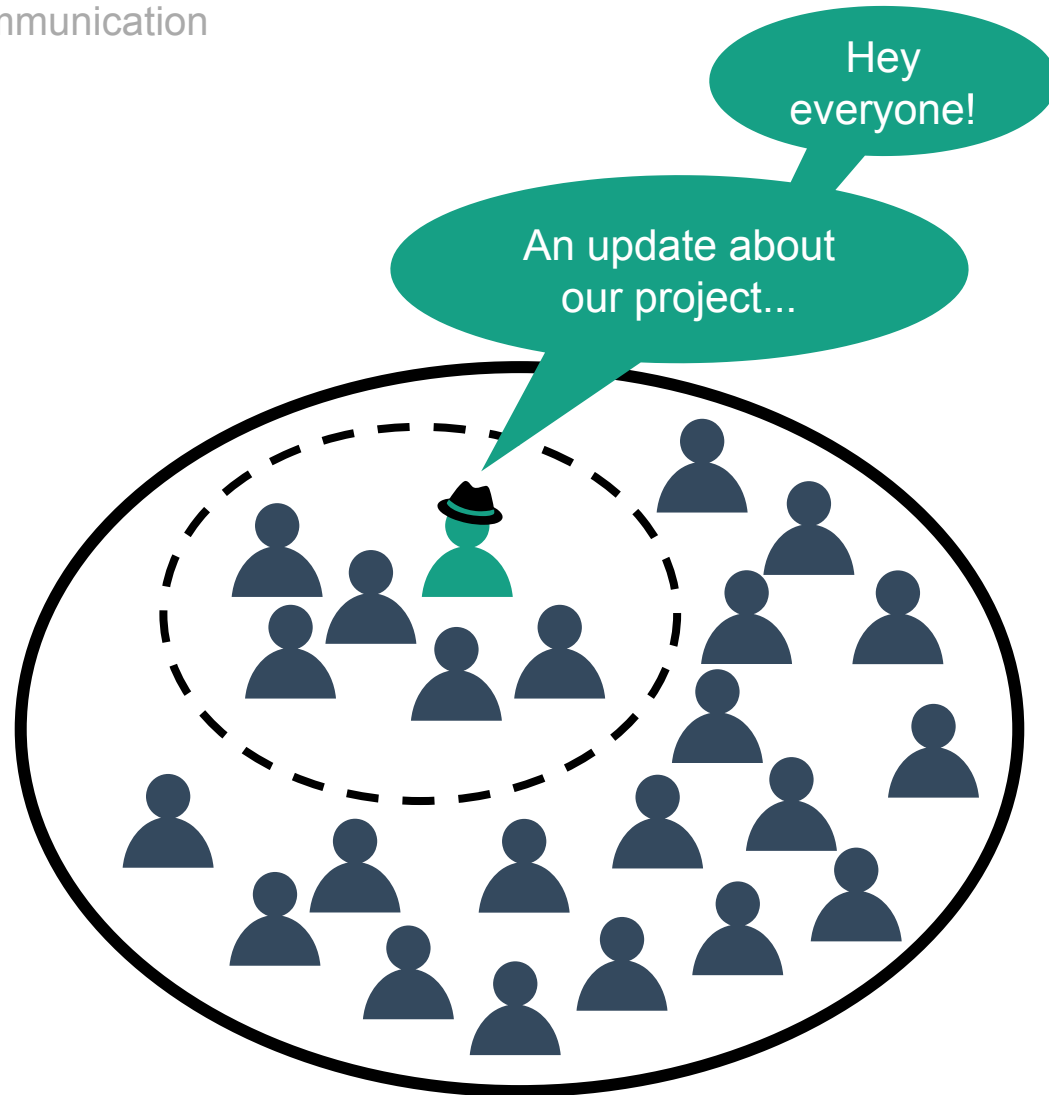


C4 - Conduct a focused communication

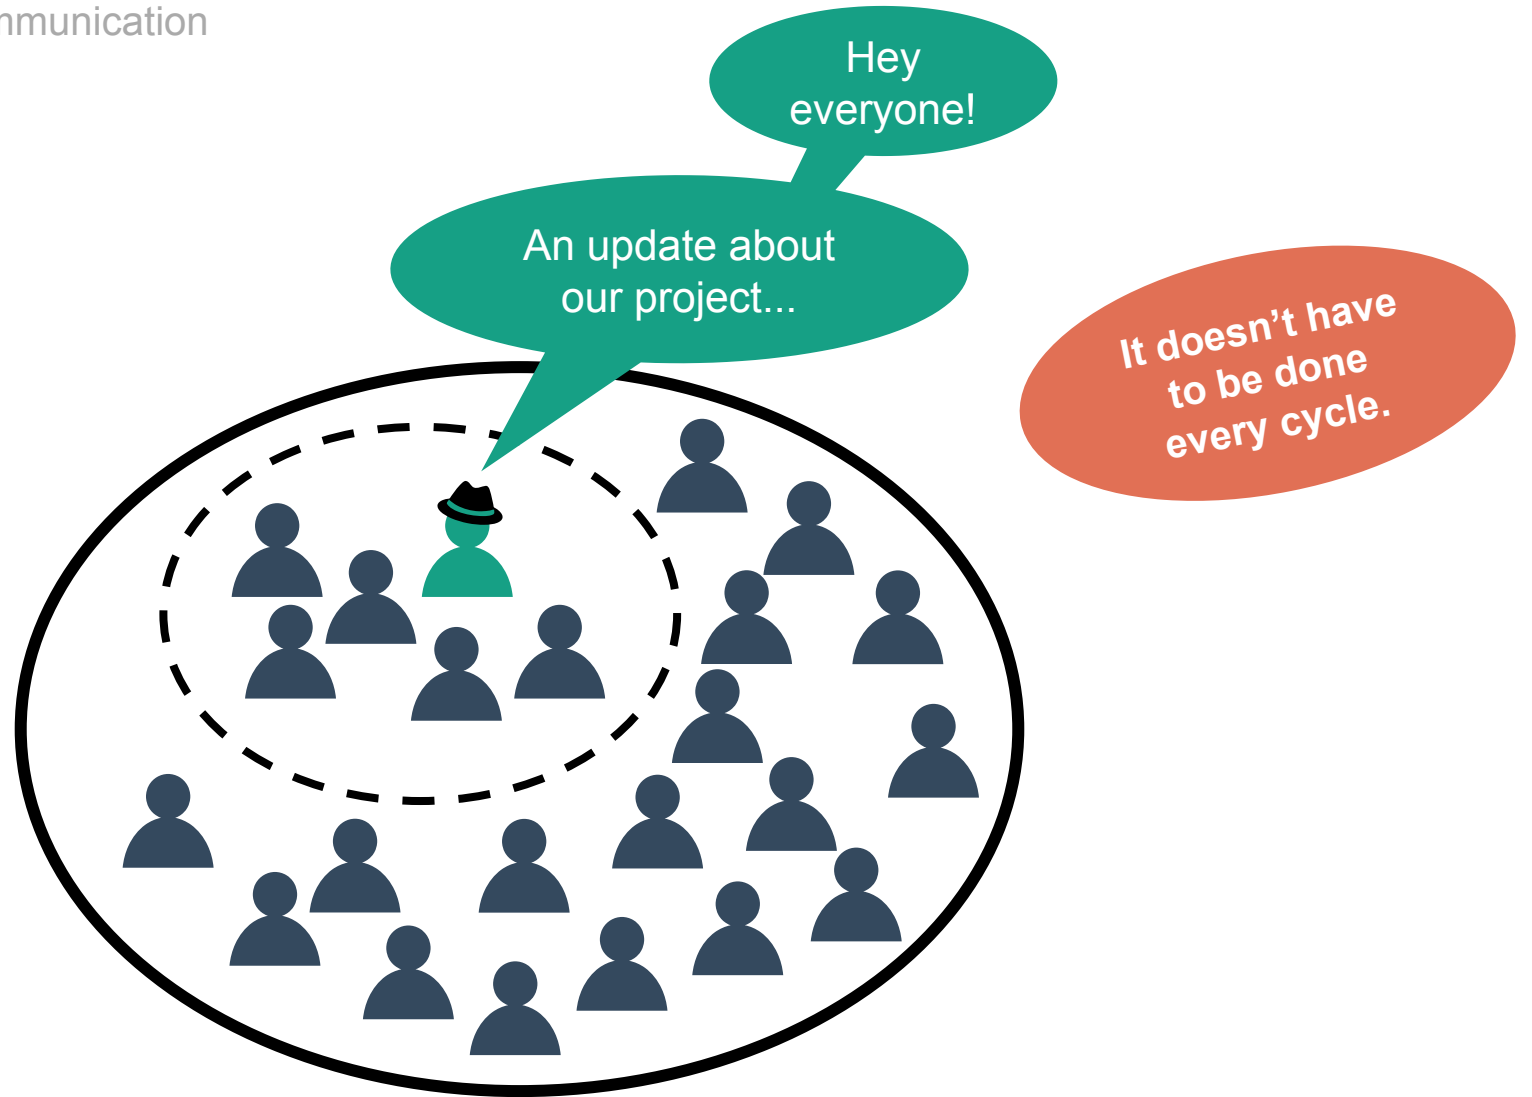



C4 - Conduct a focused communication





C4 - Conduct a focused communication

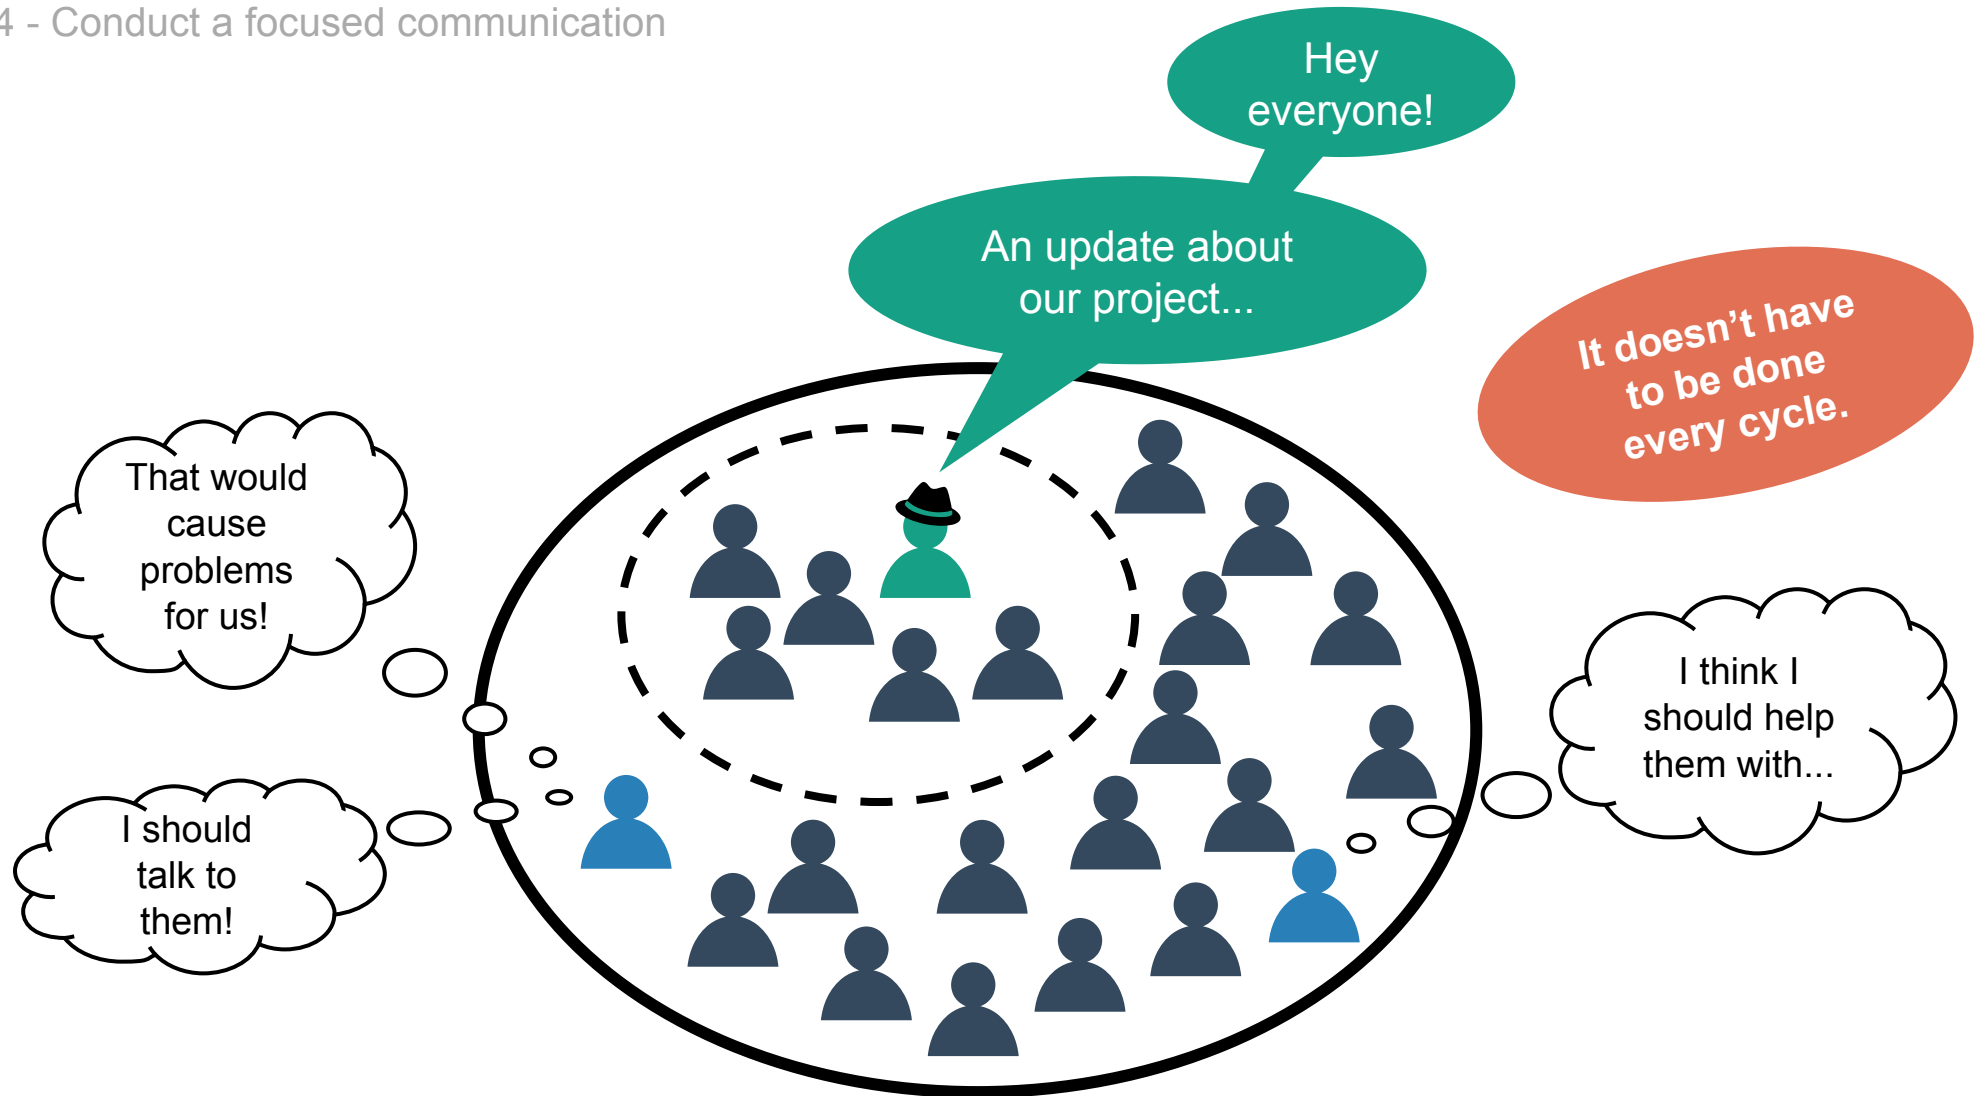

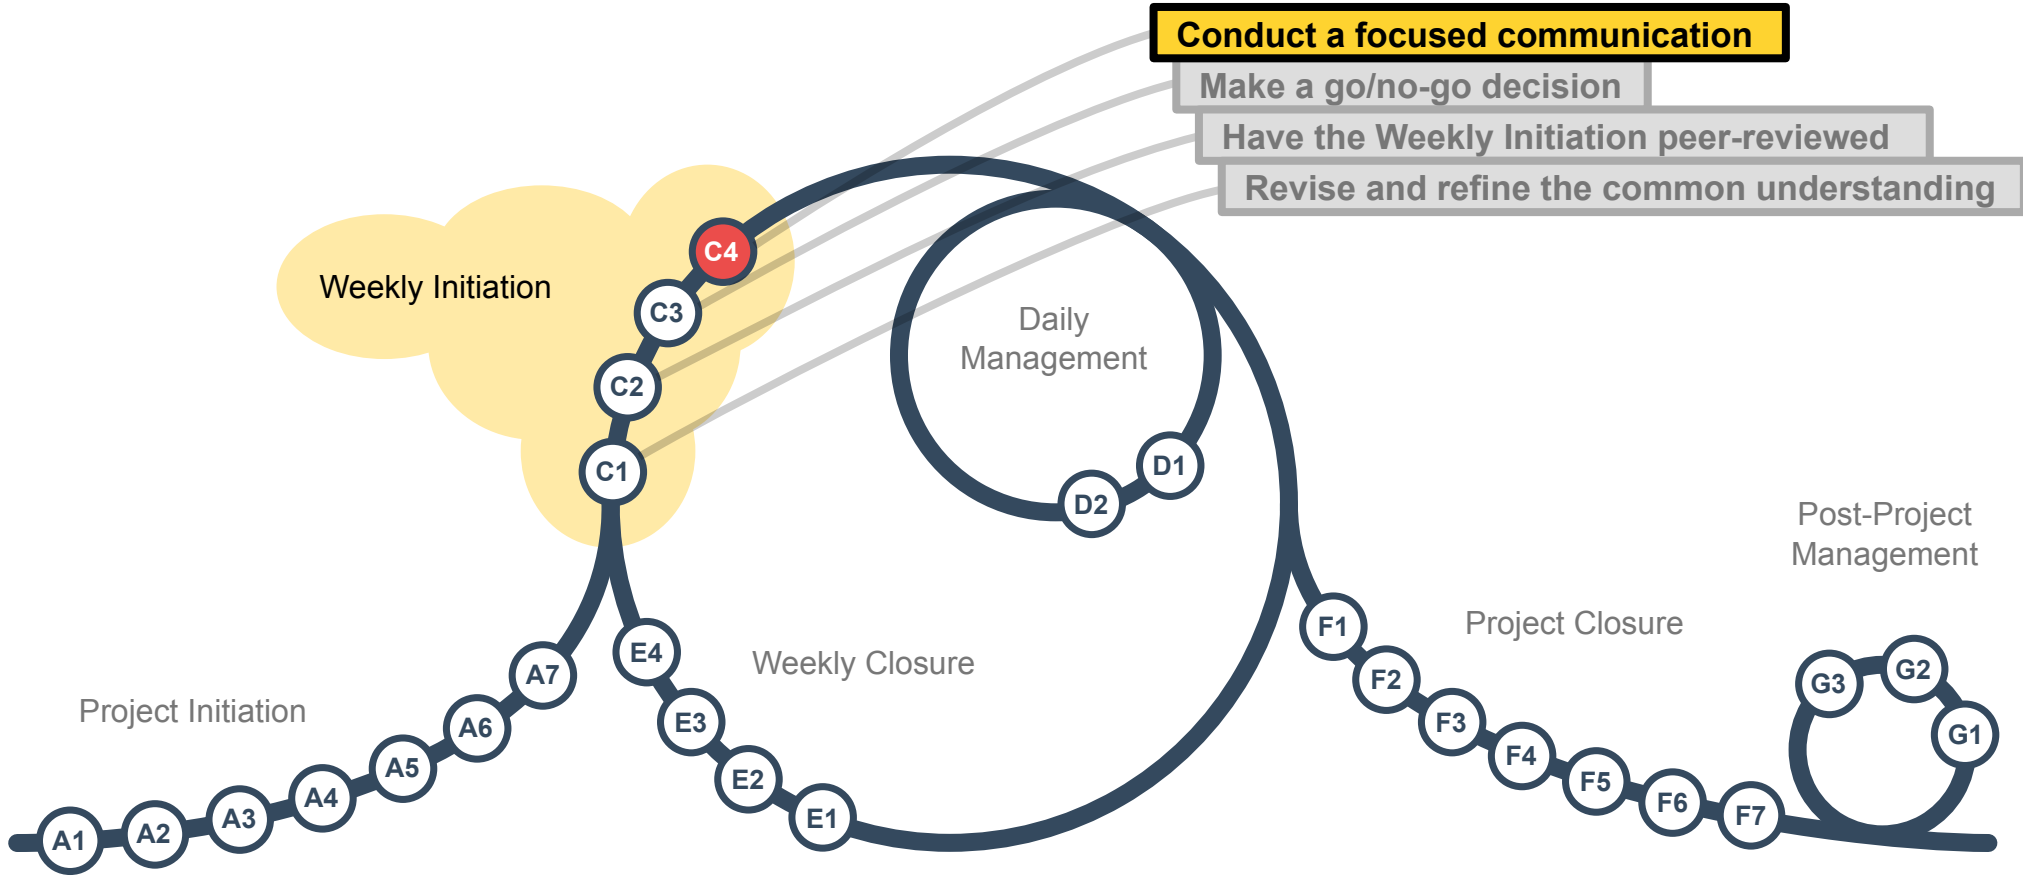

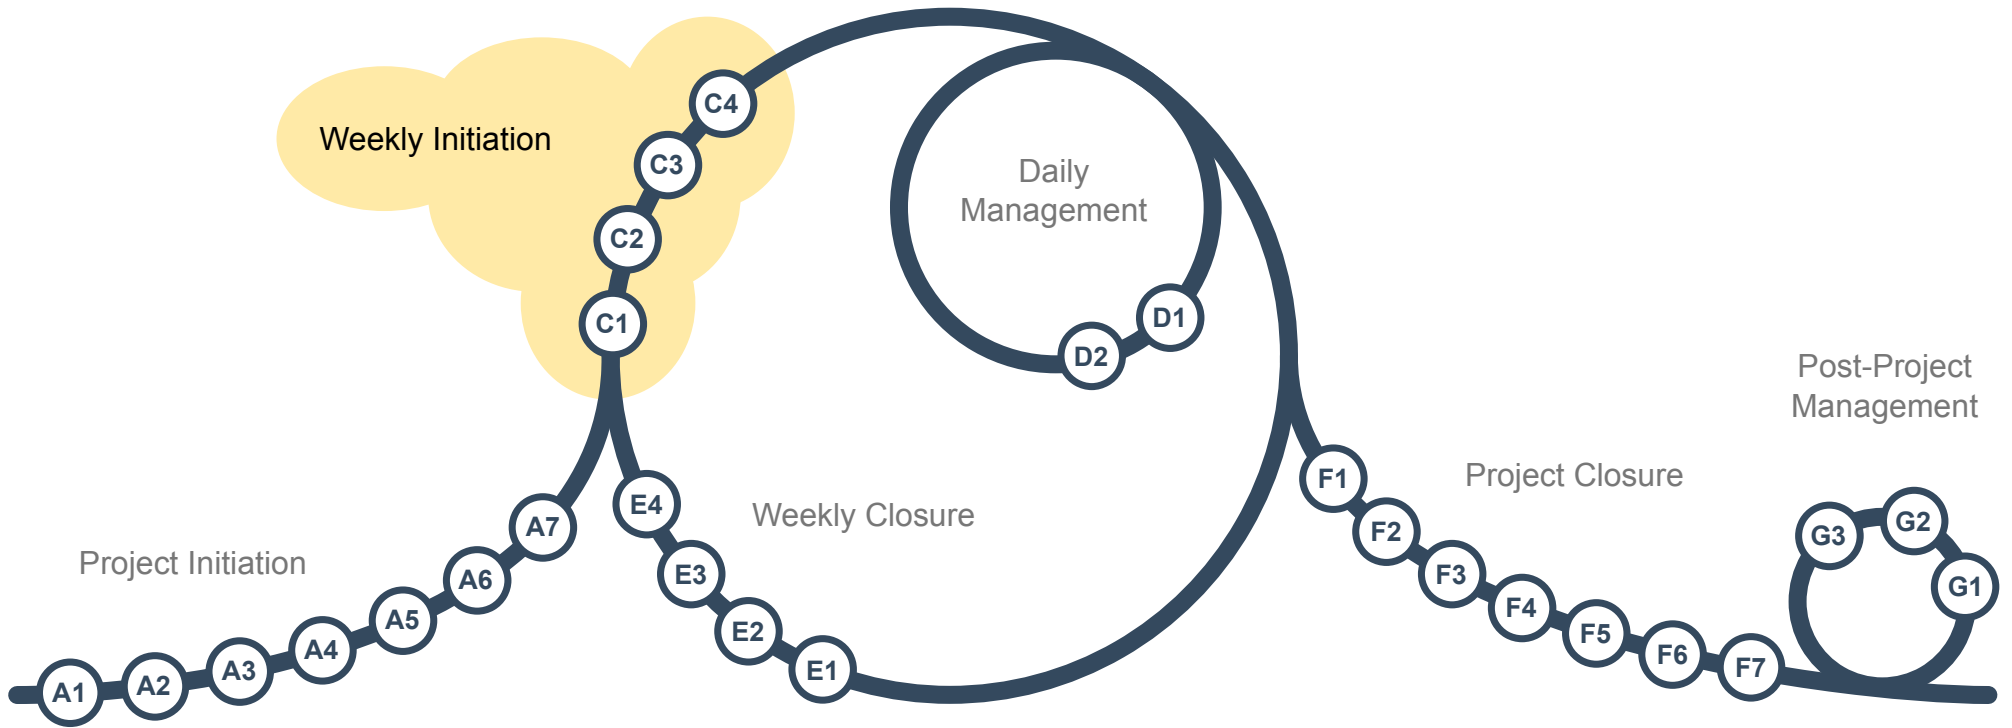


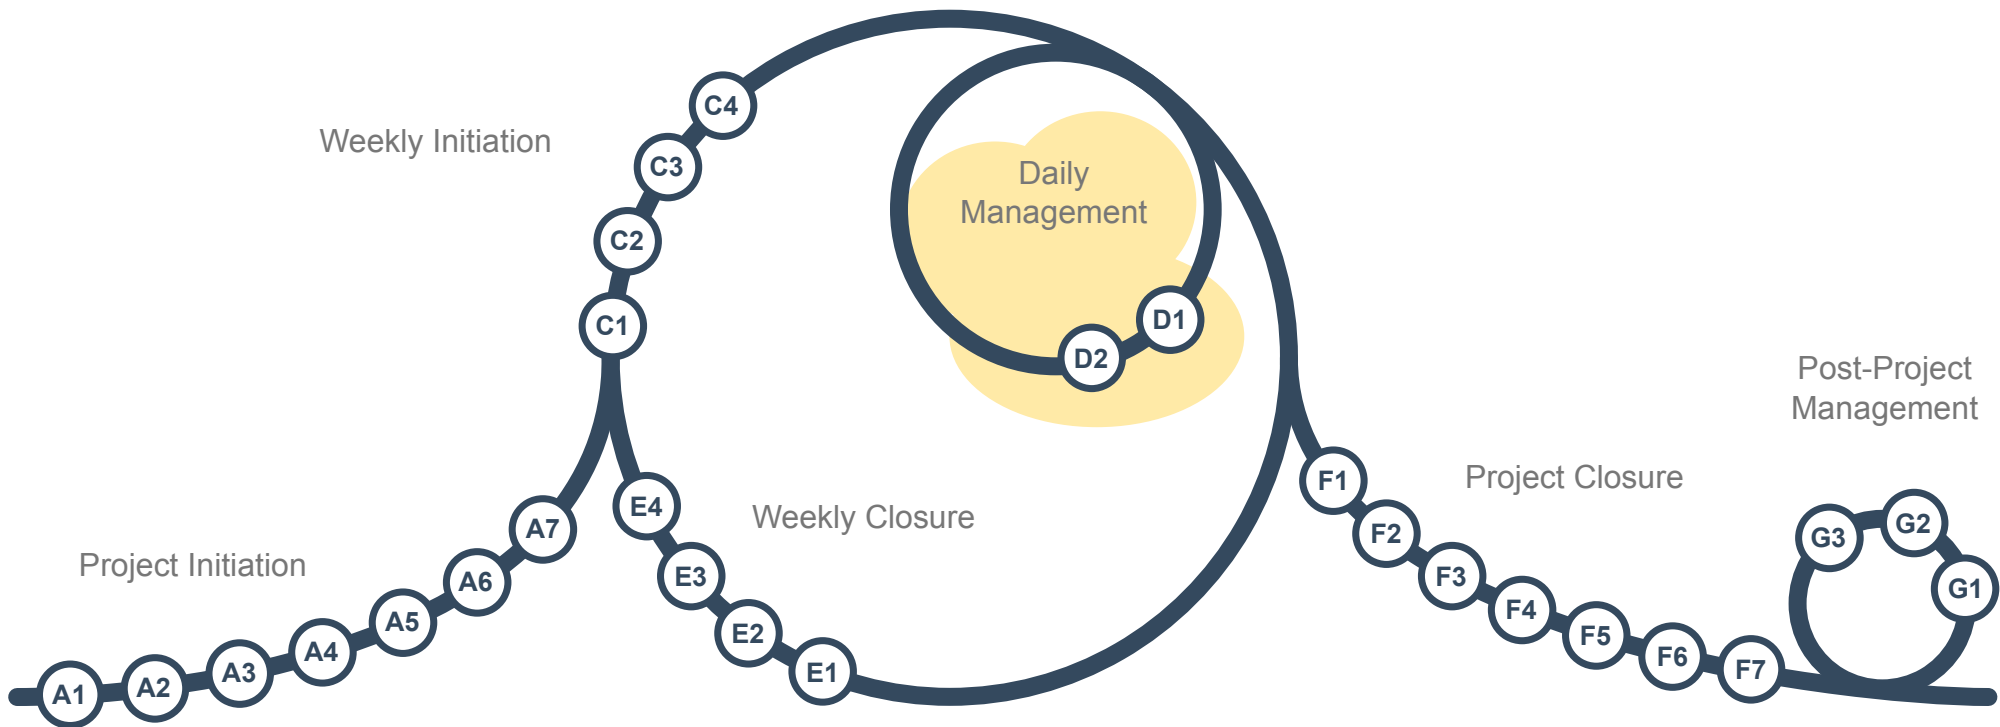

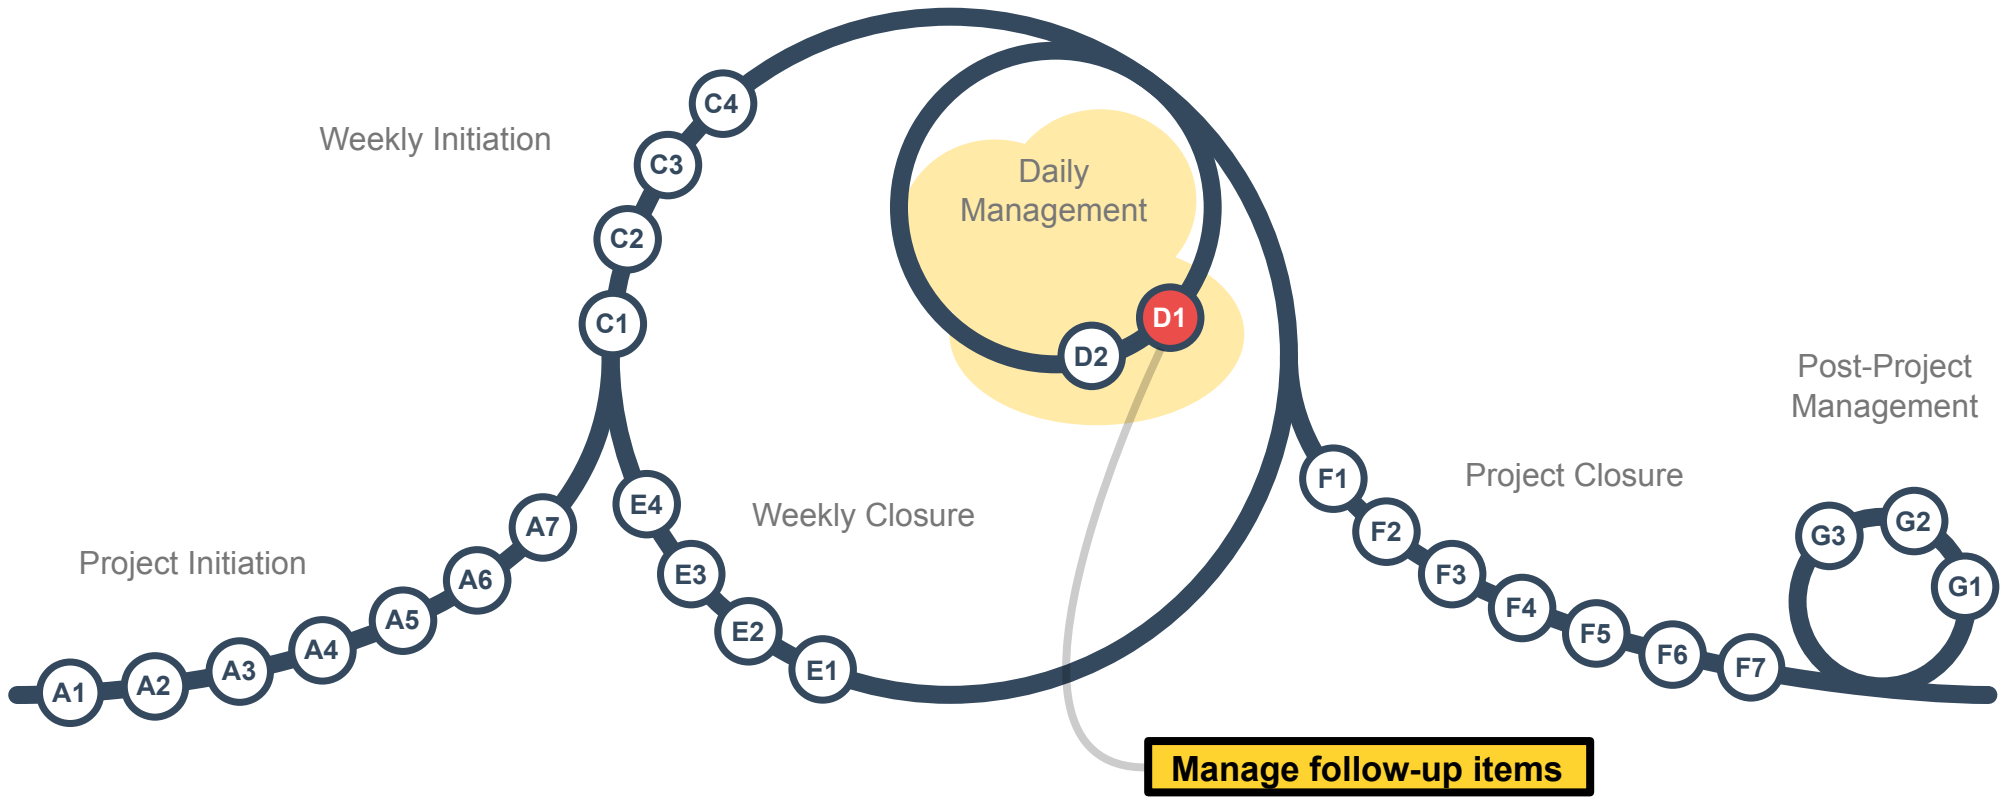


Manage follow-up items


Integrated Project Board

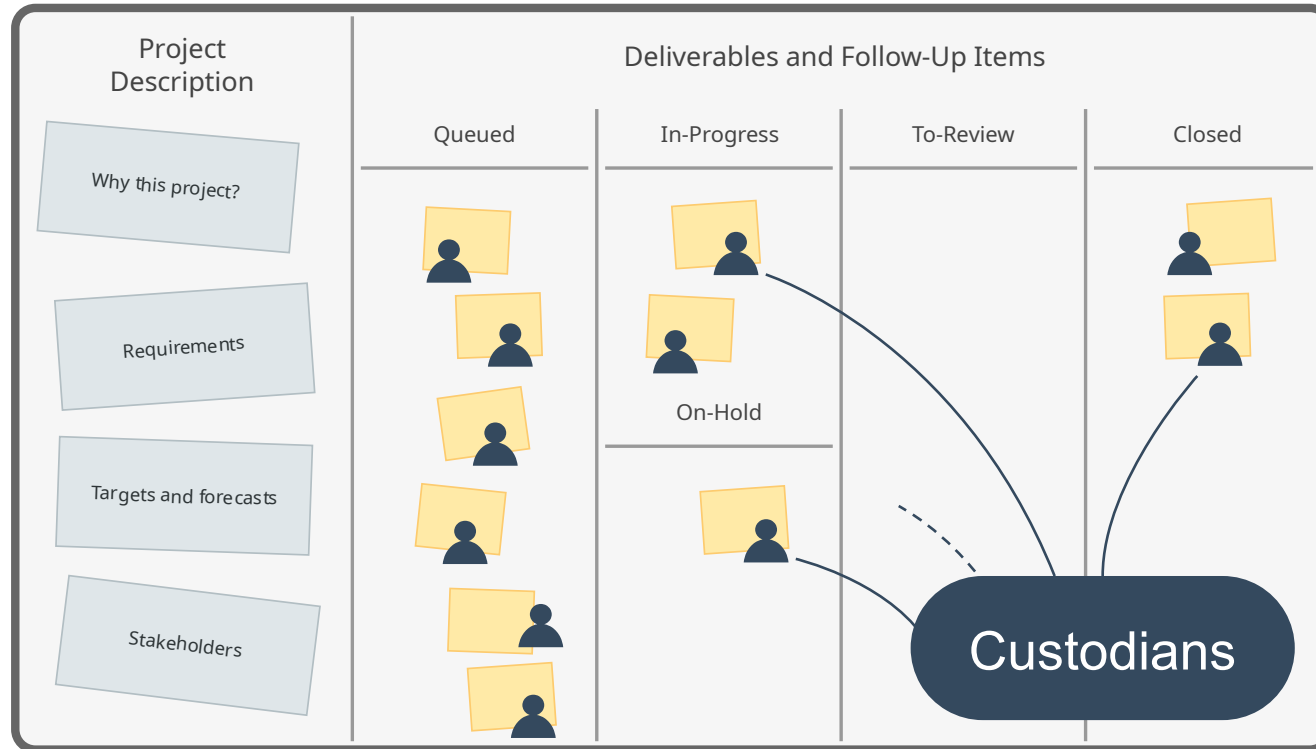

Integrated Project Board

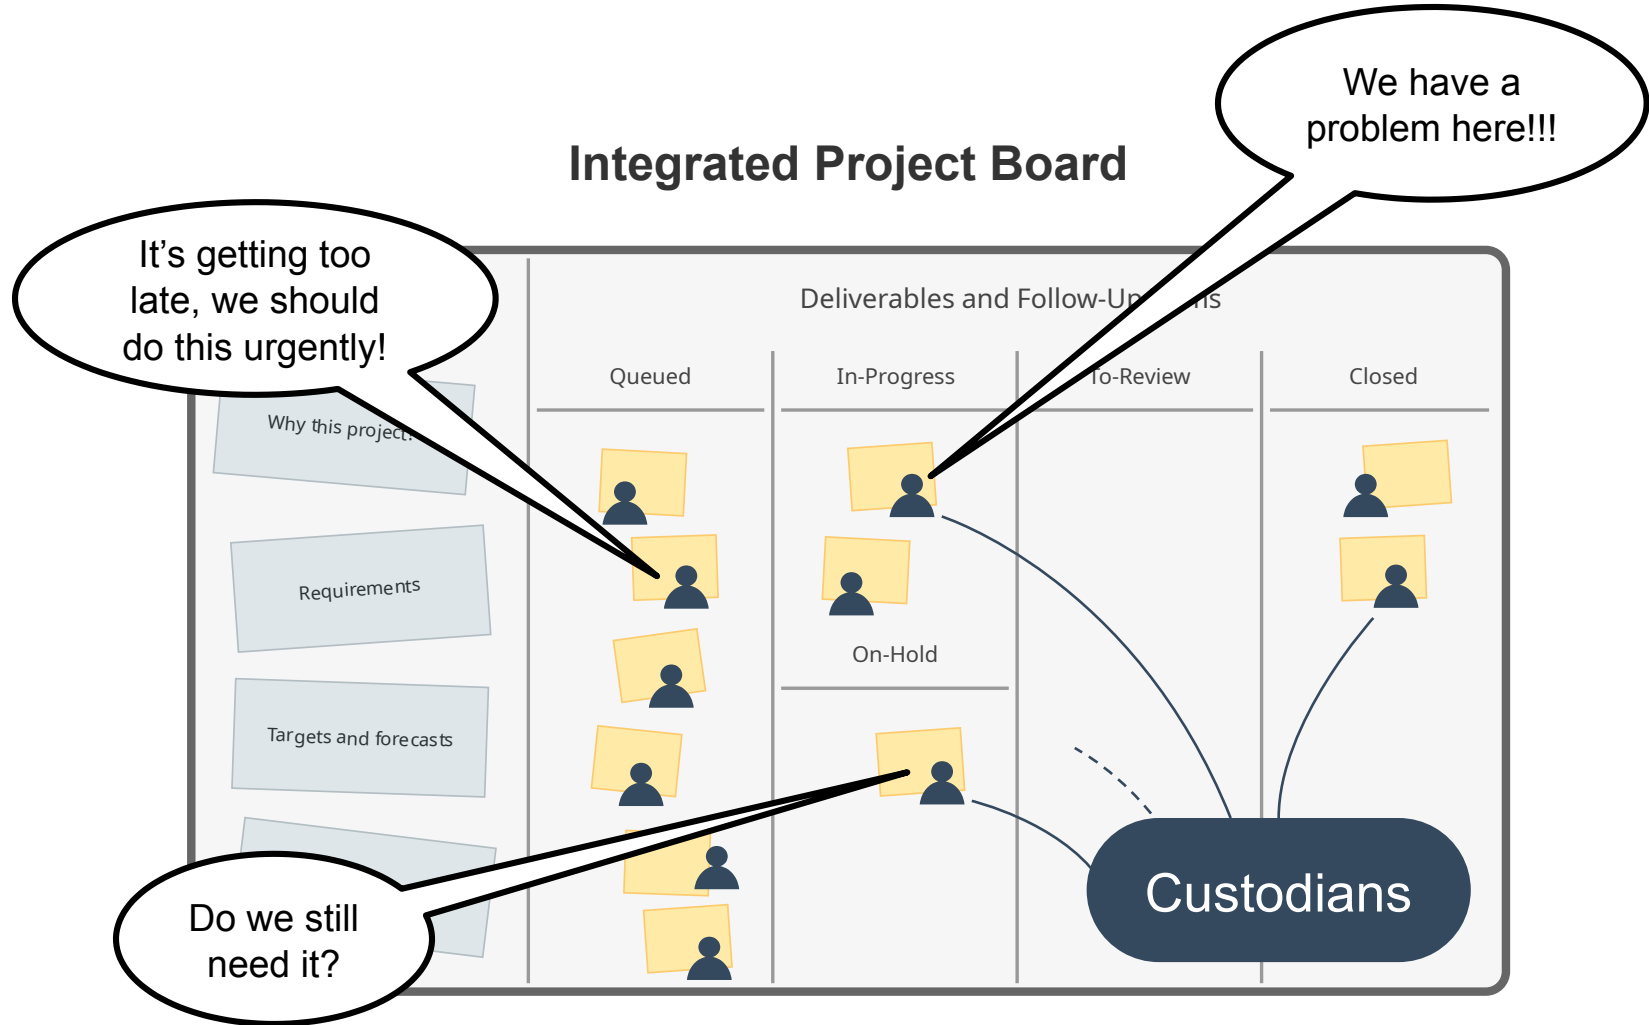

D1 – Manage follow-up items

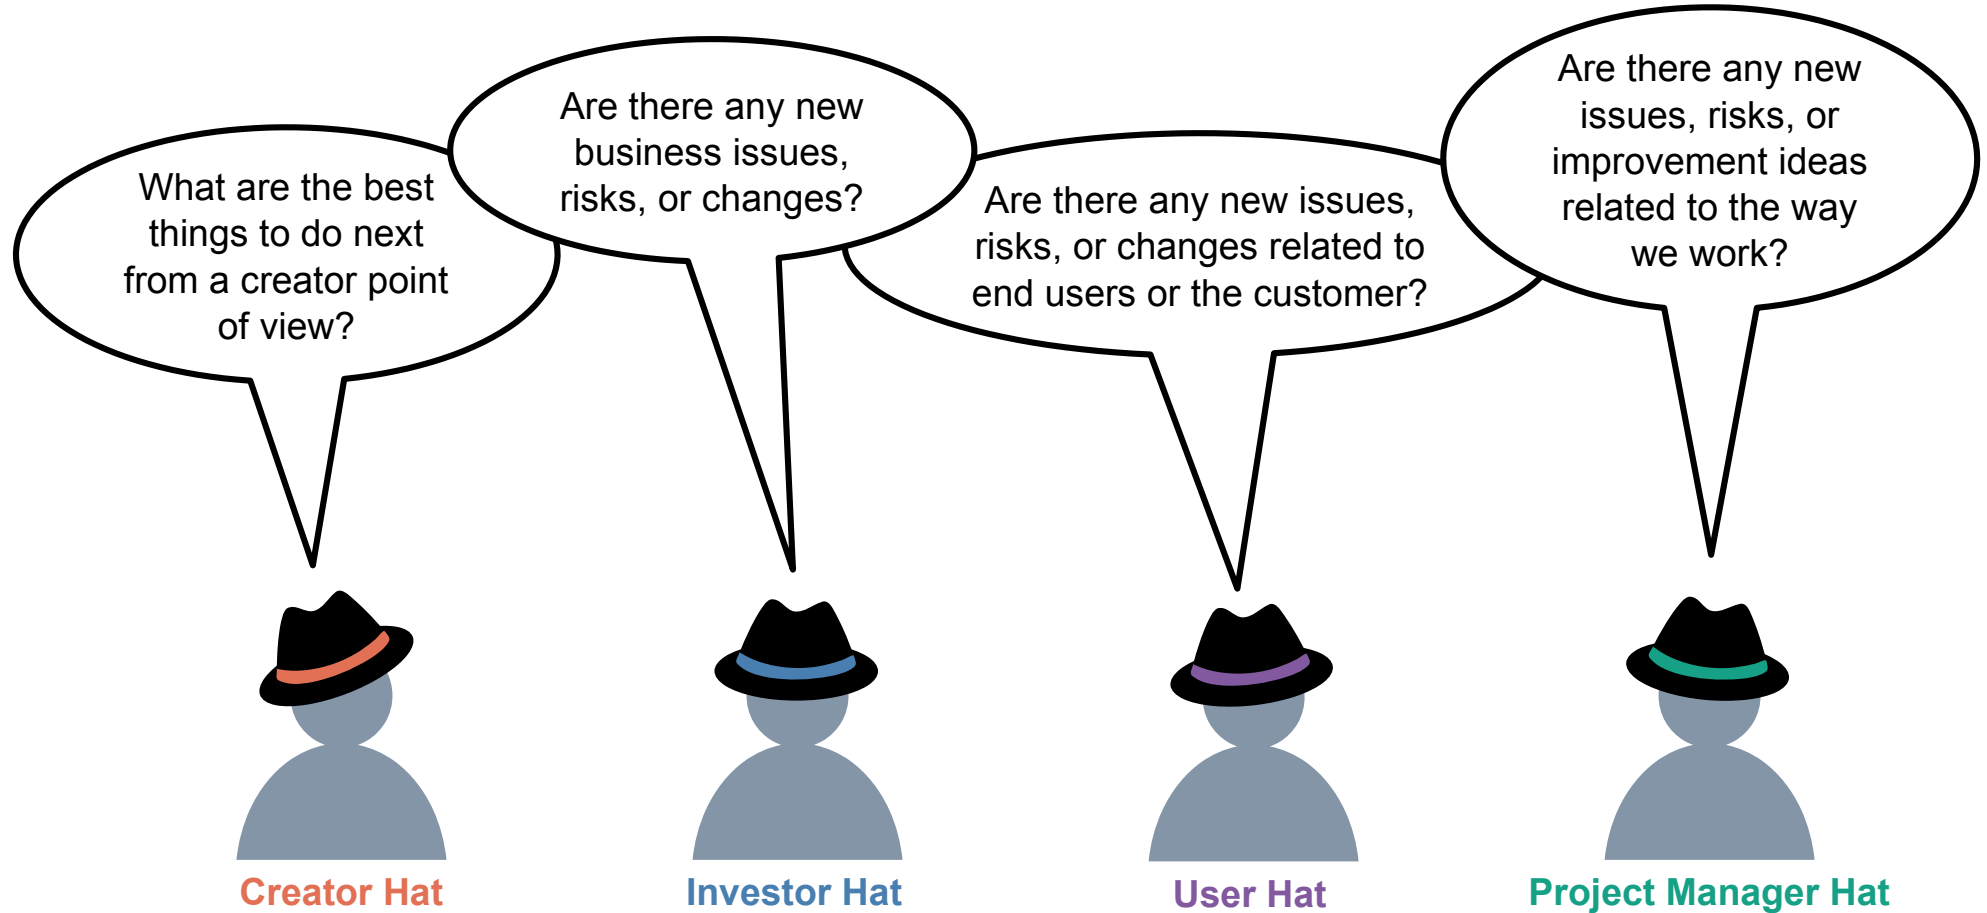


D1 – Manage follow-up items




Project Manager Hat

D1 – Manage follow-up items




**Are the documents
clear and easy to
understand?**

Project Manager Hat

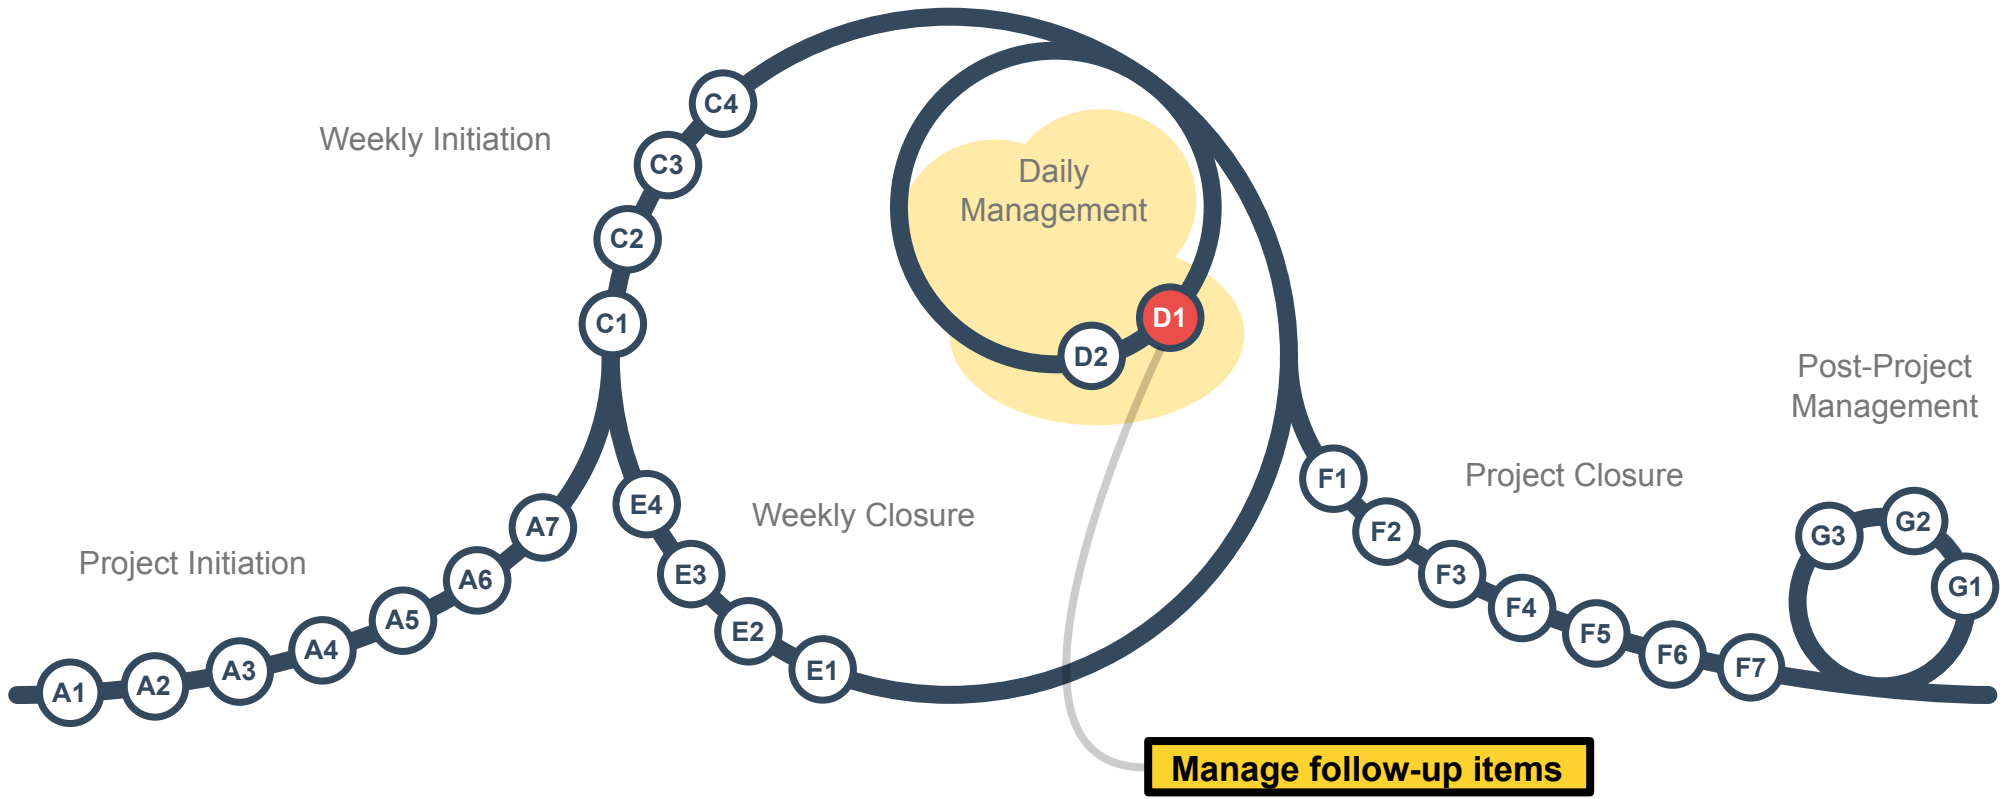

Manage follow-up items

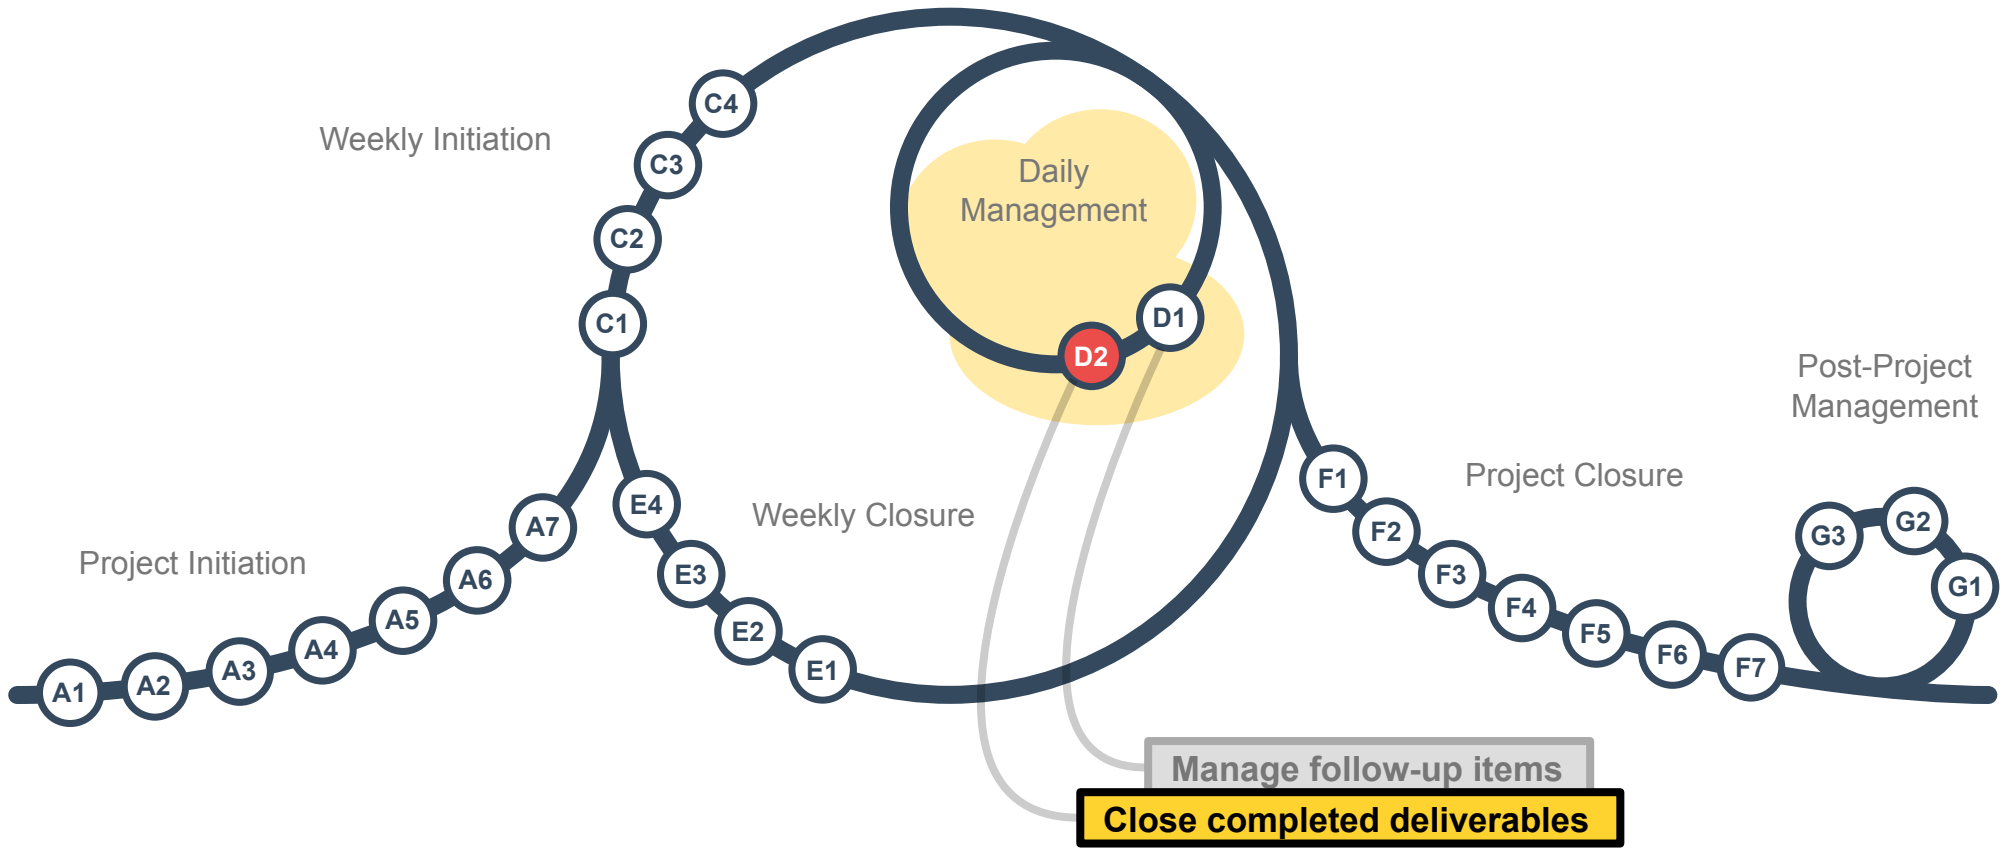

Weekly Initiation

Daily Management

Post-Project Management

Project Initiation


Weekly Closure

Project Closure


Manage follow-up items

Close completed deliverables

Integrated Project Board

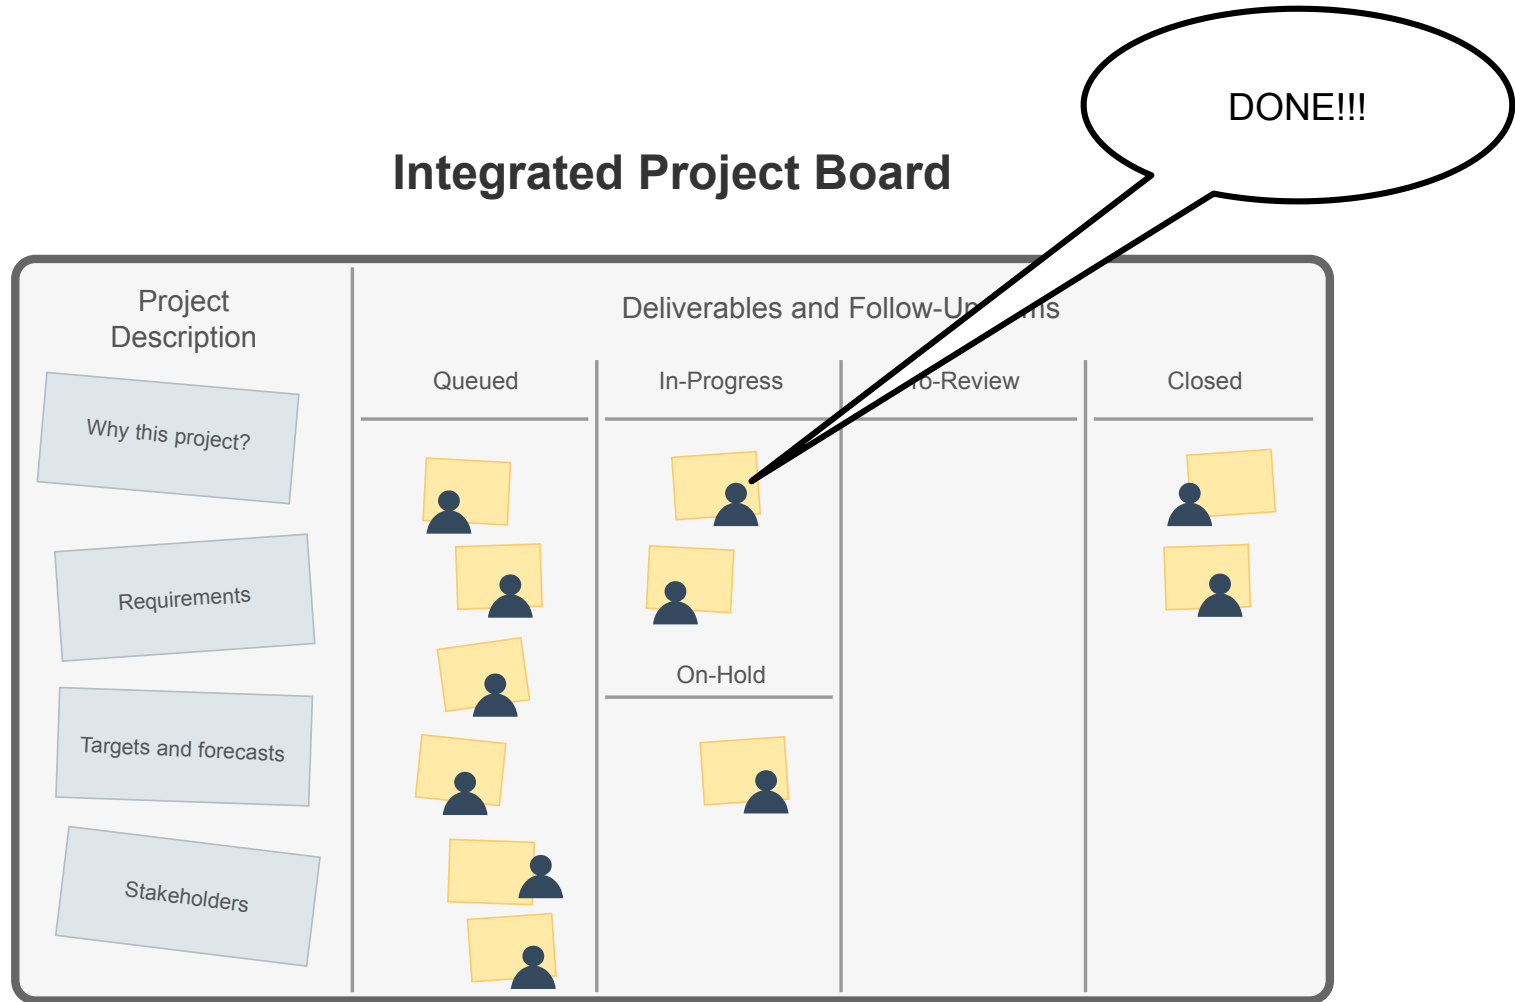


Integrated Project Board

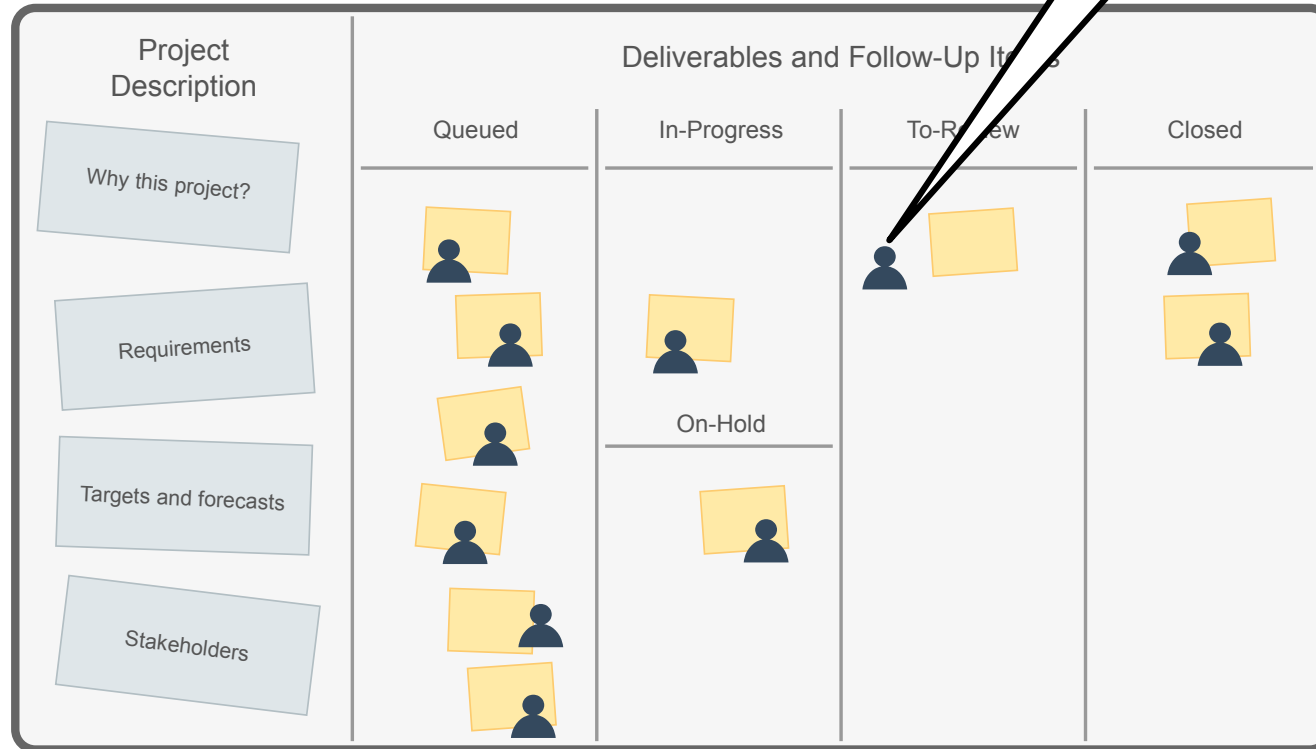


Integrated Project Board

The whole team or a subset of it reviews the card

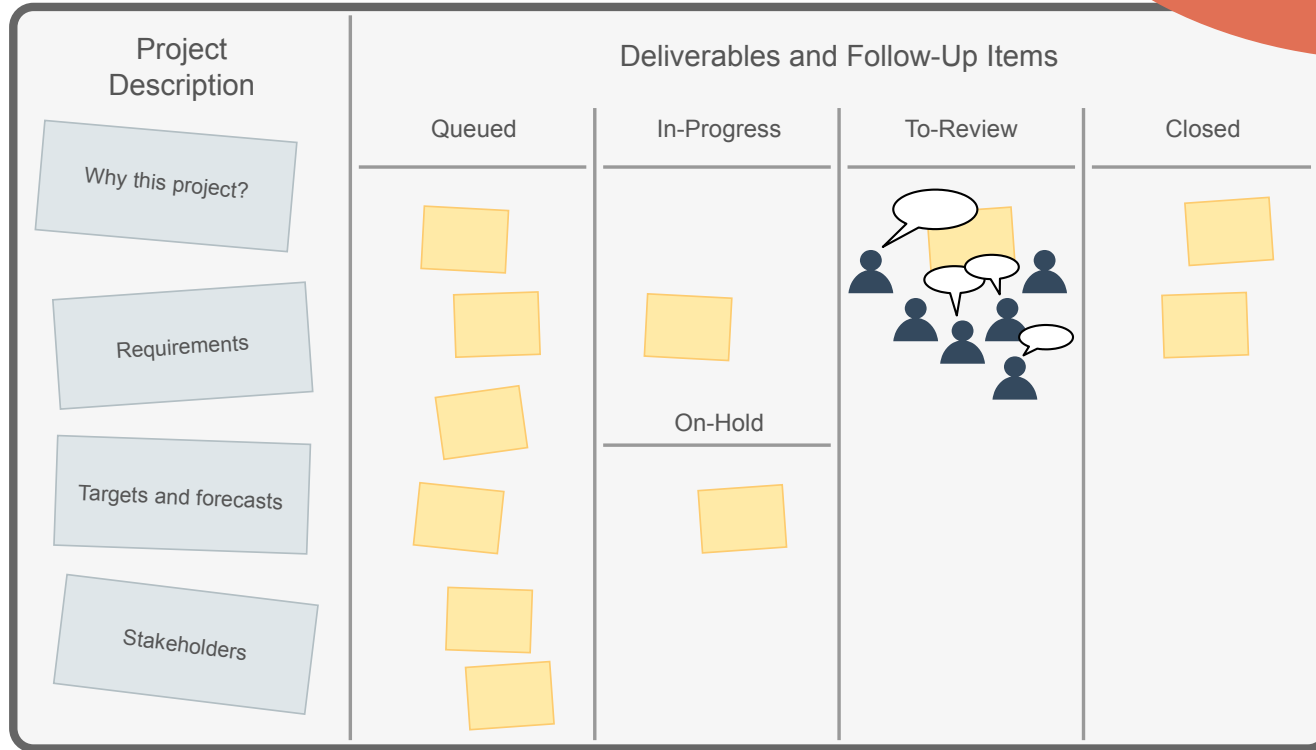


Integrated Project Board

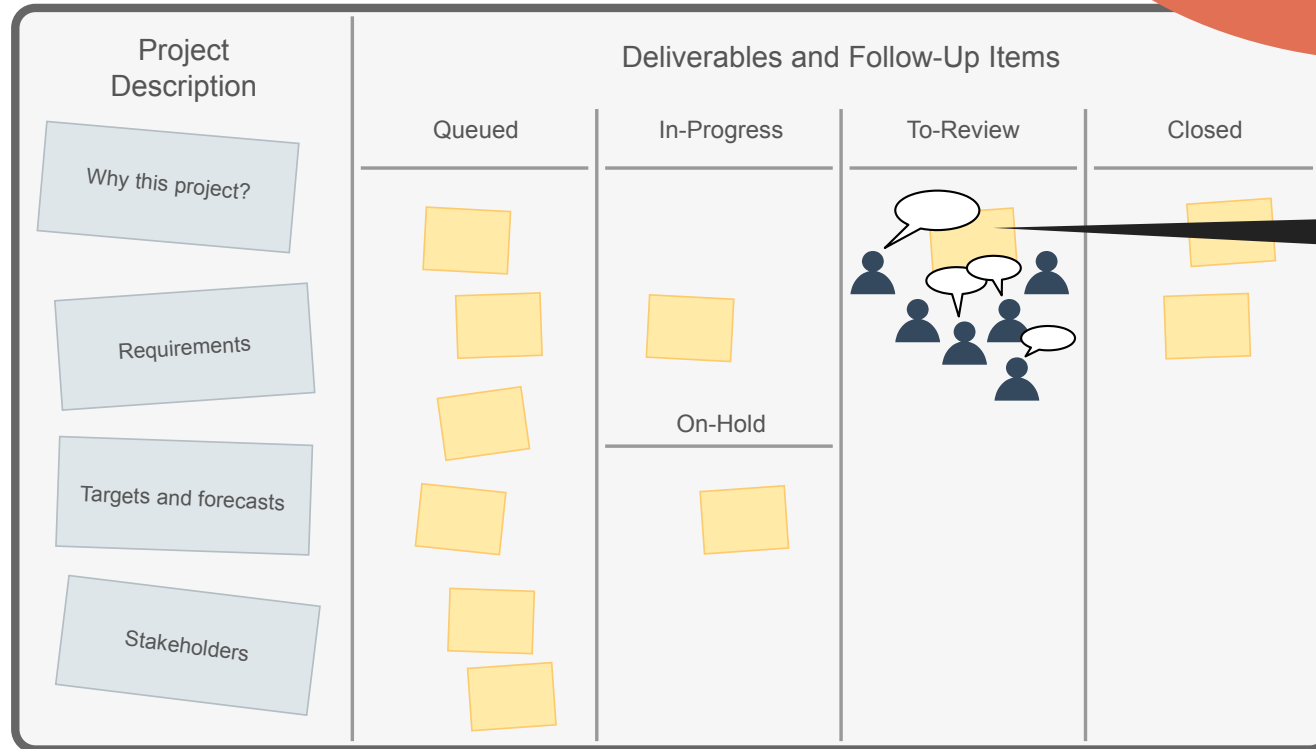


The whole team or a subset of it reviews the card

Acceptance criteria

Integrated Project Board

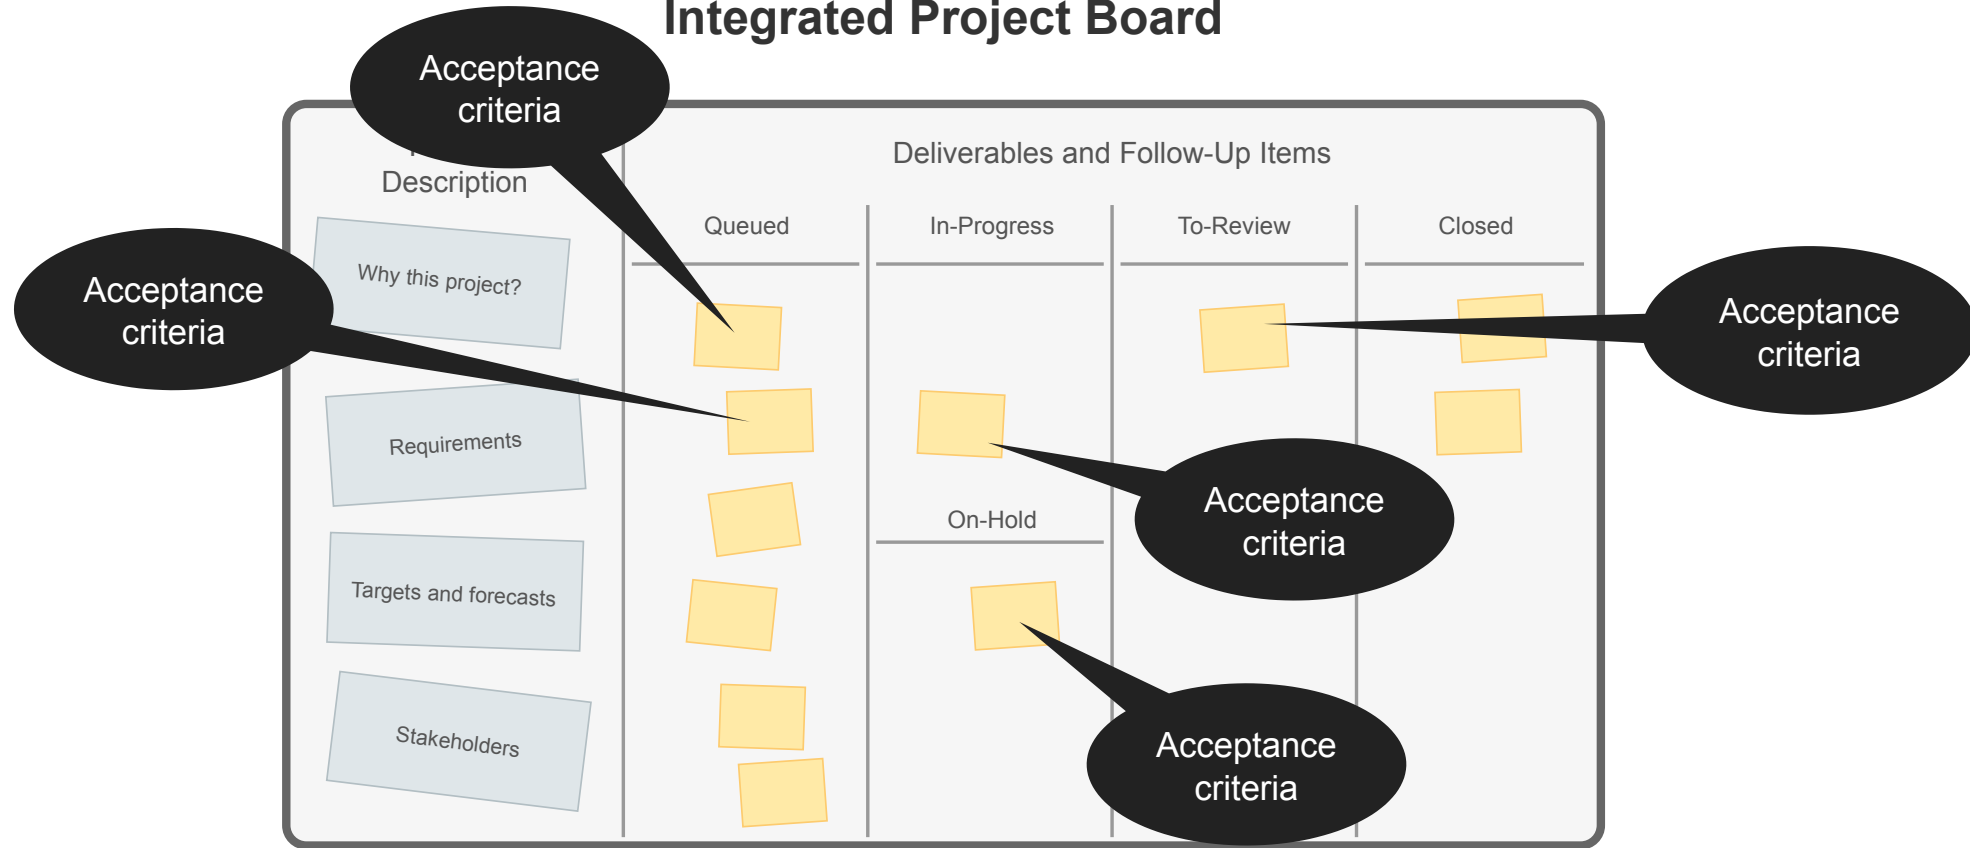


Integrated Project Board

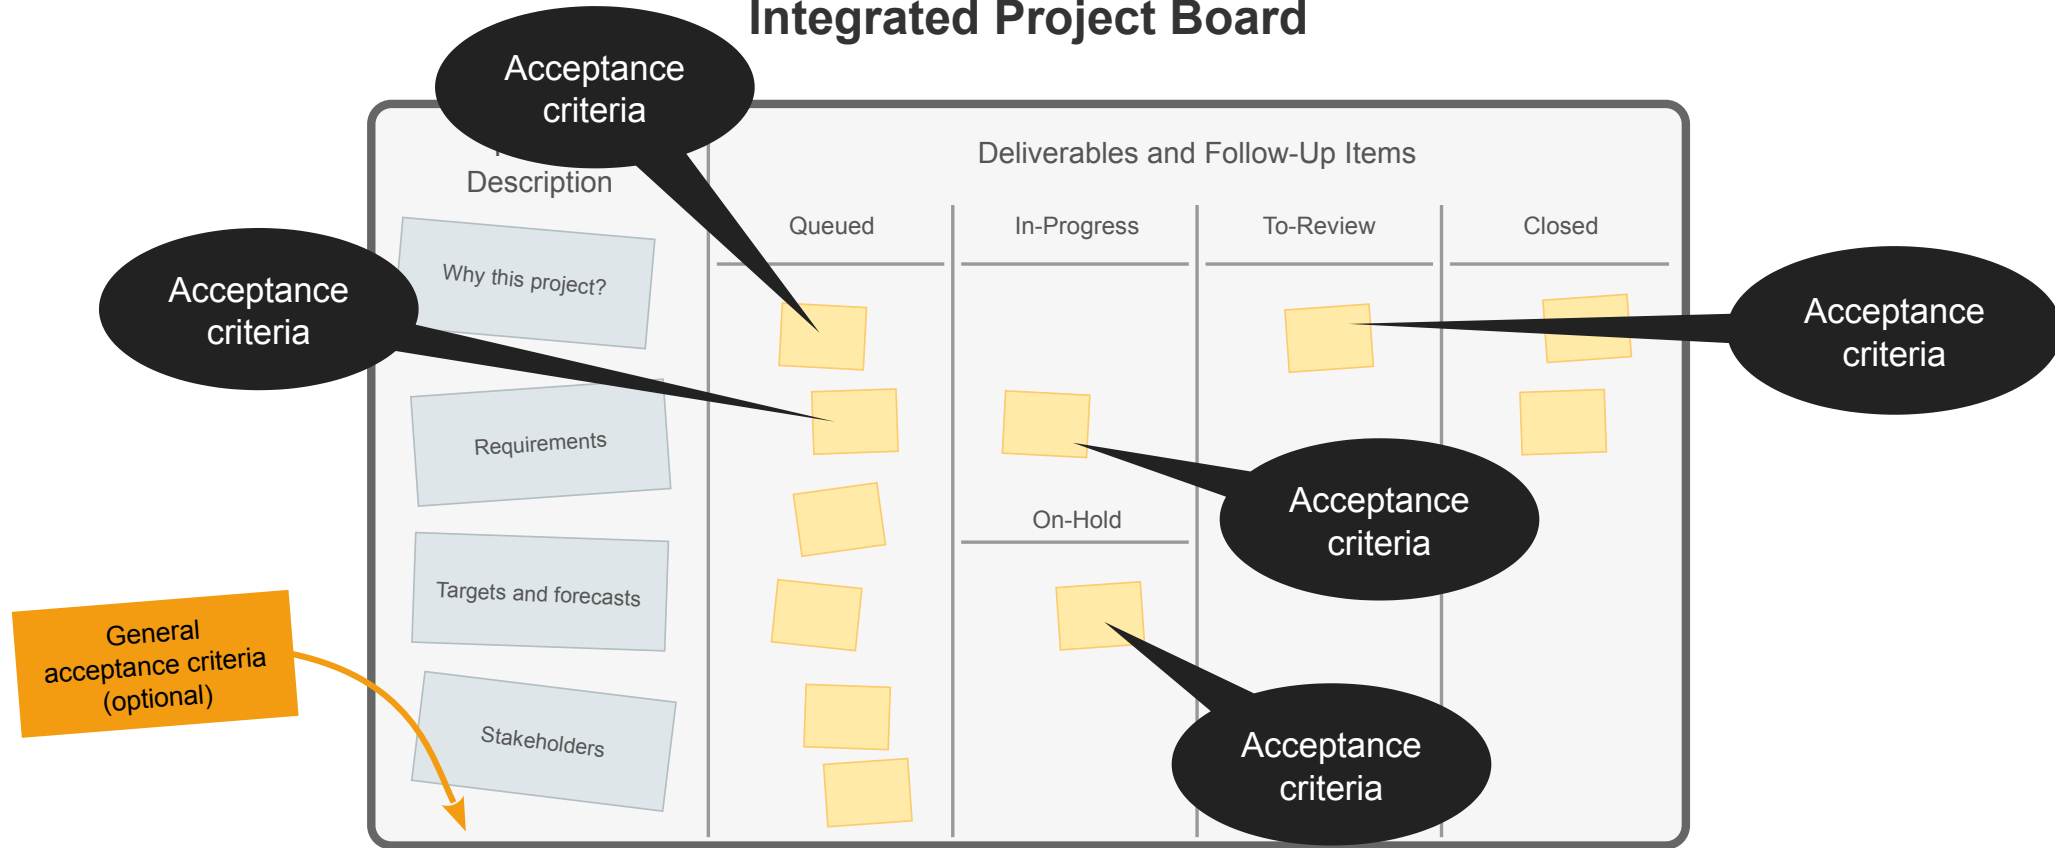


Integrated Project Board


The whole team or a subset of it reviews the card

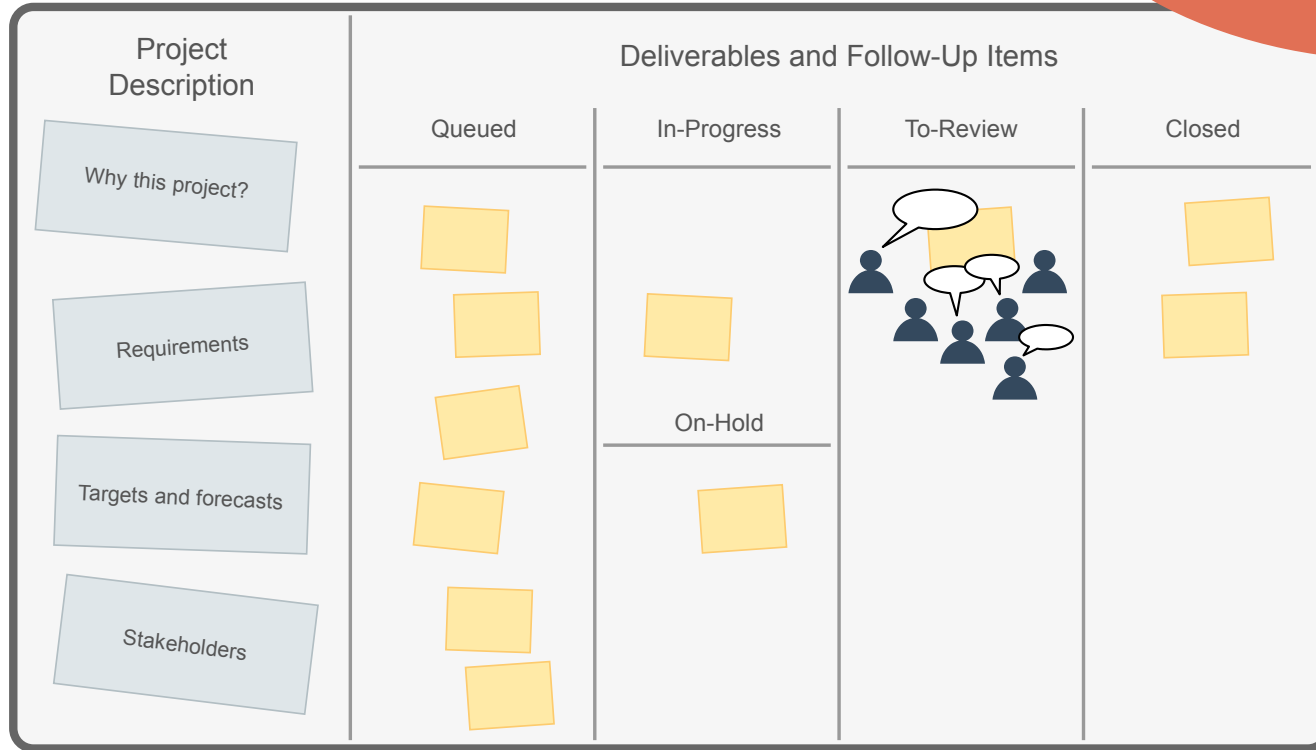


Integrated Project Board

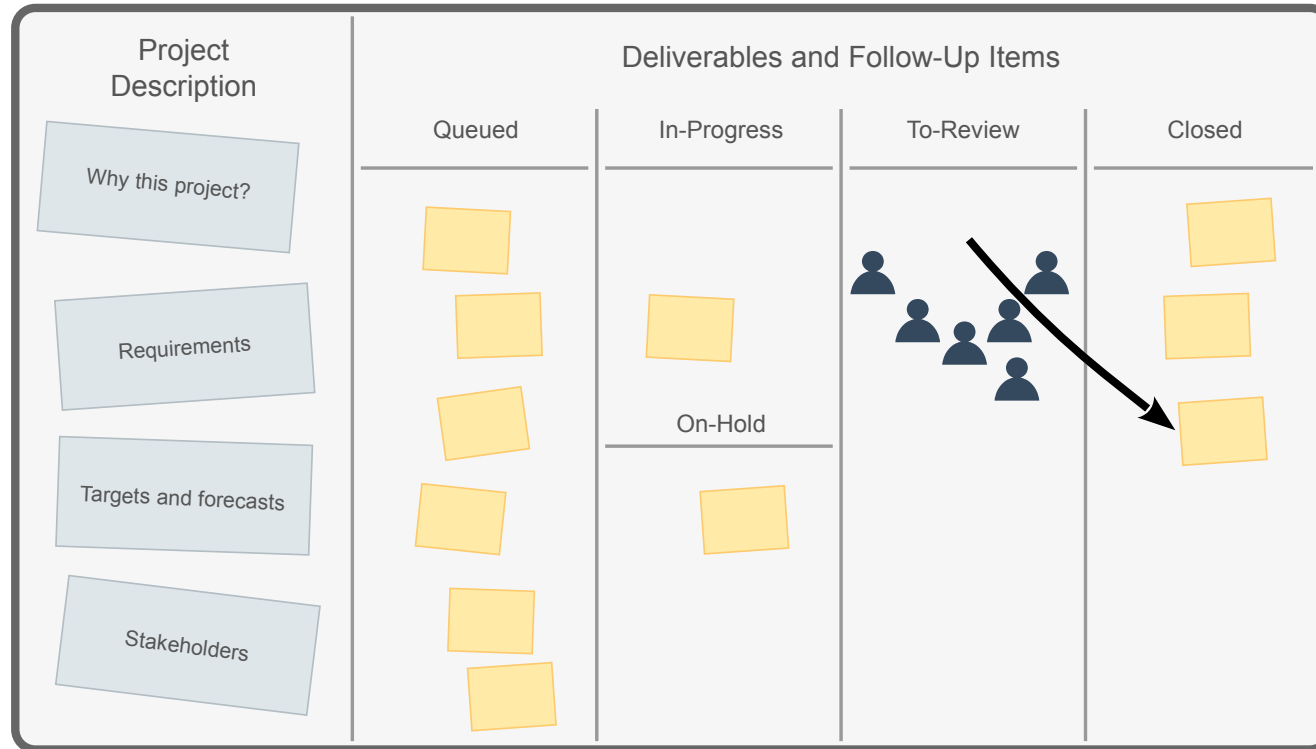


D2 – Close completed deliverables

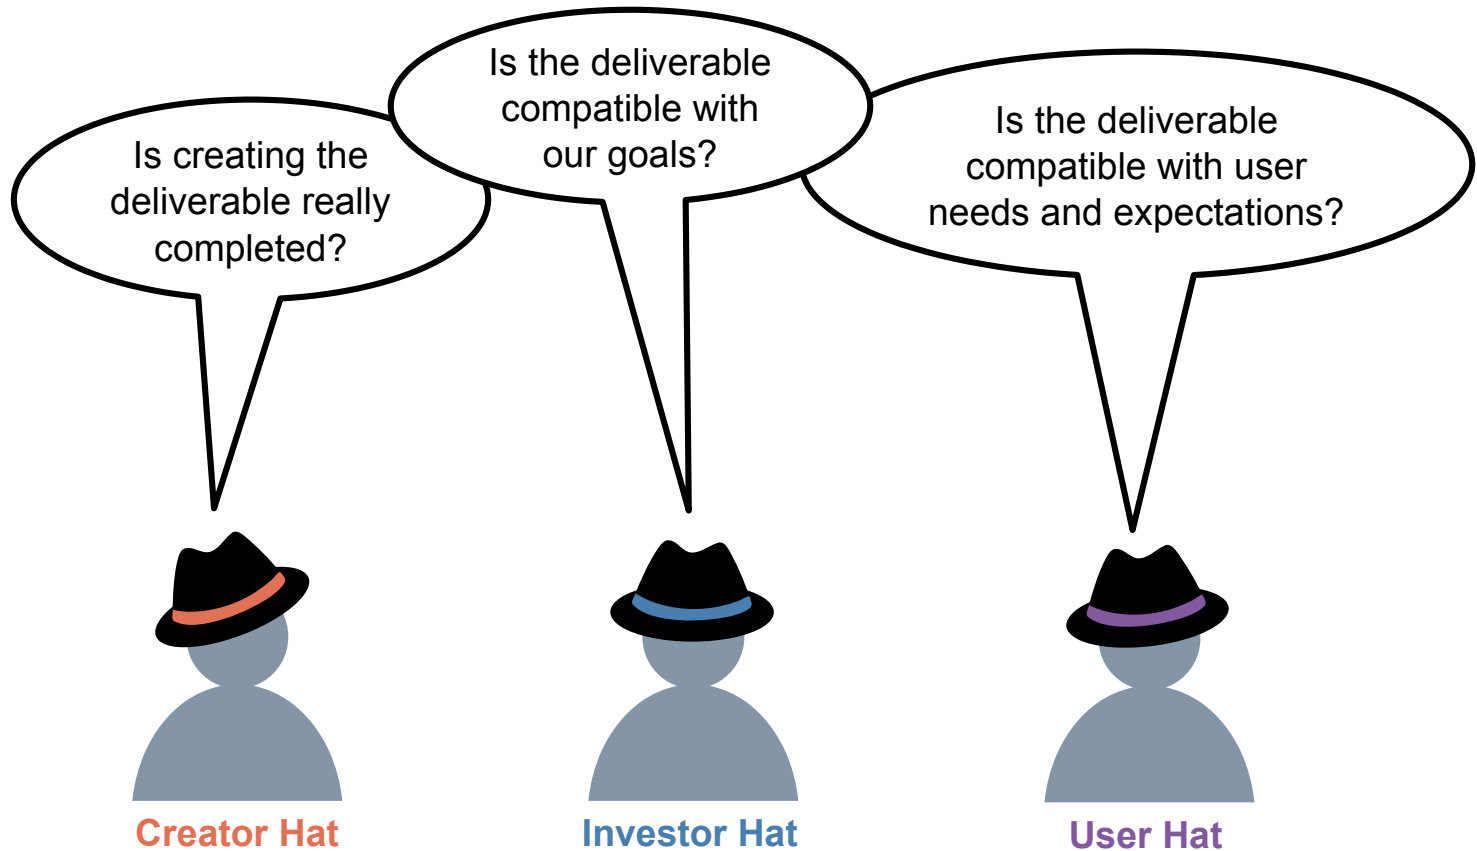

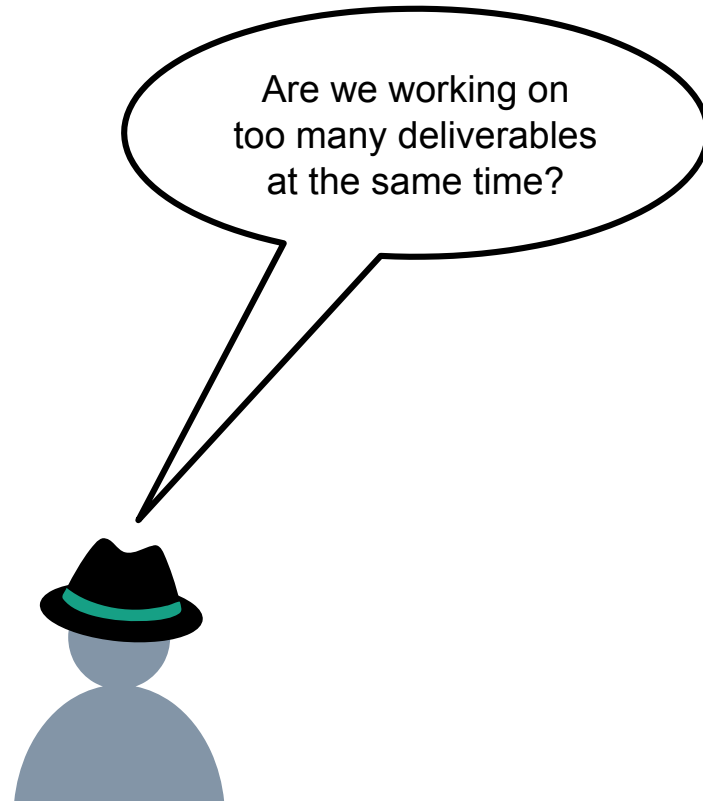



Project Manager Hat




**Are the documents
clear and easy to
understand?**

Project Manager Hat

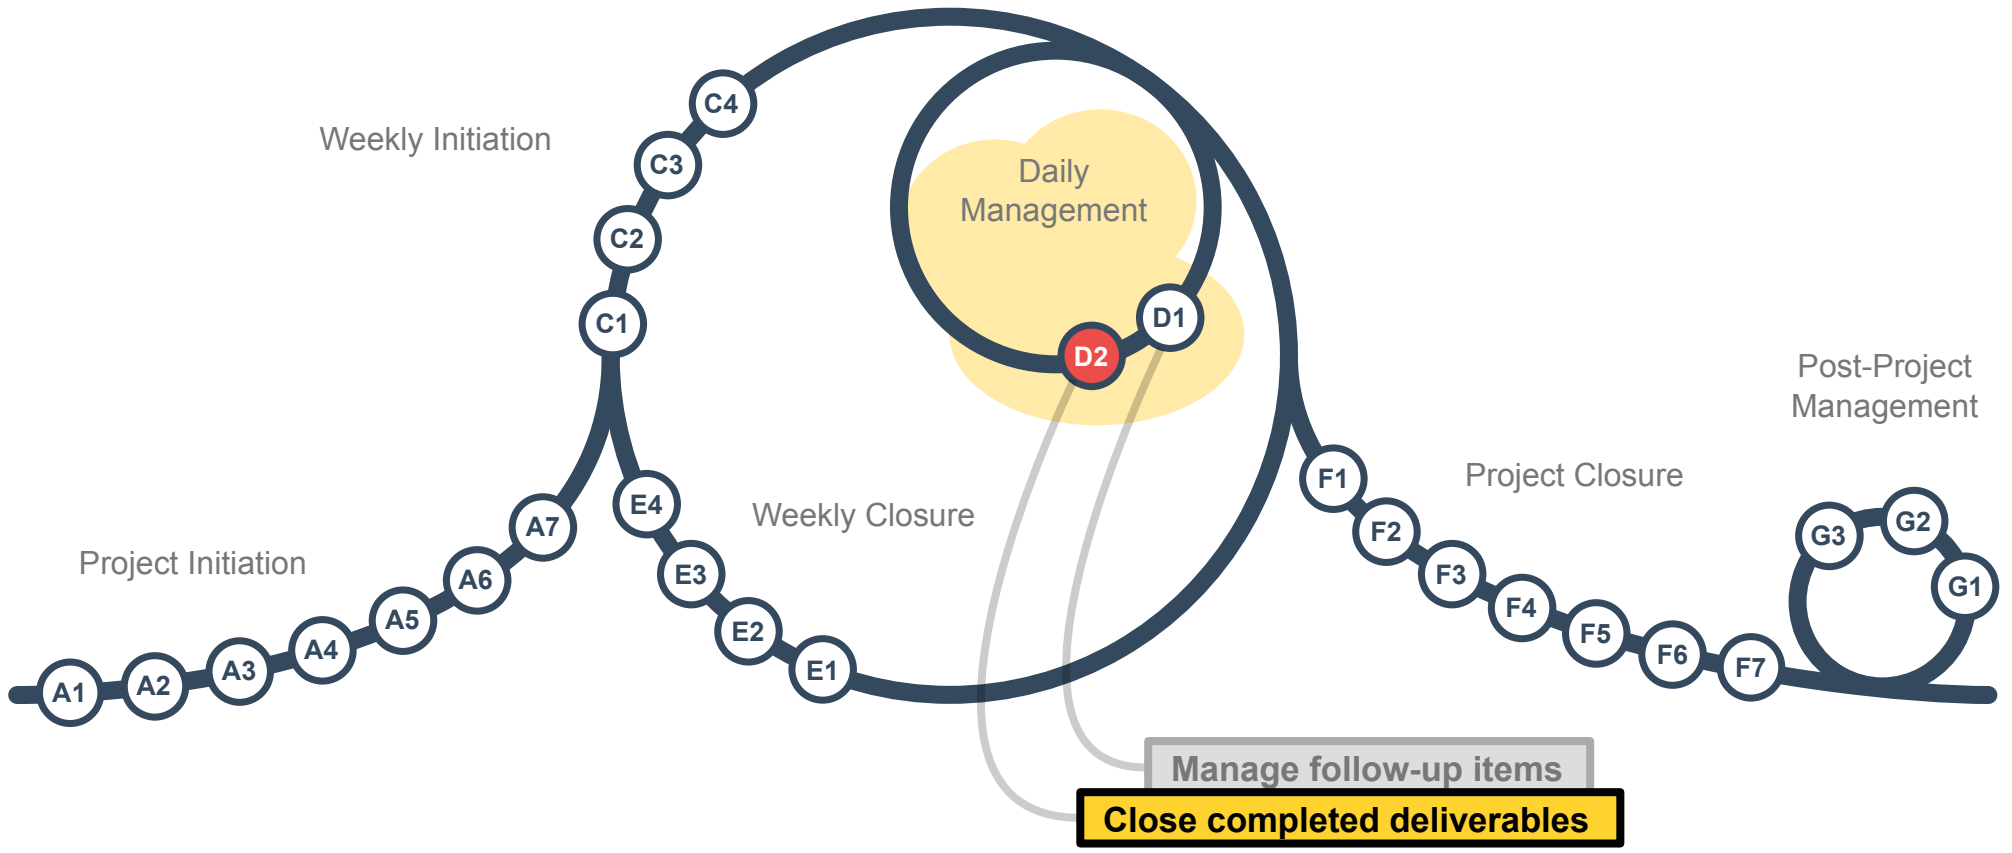

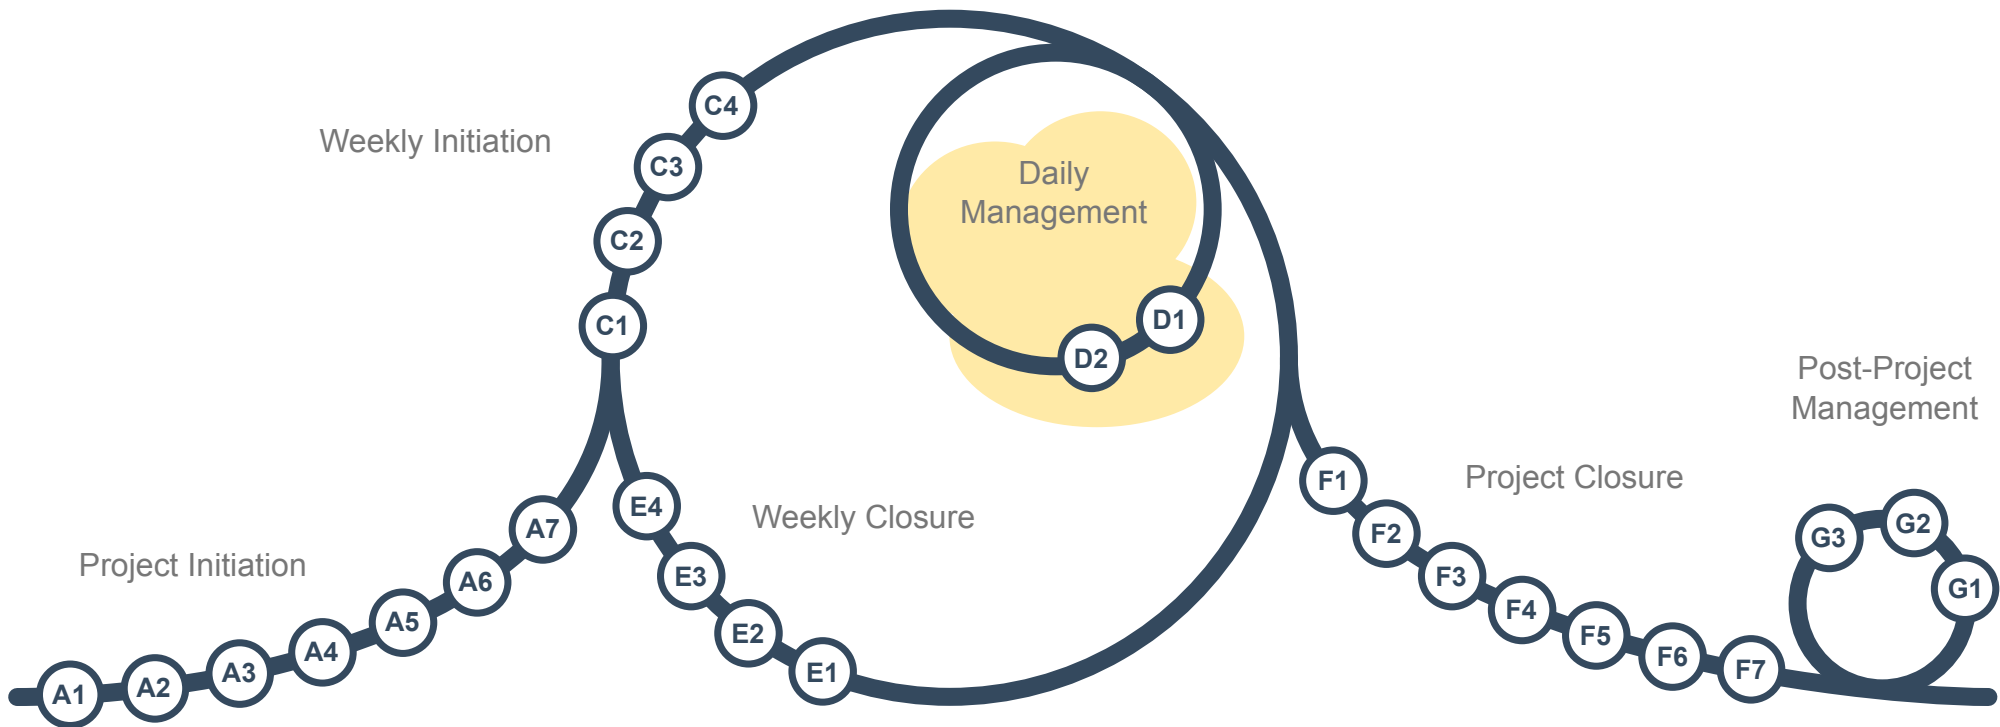

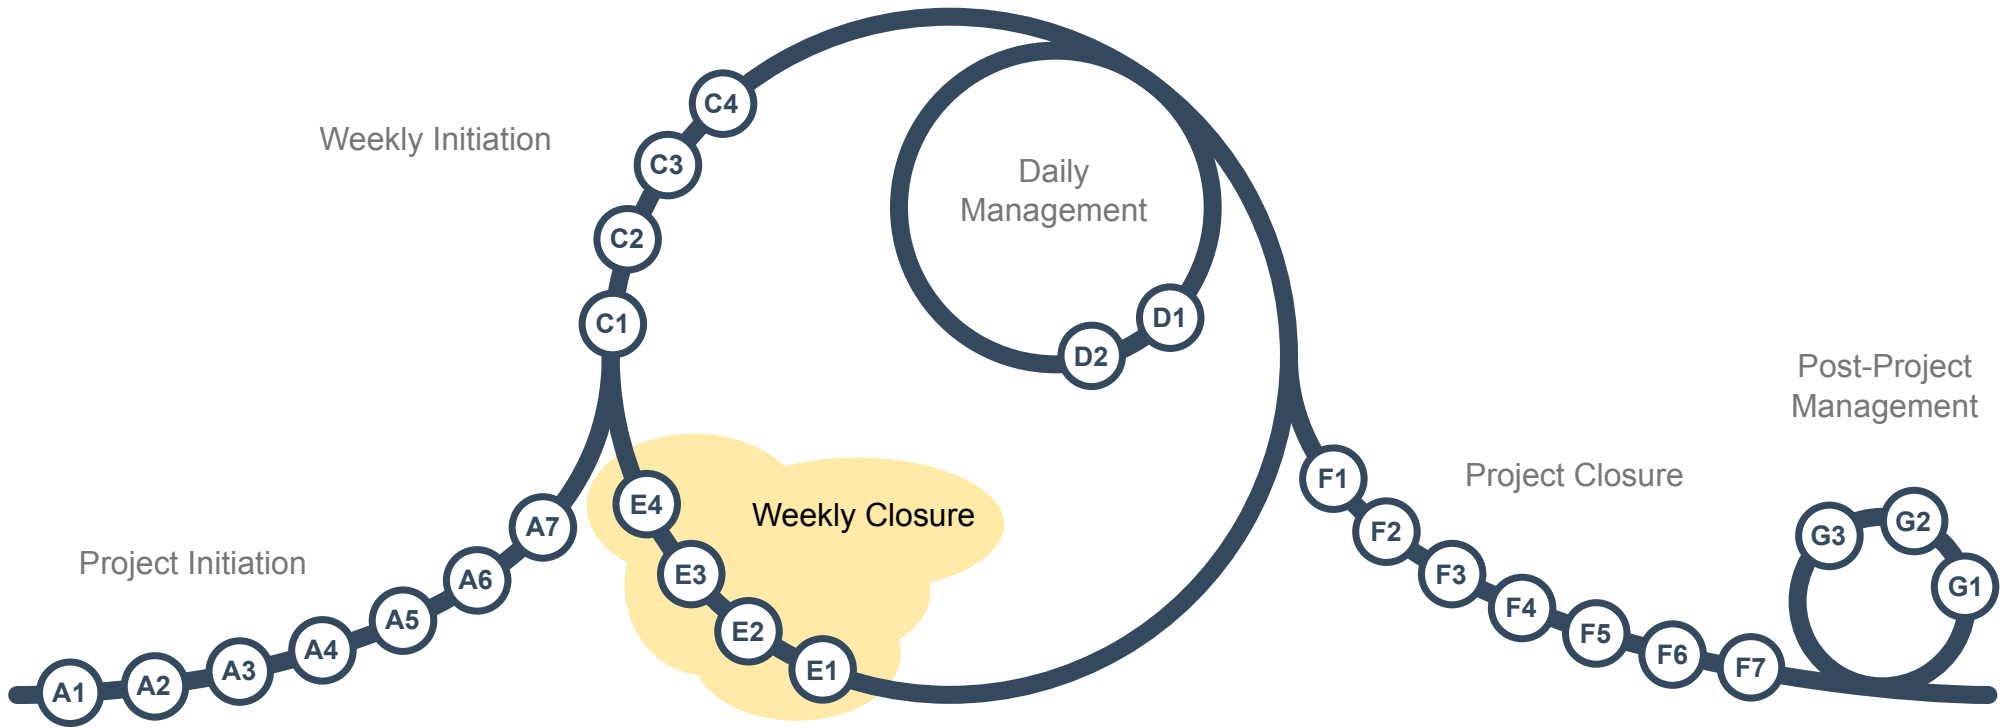

Weekly Initiation

Daily Management

Post-Project Management

Project Closure

Weekly Closure

Project Initiation

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C1

C2

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6

F7

G3

G2

G1

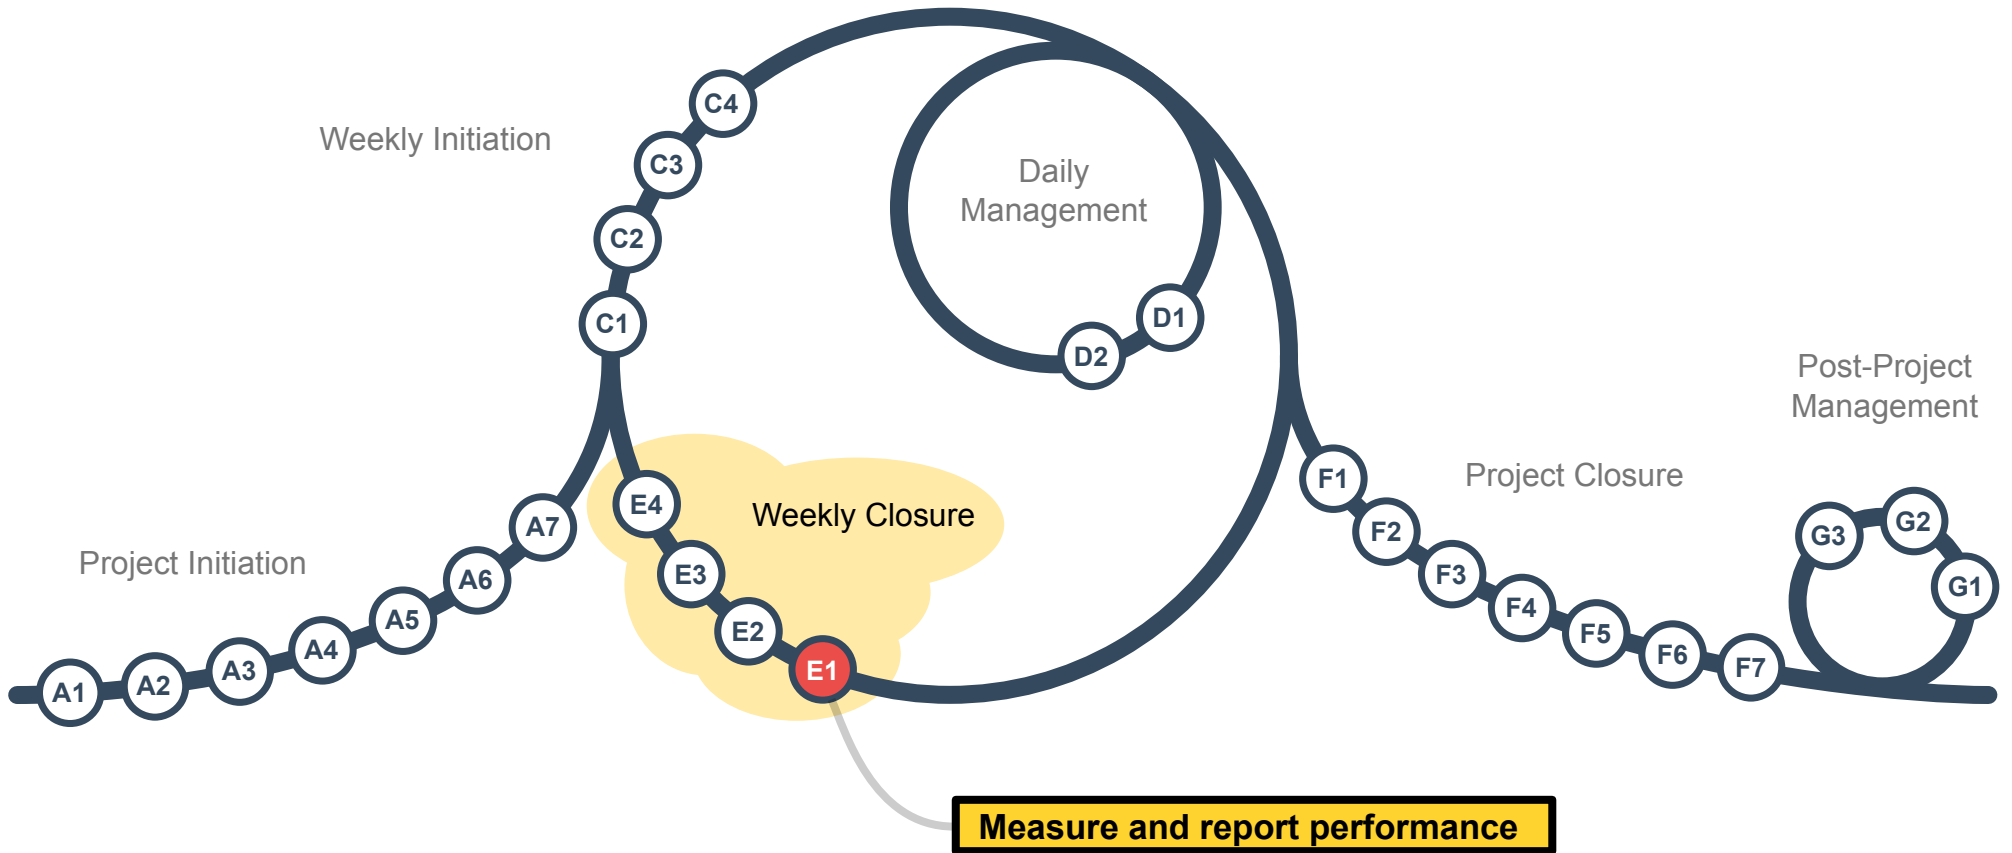

Weekly Initiation

Daily Management

Post-Project Management


Project Initiation

Weekly Closure

Project Closure

Measure and report performance

Integrated Project Board

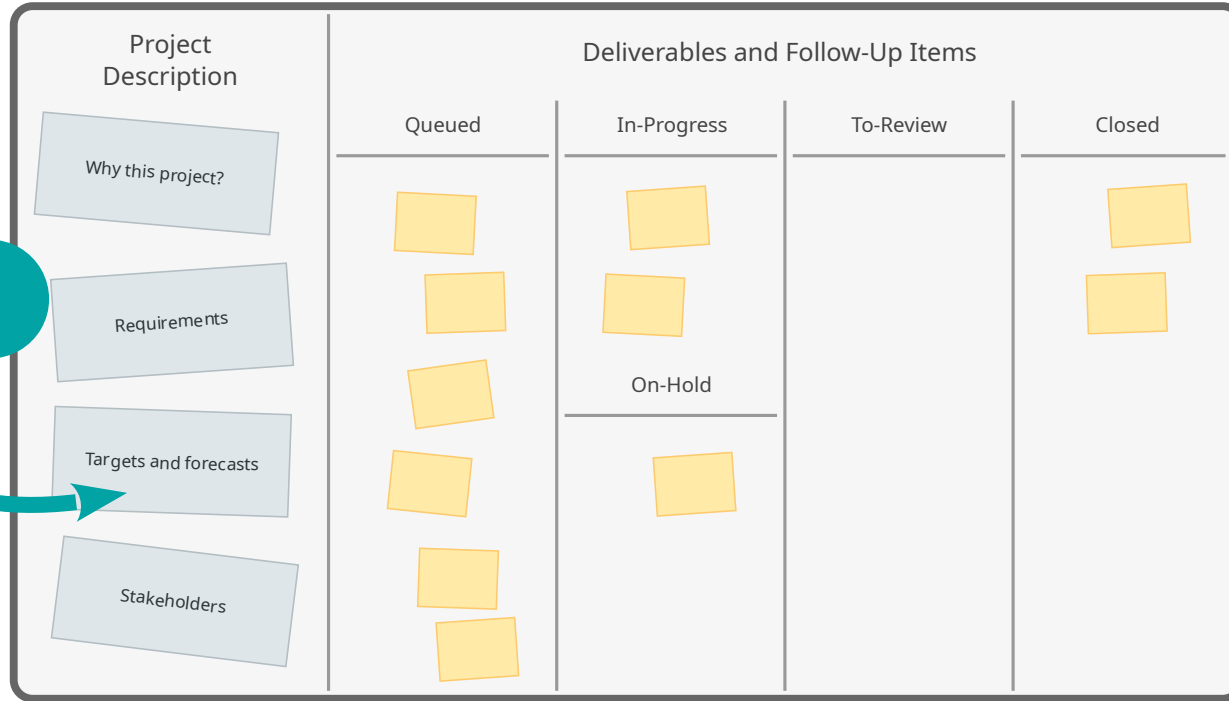


New Forecasts


What concerns do you think each hat should have
in this management activity?




E1 – Measure and report performance

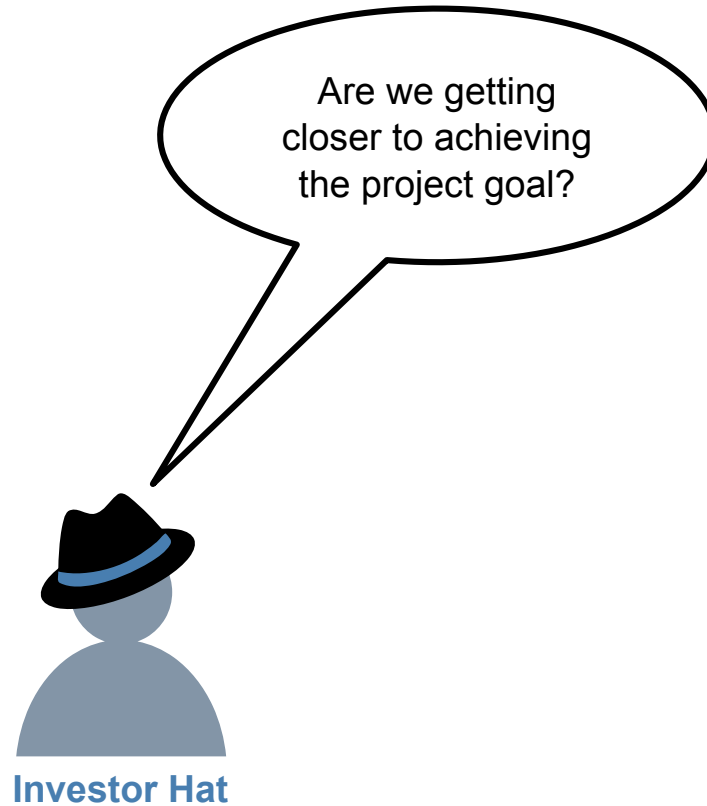

E1 – Measure and report performance

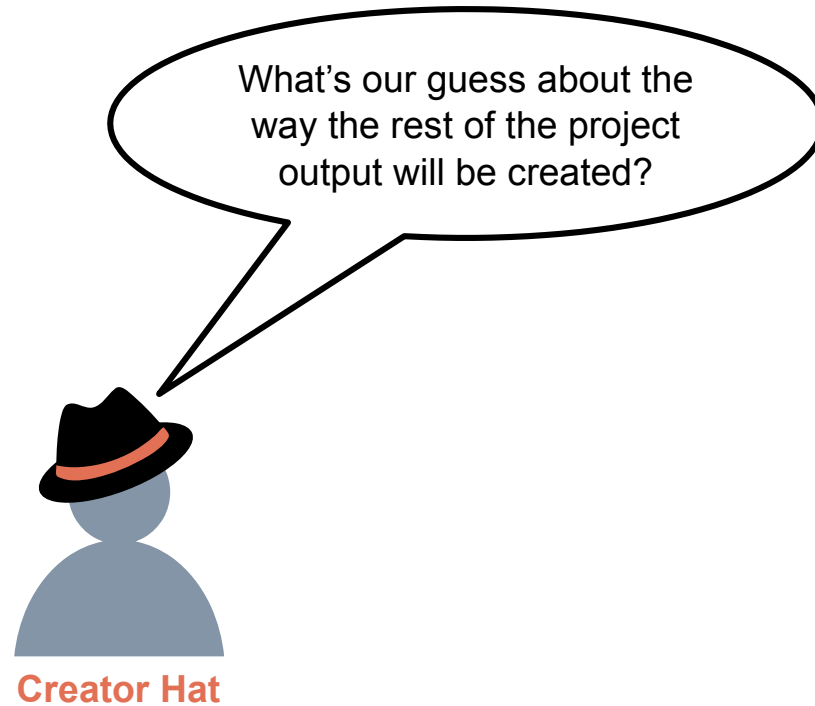



E1 – Measure and report performance

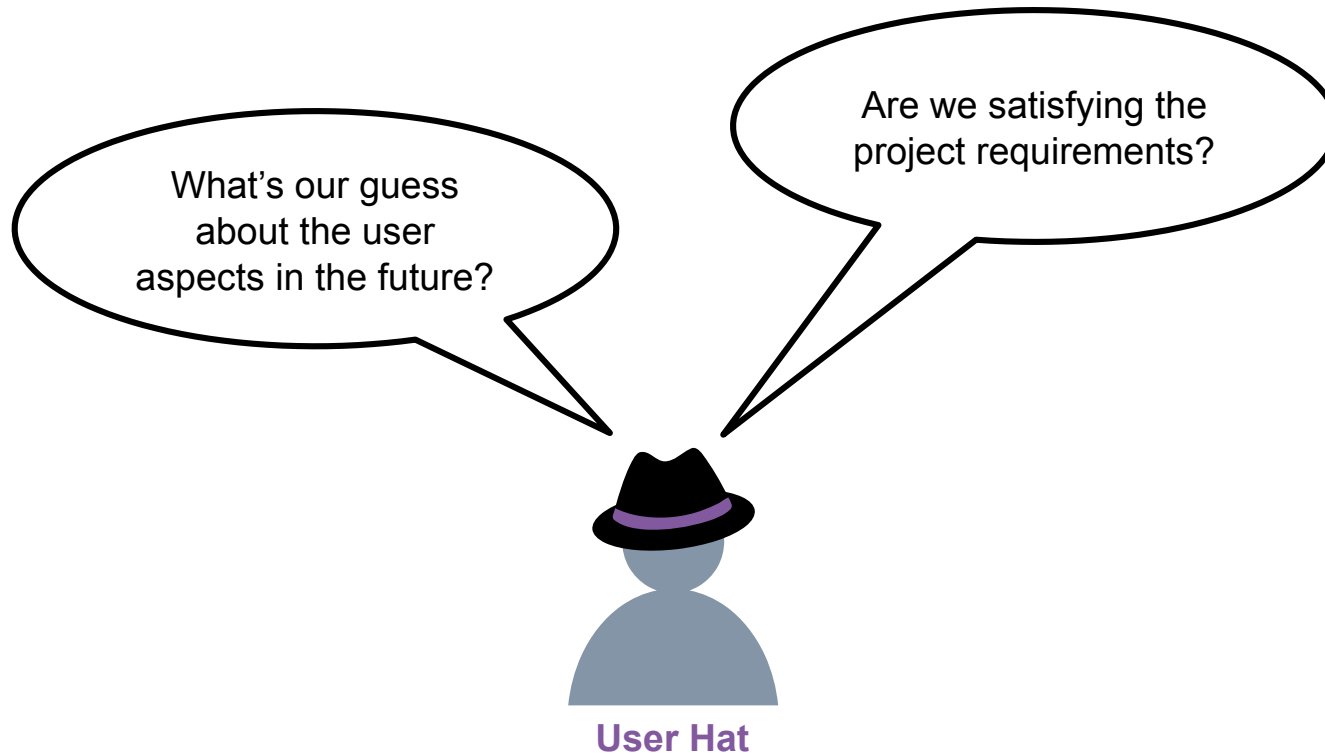

E1 – Measure and report performance



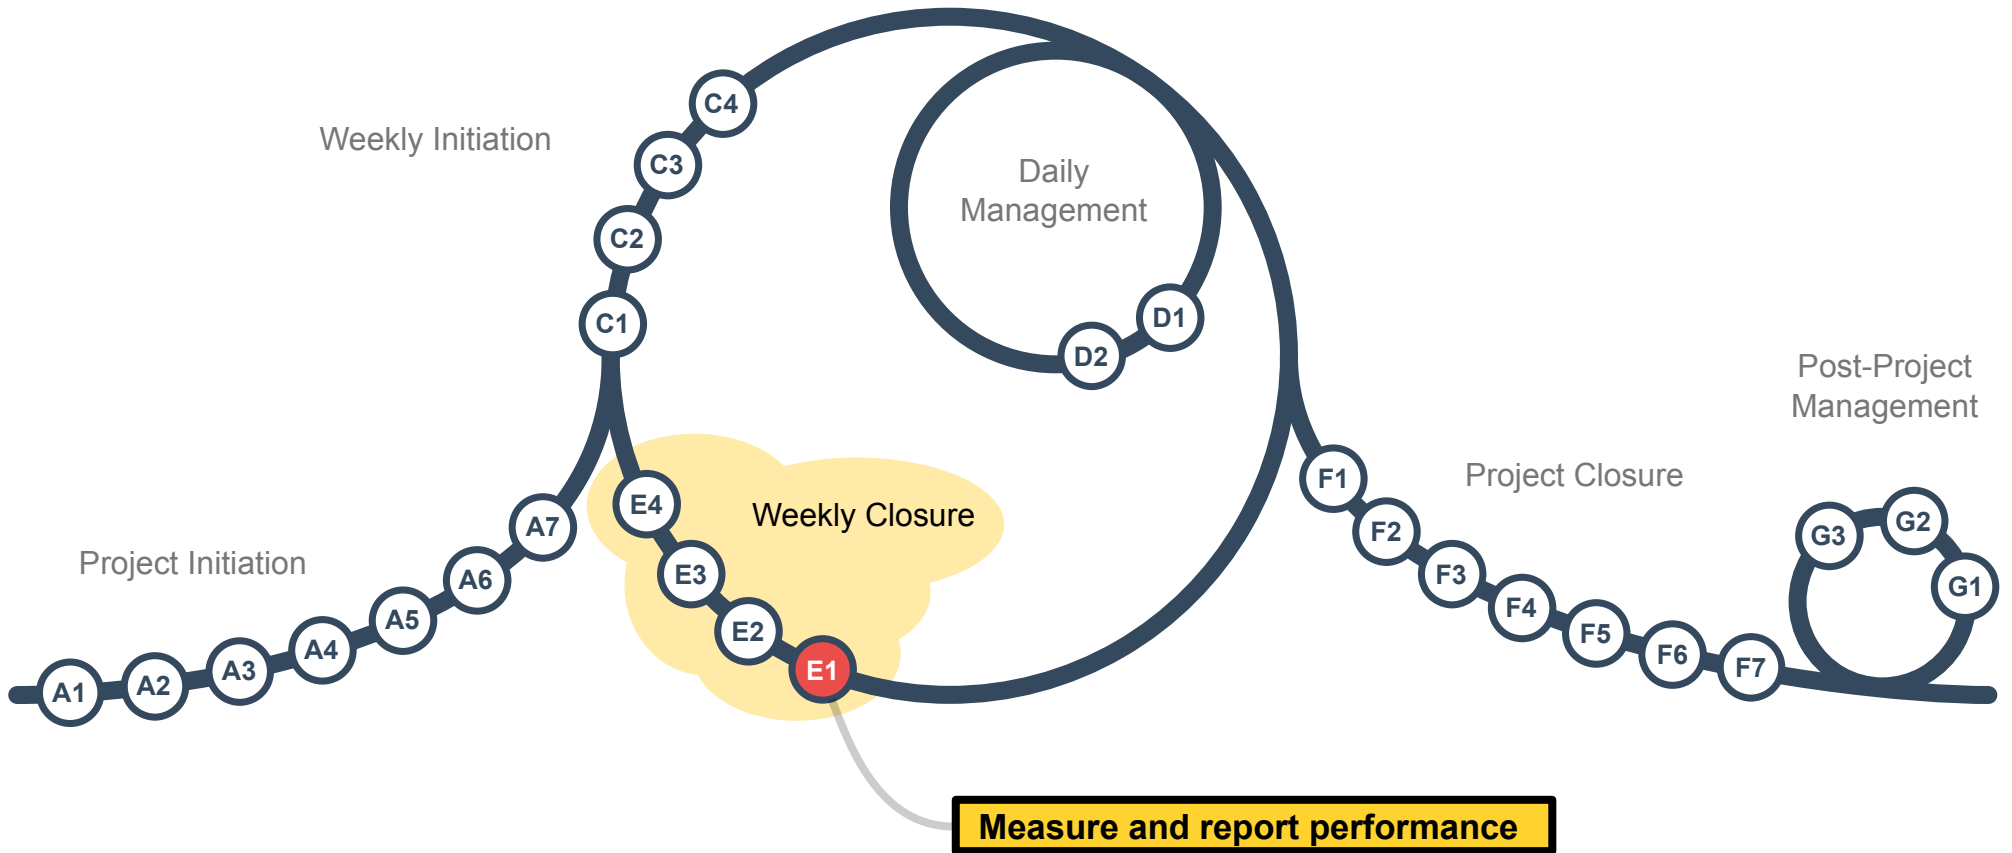


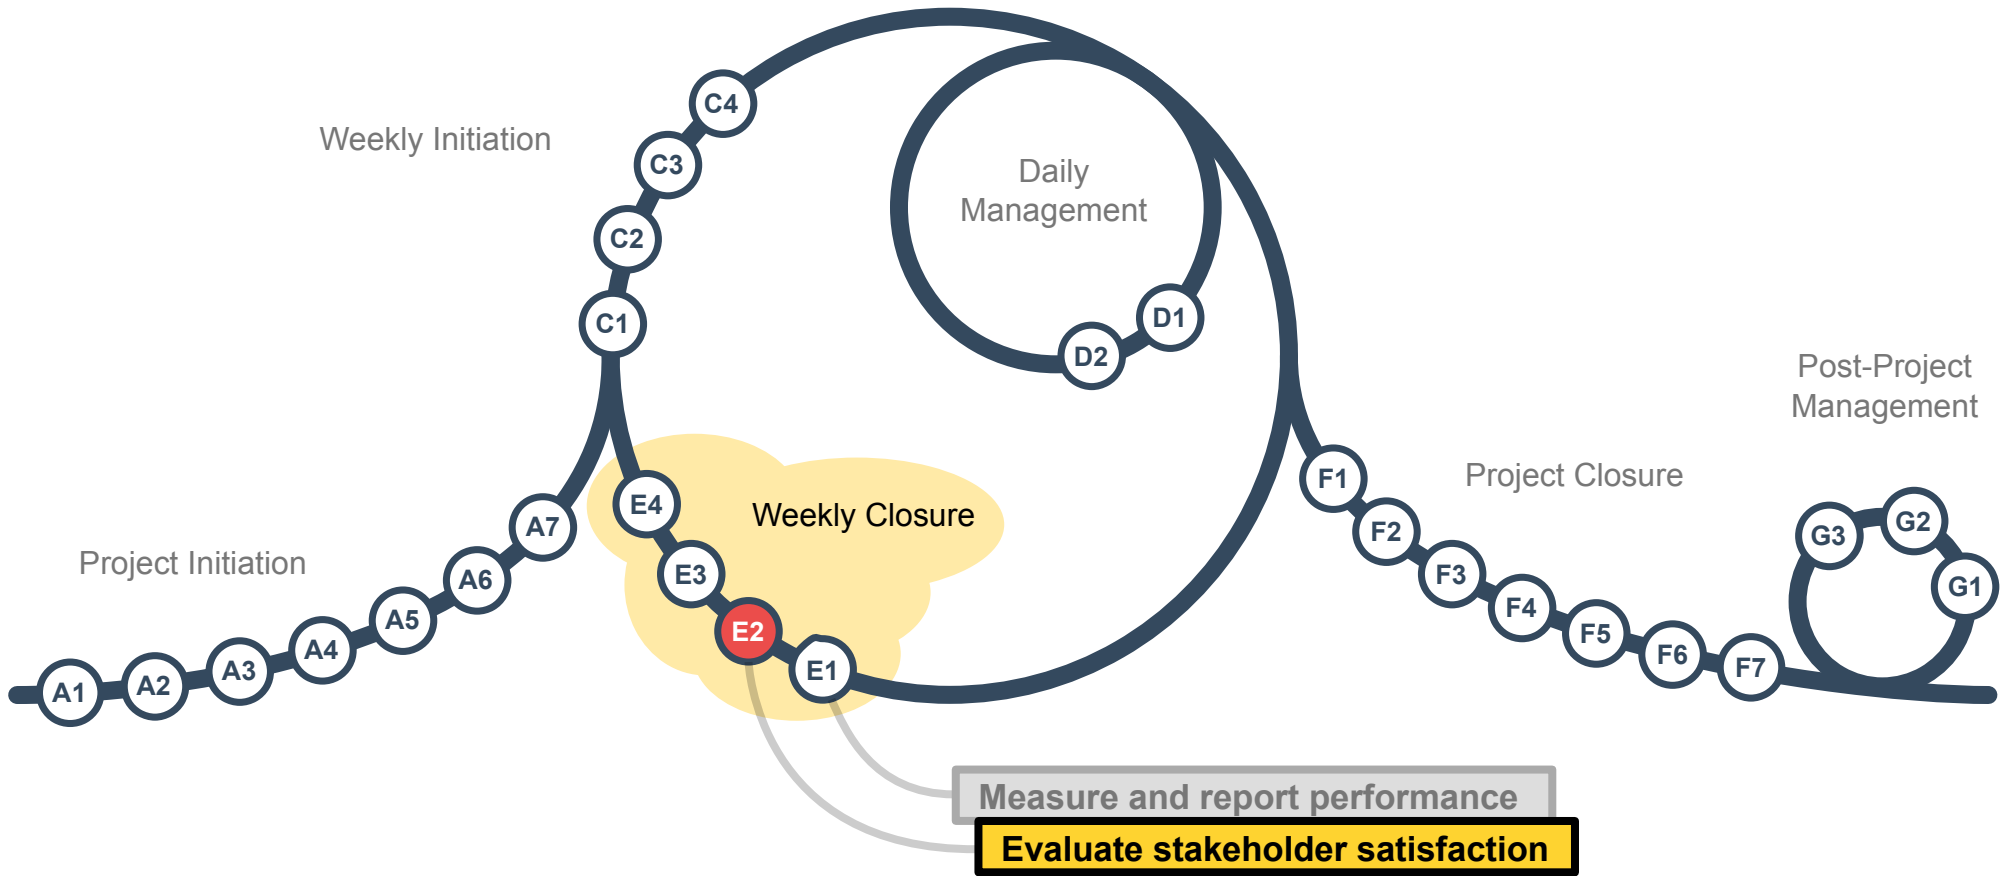


E2 – Evaluate stakeholder satisfaction



E2 – Evaluate stakeholder satisfaction

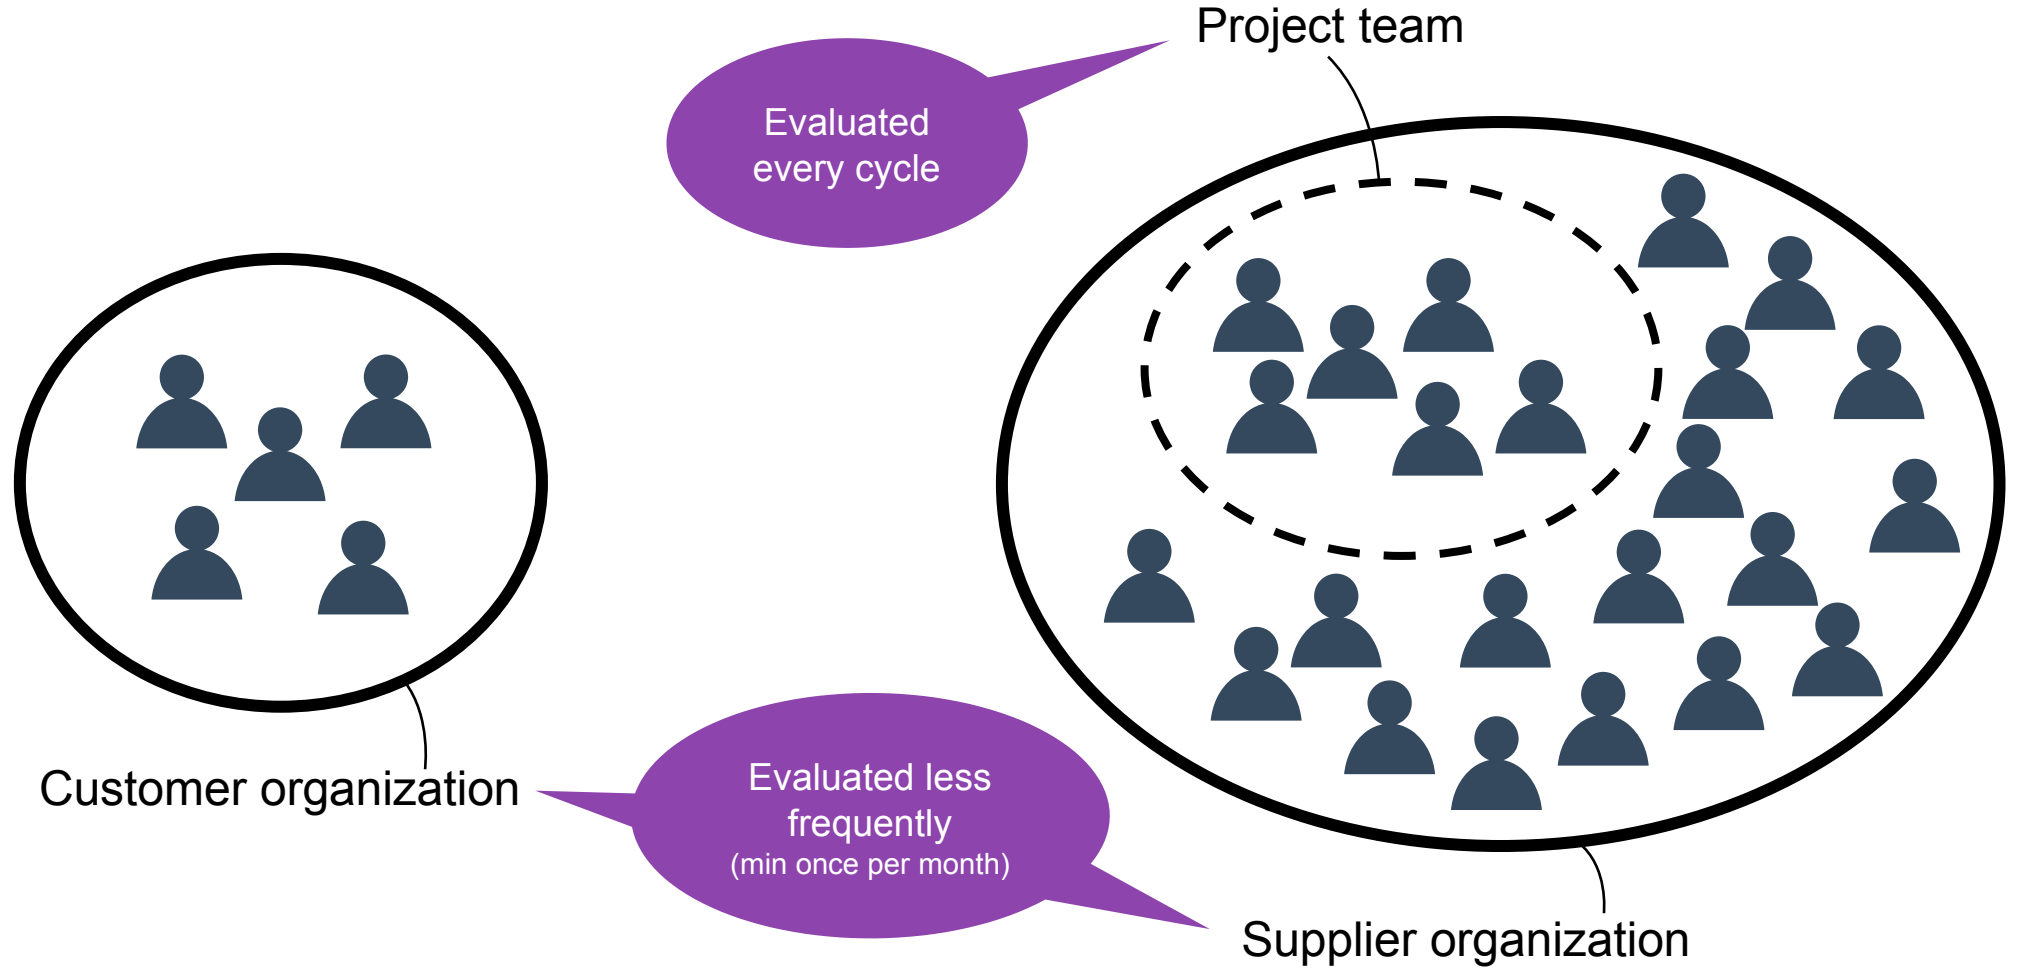



Integrated Project Board

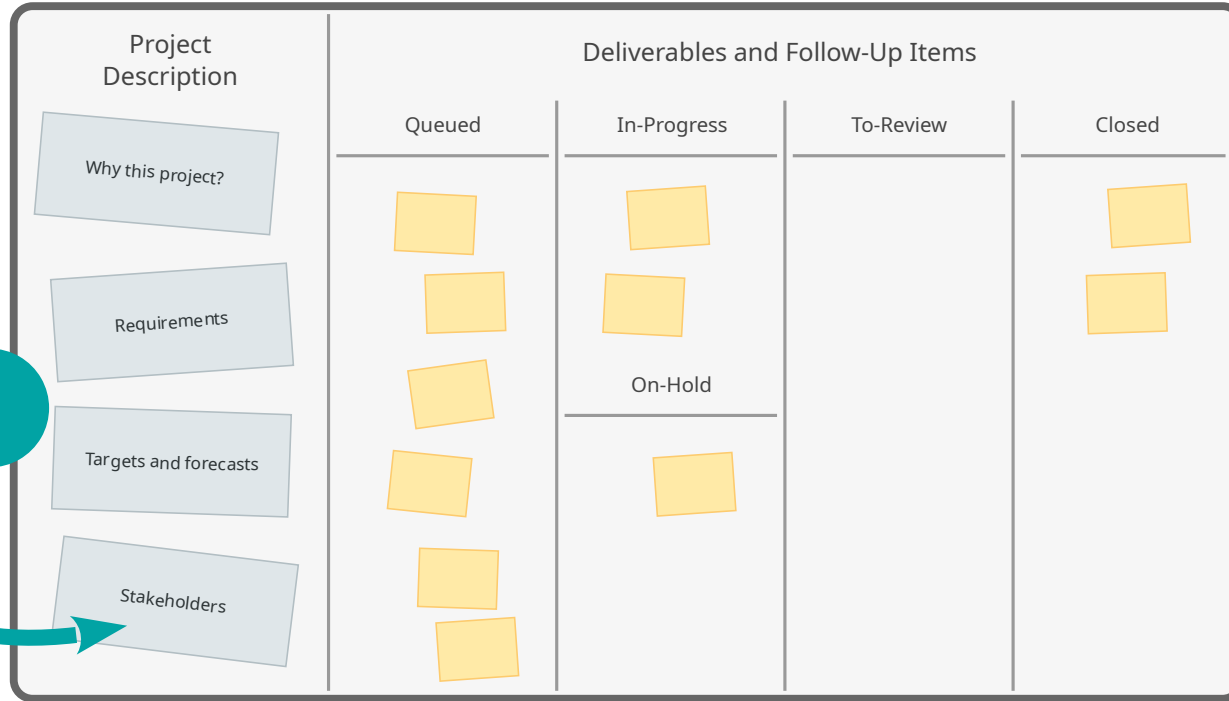


Evaluation Results



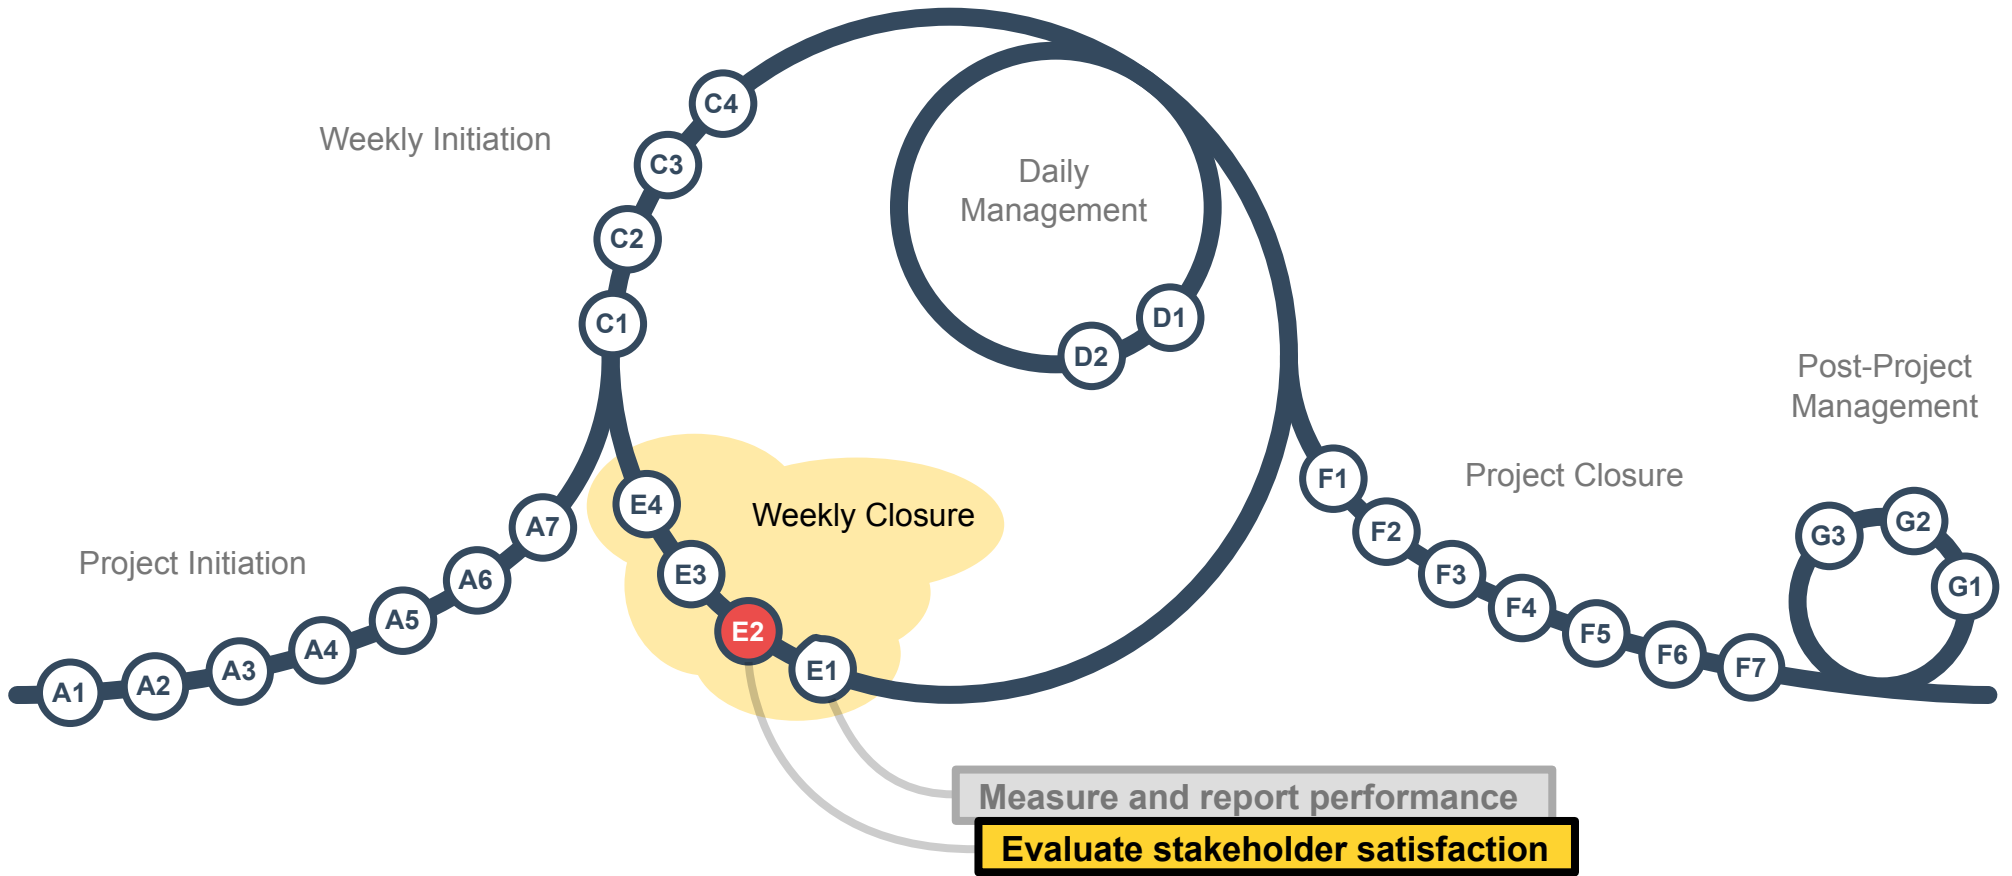


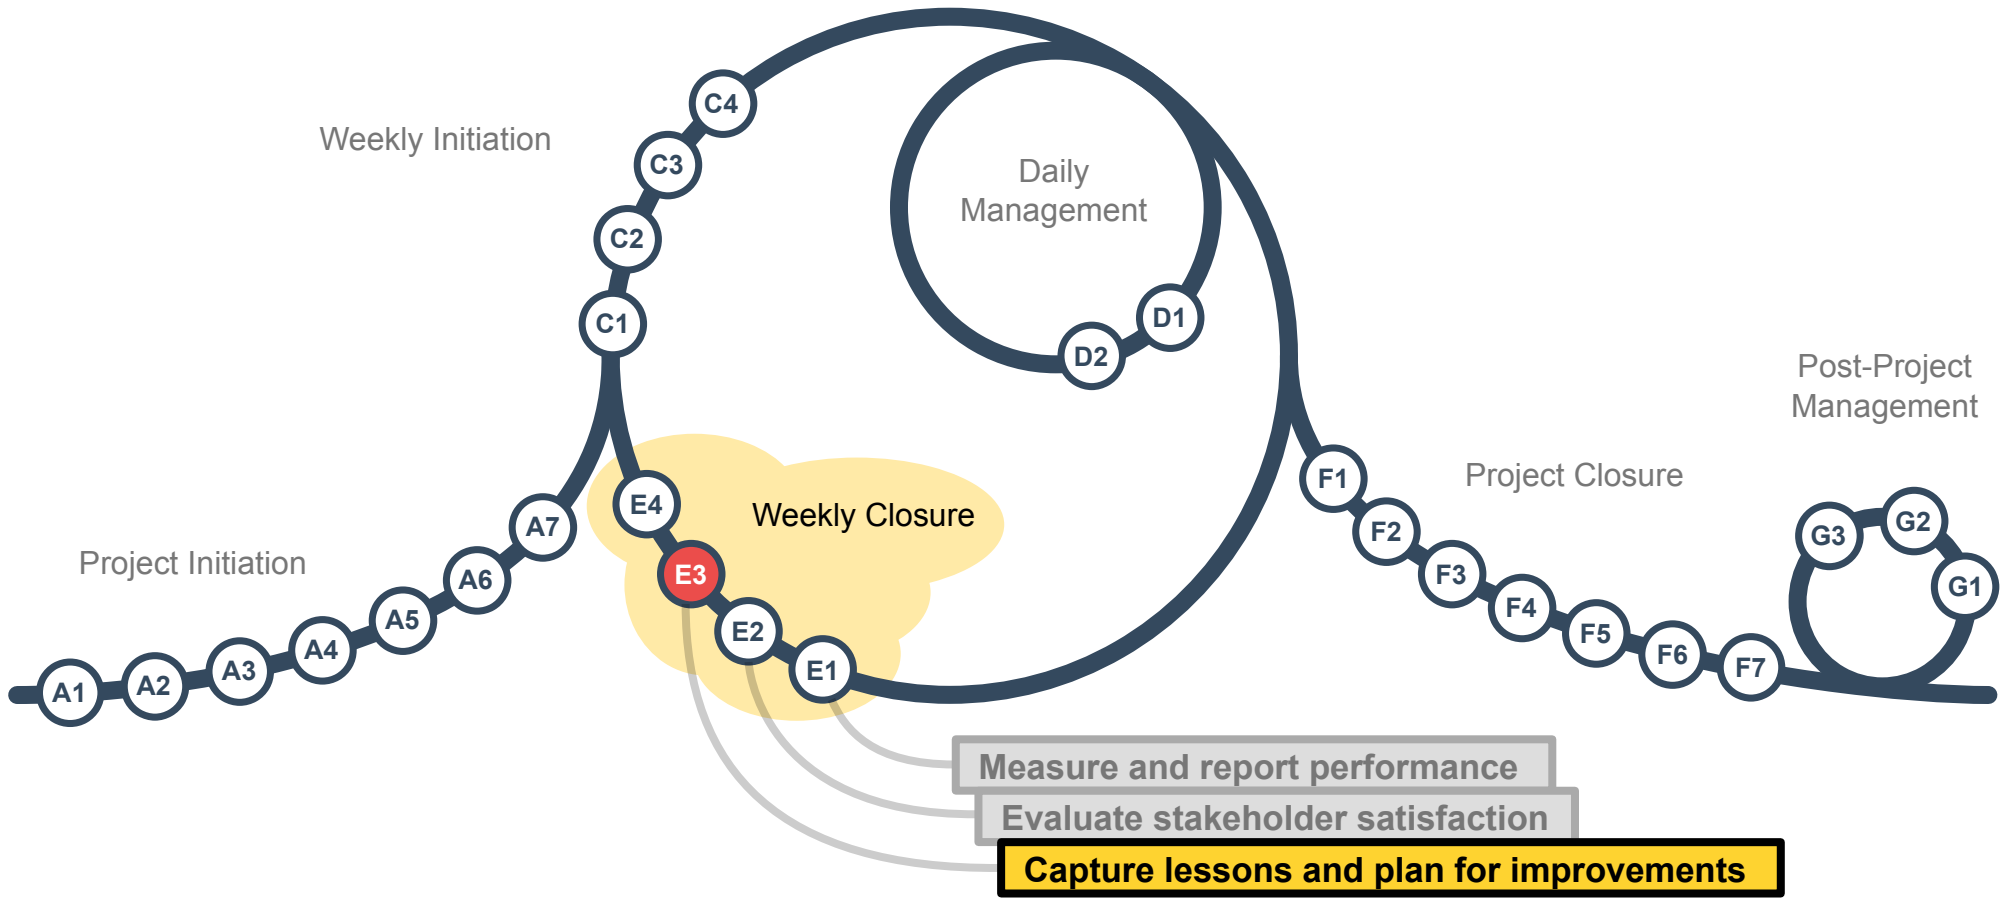


E3 – Capture lessons and plan for improvements

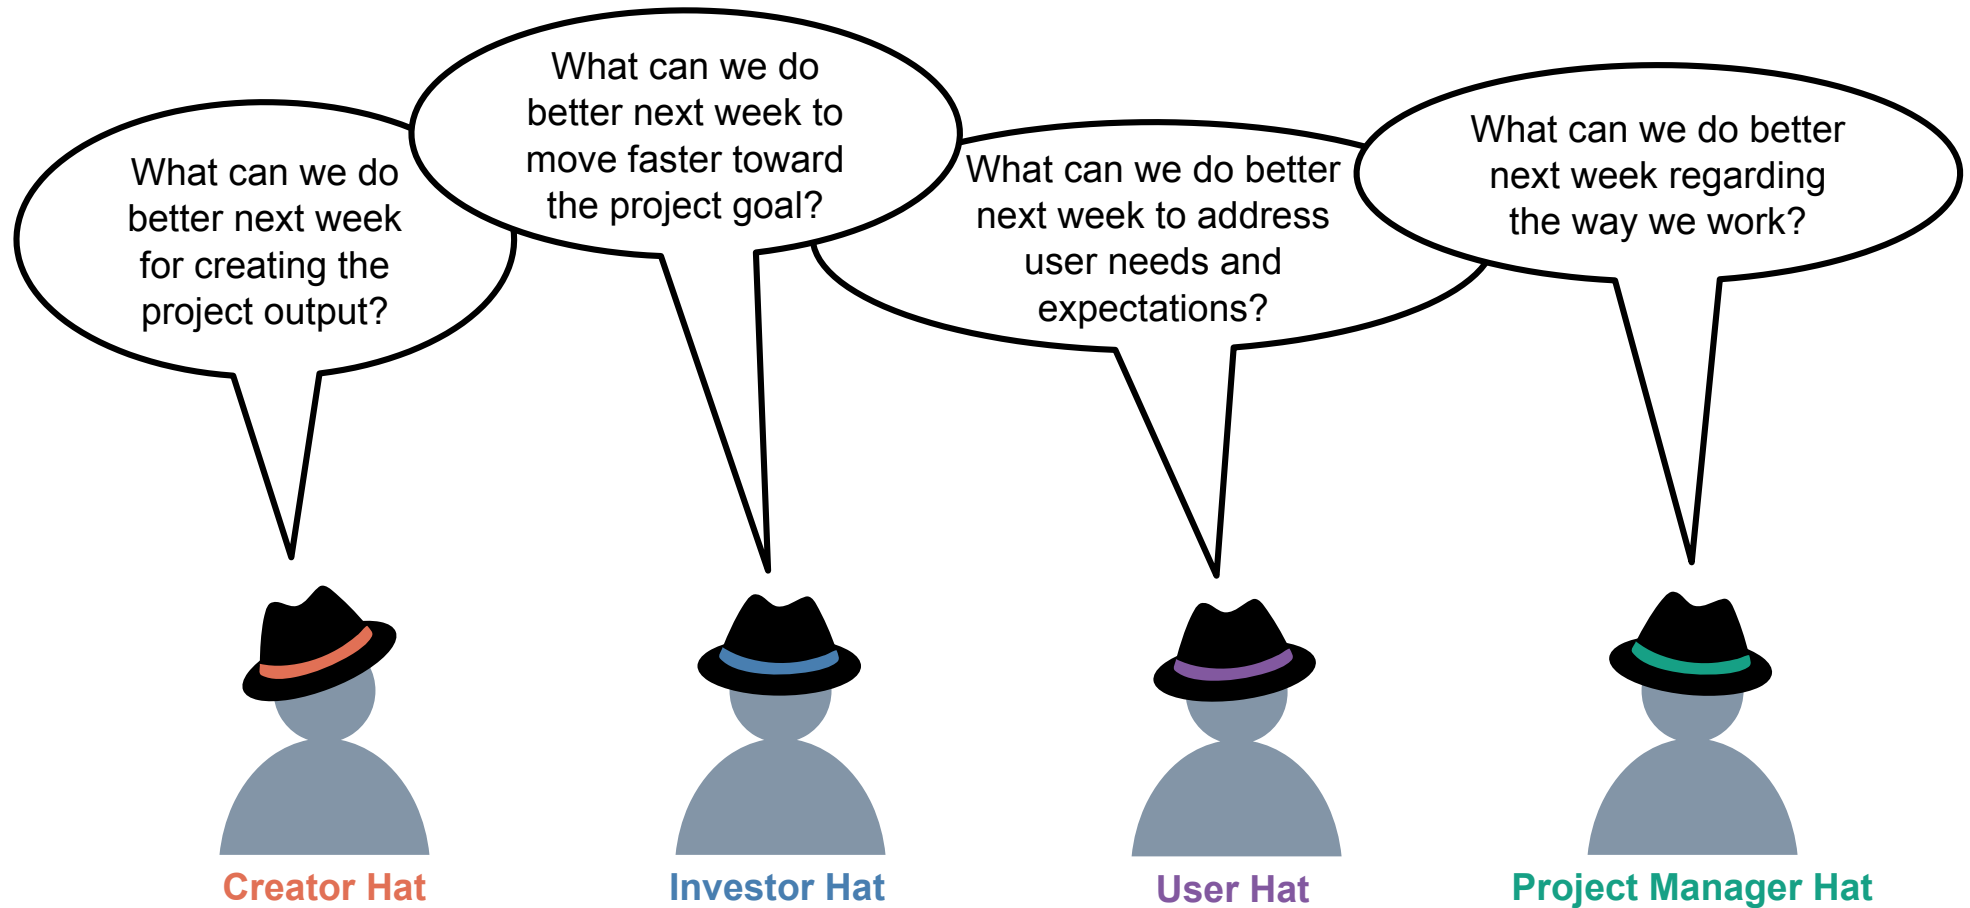

Integrated Project Board

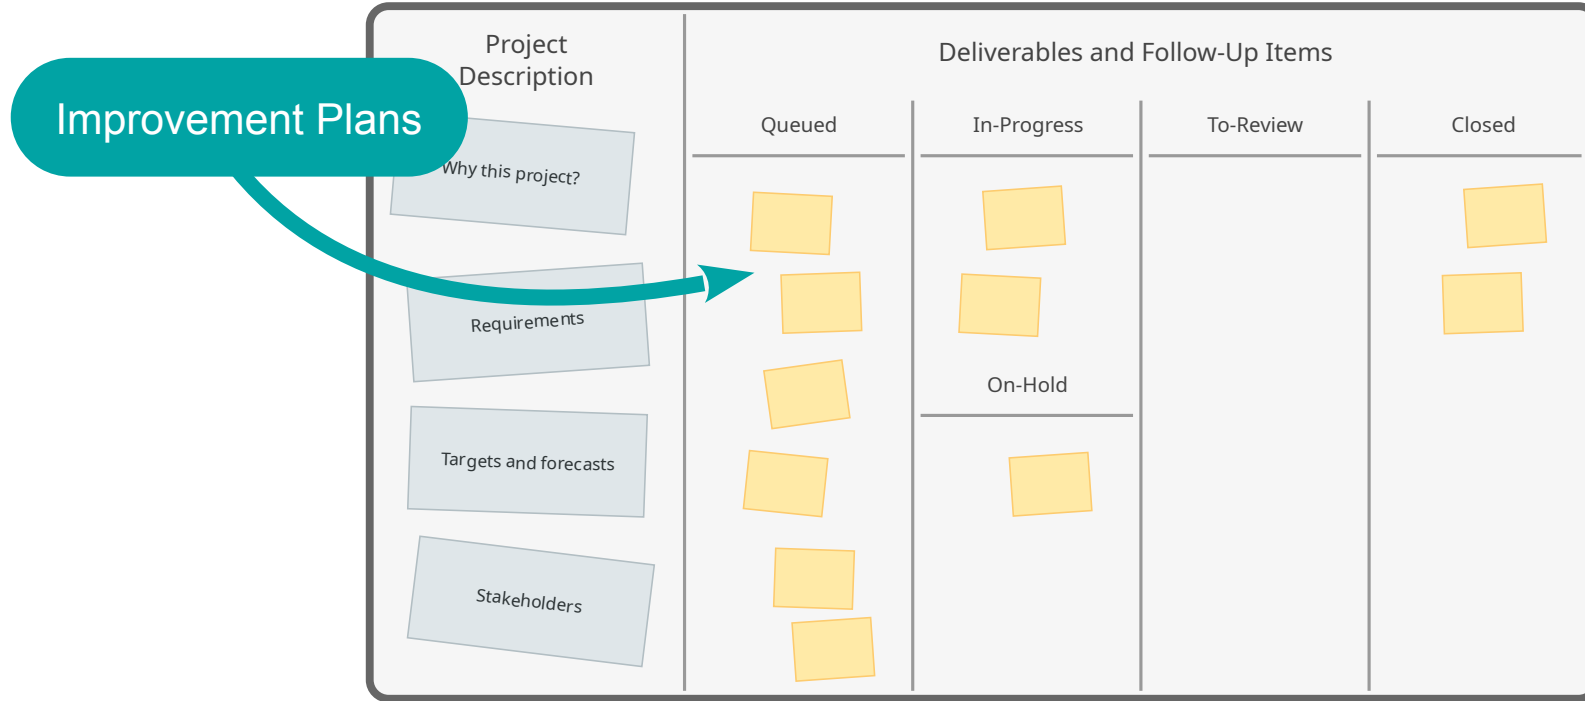


E3 – Capture lessons and plan for improvements

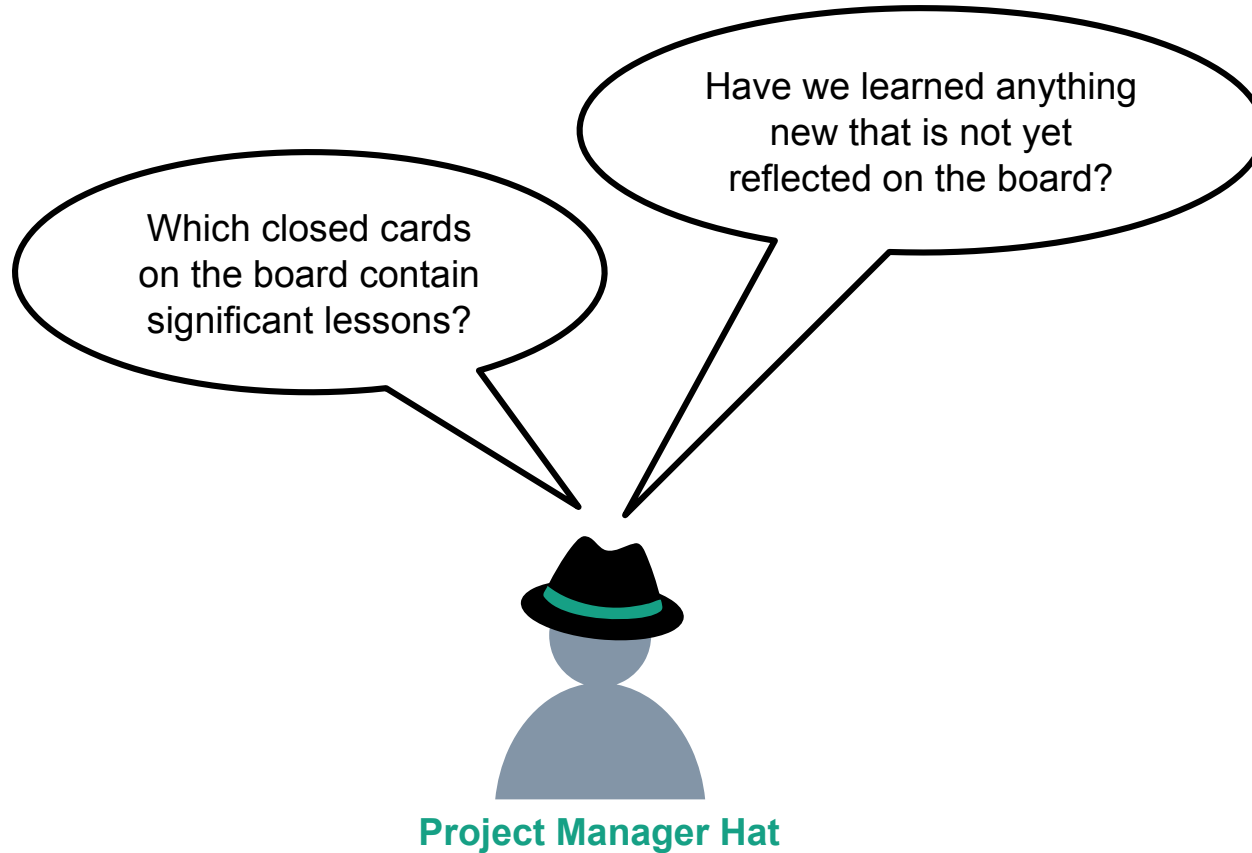


Lessons Learned

Integrated Project Board

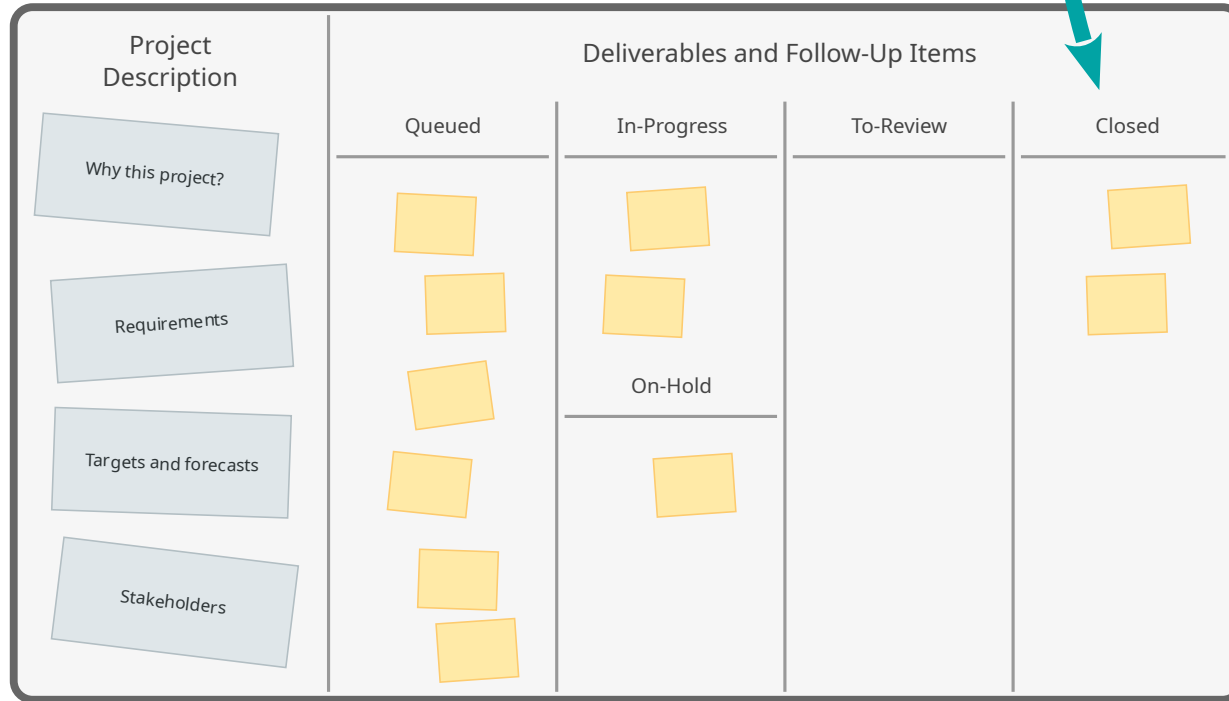



Lessons Learned

Integrated Project Board

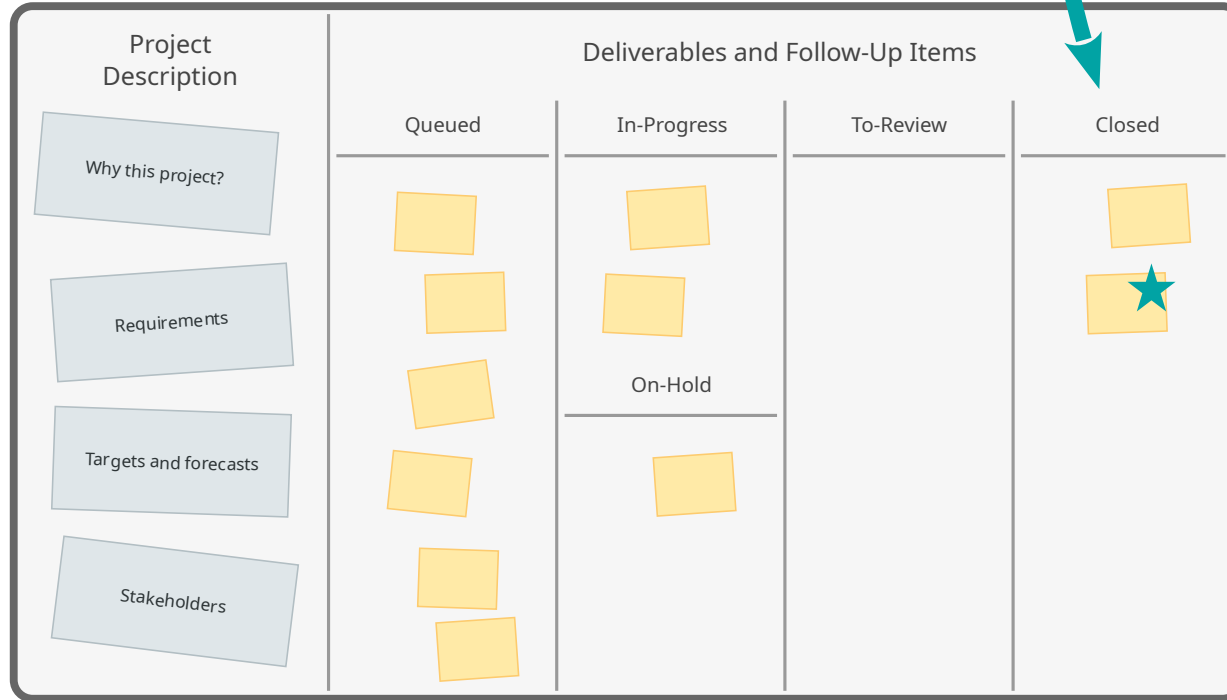

Mark deliverables and follow-up items that contain important lessons.

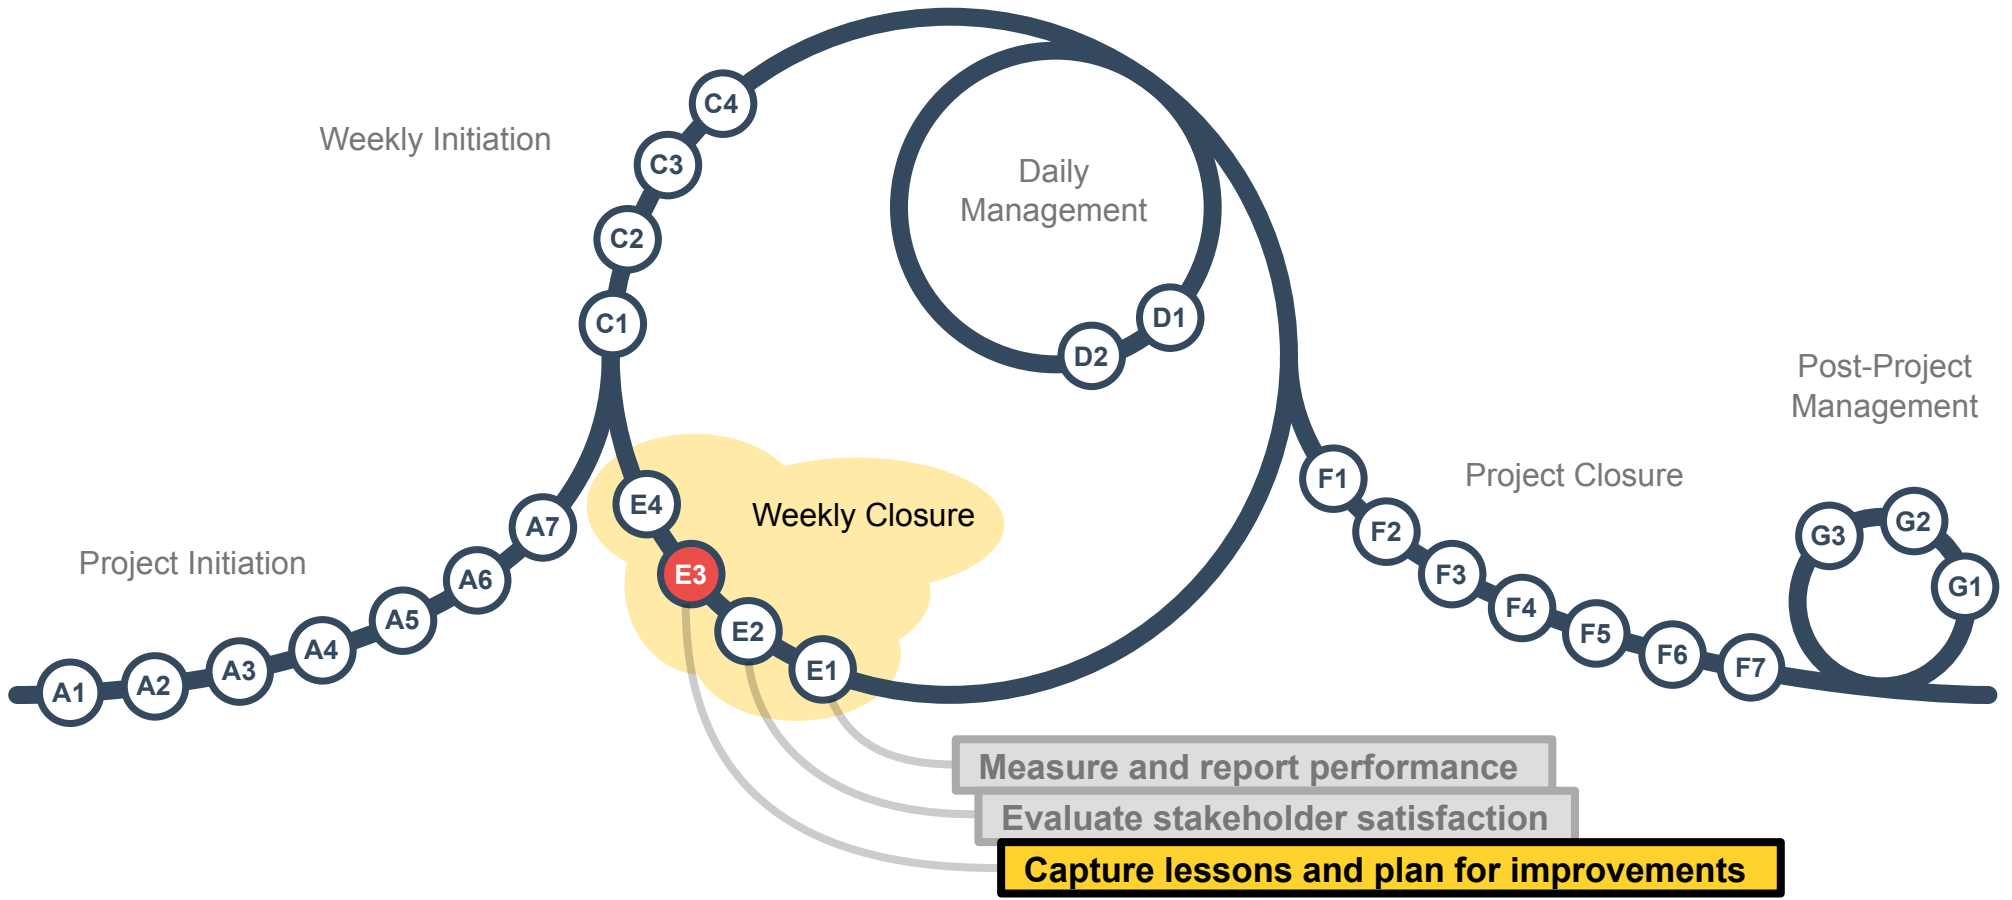

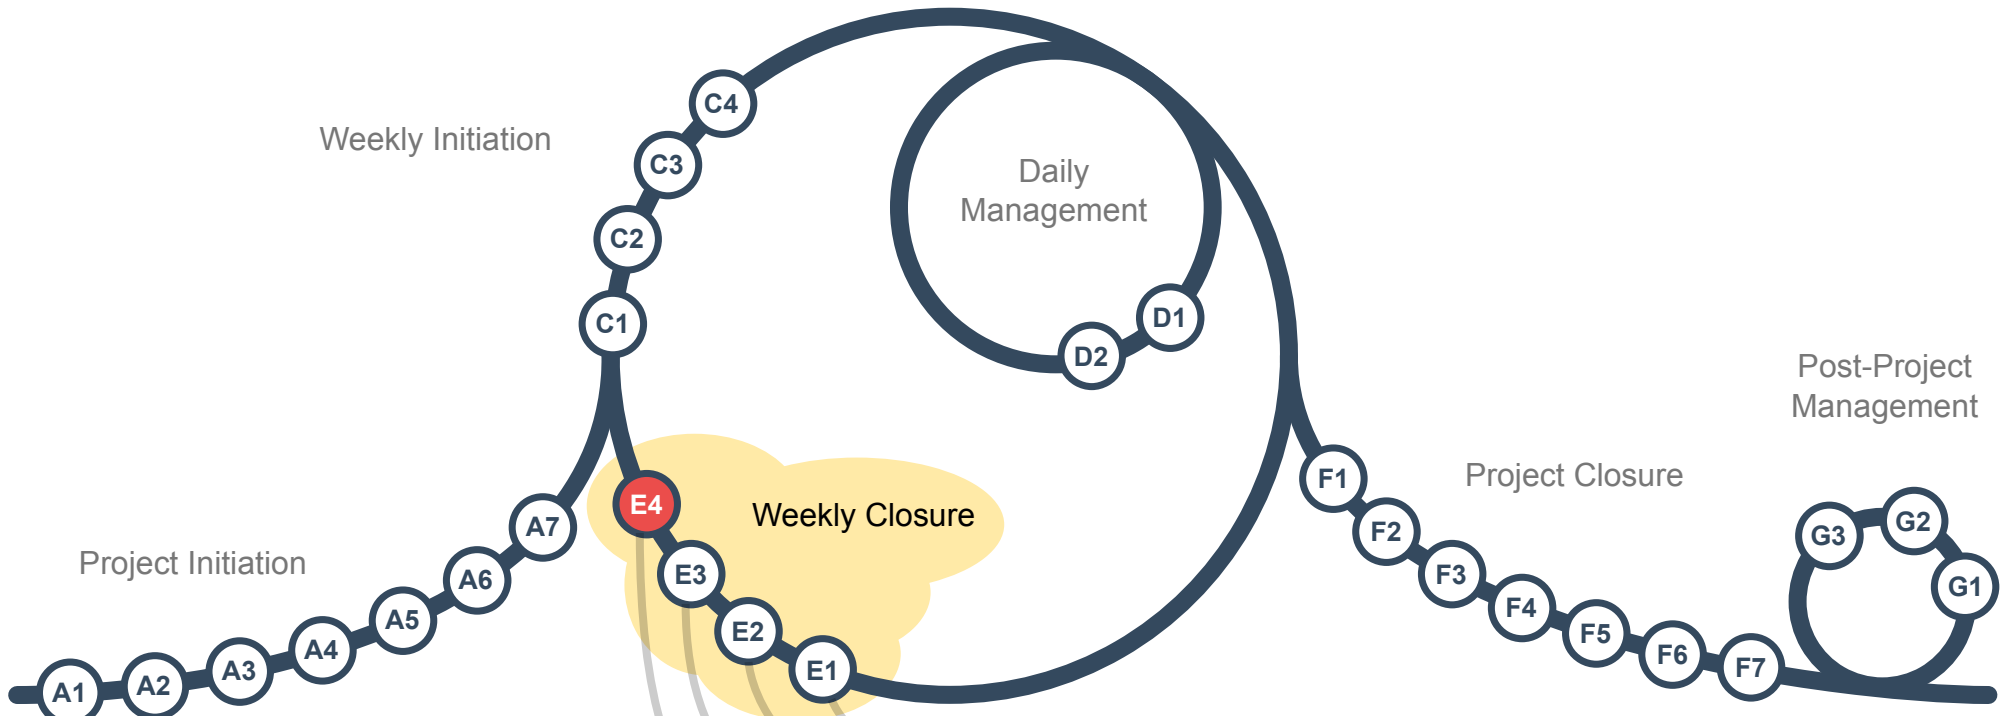

Project Initiation

Weekly Initiation

Daily Management

Post-Project Management

Project Closure

Weekly Closure

Measure and report performance

Evaluate stakeholder satisfaction

Capture lessons and plan for improvements

Consider swapping hats for the week

E4 – Consider swapping hats for the week


Project Initiation




Cycle 1



Cycle 2



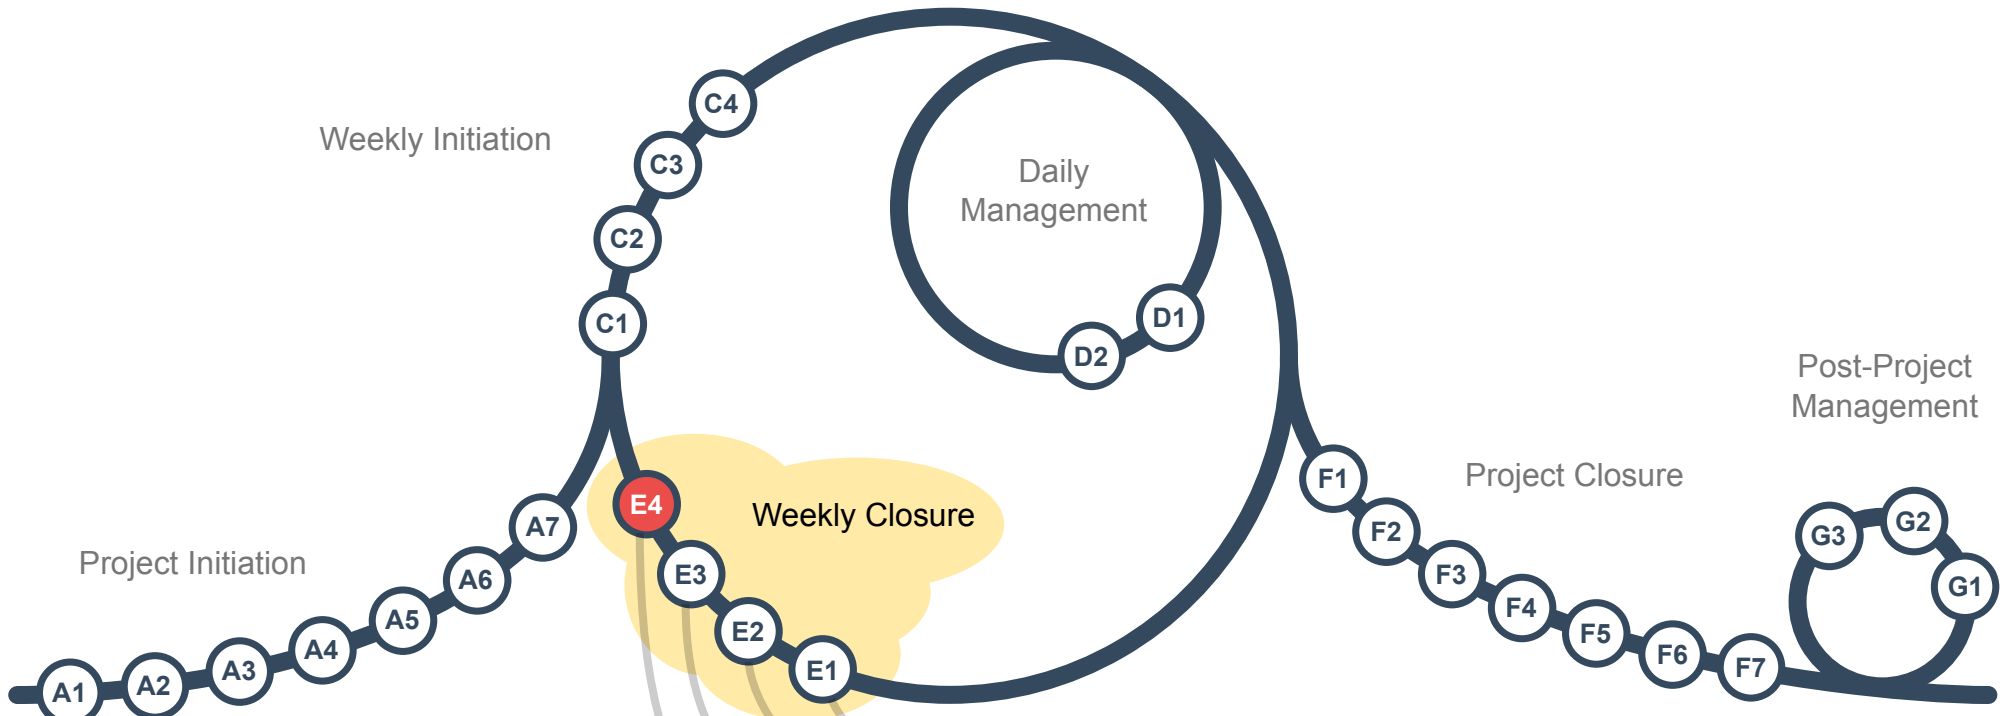

Project Initiation

Weekly Initiation

Daily Management

Post-Project Management

Project Closure


Weekly Closure

Measure and report performance

Evaluate stakeholder satisfaction

Capture lessons and plan for improvements

Consider swapping hats for the week

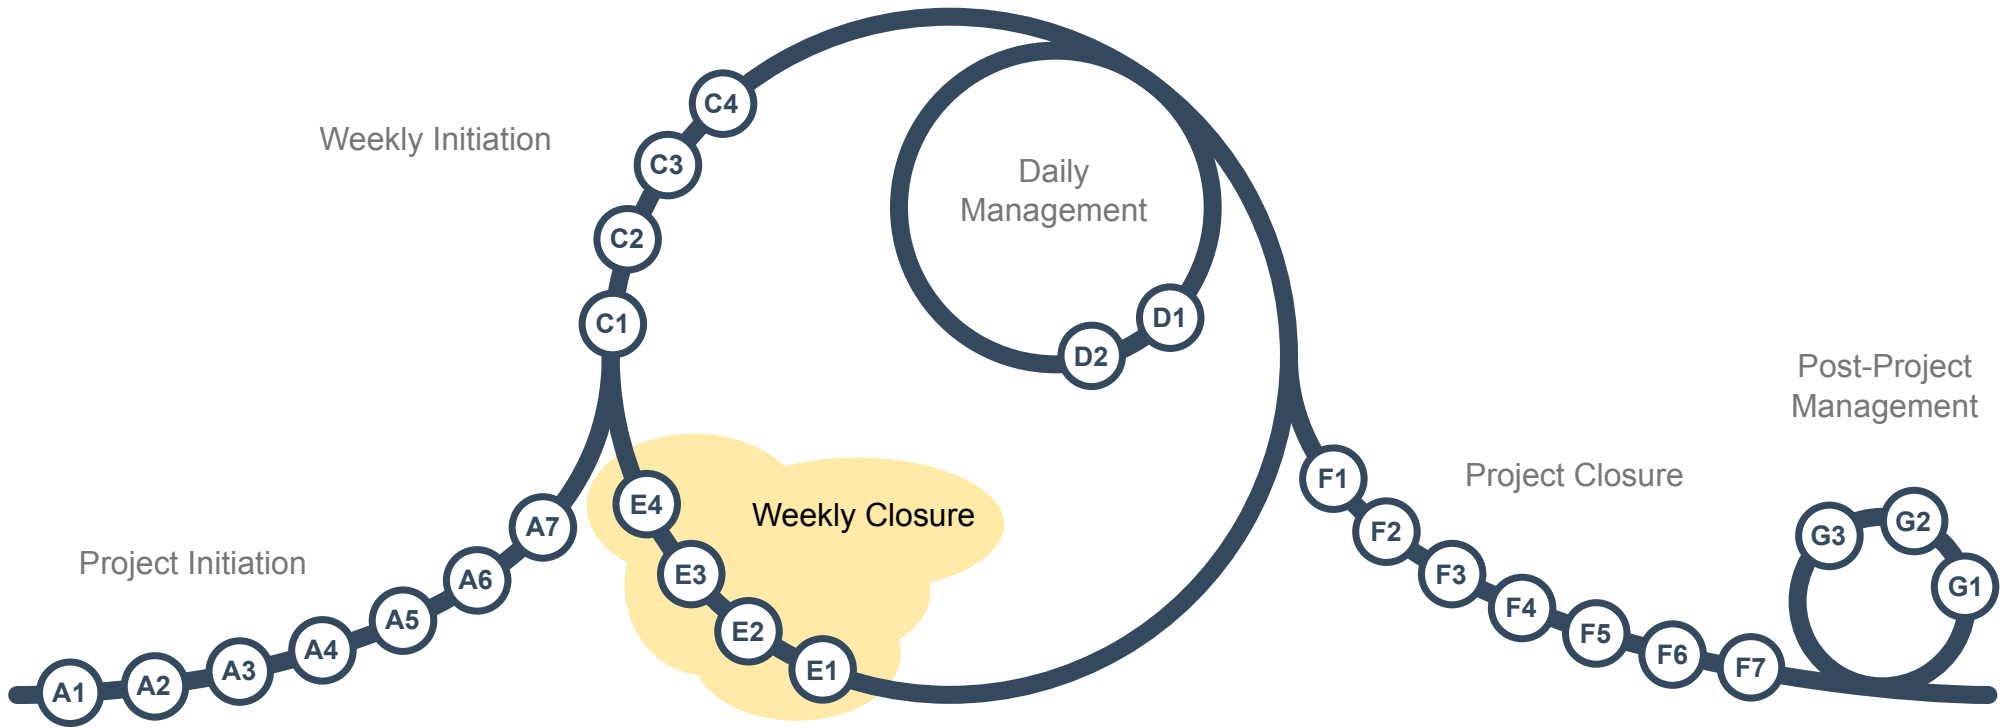

Project Initiation


Weekly Initiation


Daily Management

Weekly Closure


Project Closure

Post-Project Management

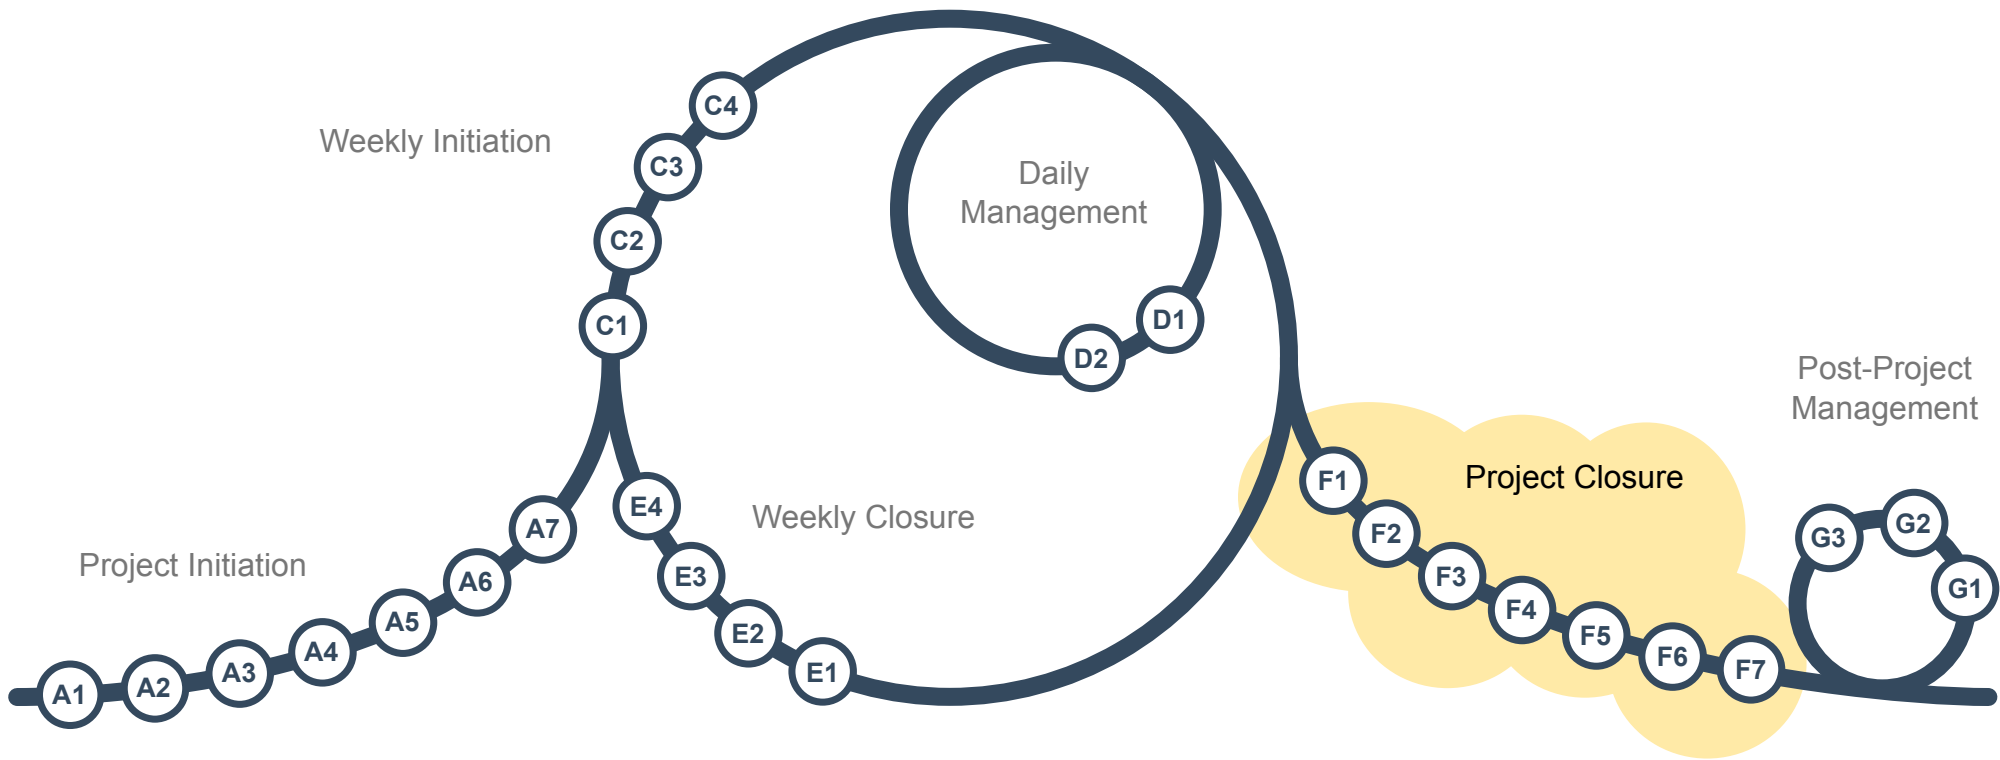

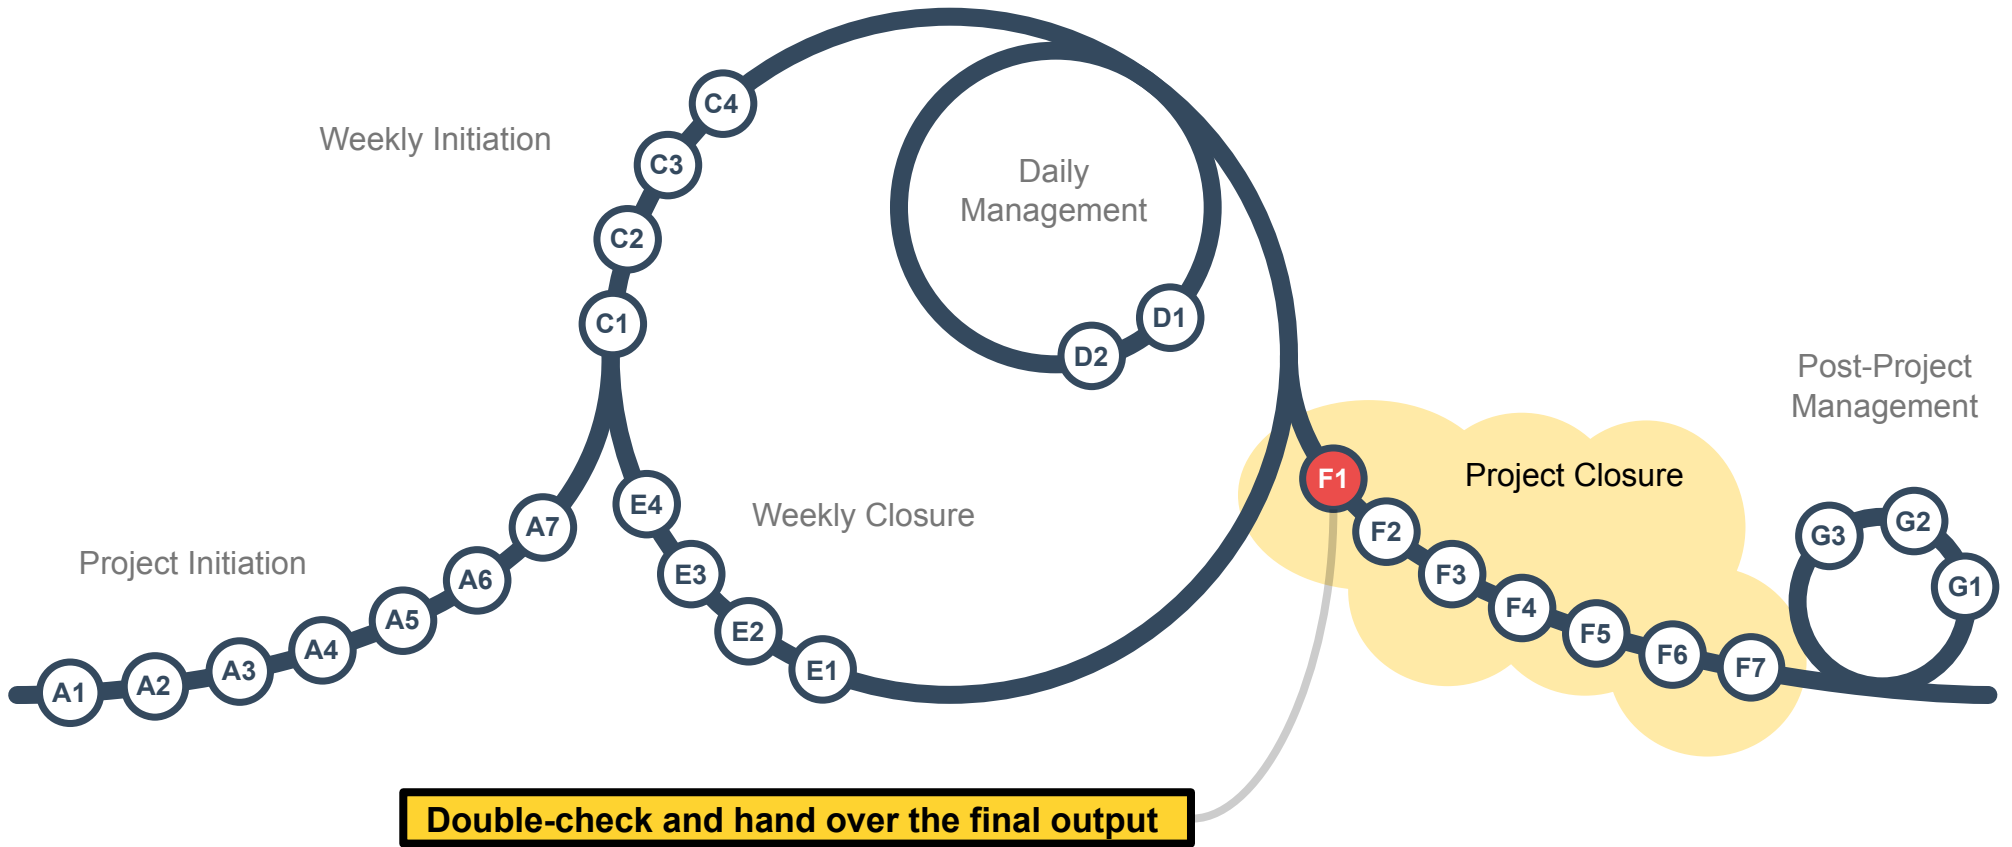

F1 – Double-check and hand over the final product

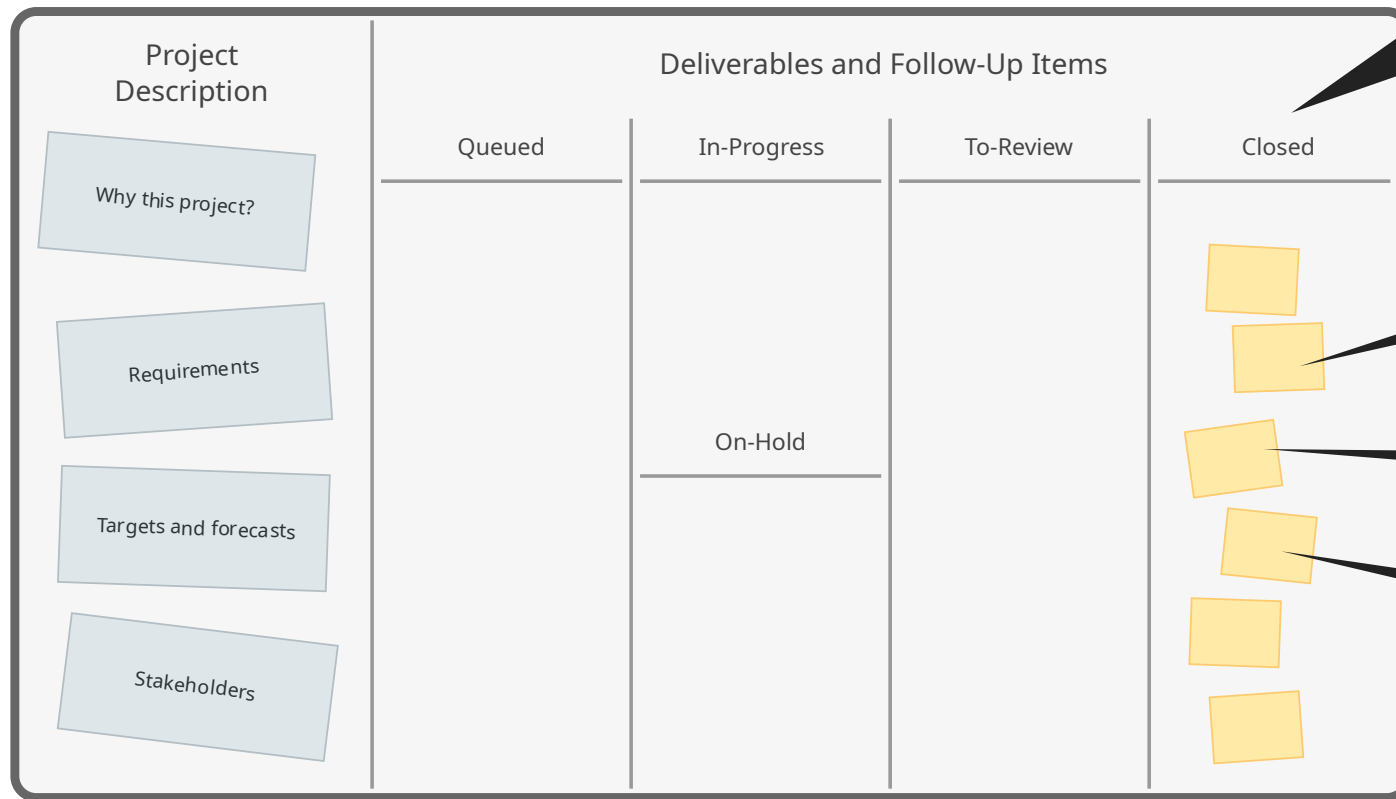

Everything must be closed

Completed

Transferred


Cancelled

Don't delete anything!


What concerns do you think each hat should have
in this management activity?



F1 – Double-check and hand over the final product

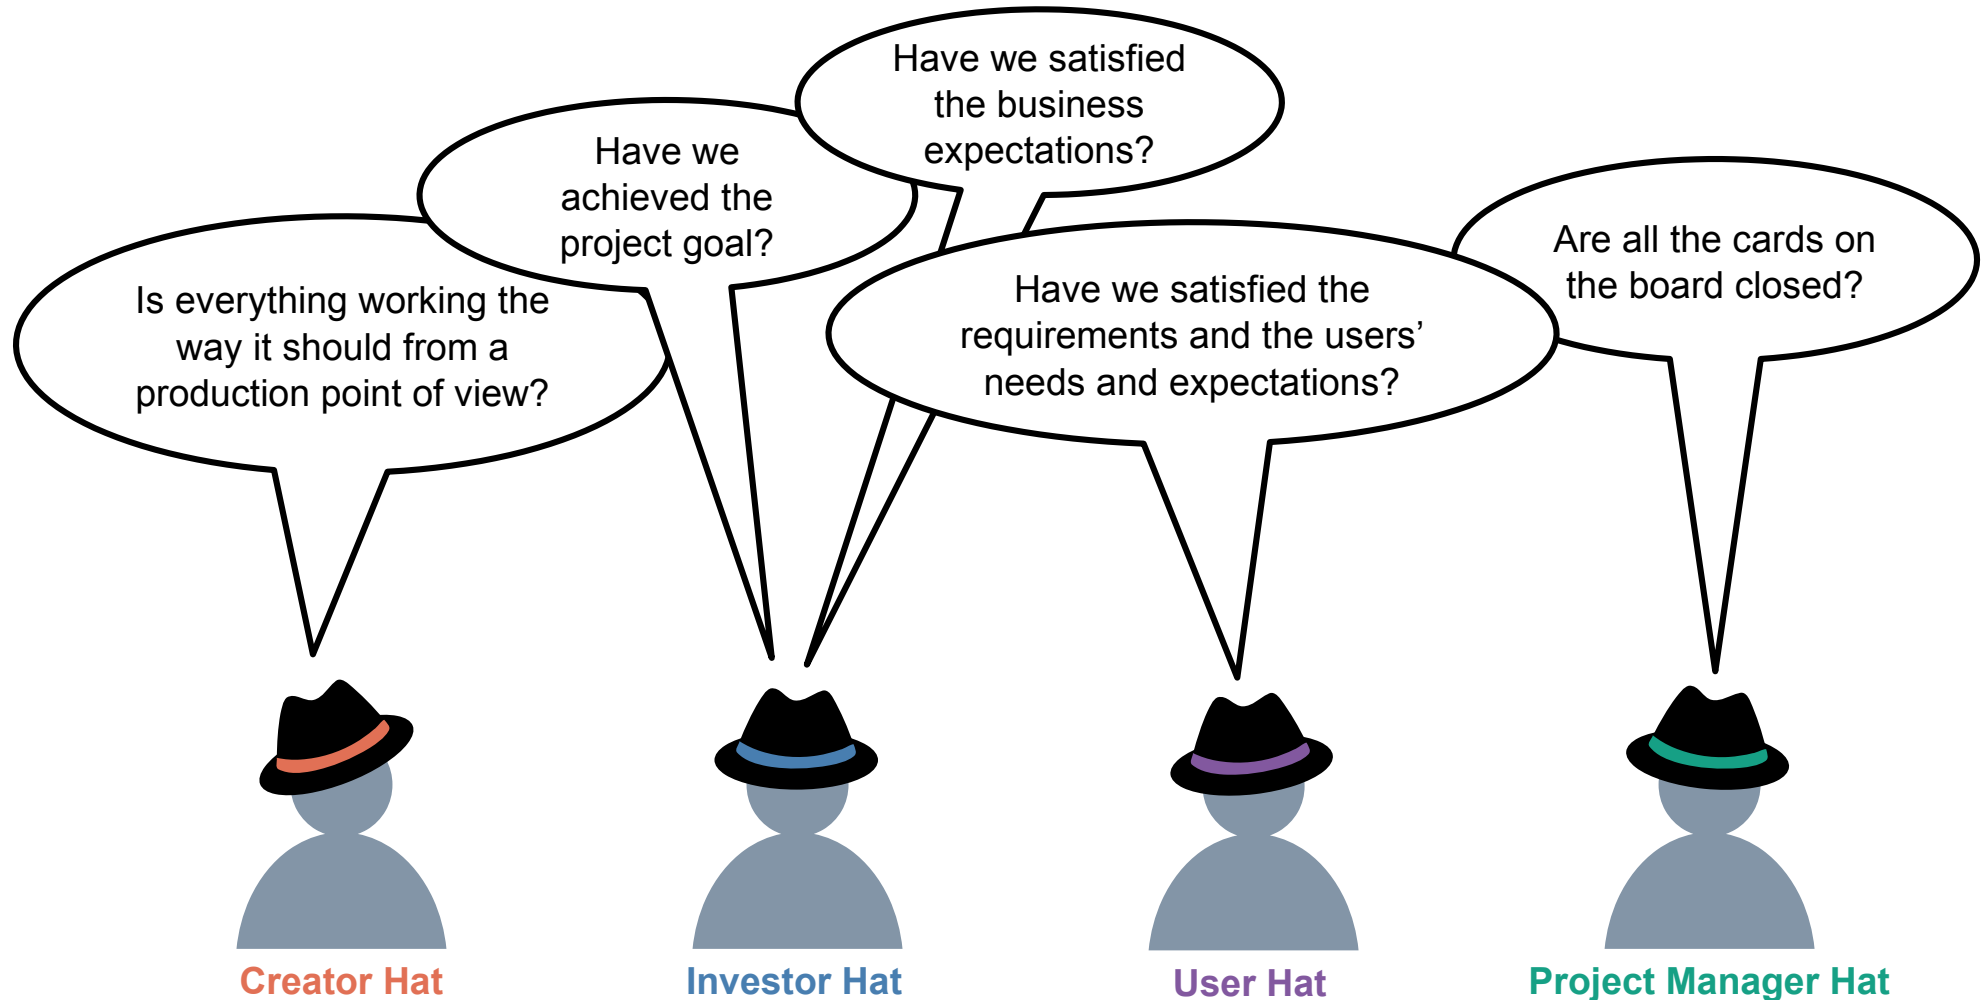



F1 – Double-check and hand over the final product

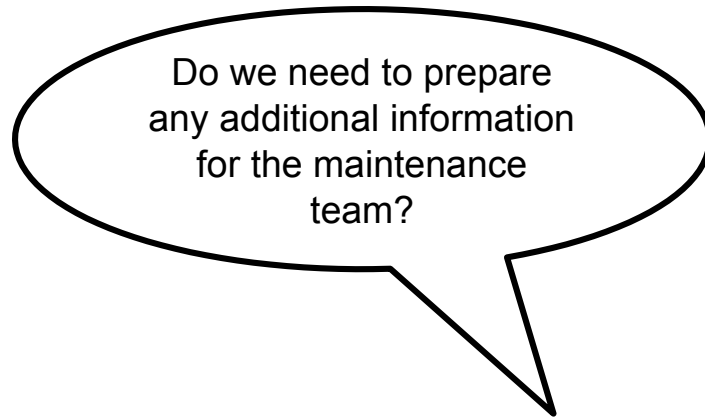



Creator Hat


F1 – Double-check and hand over the final product

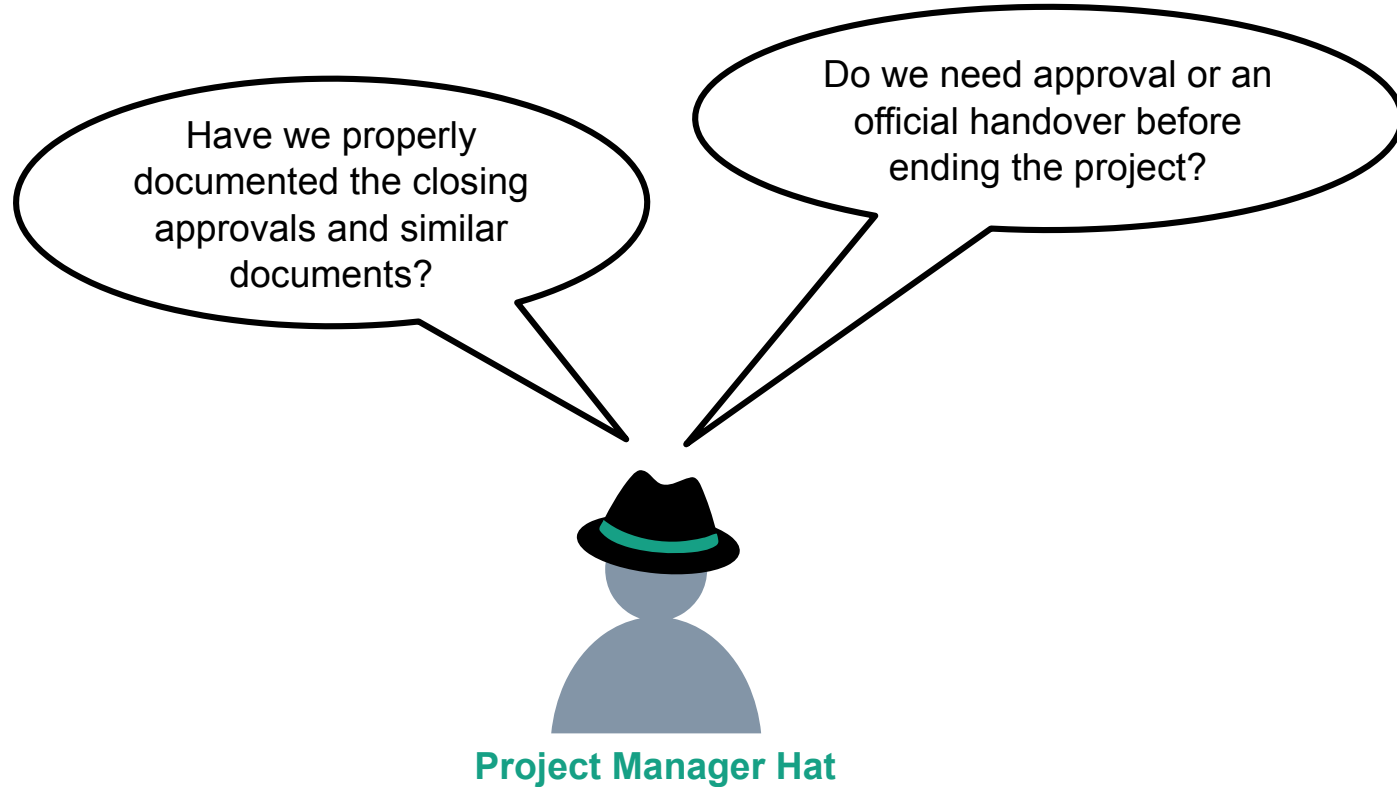

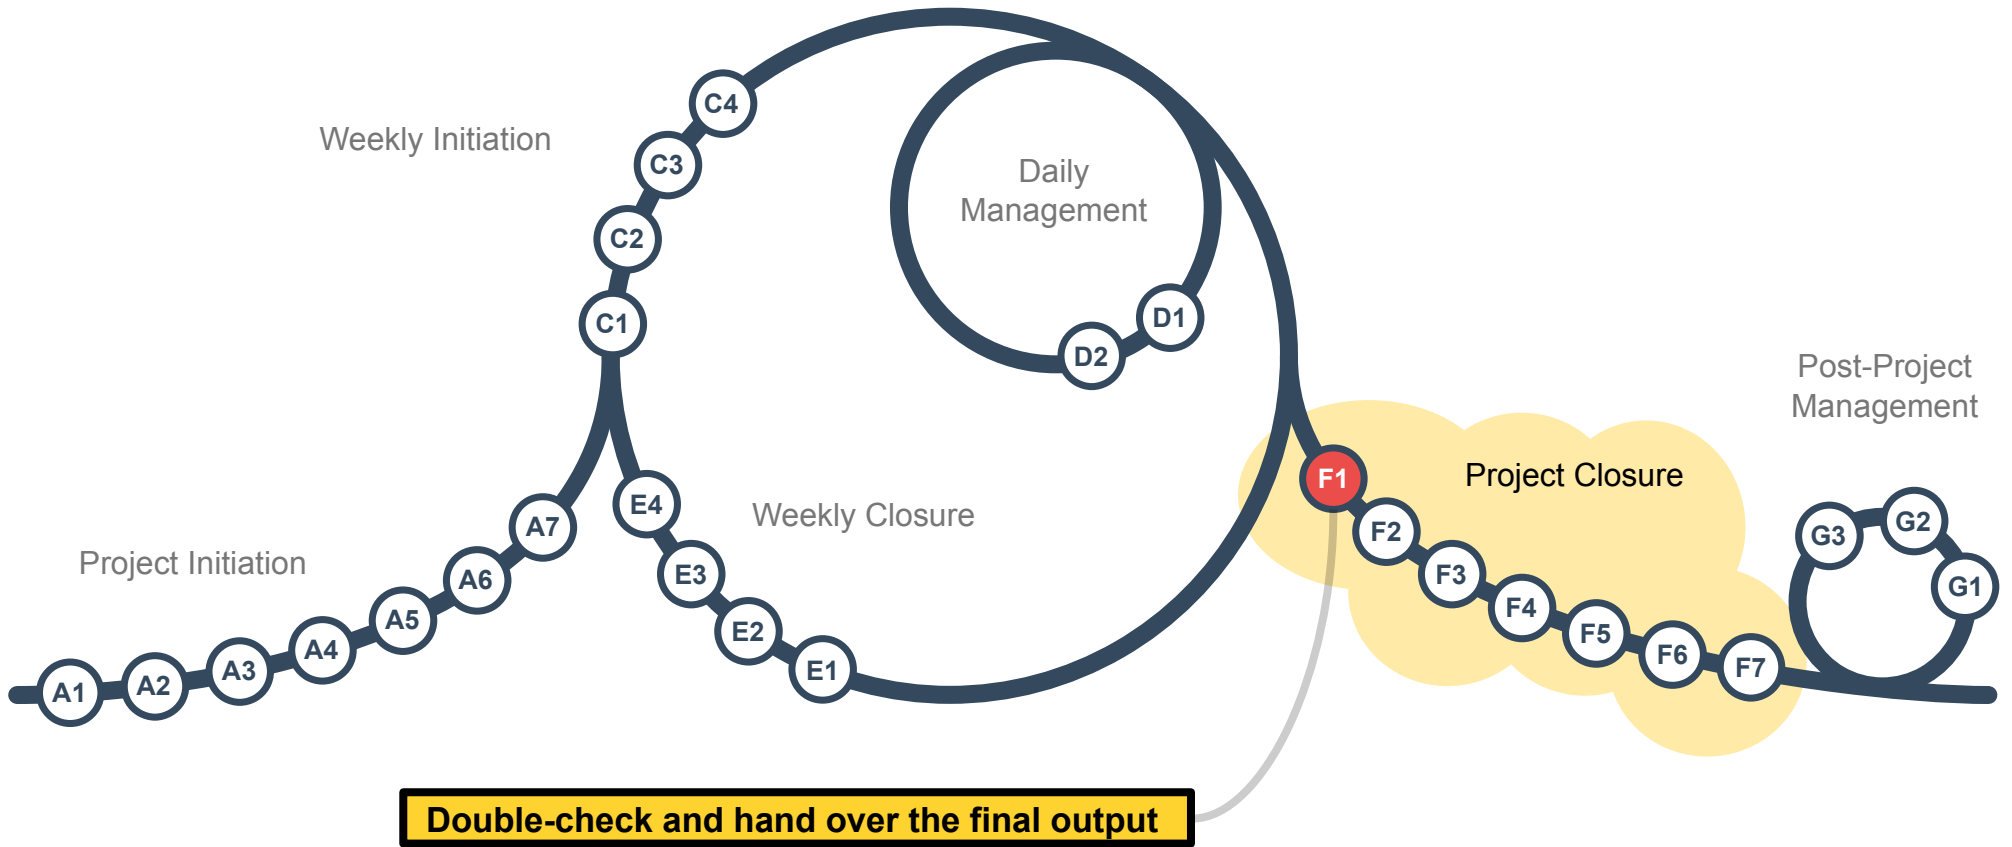


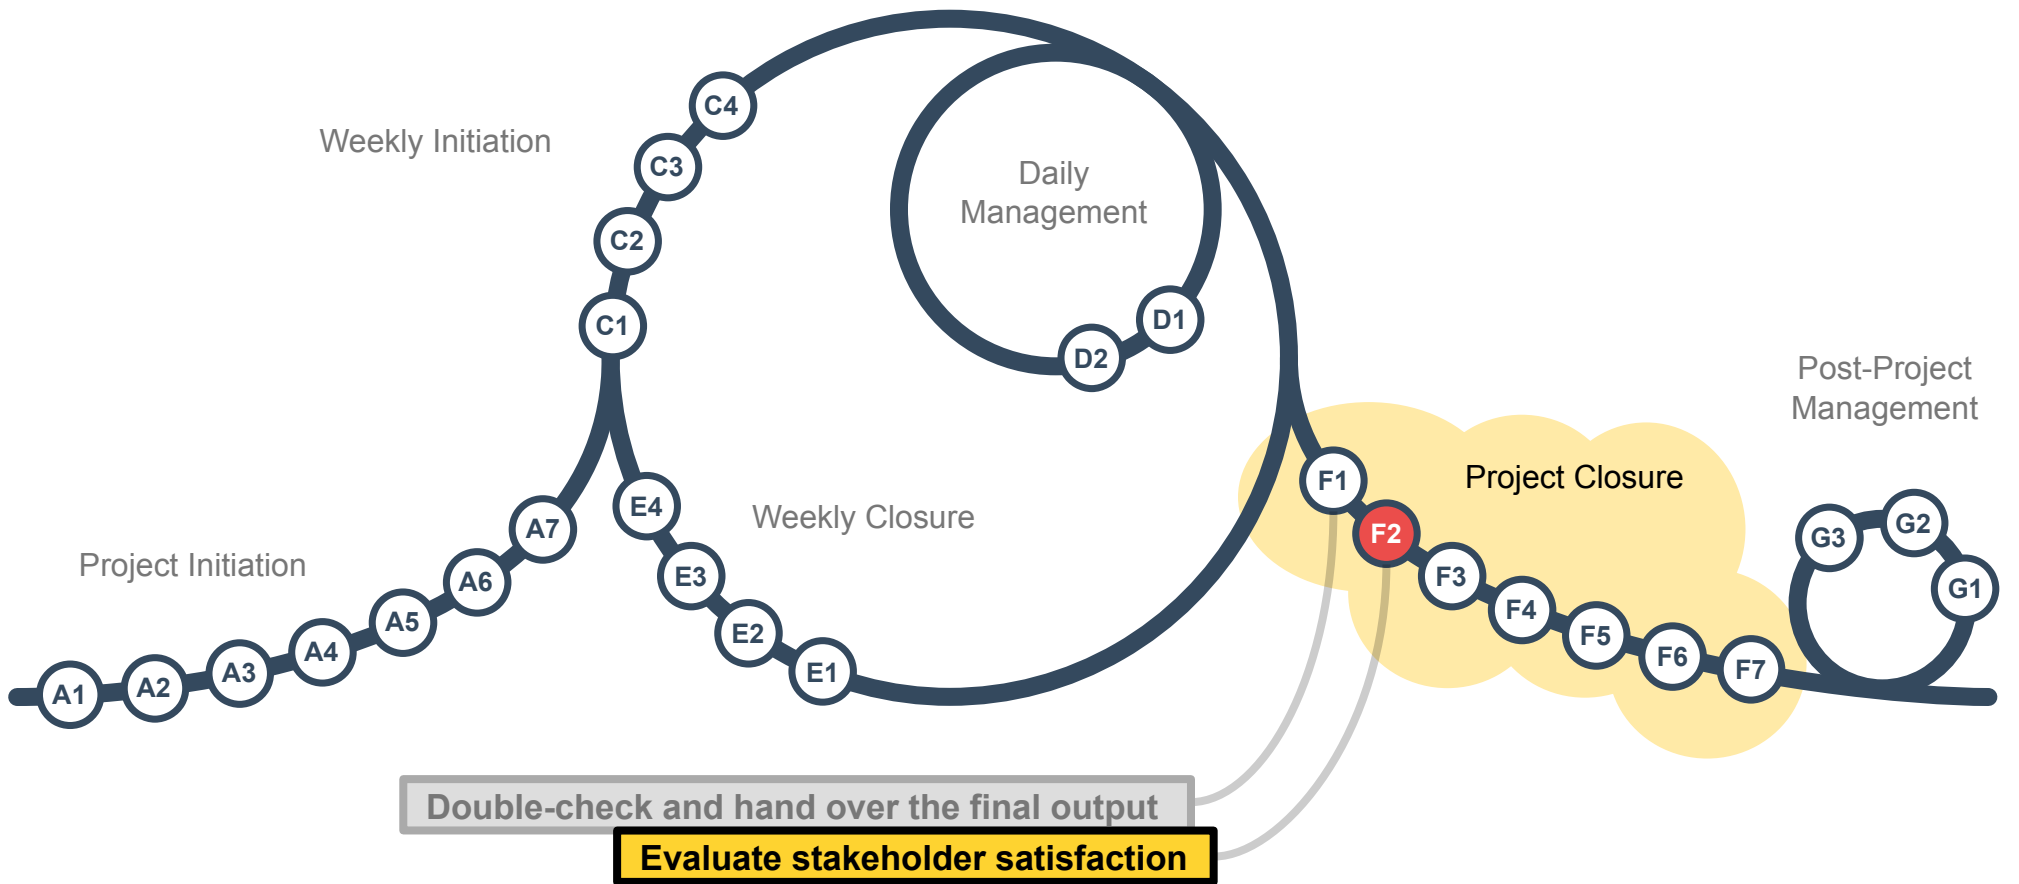

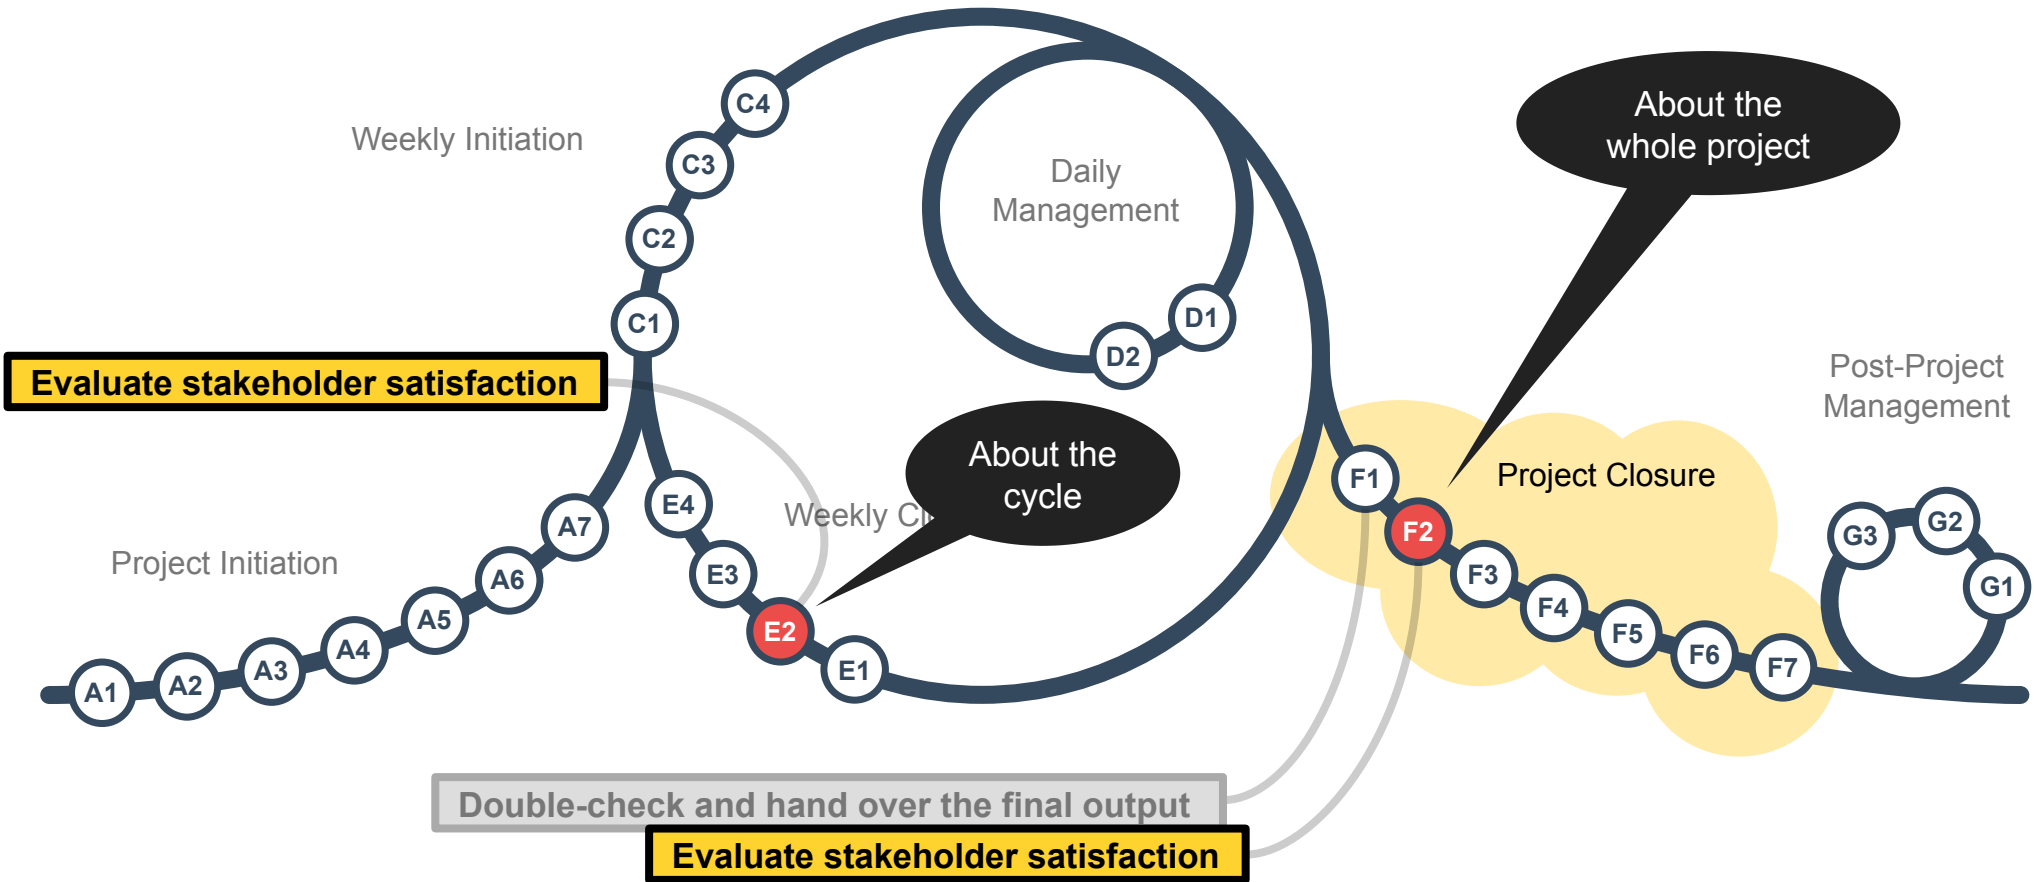

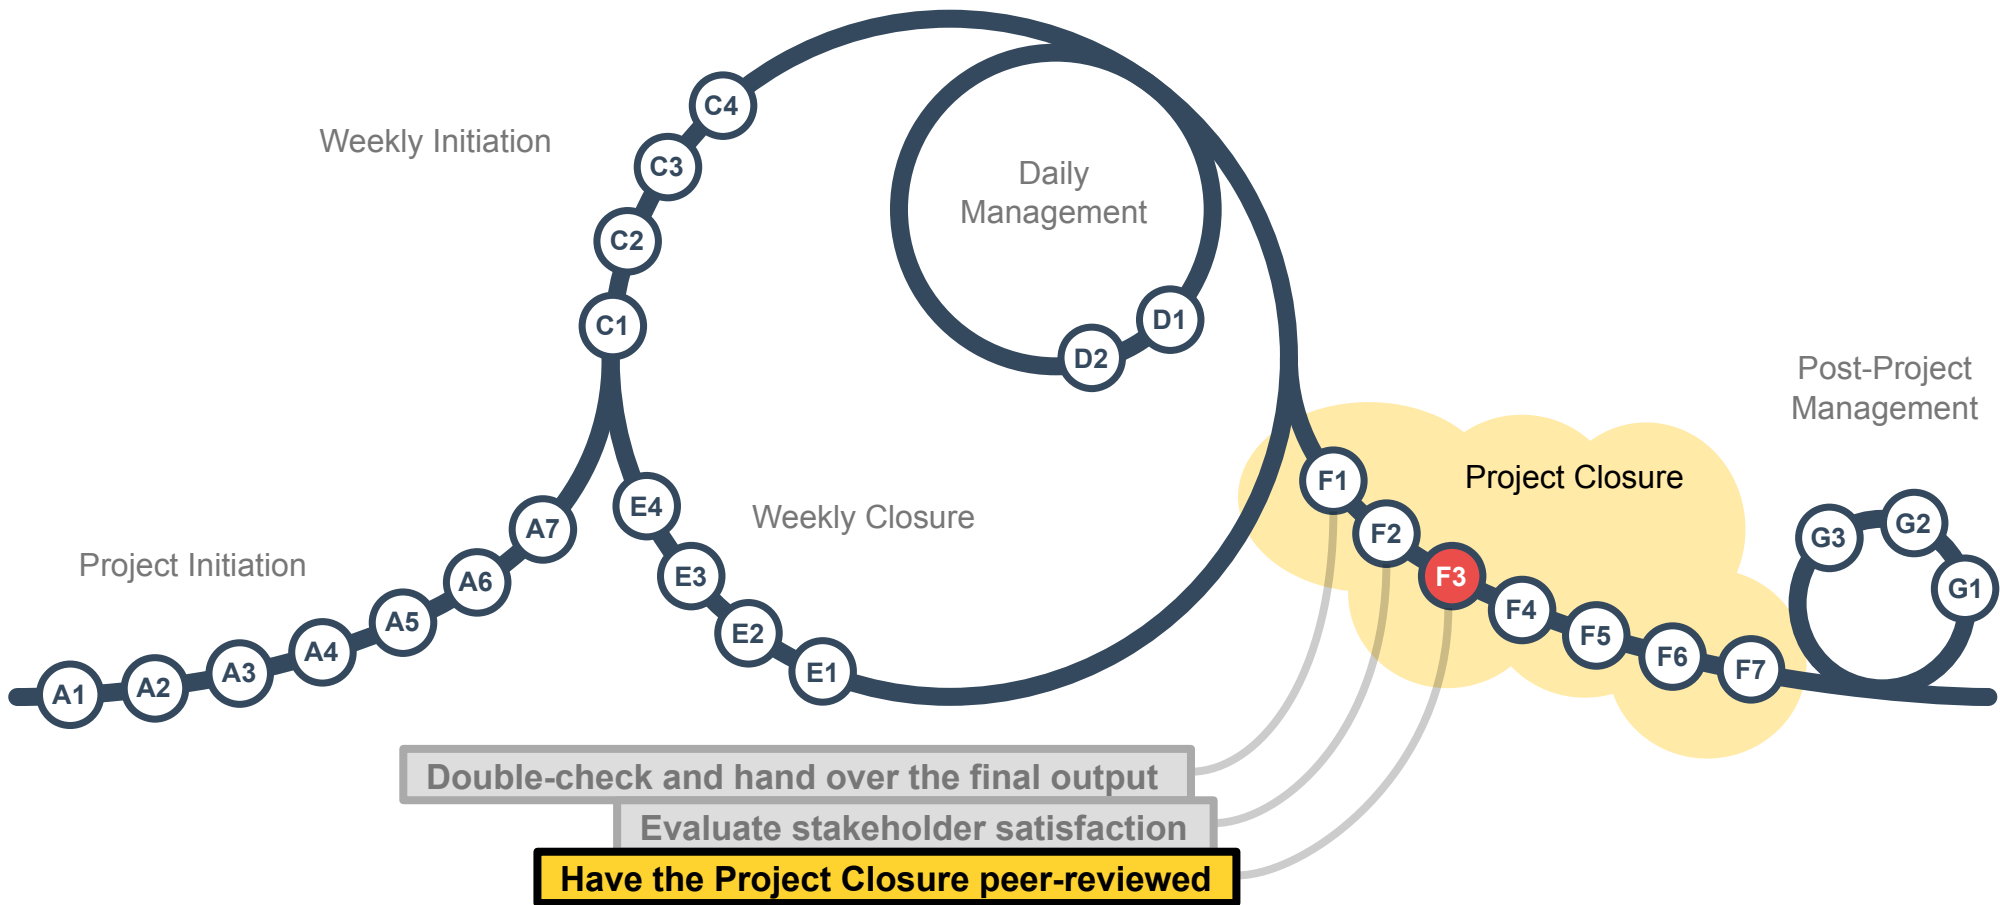


F3 – Have the Project Closure peer-reviewed

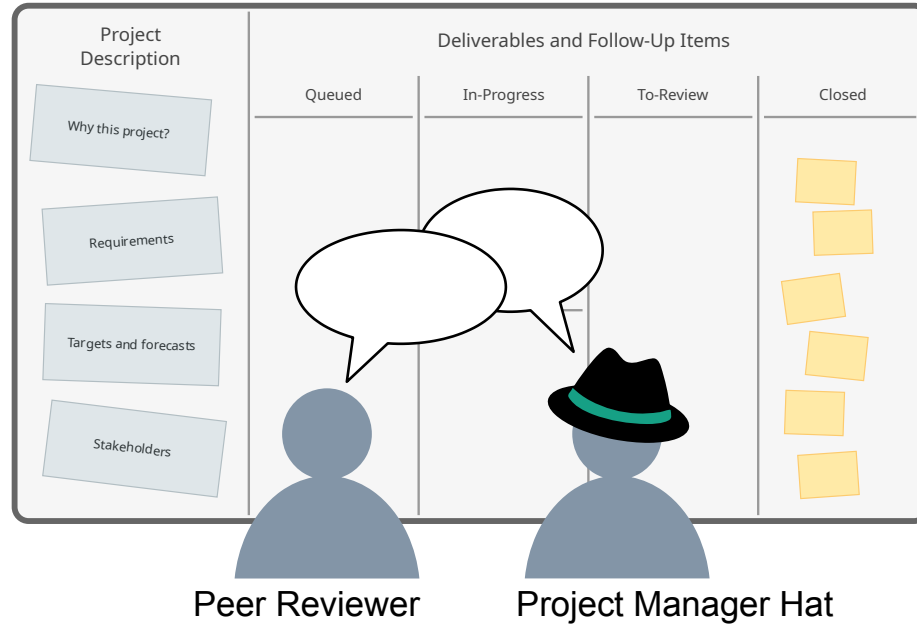



External to the project
Expert in project management
(A different person each time)

- ★ Helps find mistakes
- ★ Both learn from each other

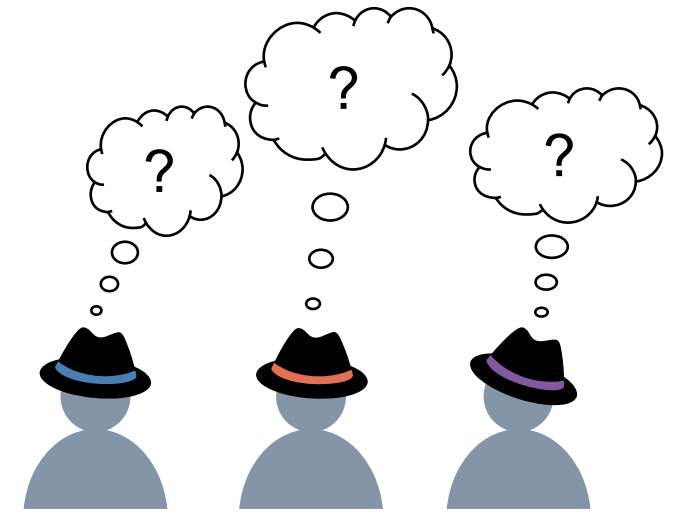

Do other hats need peer-reviews as well?

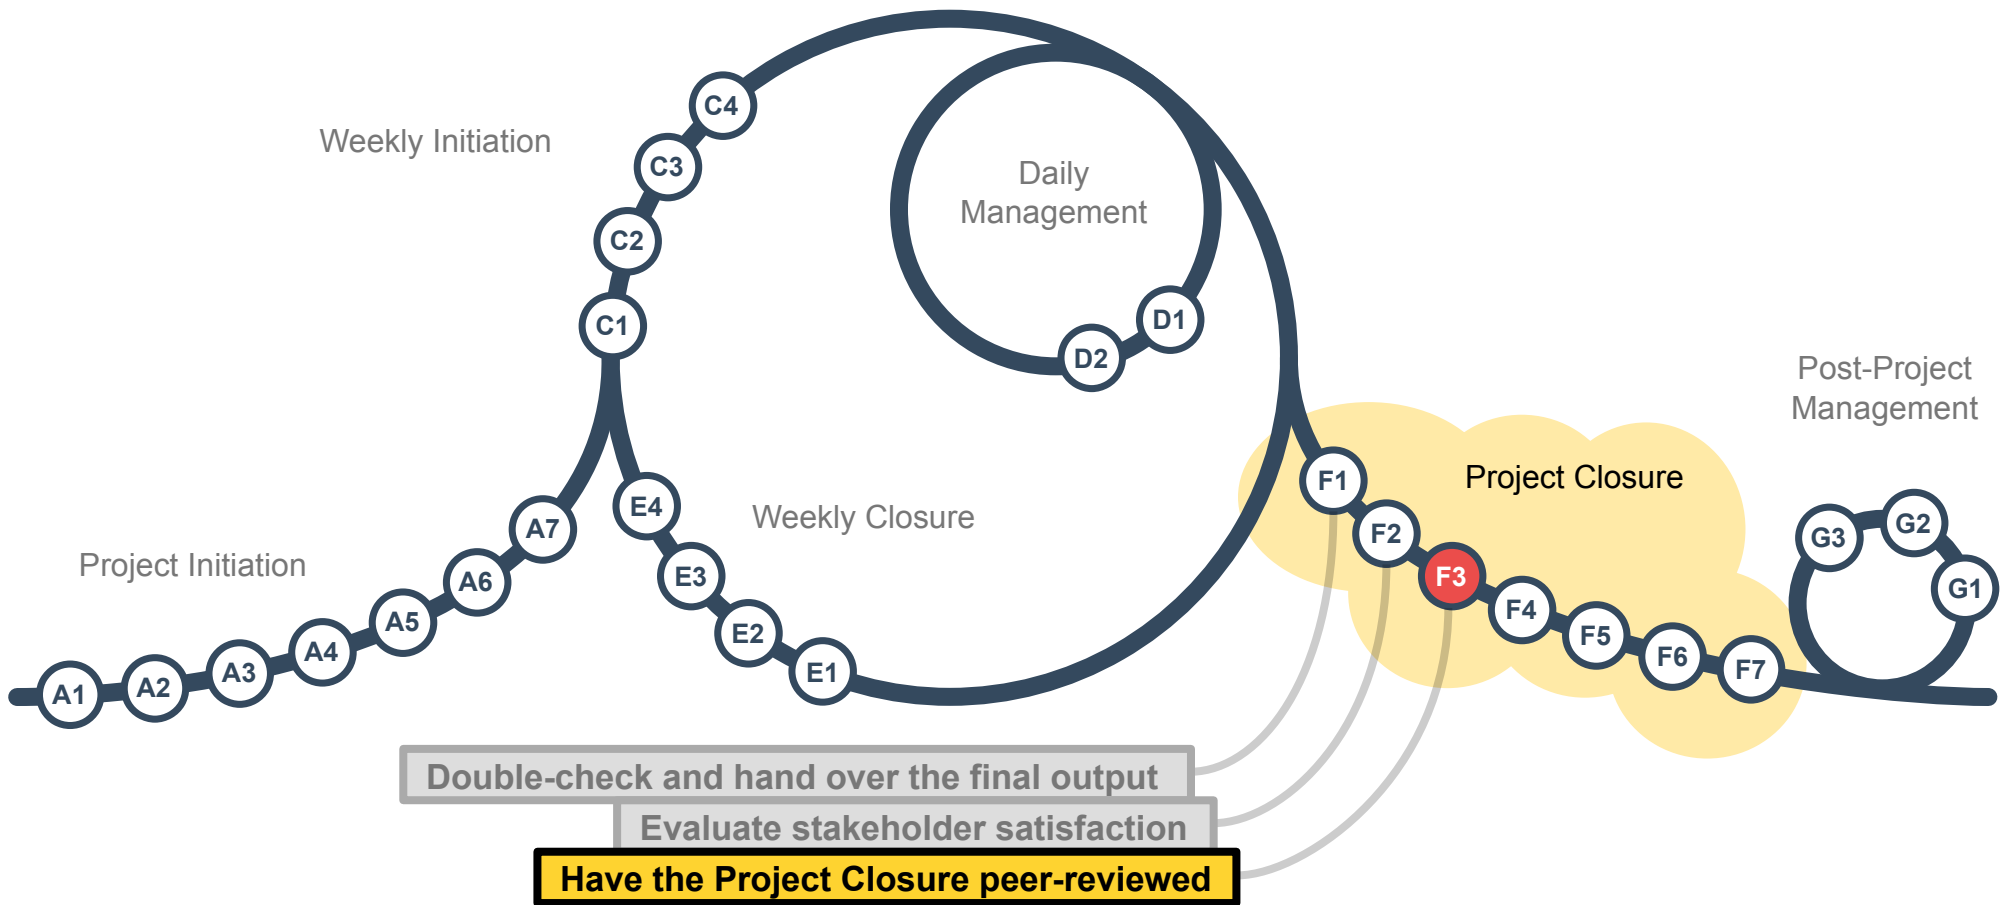

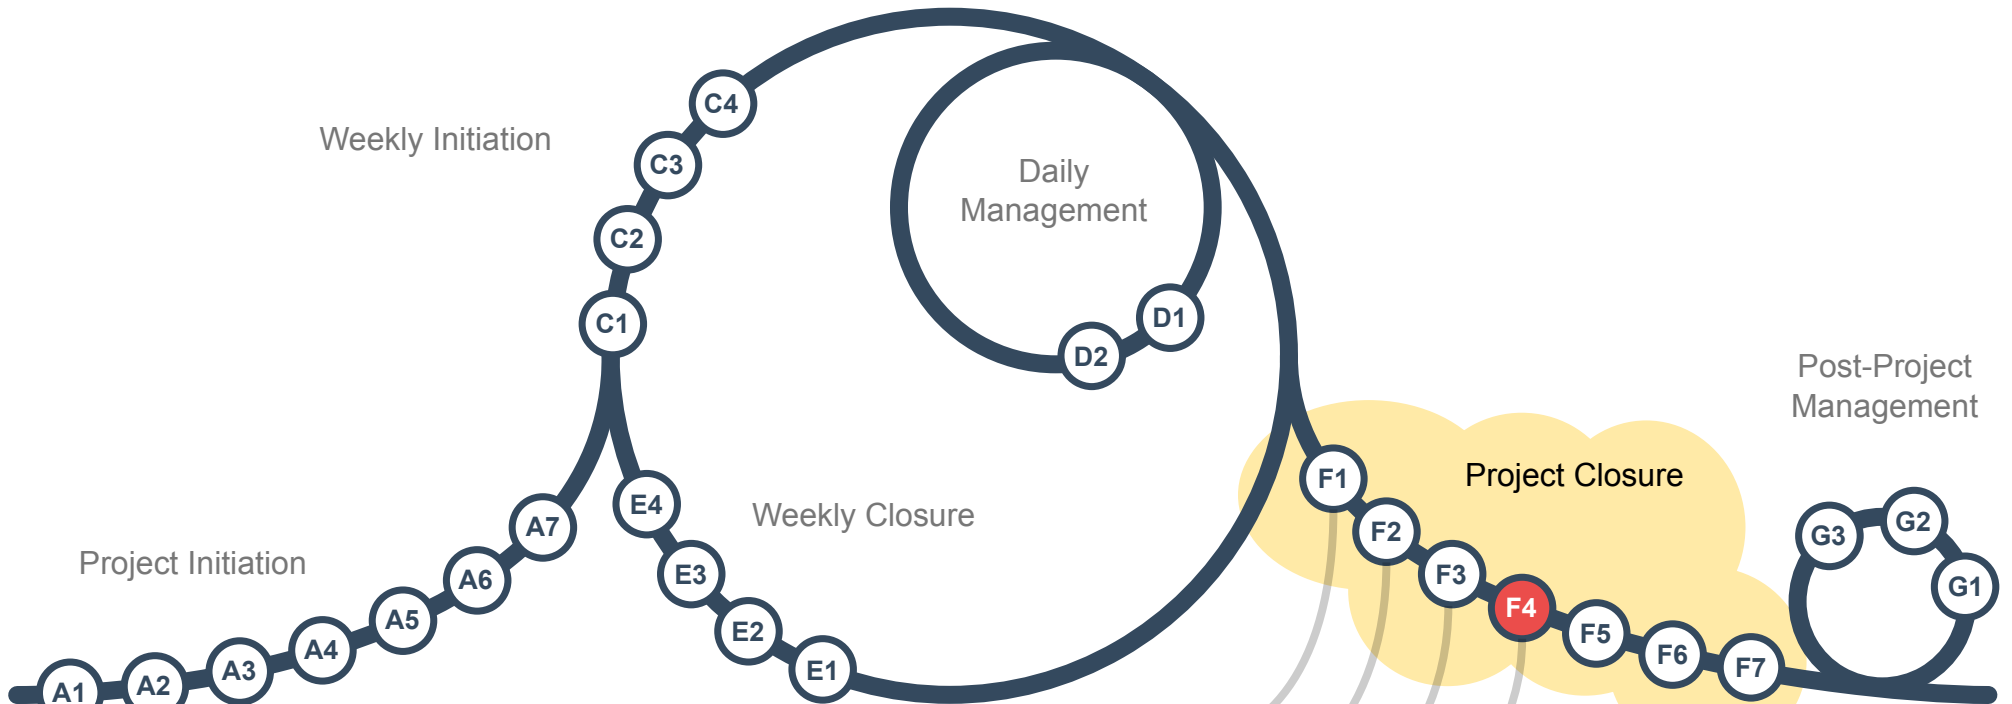

Double-check and hand over the final output

Evaluate stakeholder satisfaction

Have the Project Closure peer-reviewed

Consider swapping hats for Post-Project Management

F4 – Consider swapping hats for Post-Project Management

Next to last cycle




Last cycle



Post-Project Management



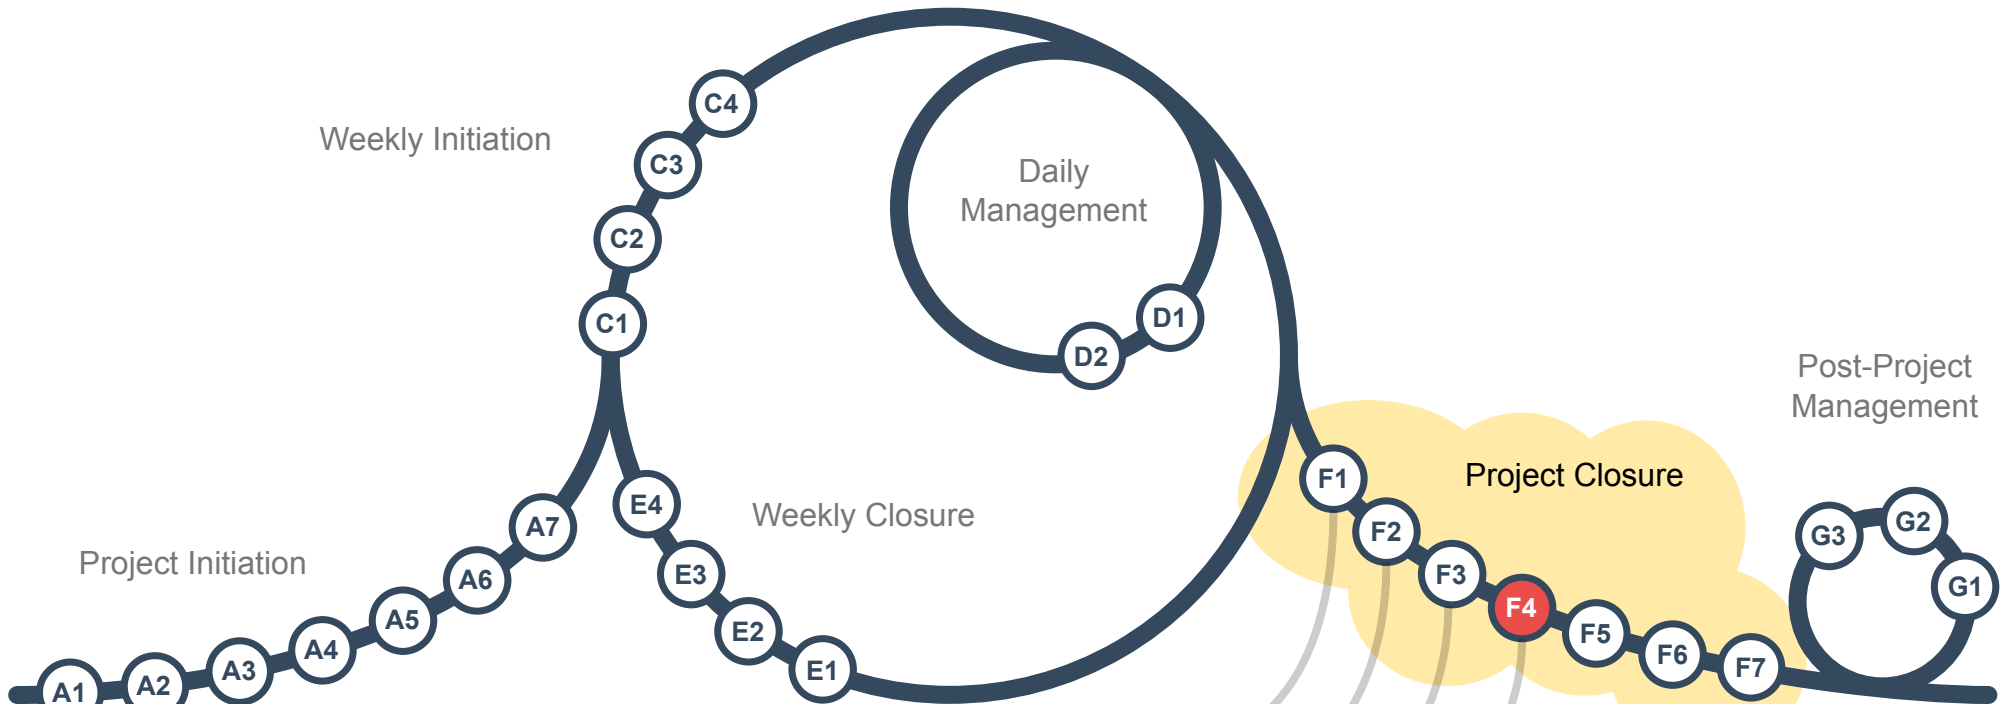


Double-check and hand over the final output

Evaluate stakeholder satisfaction

Have the Project Closure peer-reviewed


Consider swapping hats for Post-Project Management

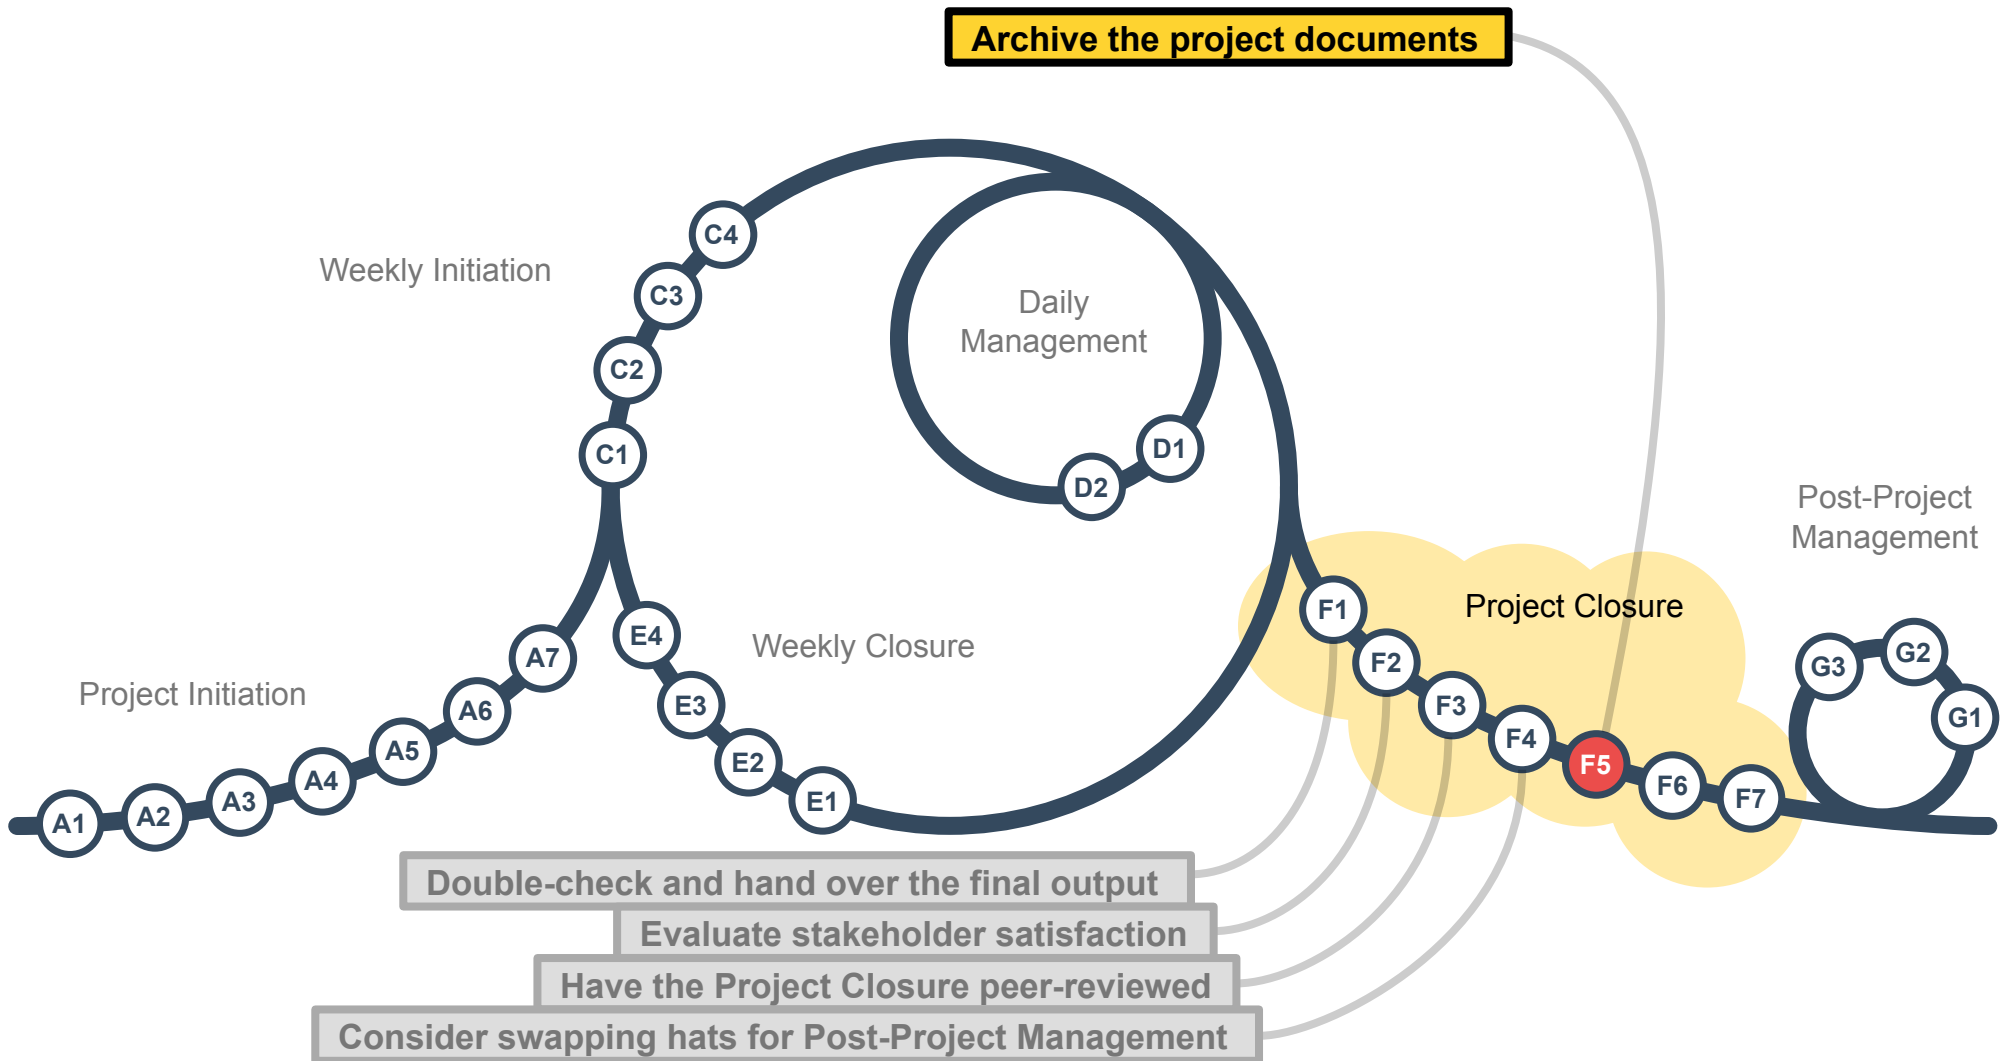



What concerns do you think each hat should have
in this management activity?




F5 – Archive the project documents

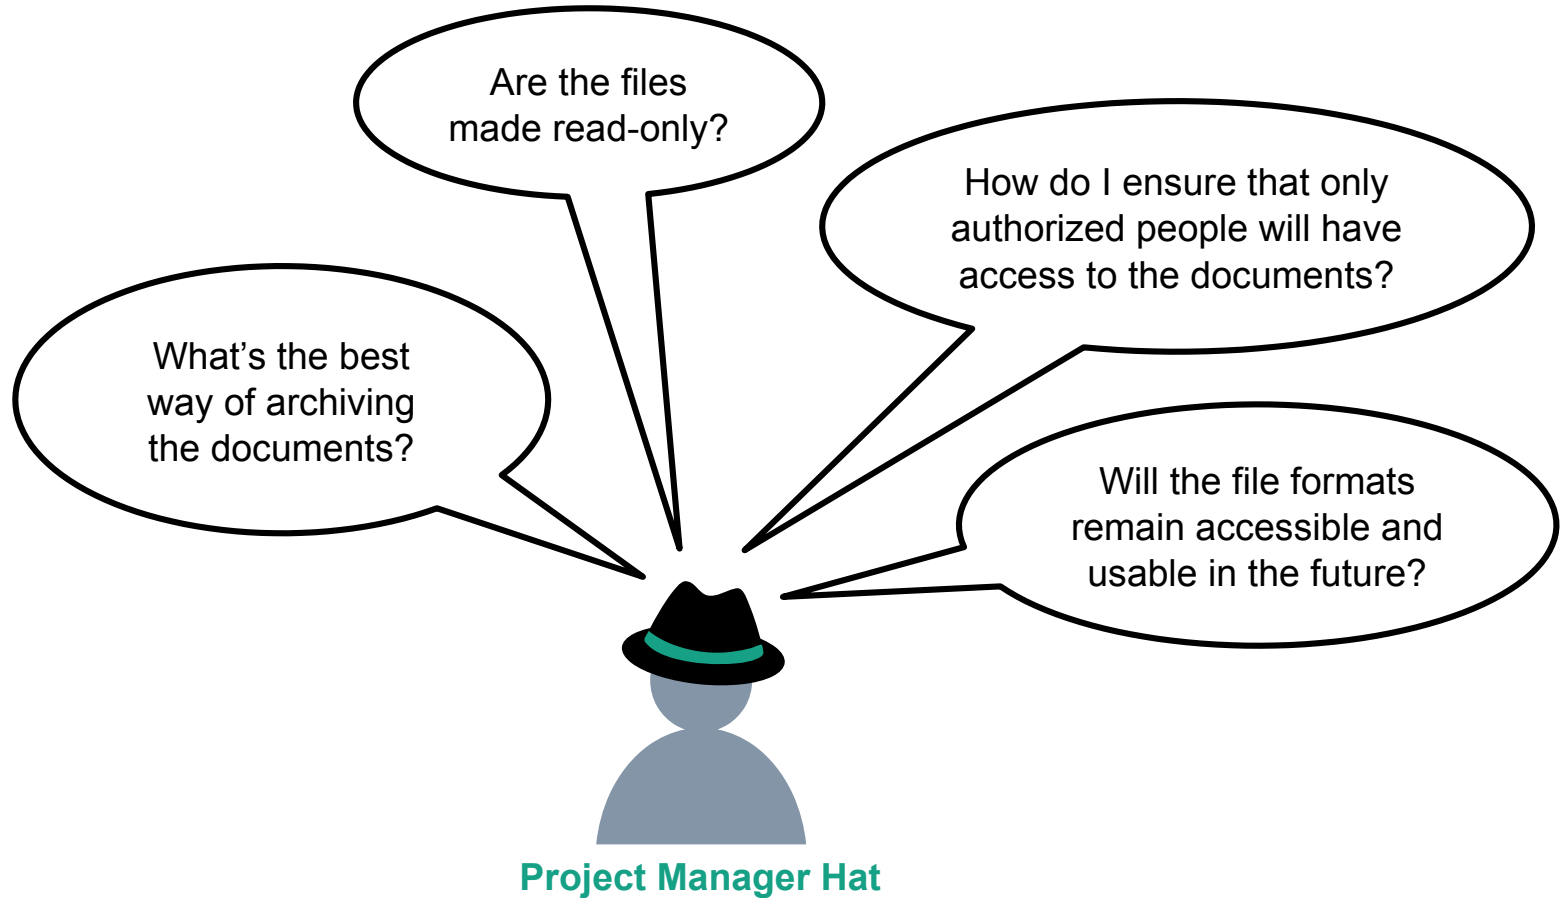


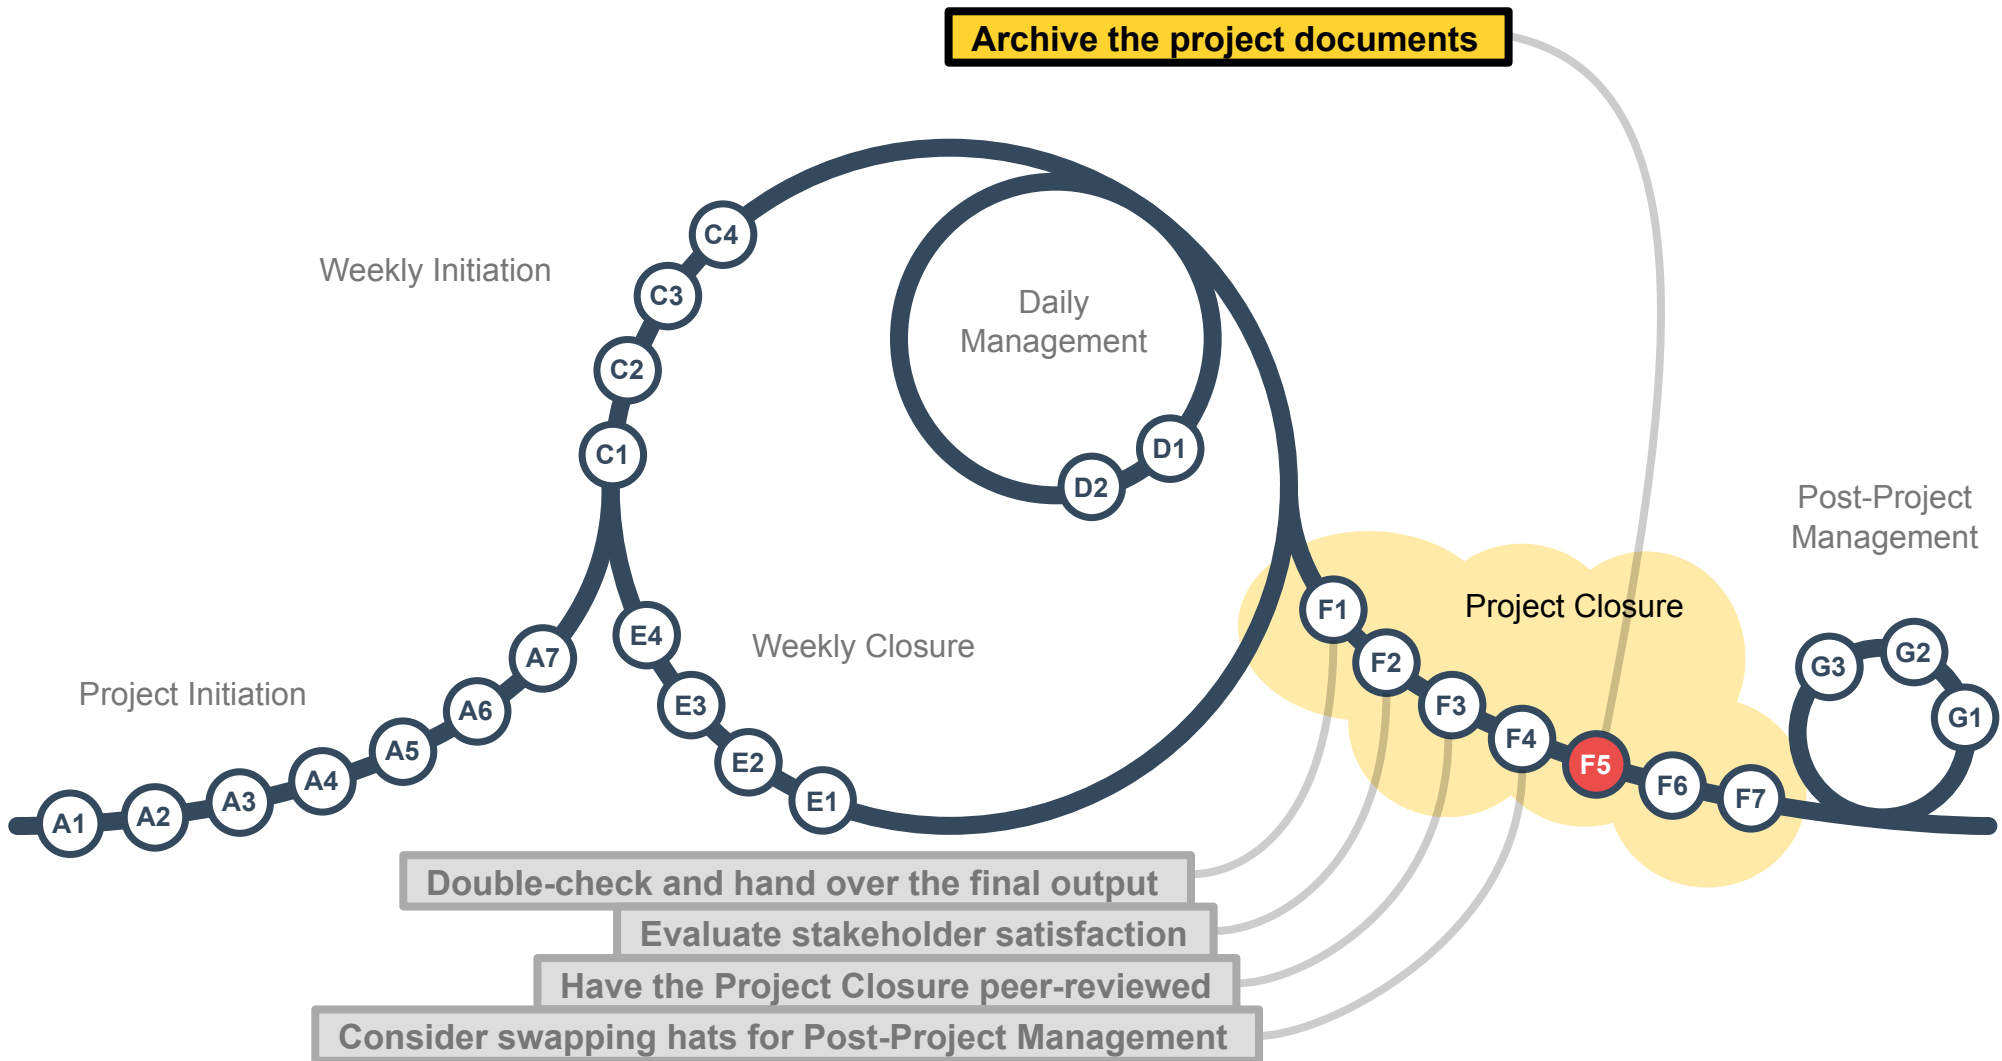


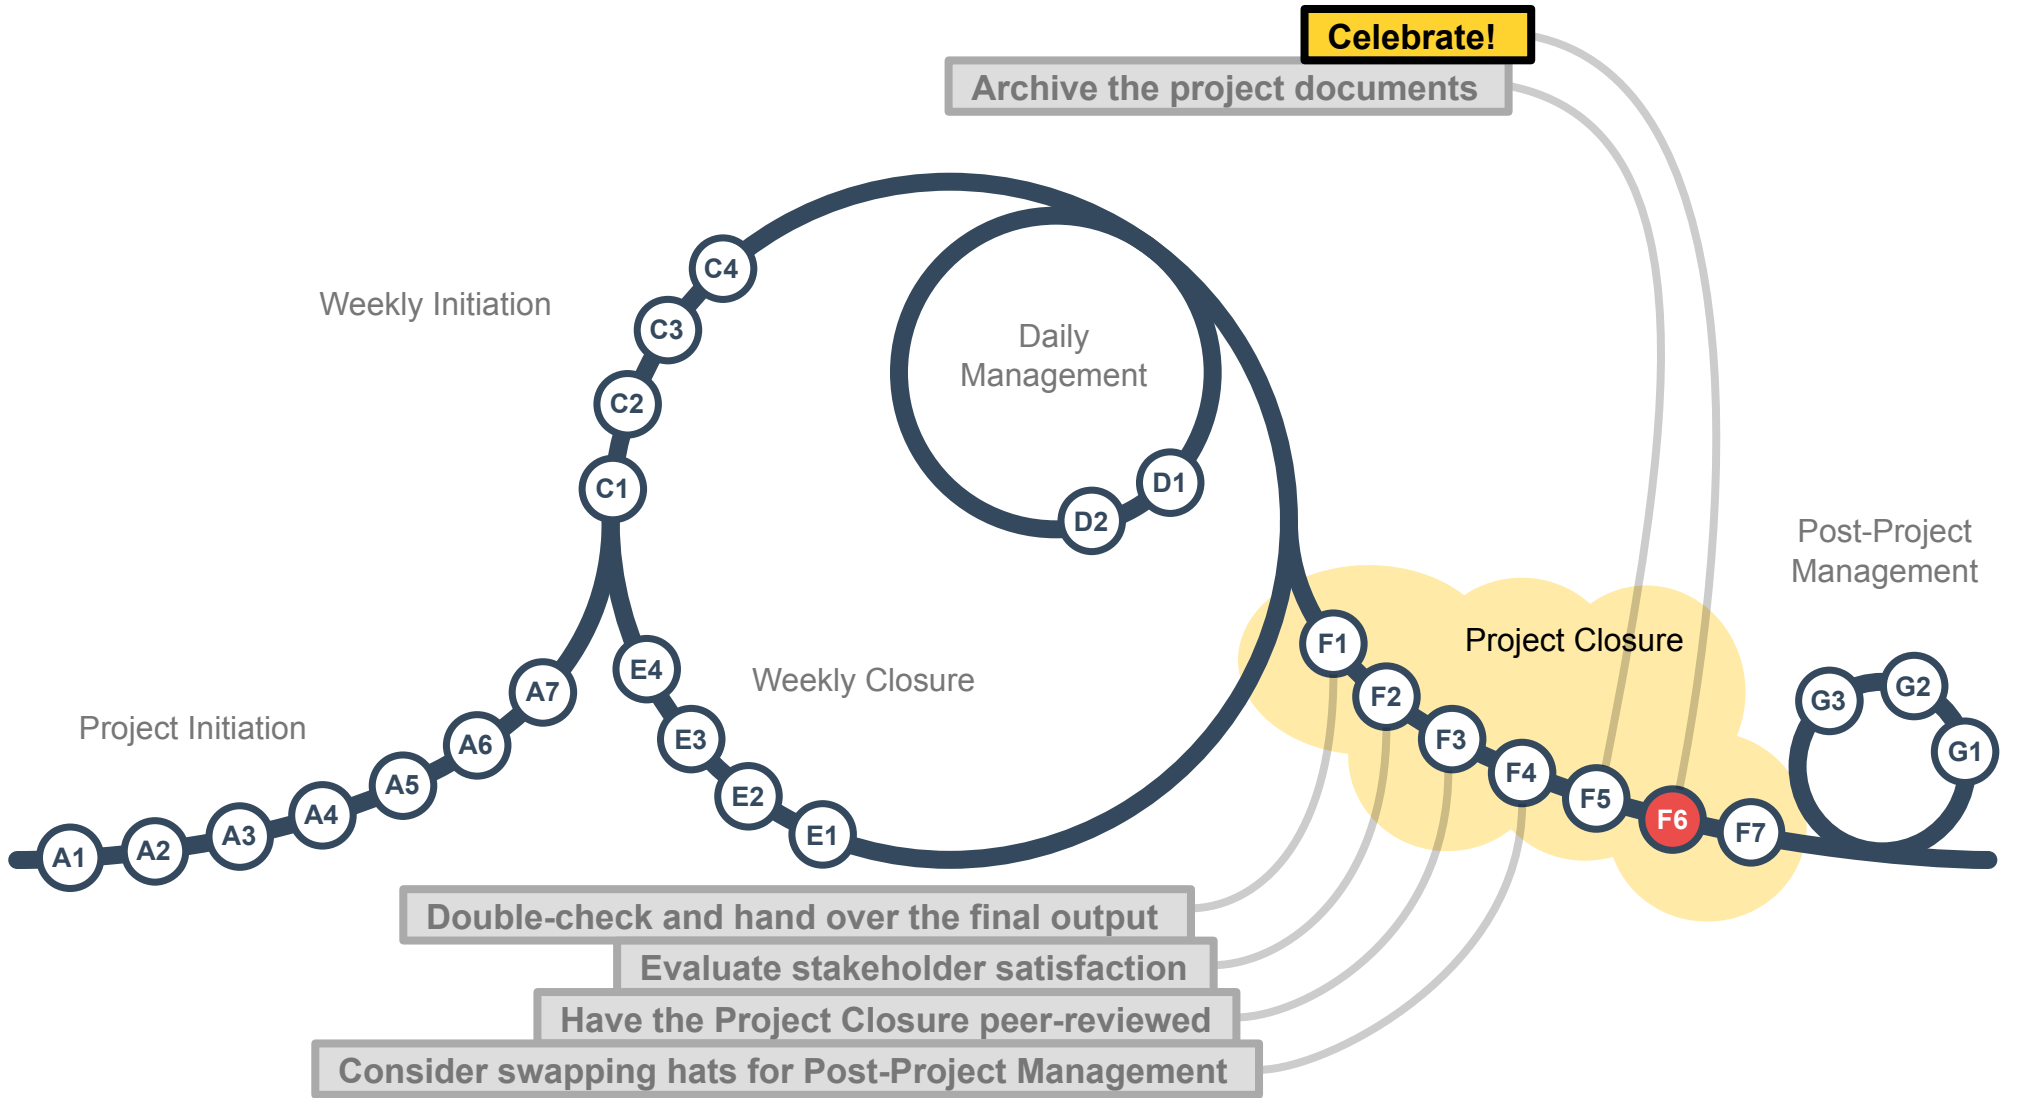

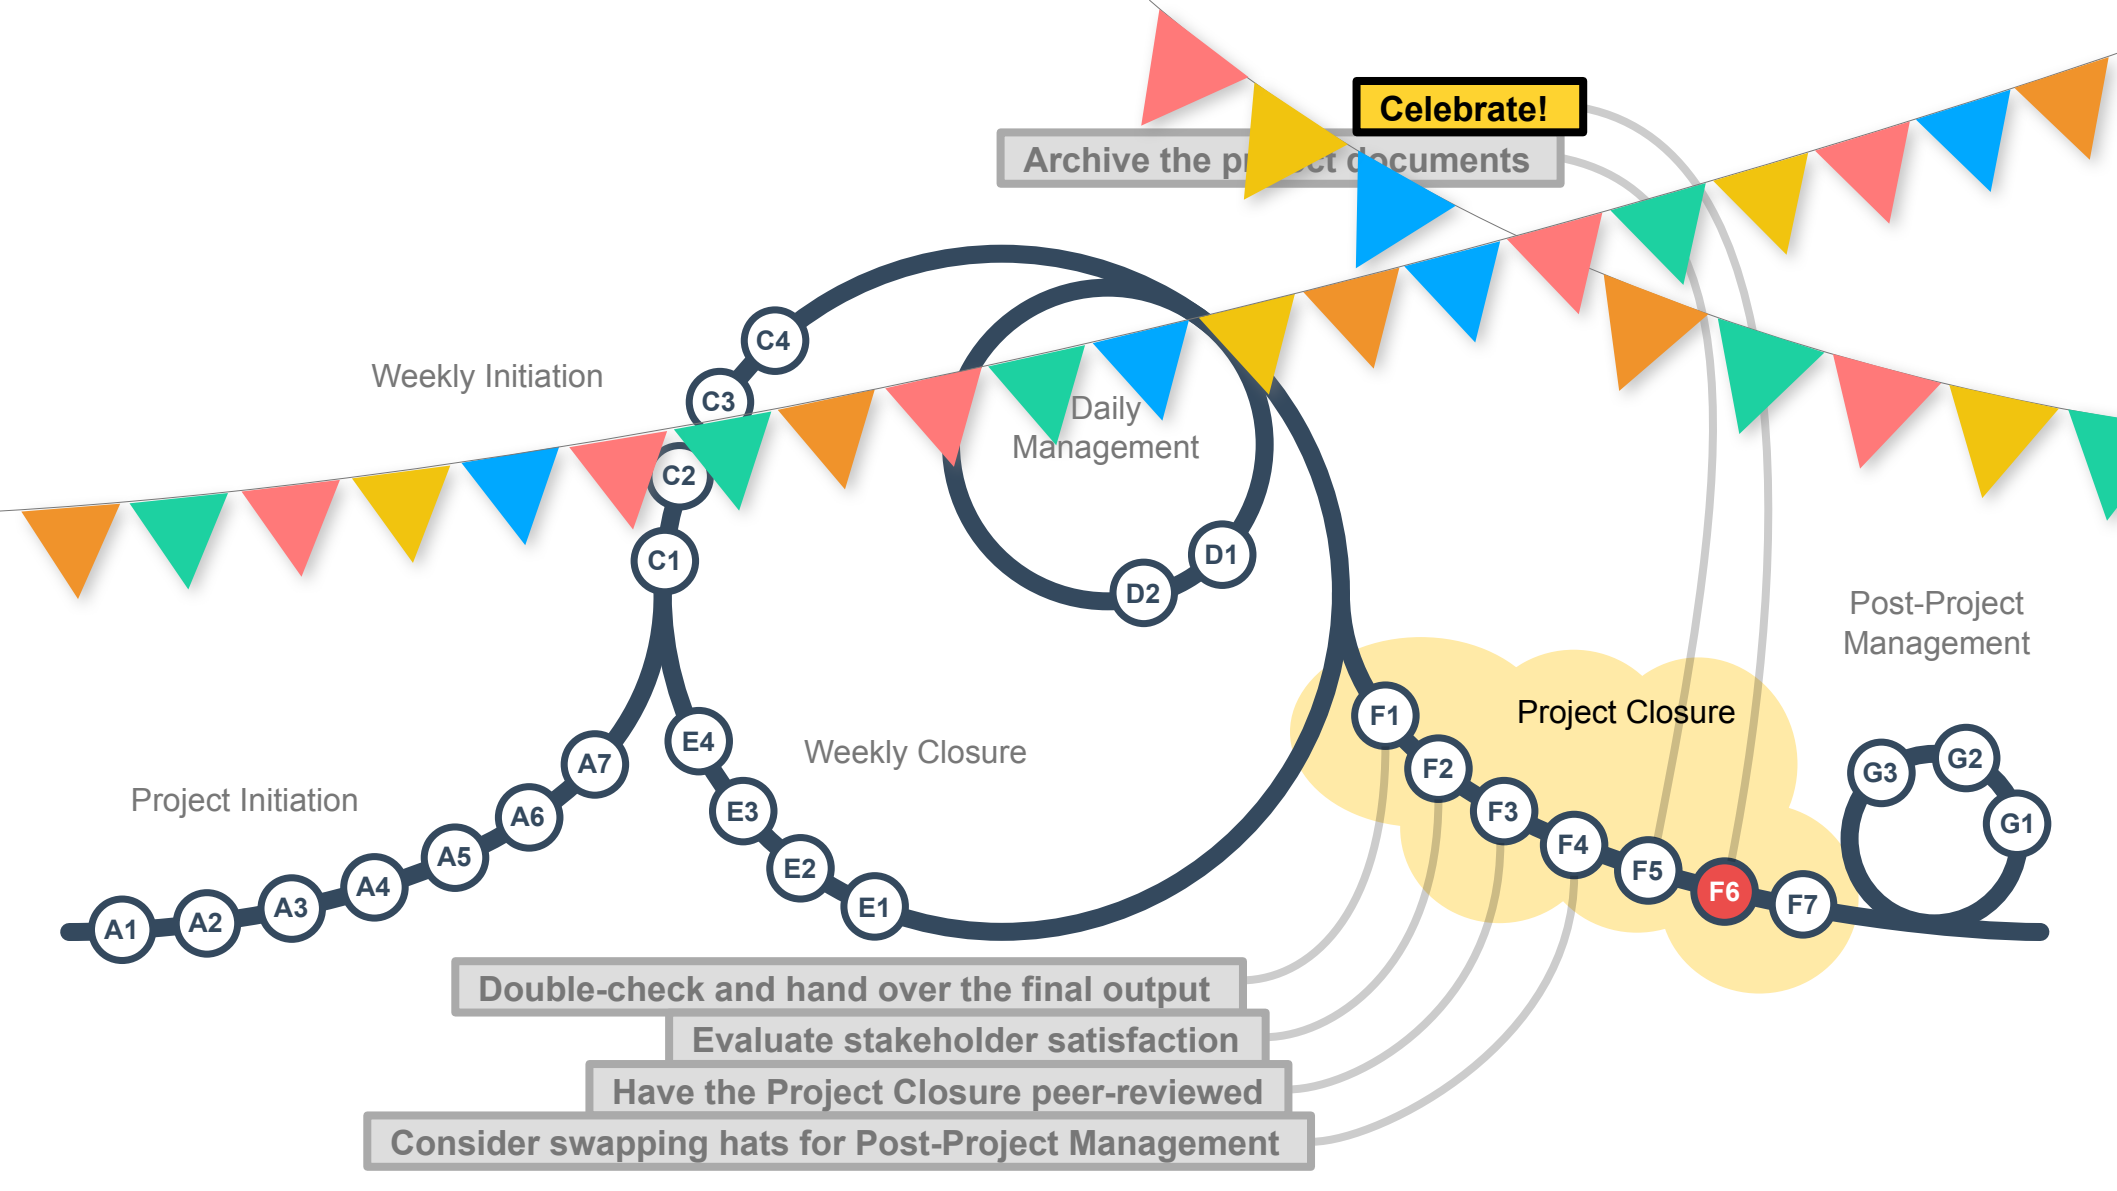


An investment in future projects

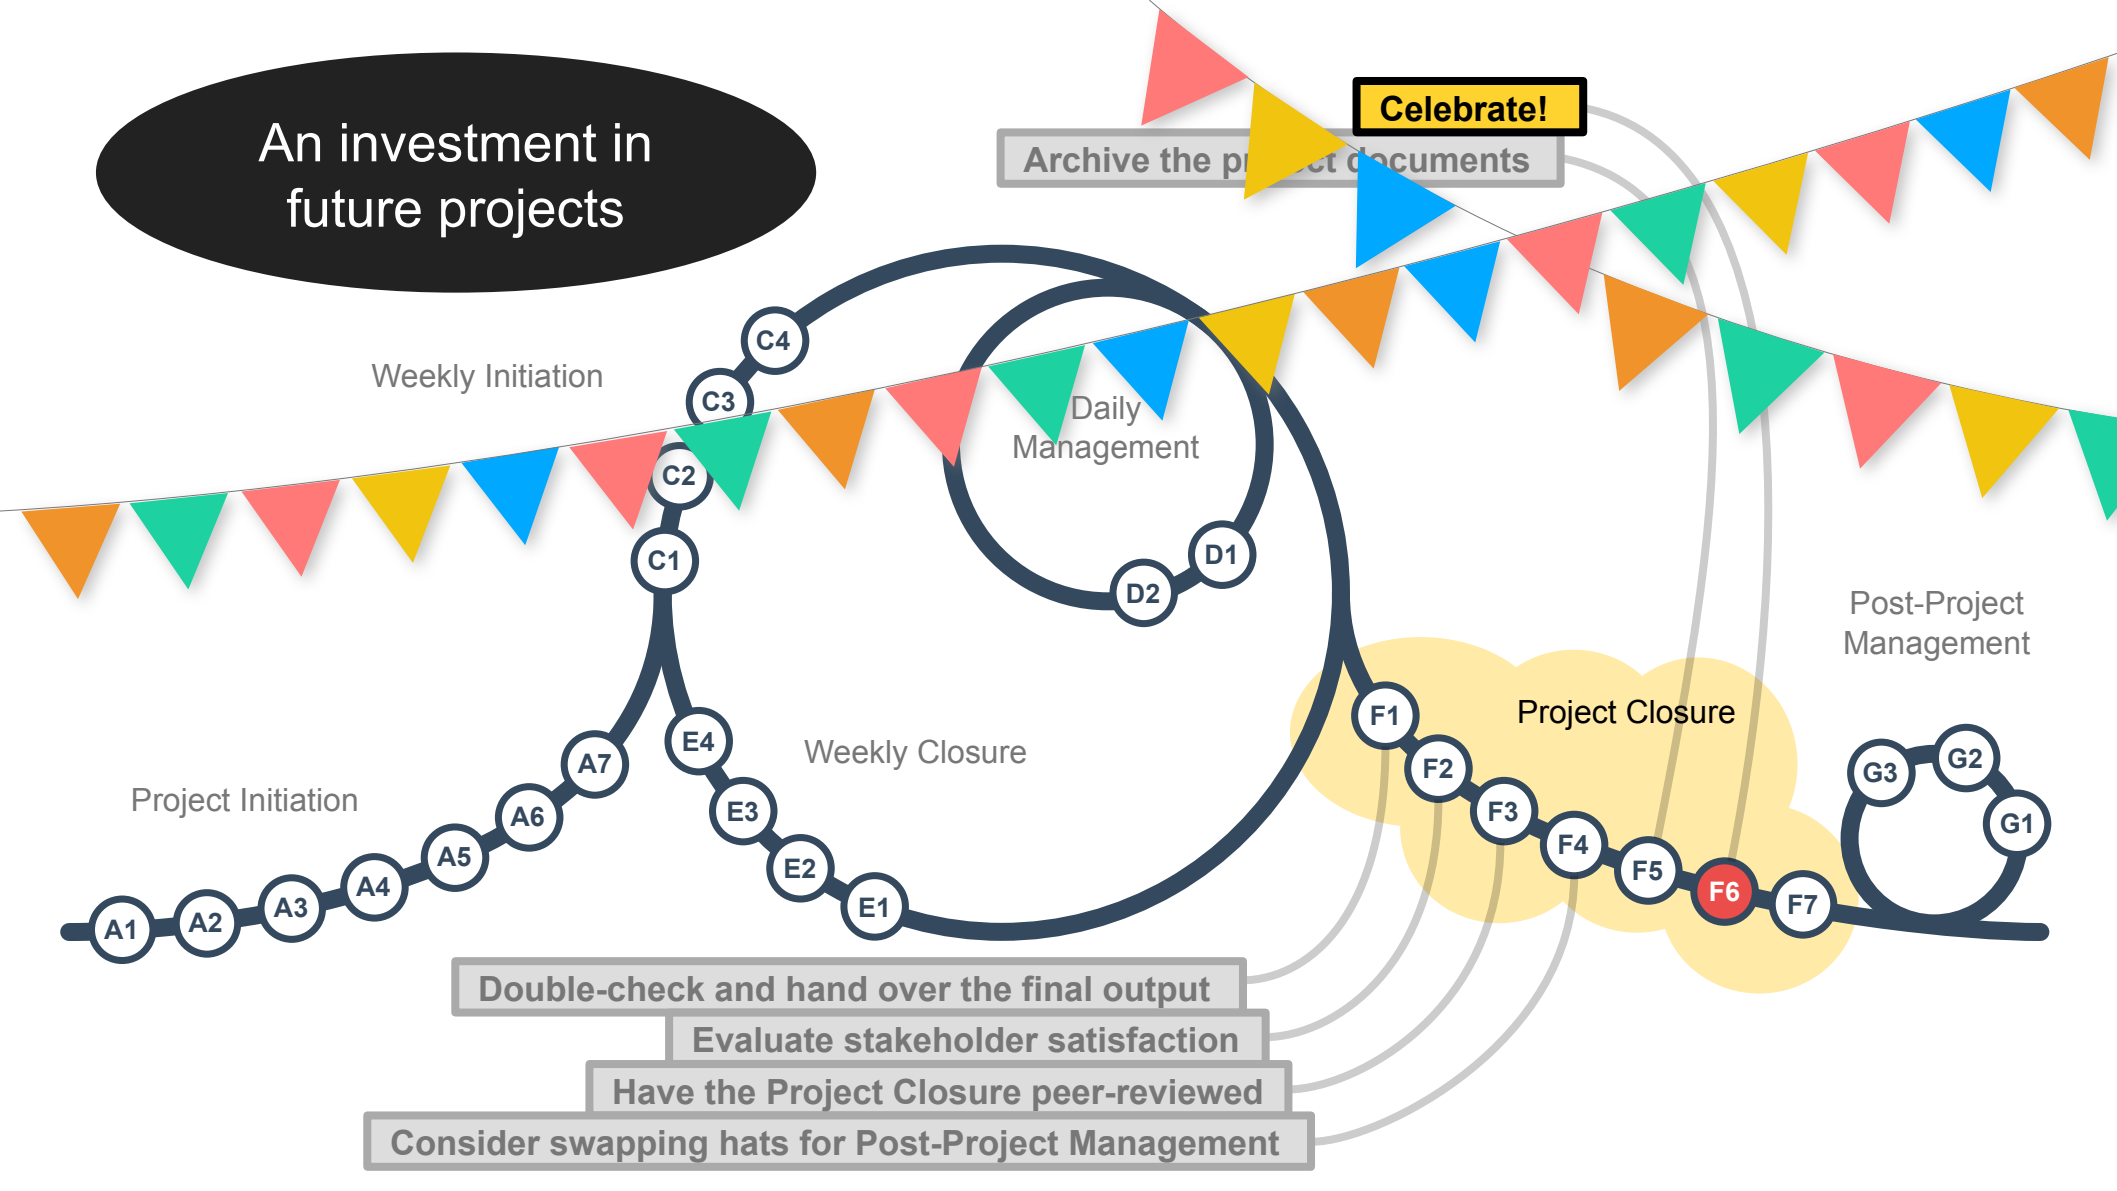


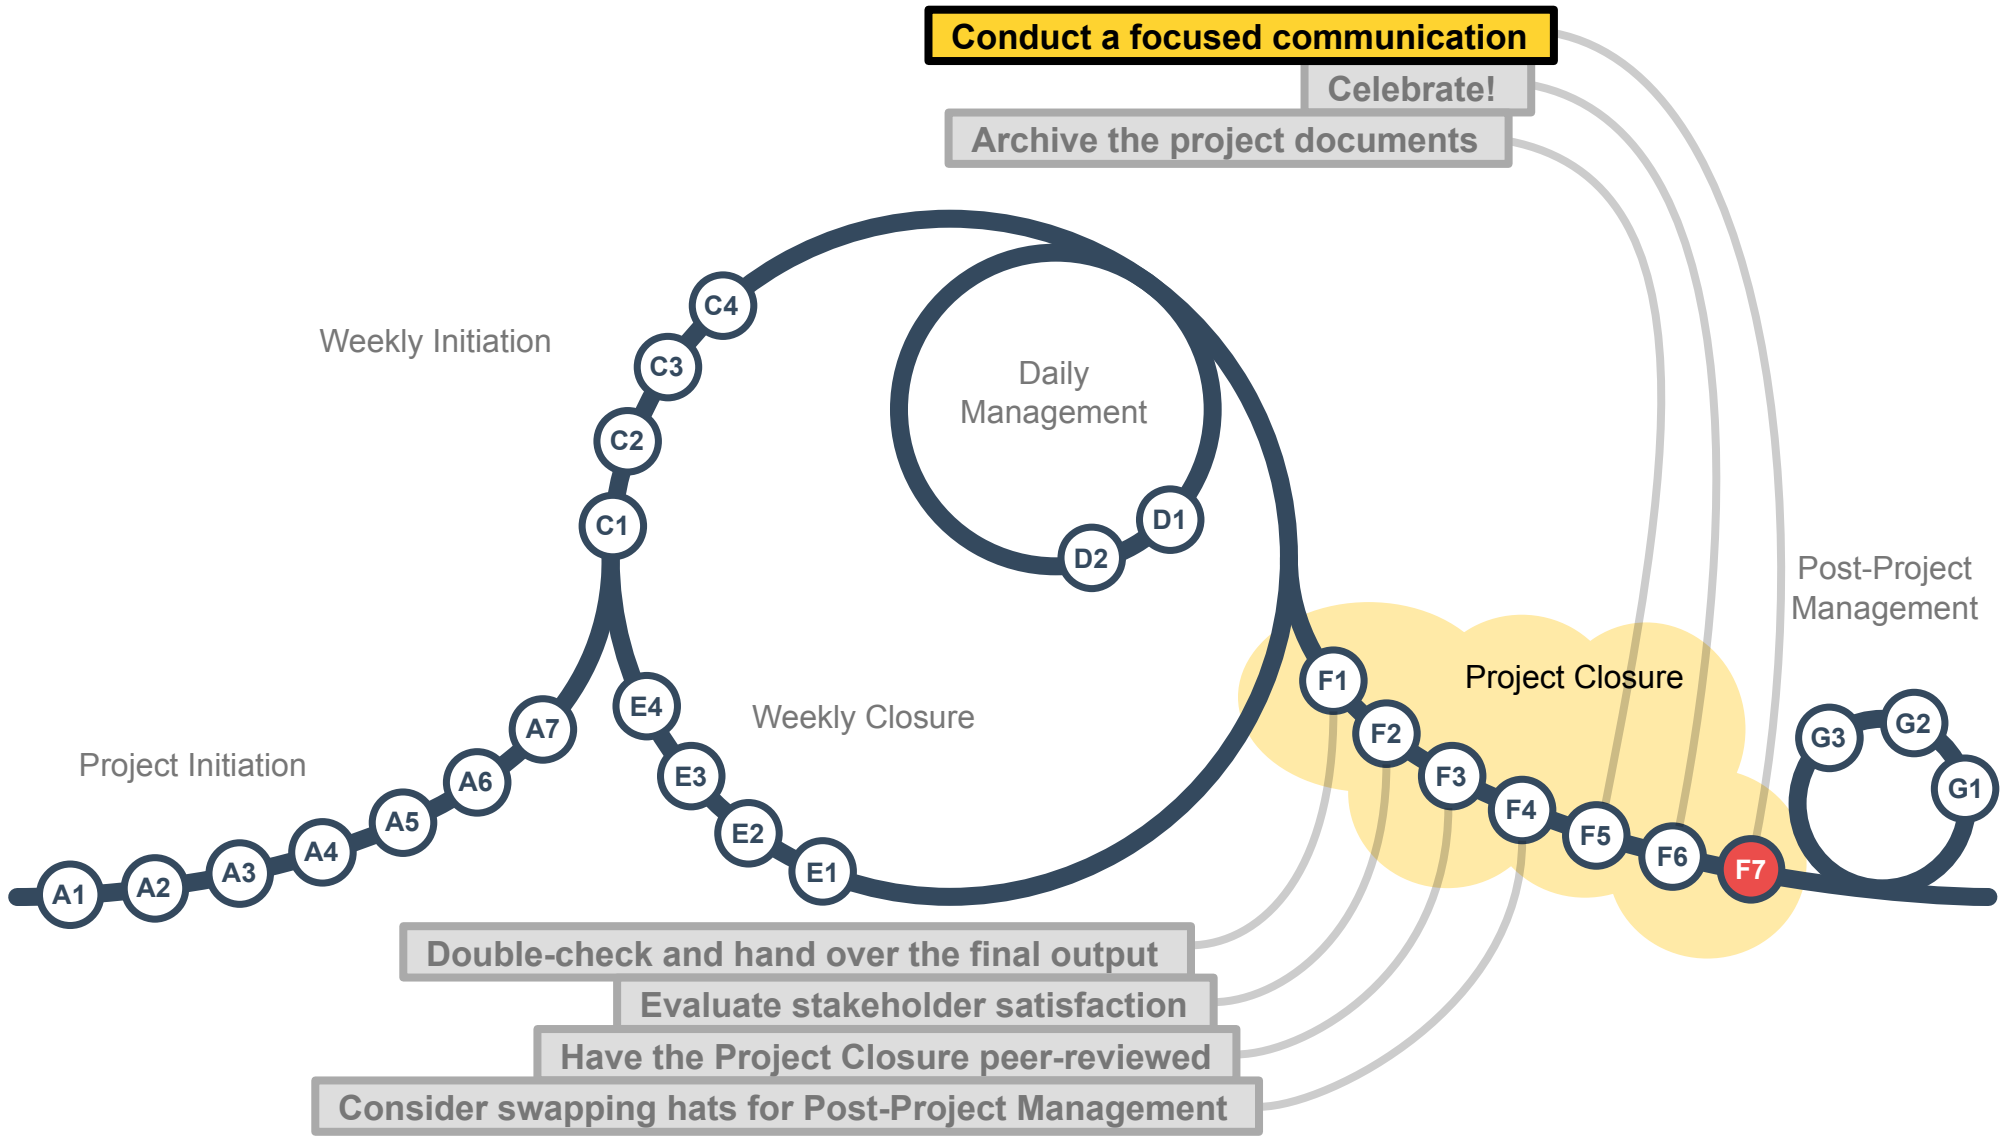



F7 – Conduct a focused communication

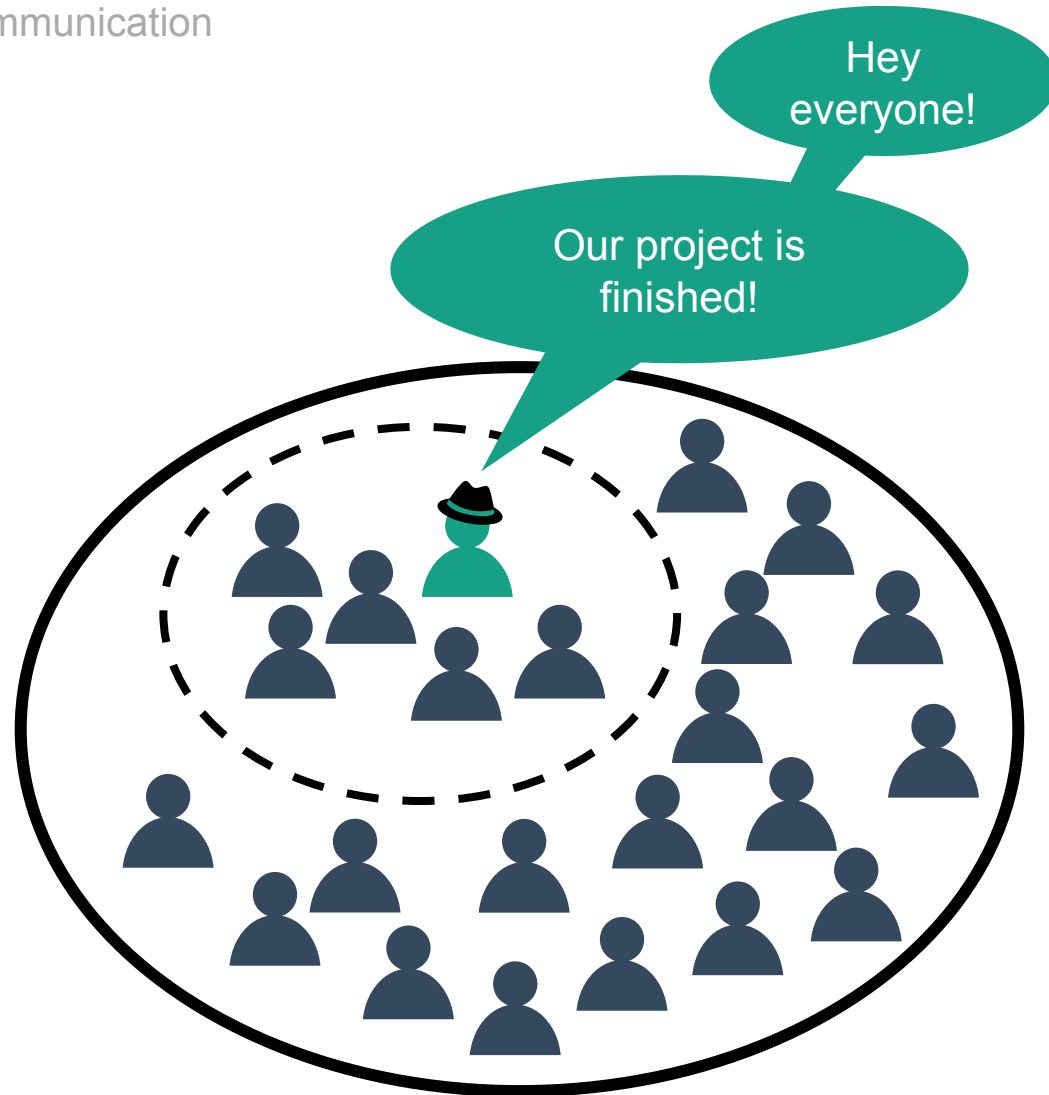


F7 – Conduct a focused communication



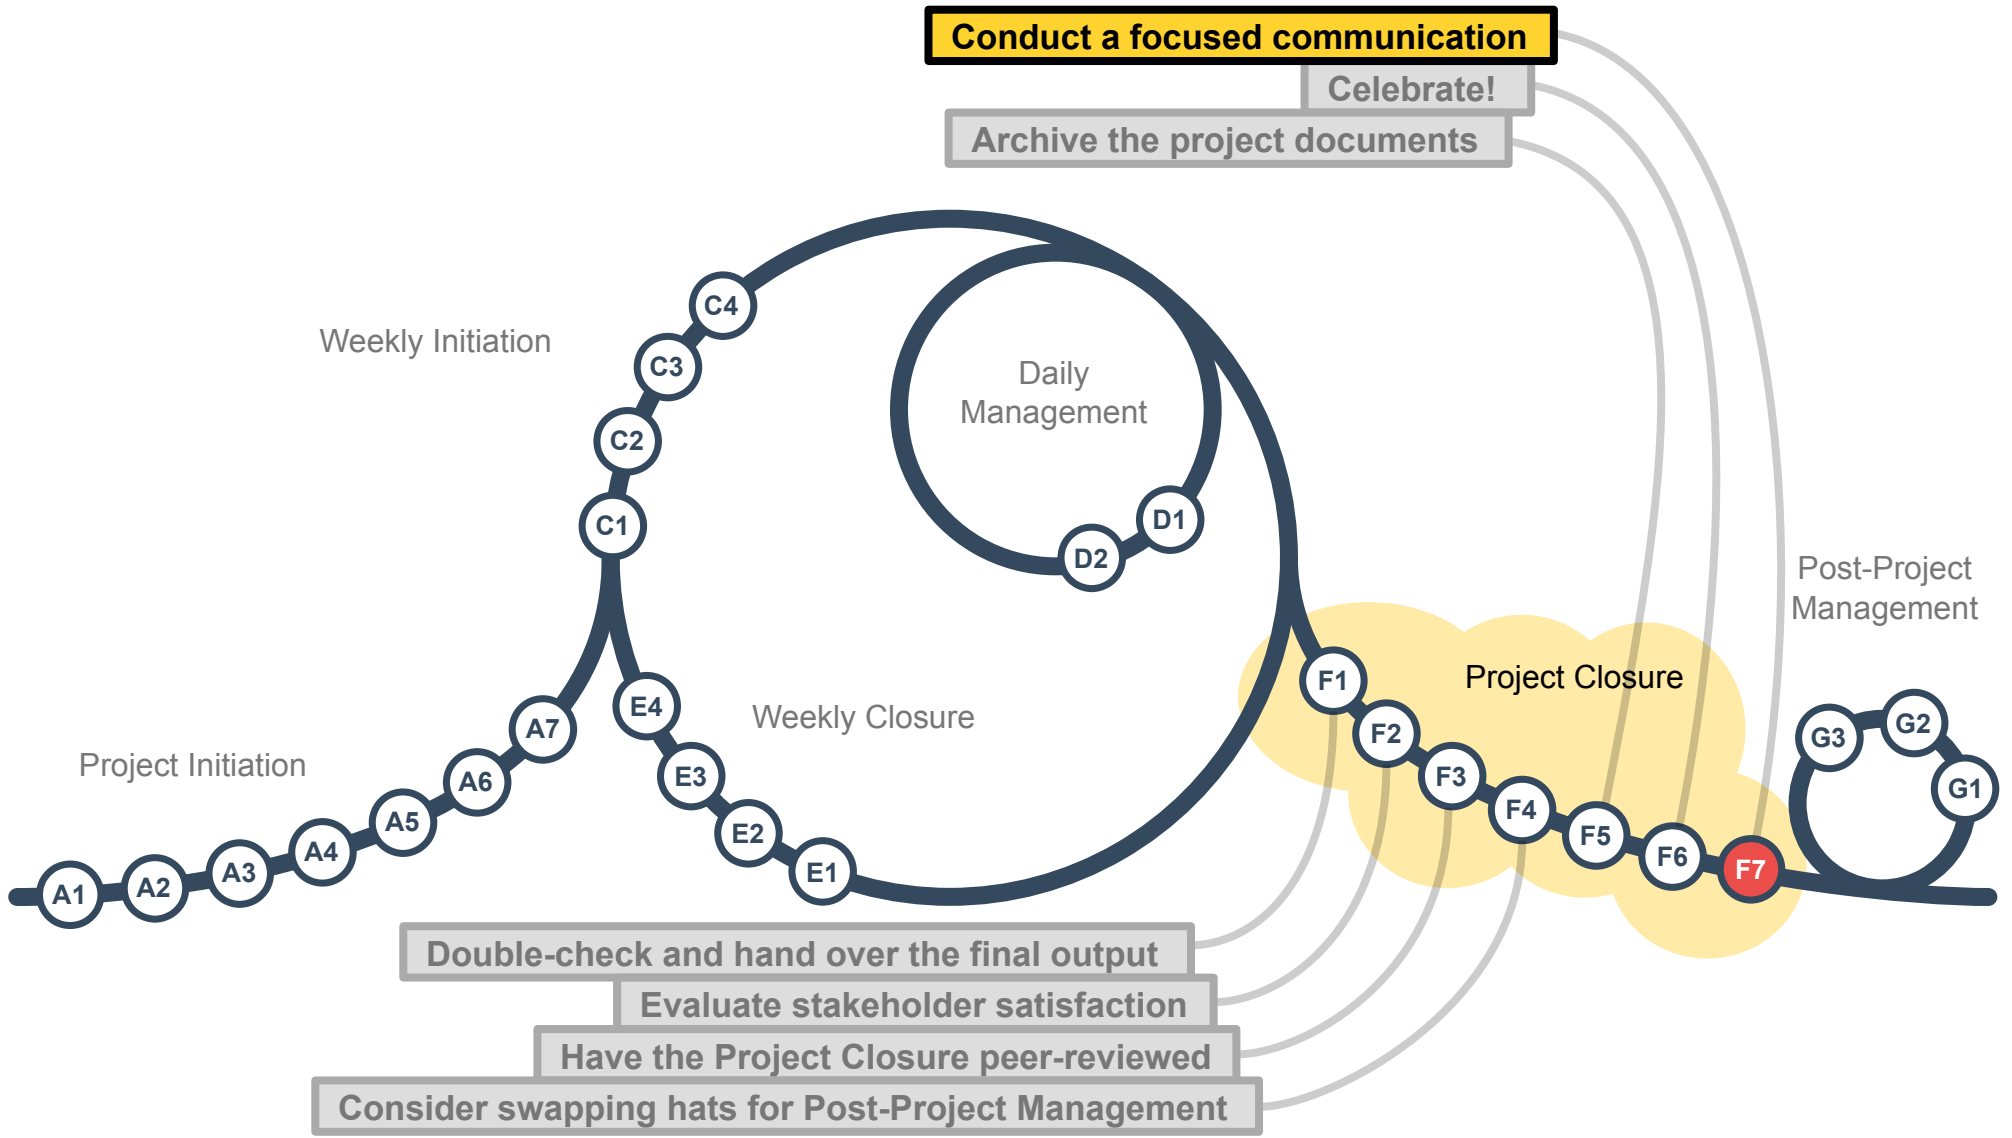

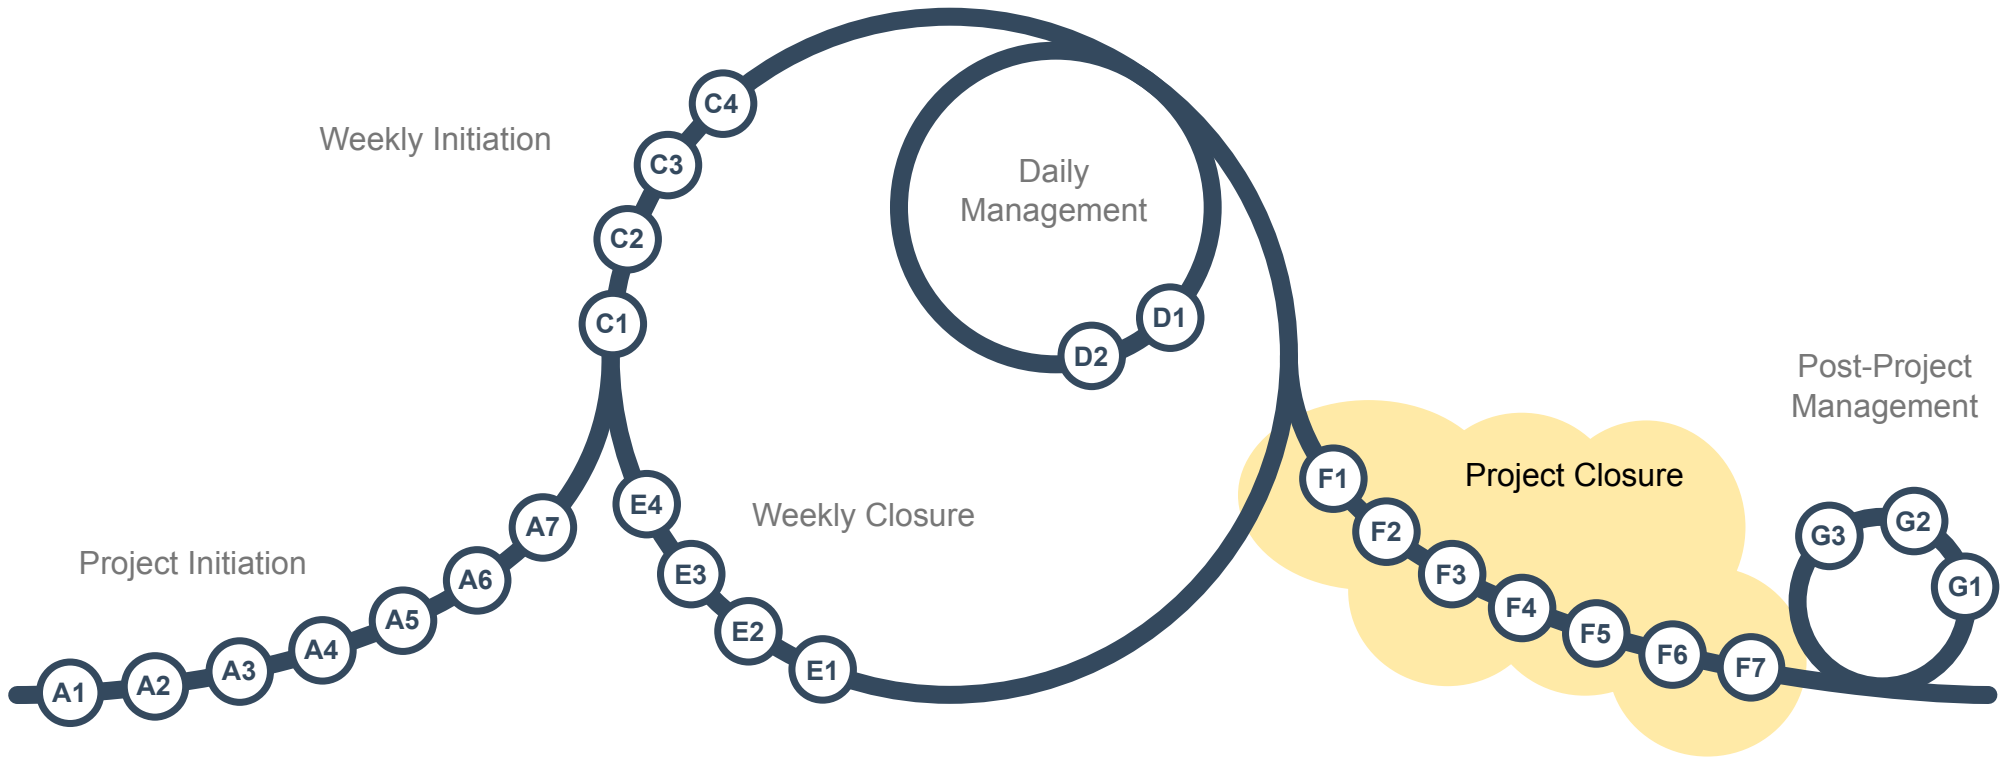

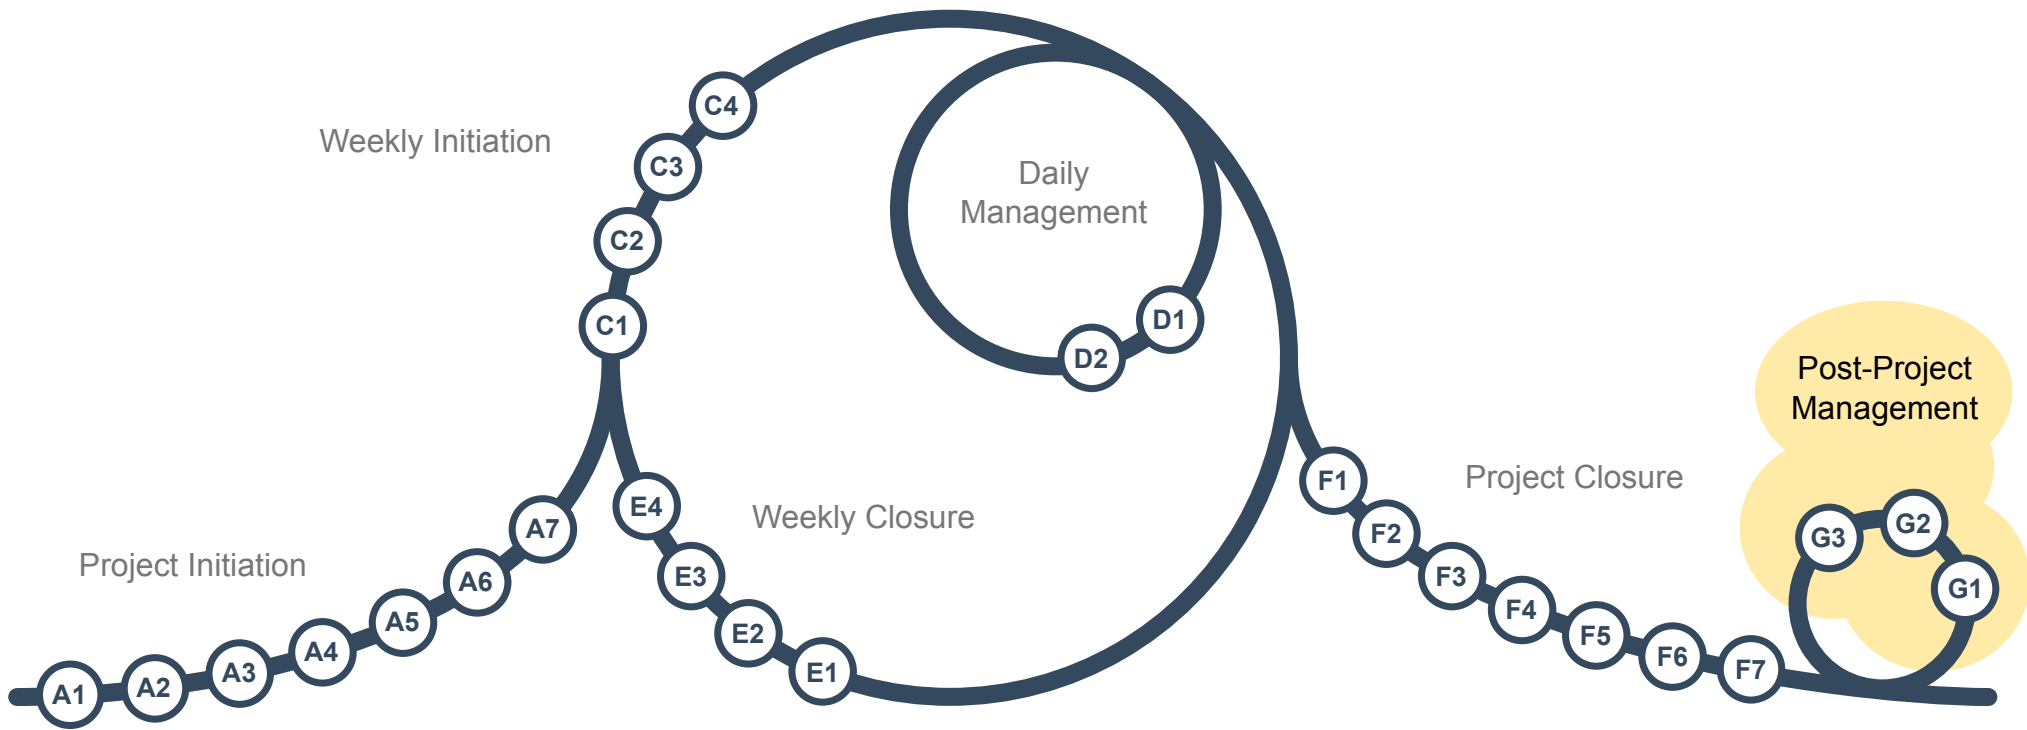

Weekly Initiation


Daily Management

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

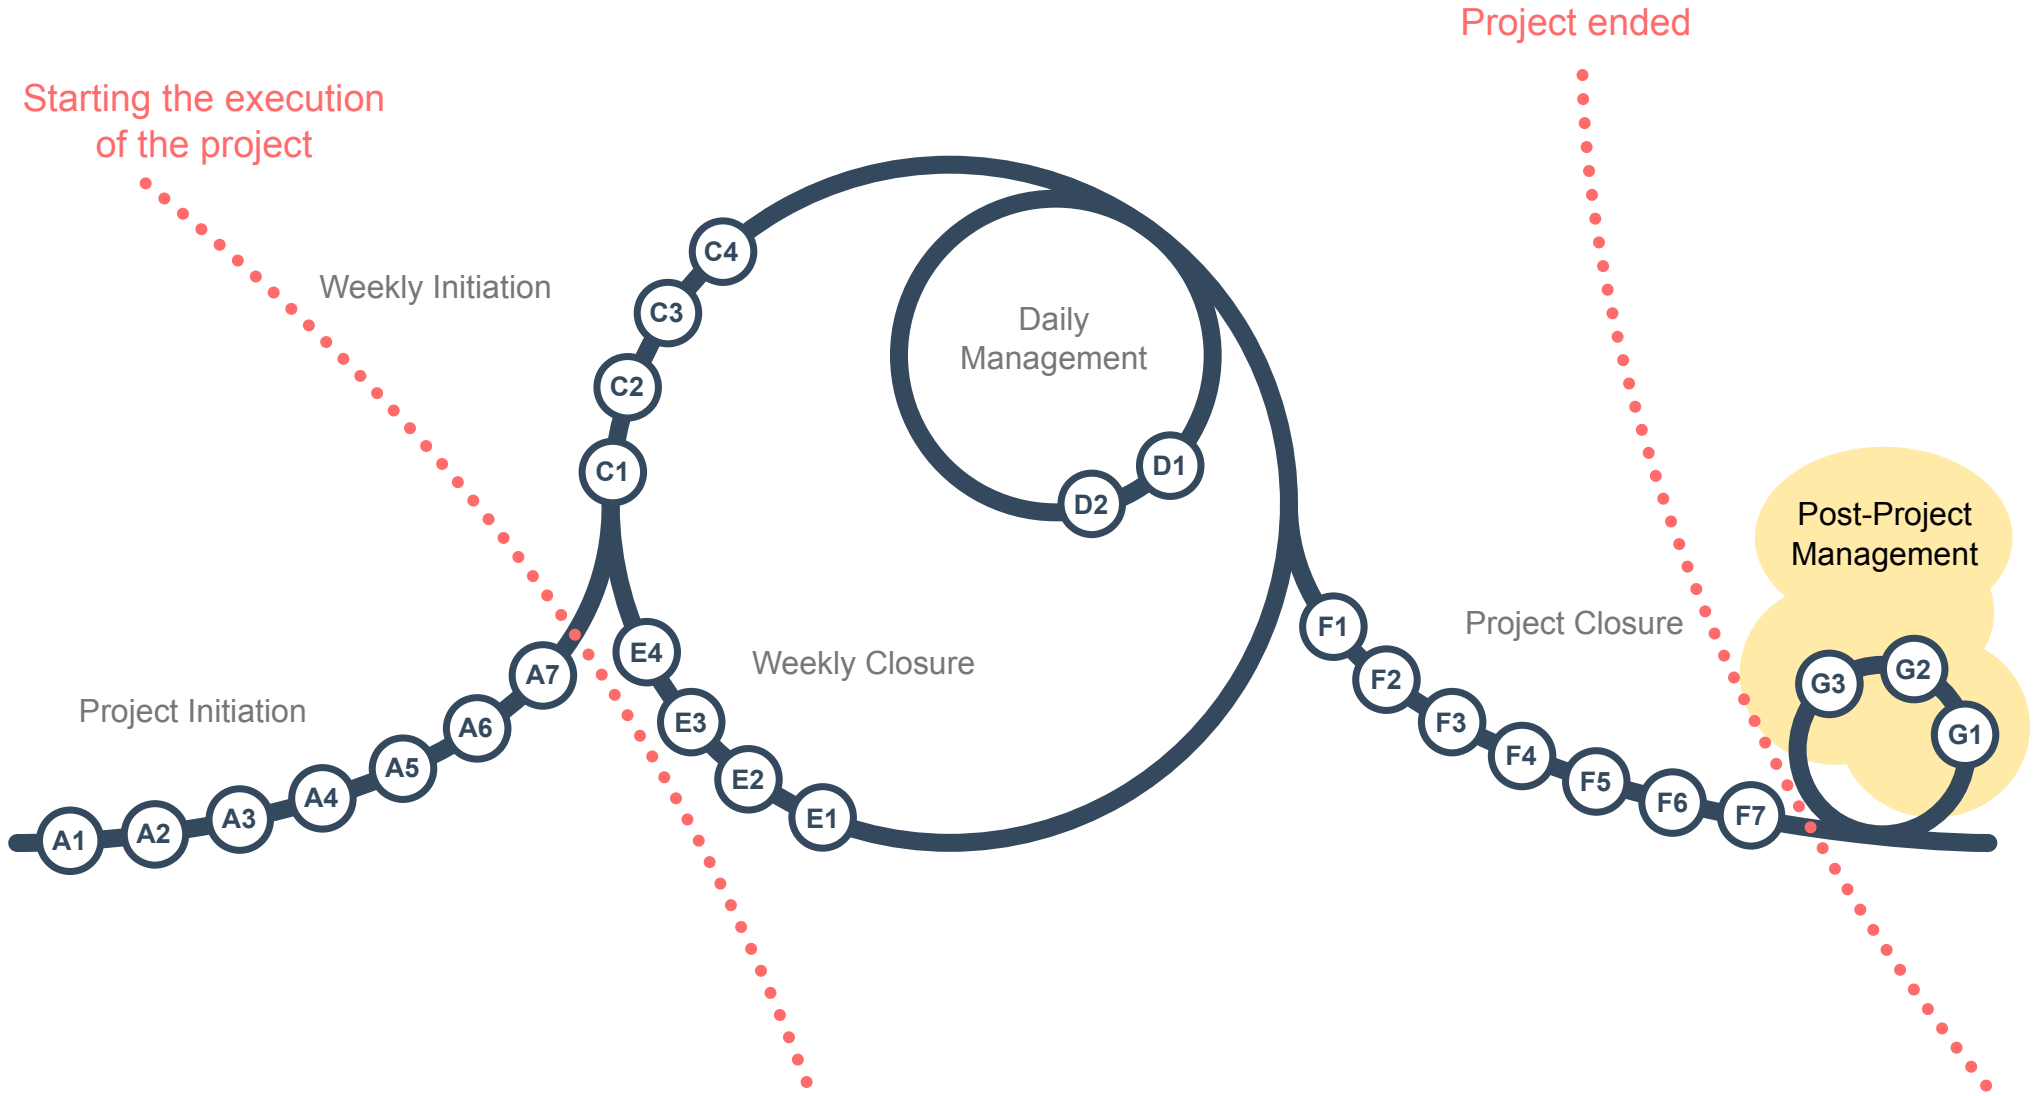

Starting the execution of the project

Weekly Initiation

Daily Management

Project ended

Post-Project Management

Project Initiation

Weekly Closure

Project Closure

A1

A2

A3

A4

A5

A6

A7

E4

E3

E2

E1

C1

C2

C3

C4

D2

D1

F1

F2

F3

F4

F5


F6


F7

G3


G2

G1

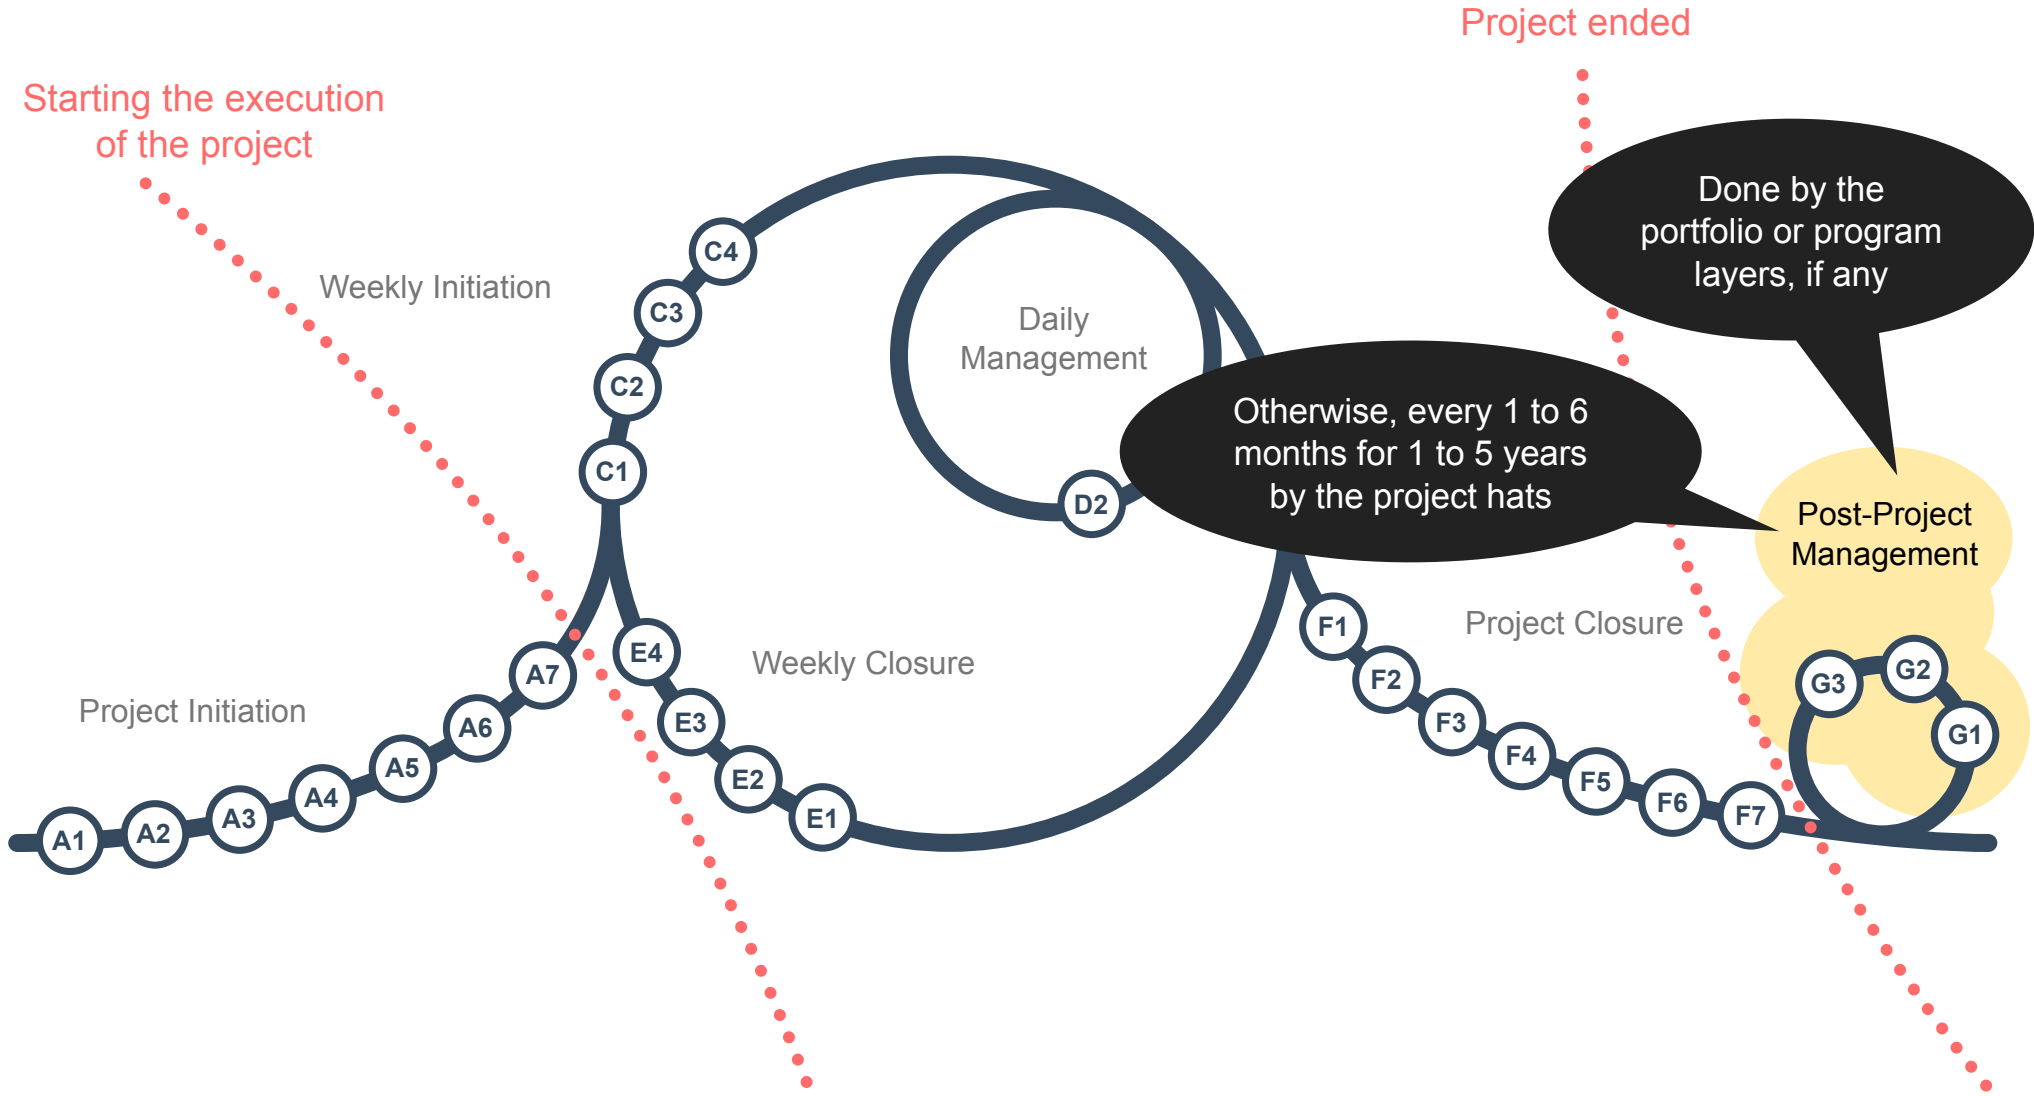


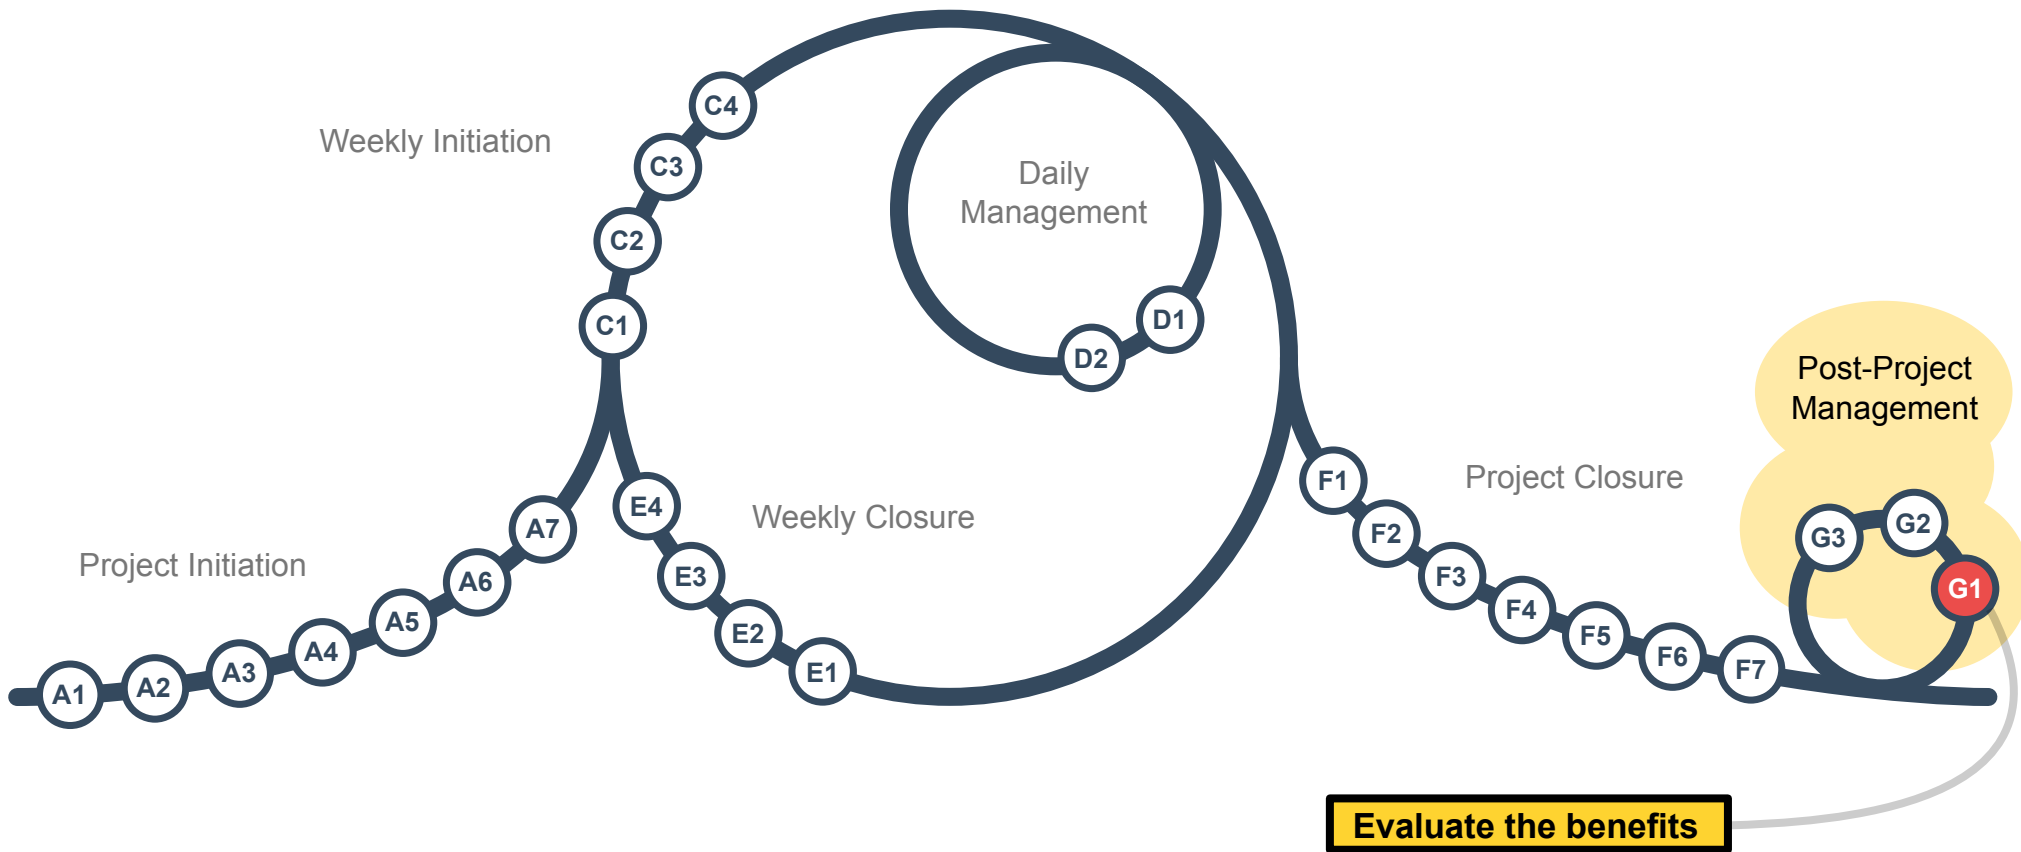


G1 – Evaluate the benefits



G1 – Evaluate the benefits

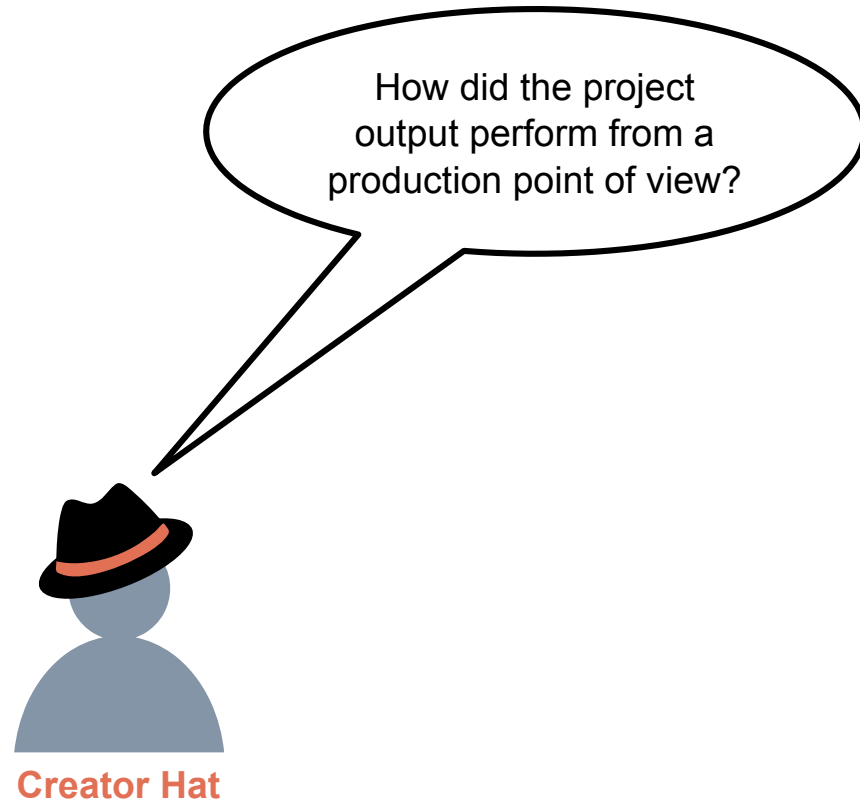



G1 – Evaluate the benefits

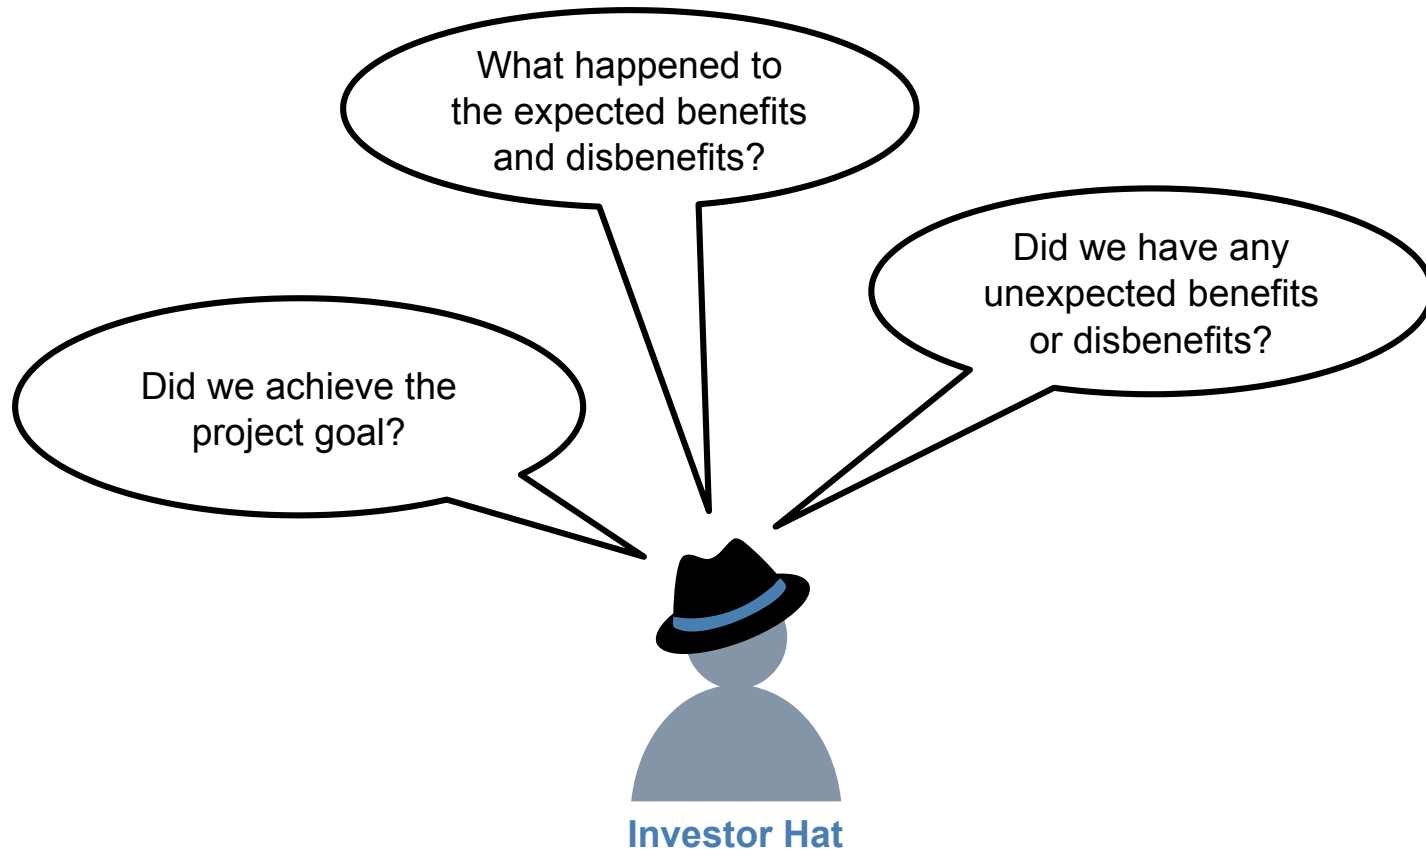


G1 – Evaluate the benefits



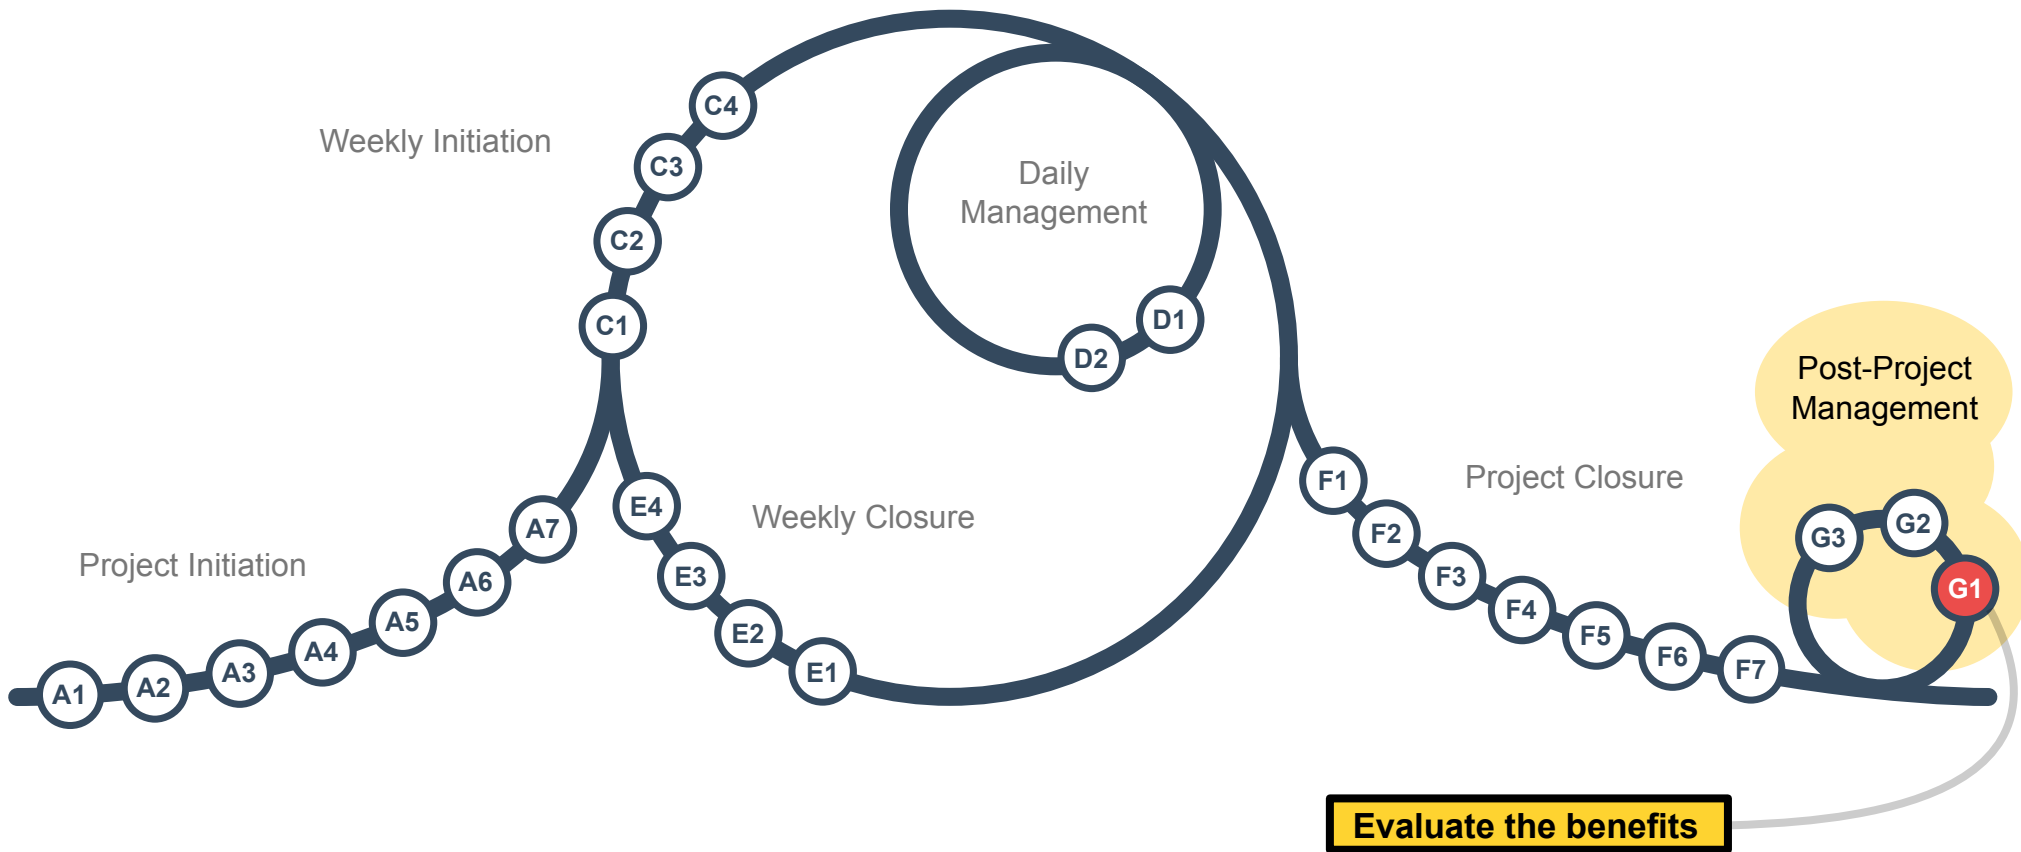


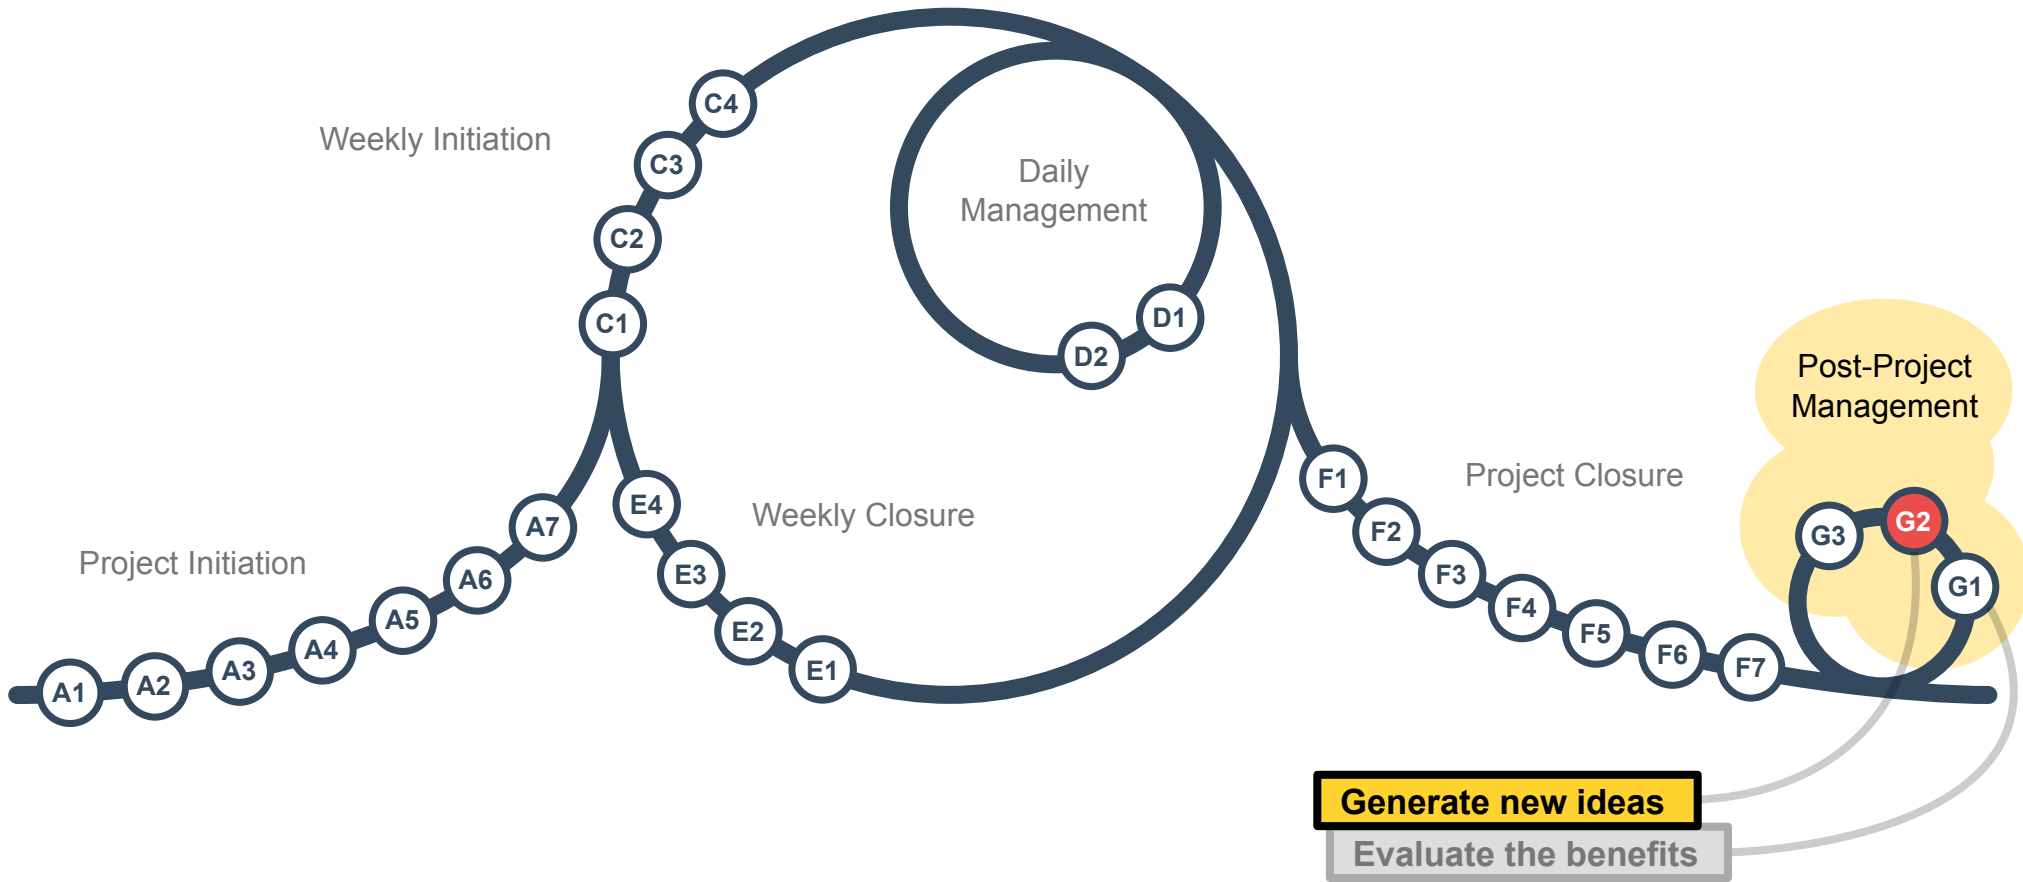


G2 – Generate new ideas




G2 – Generate new ideas

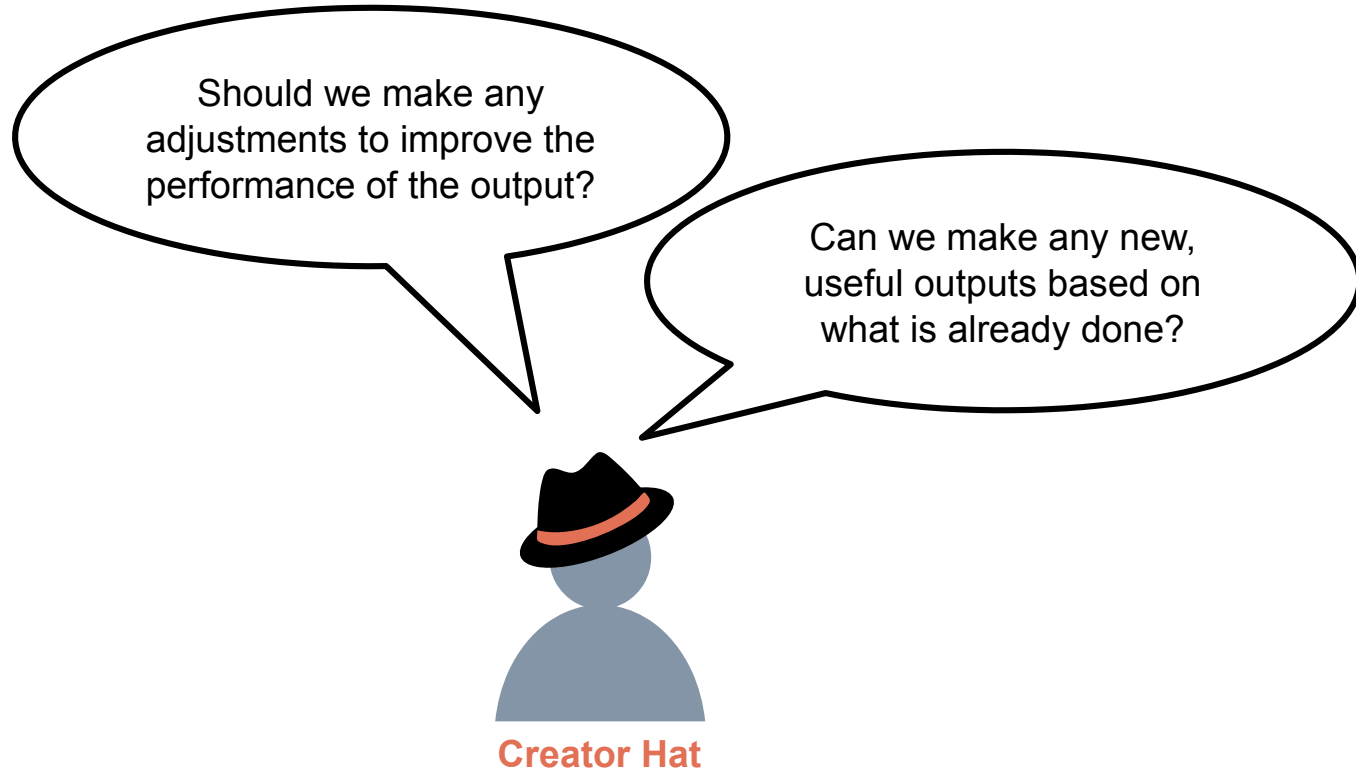



G2 – Generate new ideas

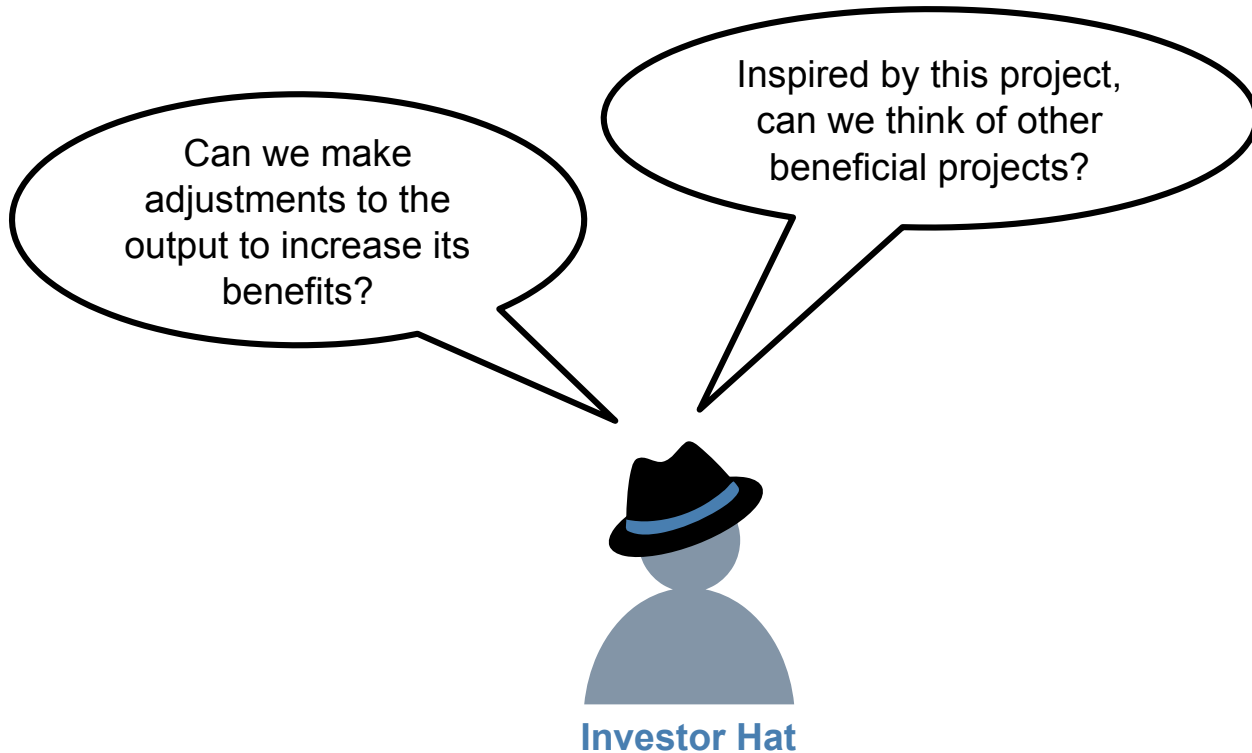

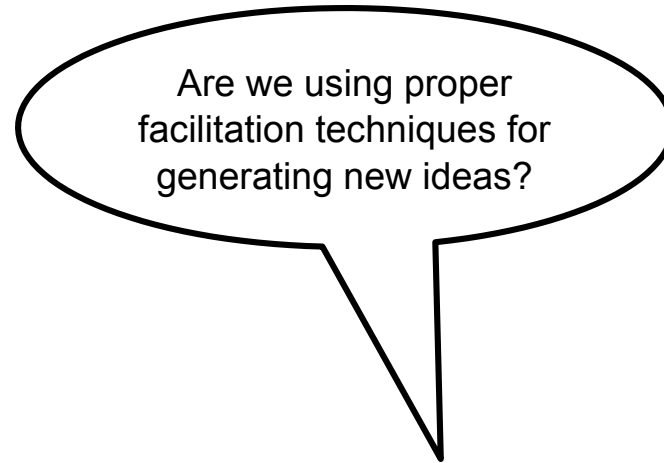

Project Manager Hat

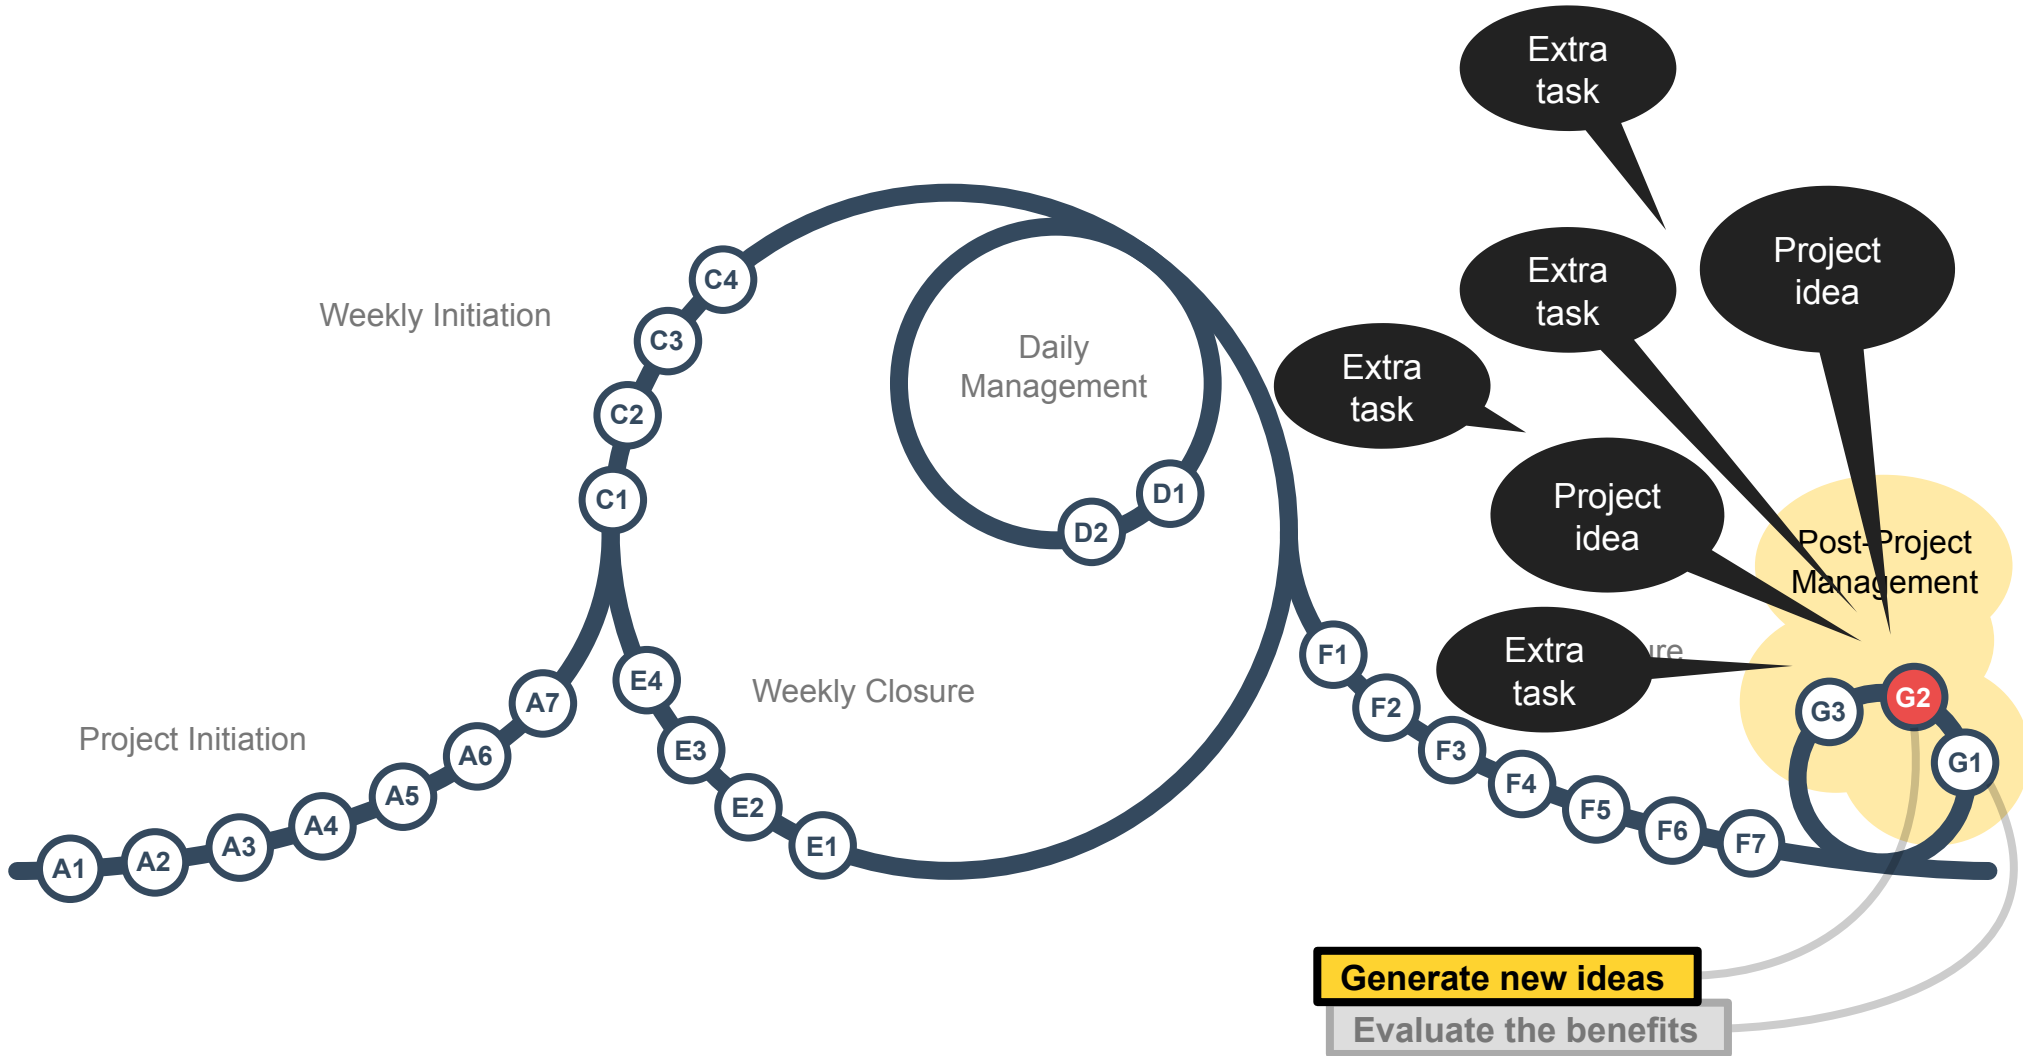


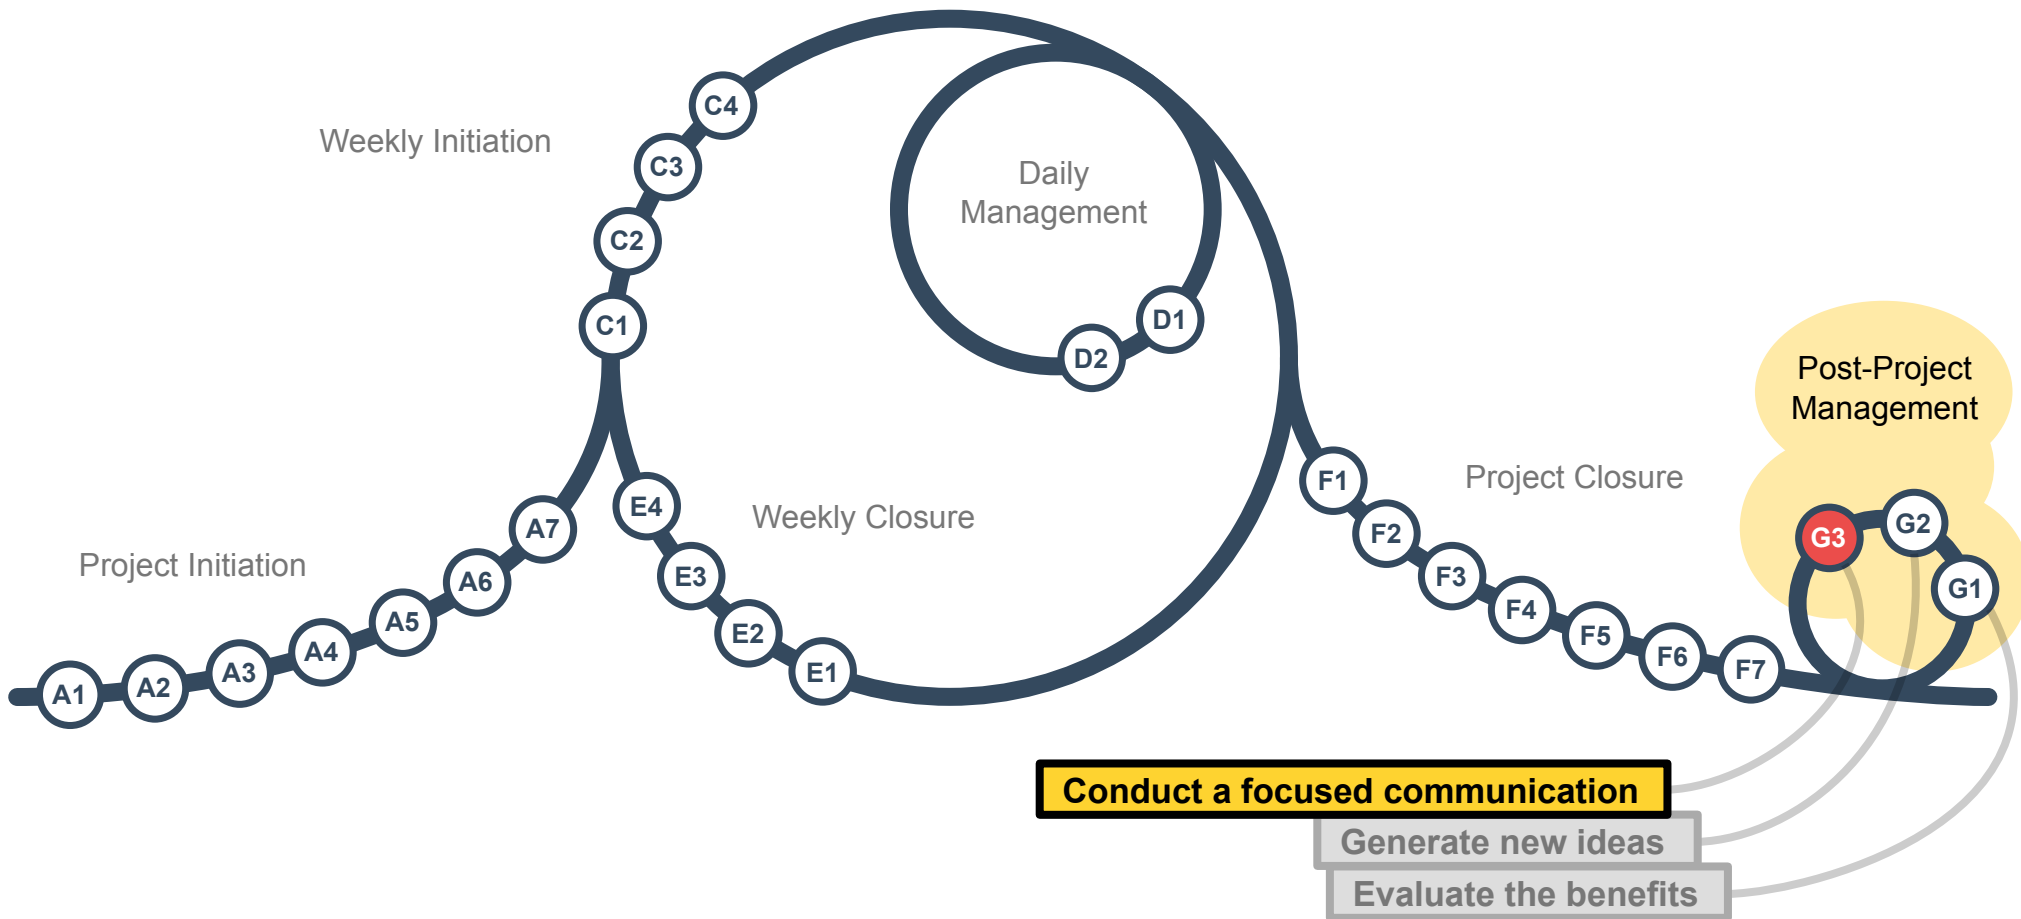


What are the advantages of informing everyone in the organization of the benefits realized from past projects?




G3 – Conduct a focused communication

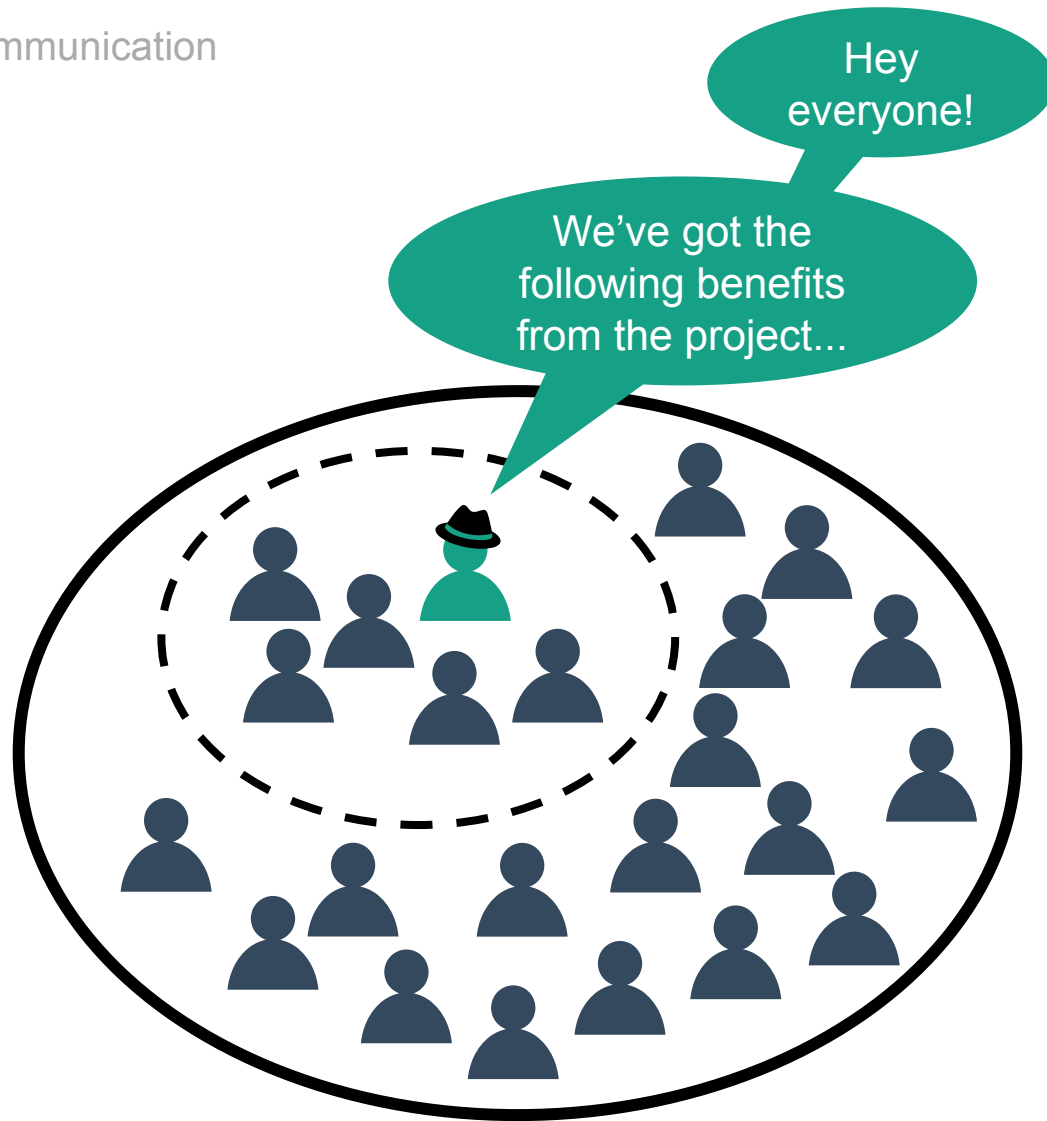



G3 – Conduct a focused communication

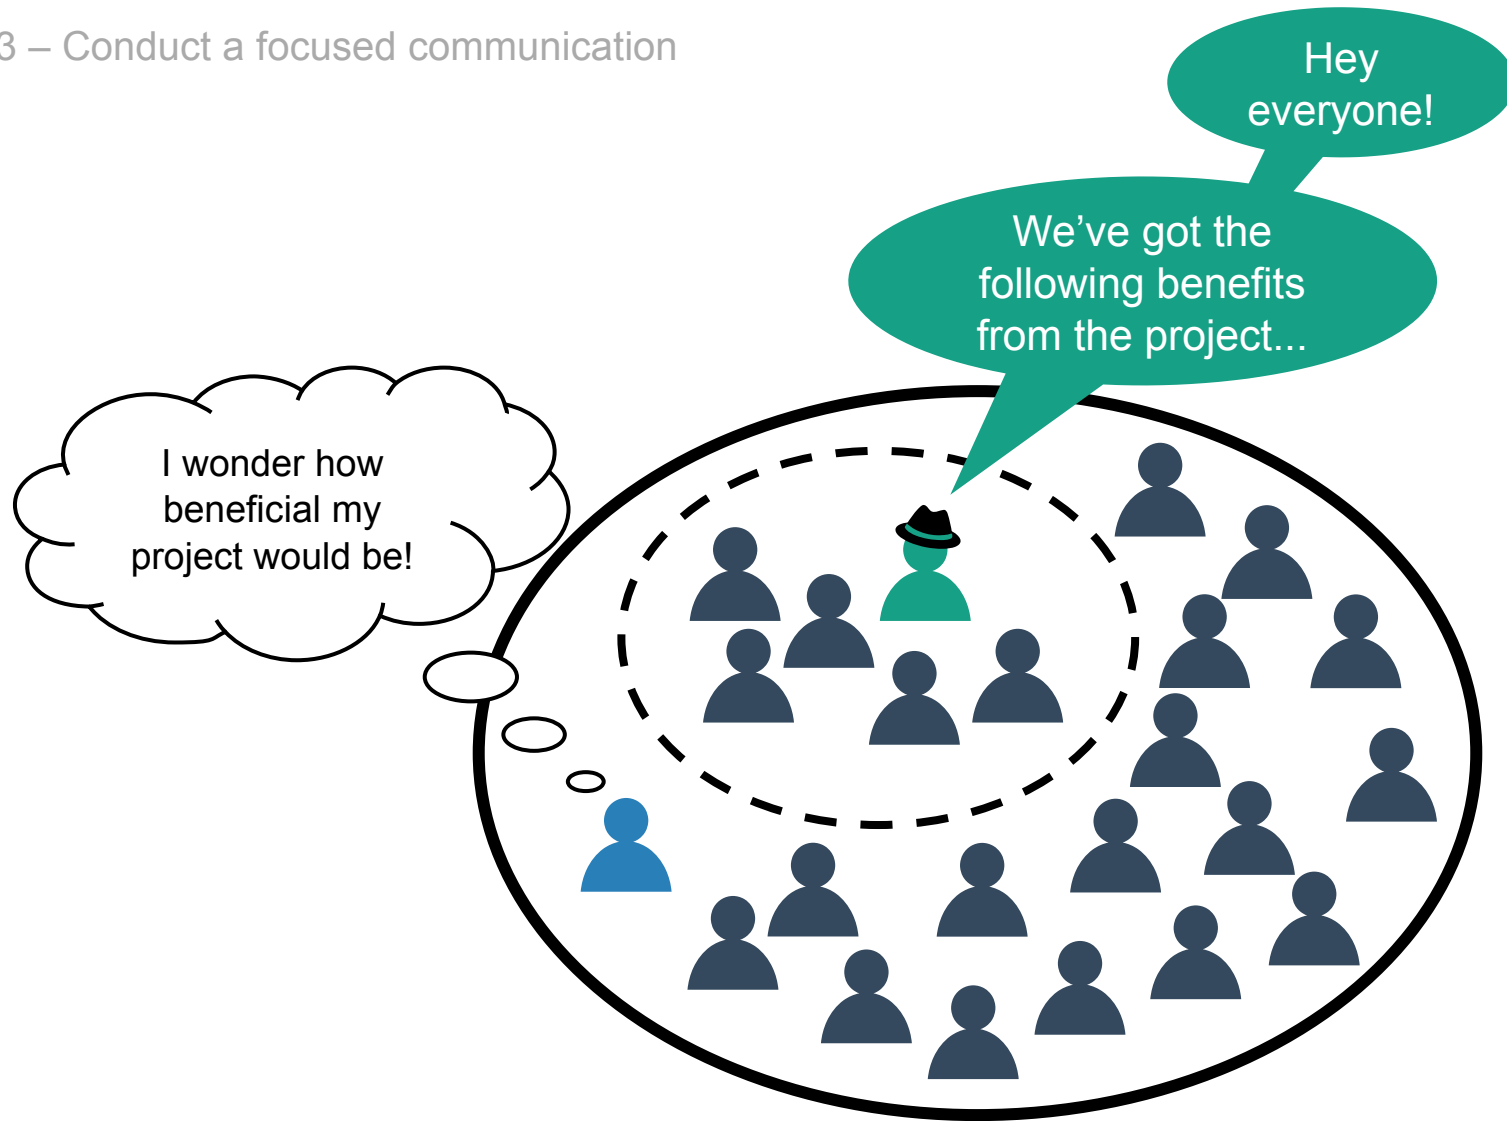


G3 – Conduct a focused communication

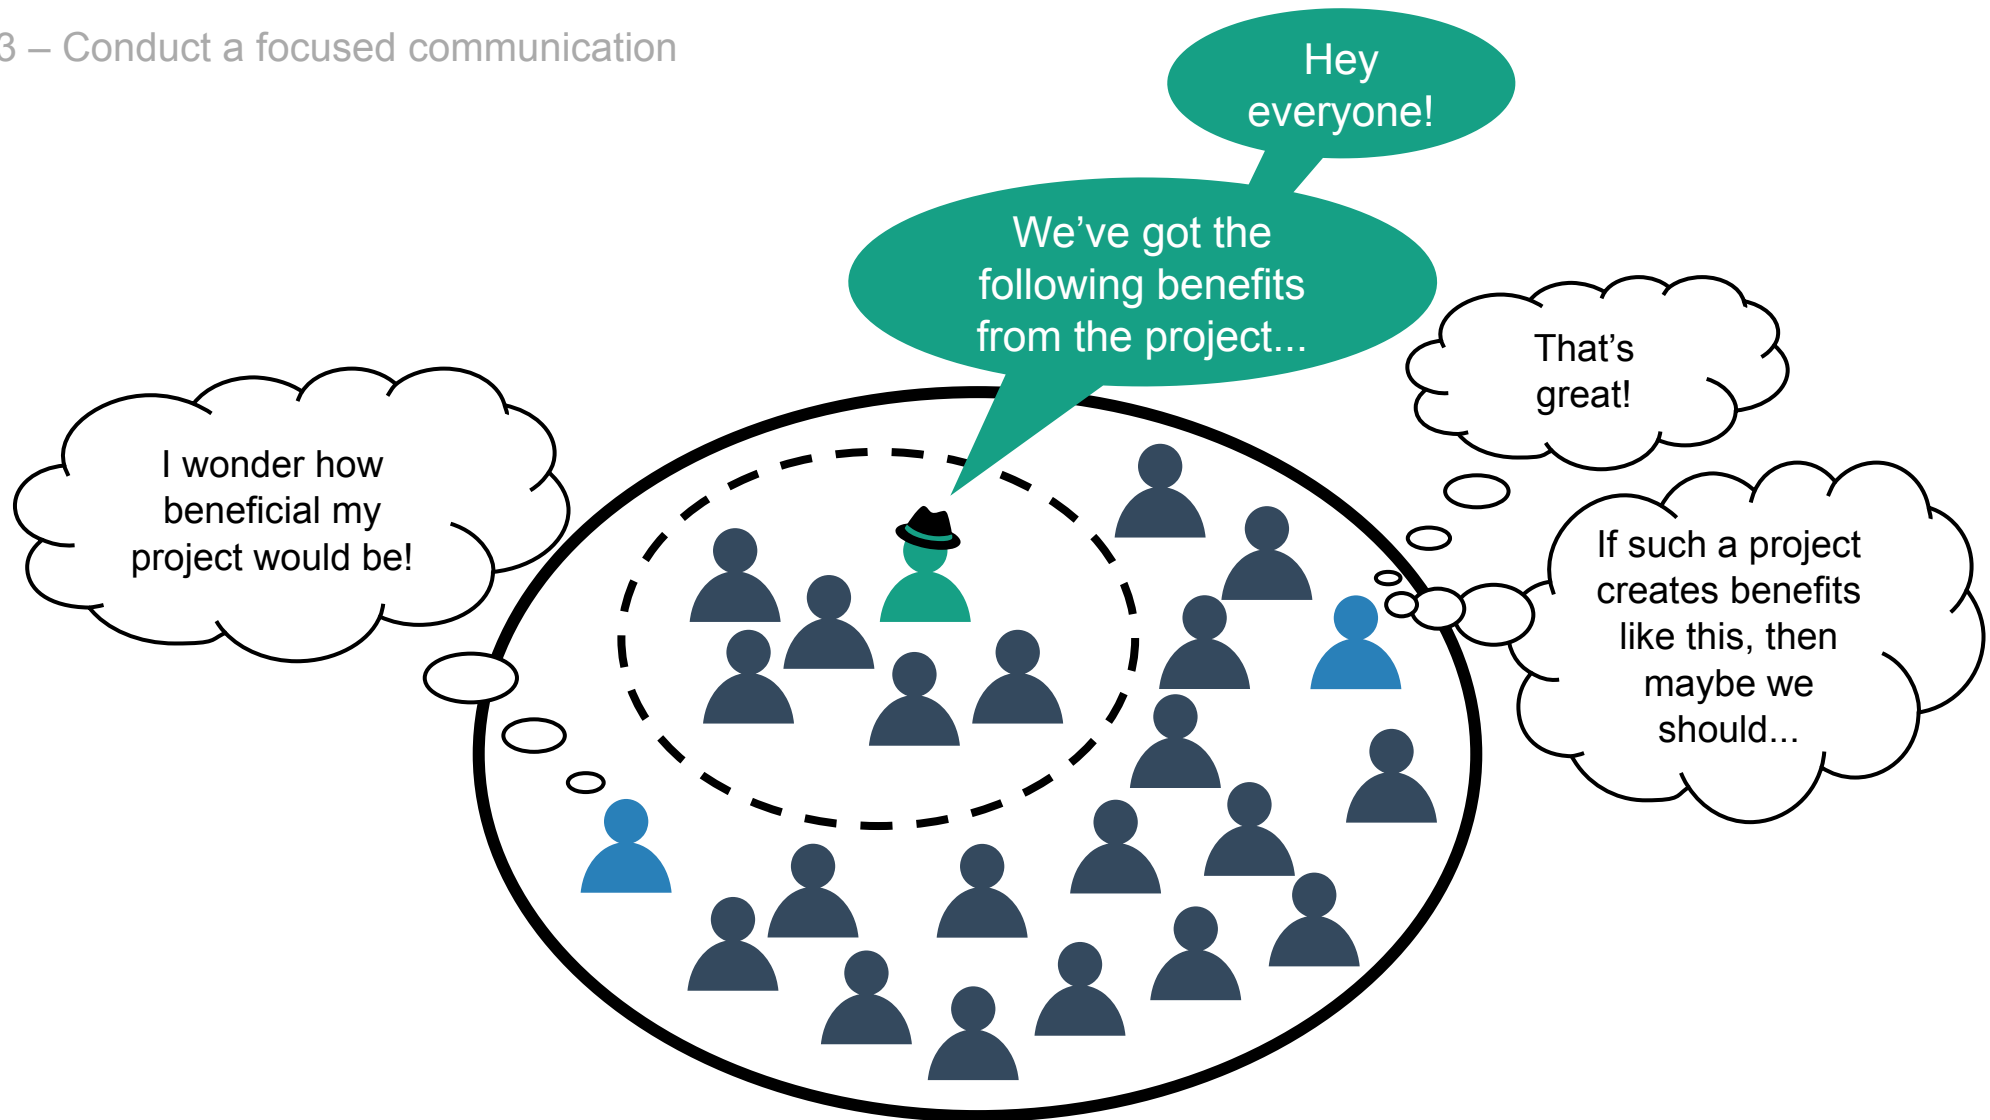

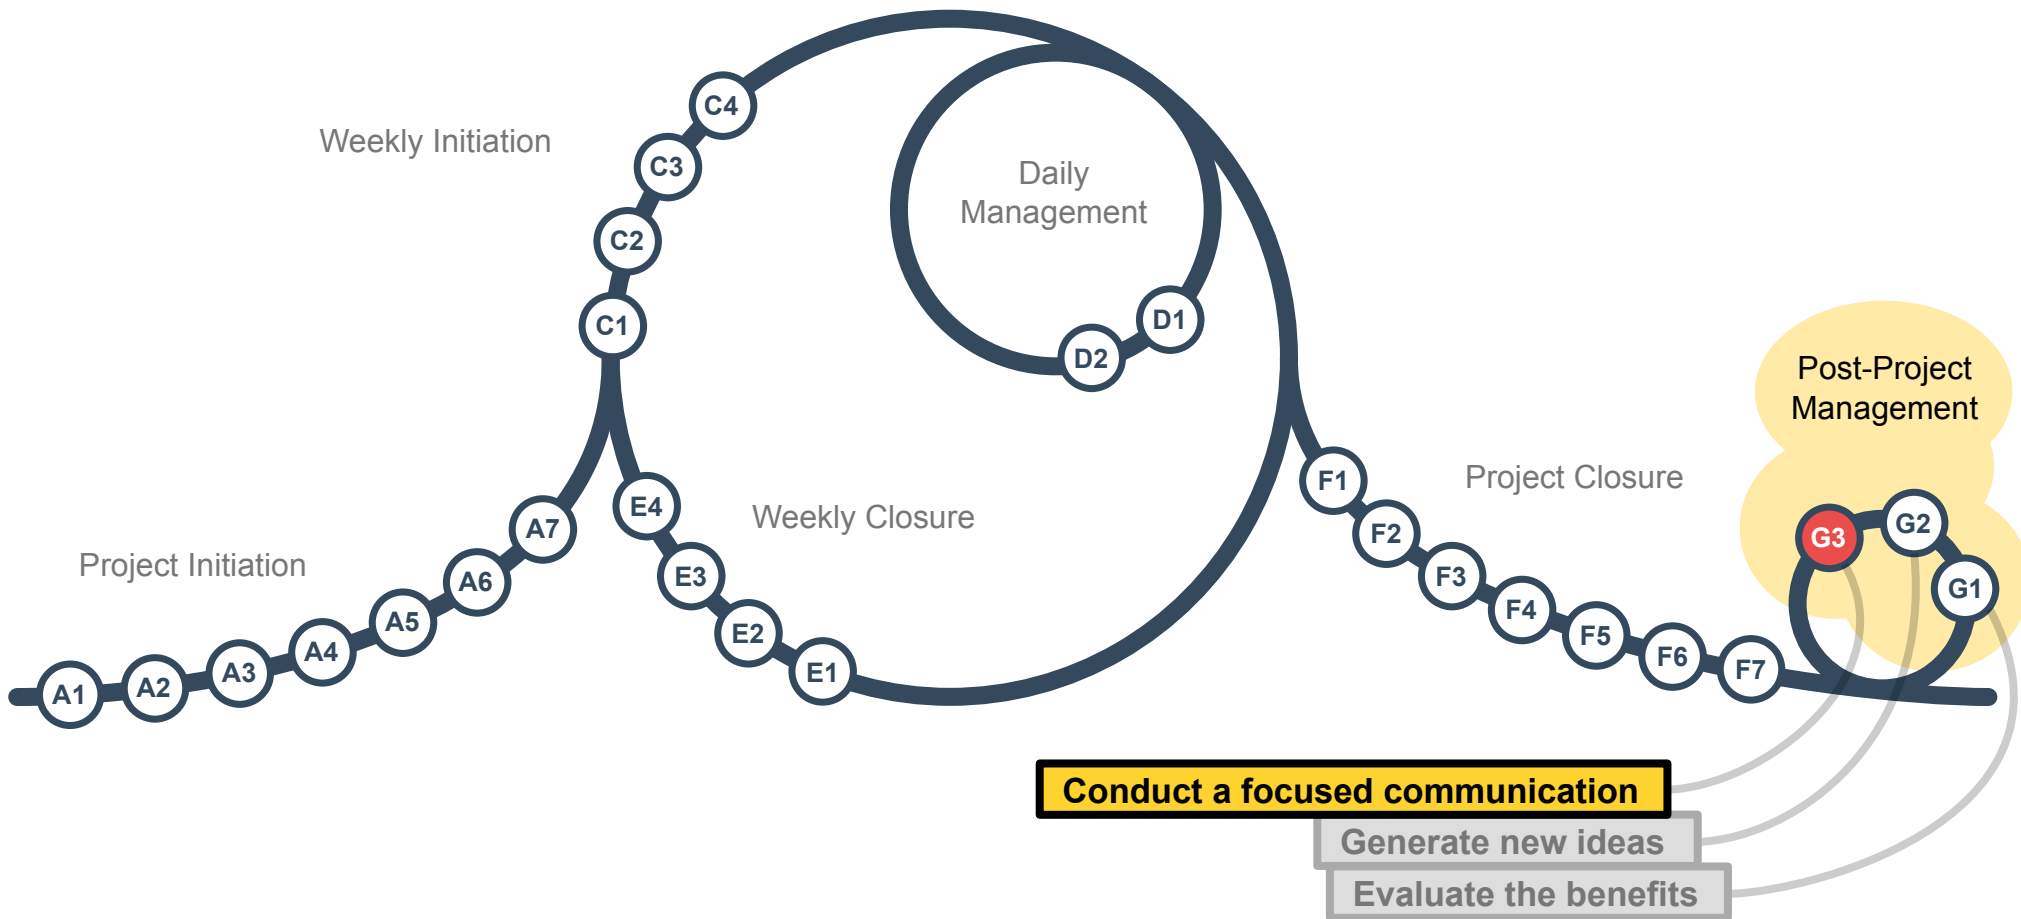

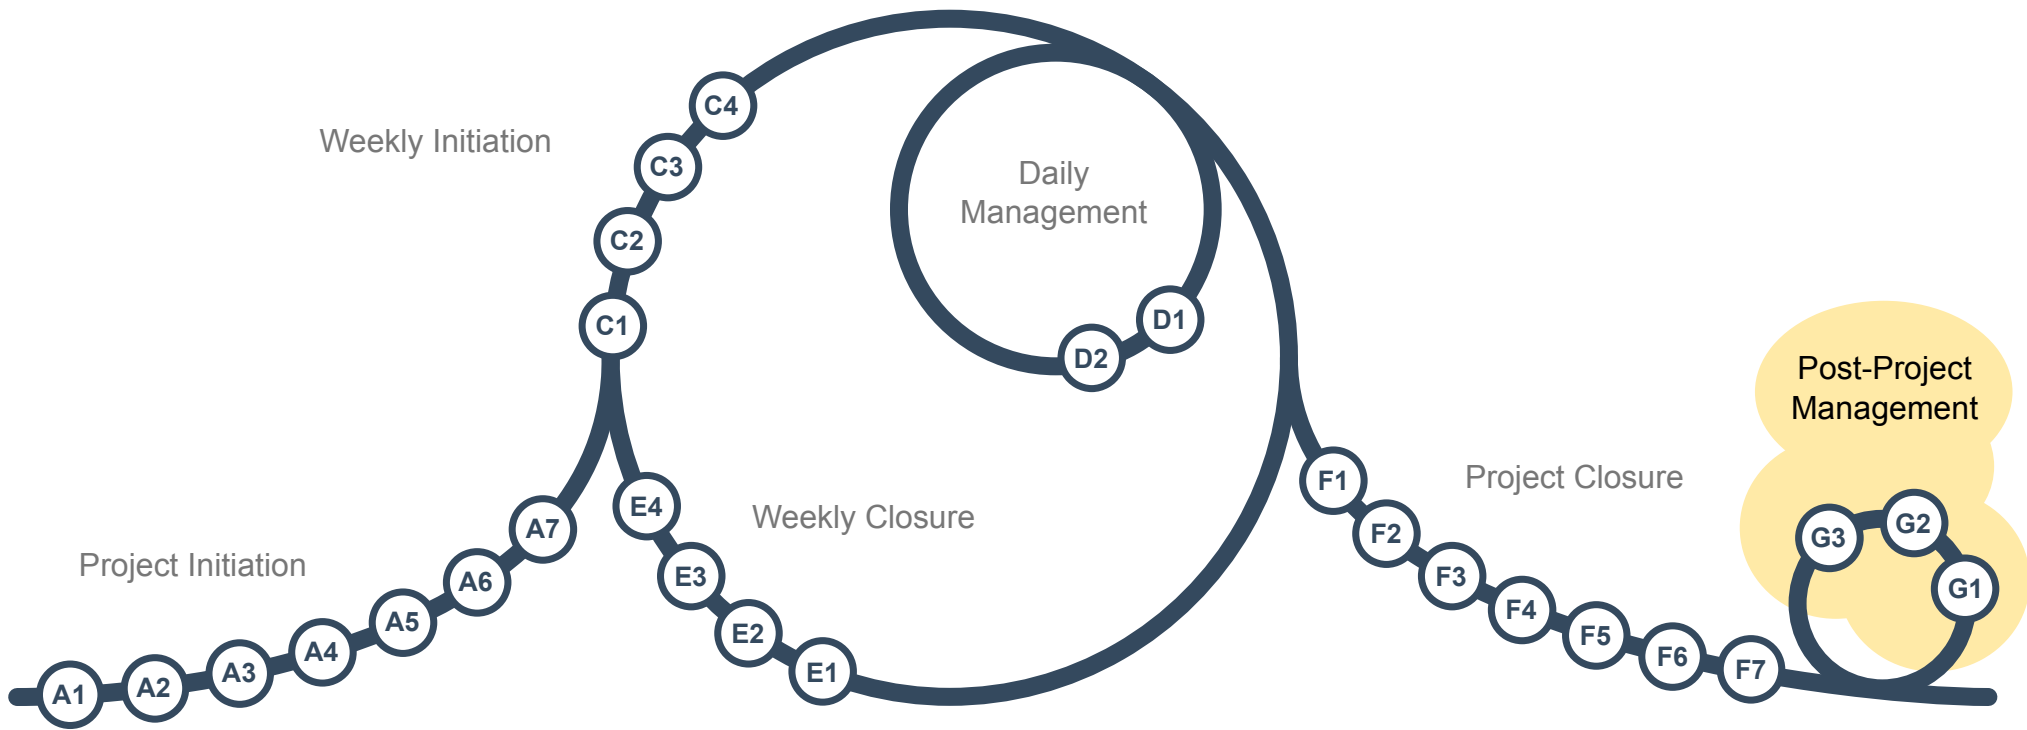

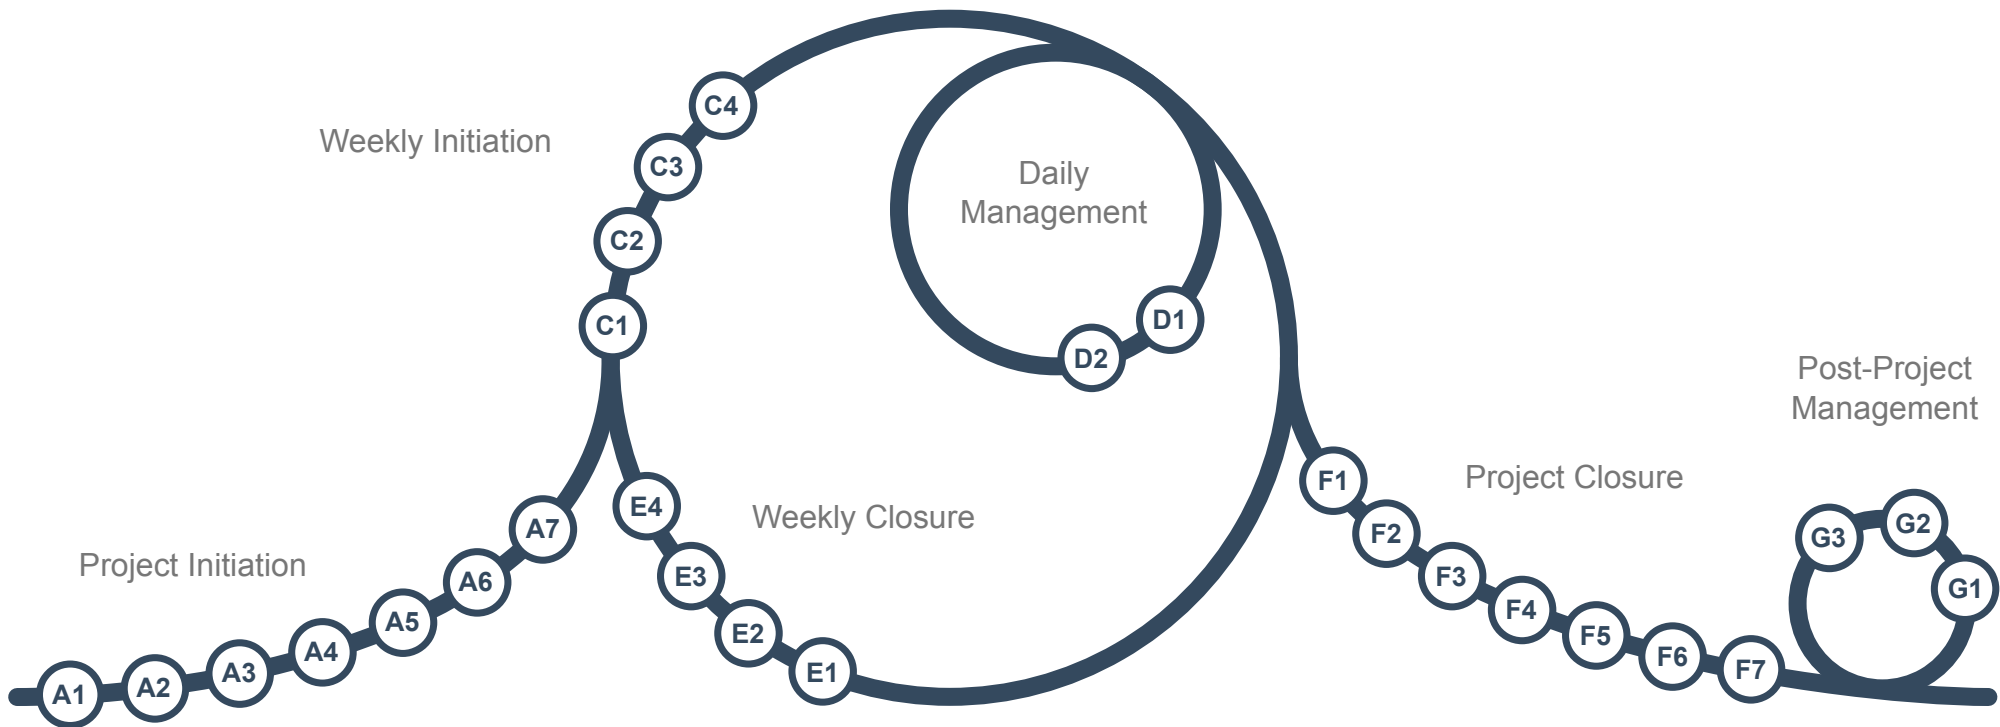

① High-level overview


② Full review

 ③ NUPP

④ Tailoring

NUPP

Nearly Universal Principles of Projects

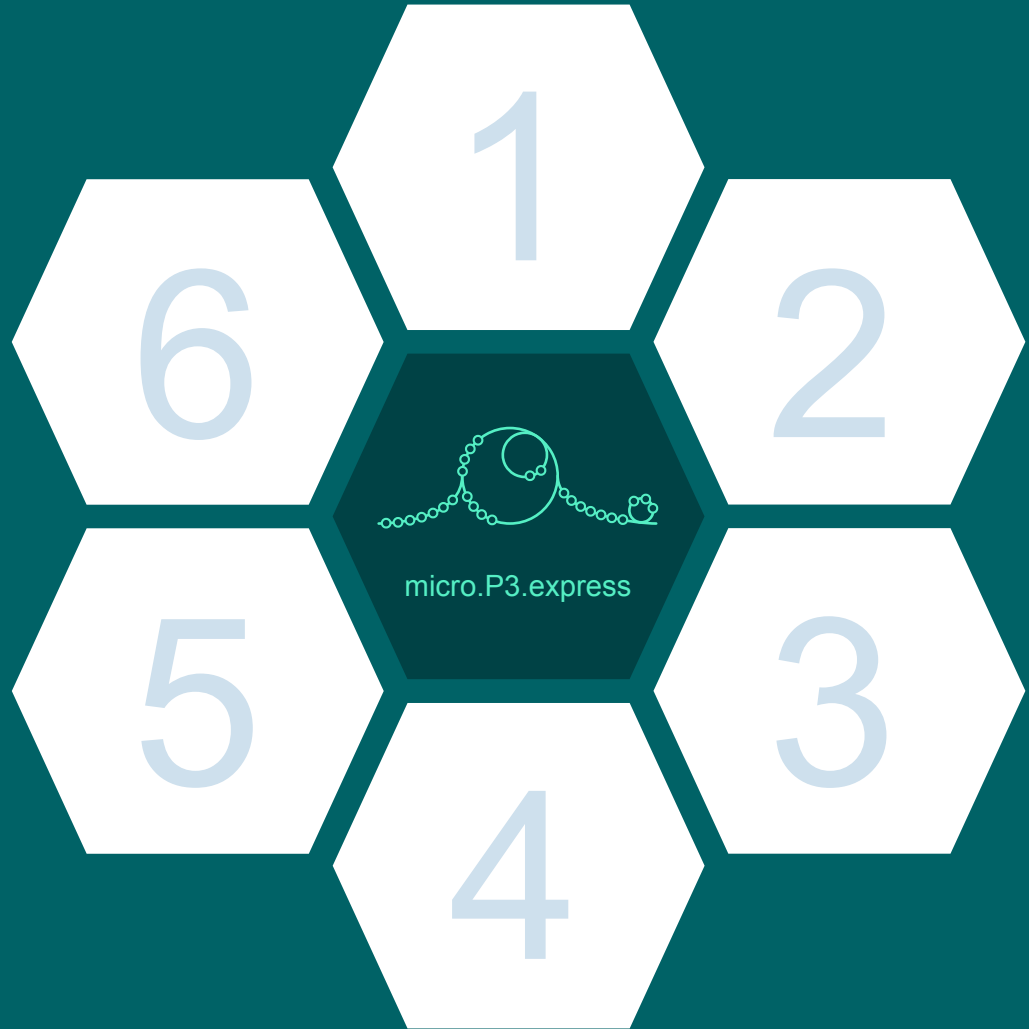


NUPP

Nearly Universal Principles of Projects

Applicable to

- P3.express
- micro.P3.express
- PRINCE2
- DSDM
- Scrum
- XP
- PM²
- PMBOK Guide
- Etc.

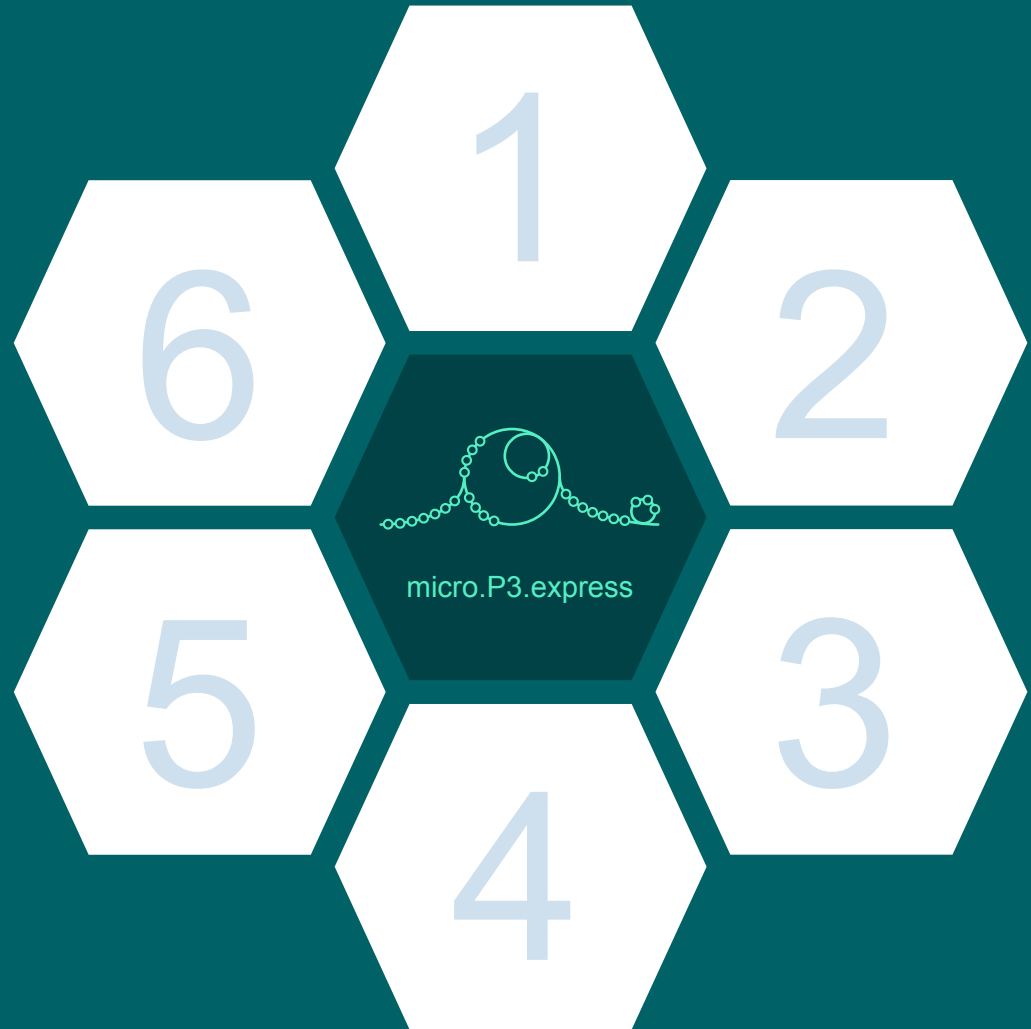

NUPP

Nearly Universal Principles of Projects

Examples:

- “Agile vs. waterfall”
- Continuous learning
- Openness




NUPP

Nearly Universal Principles of Projects

Examples:

- The 80/20 rule
- Decision fatigue
- Etc.

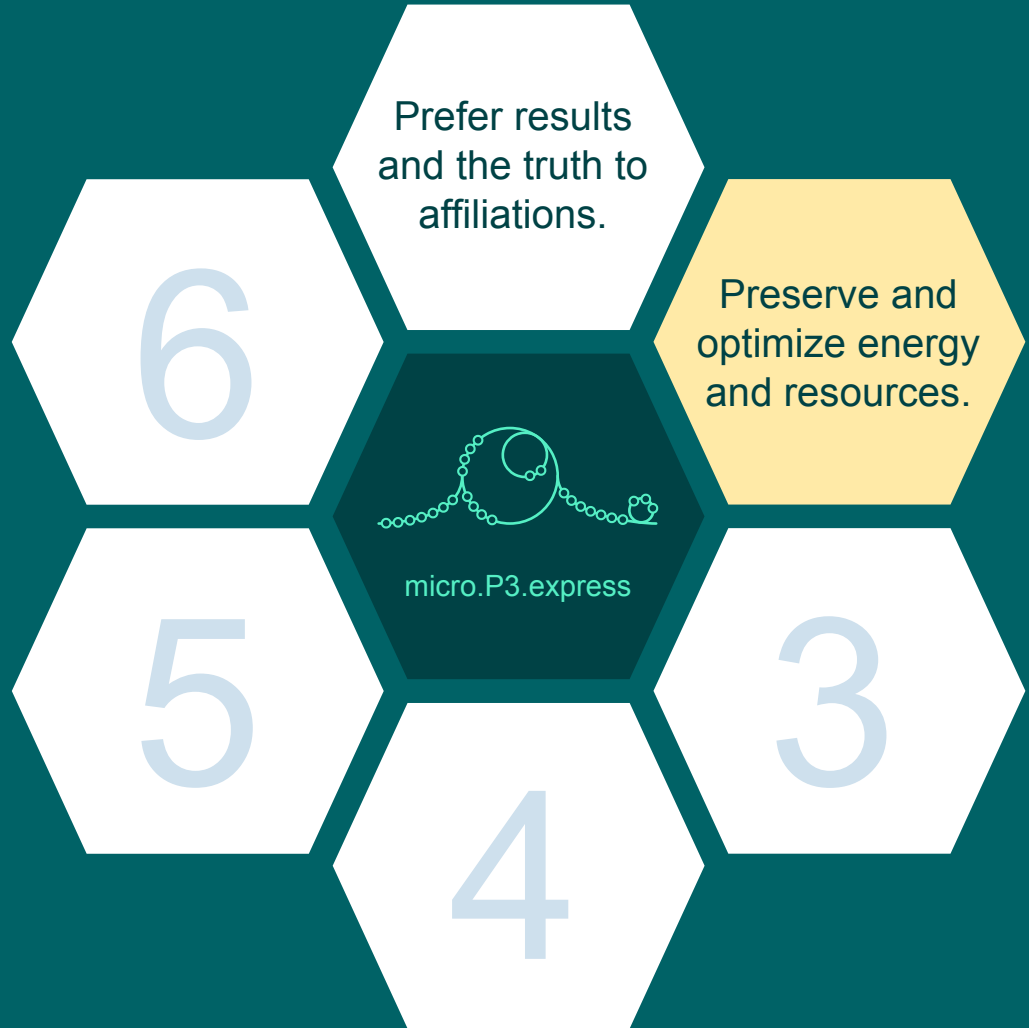

NUPP

Nearly Universal Principles of Projects

Examples:

- Risk management
- Critical thinking
- Etc.



NUPP

Nearly Universal Principles of Projects

Examples:

- Deadlines
- Cherry picking
- Etc.



NUPP

Nearly Universal Principles of Projects

Examples:

- “Business case”
- Simplicity
- Tailoring
- Etc.




NUPP

Nearly Universal Principles of Projects

Examples:

- Checklists
- Cycles
- Methods
- Etc.

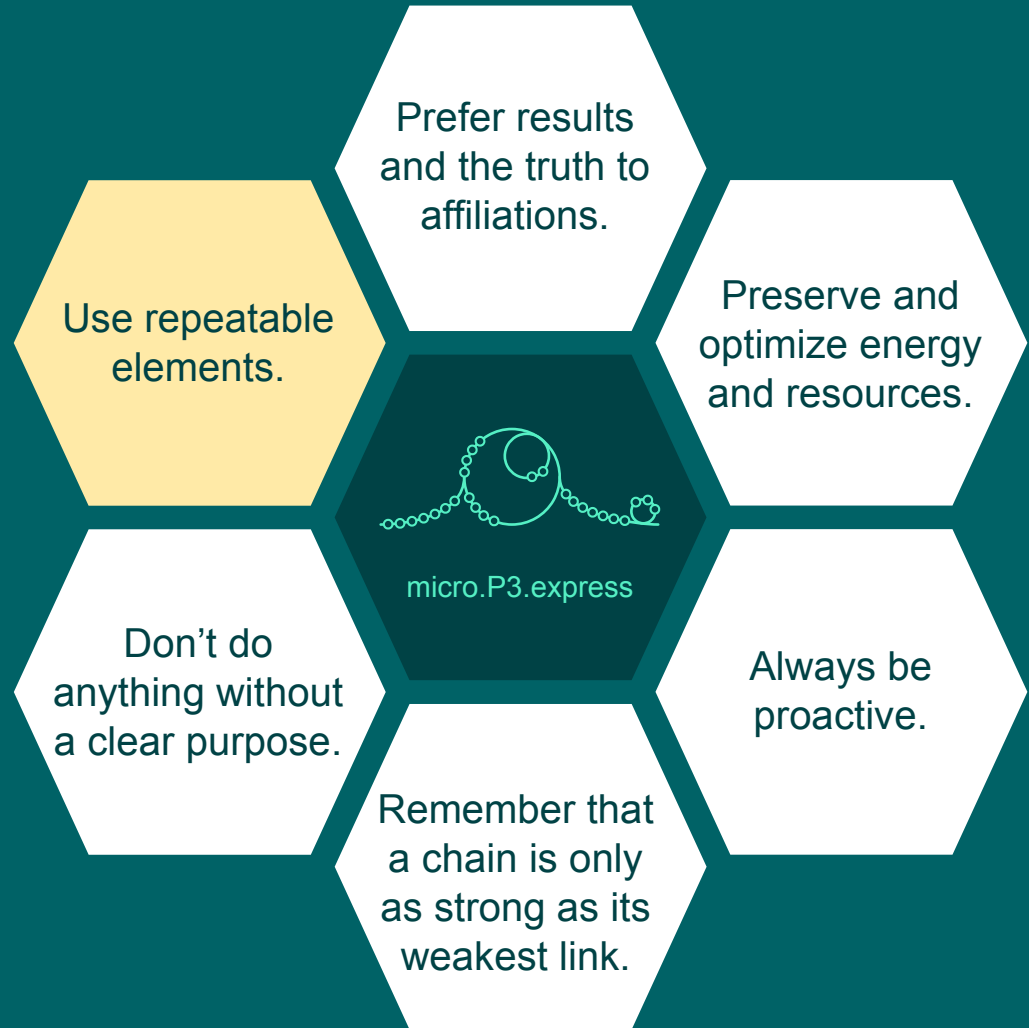

NUPP

Nearly Universal Principles of Projects




① High-level overview

② Full review

③ NUPP

 ④ Tailoring

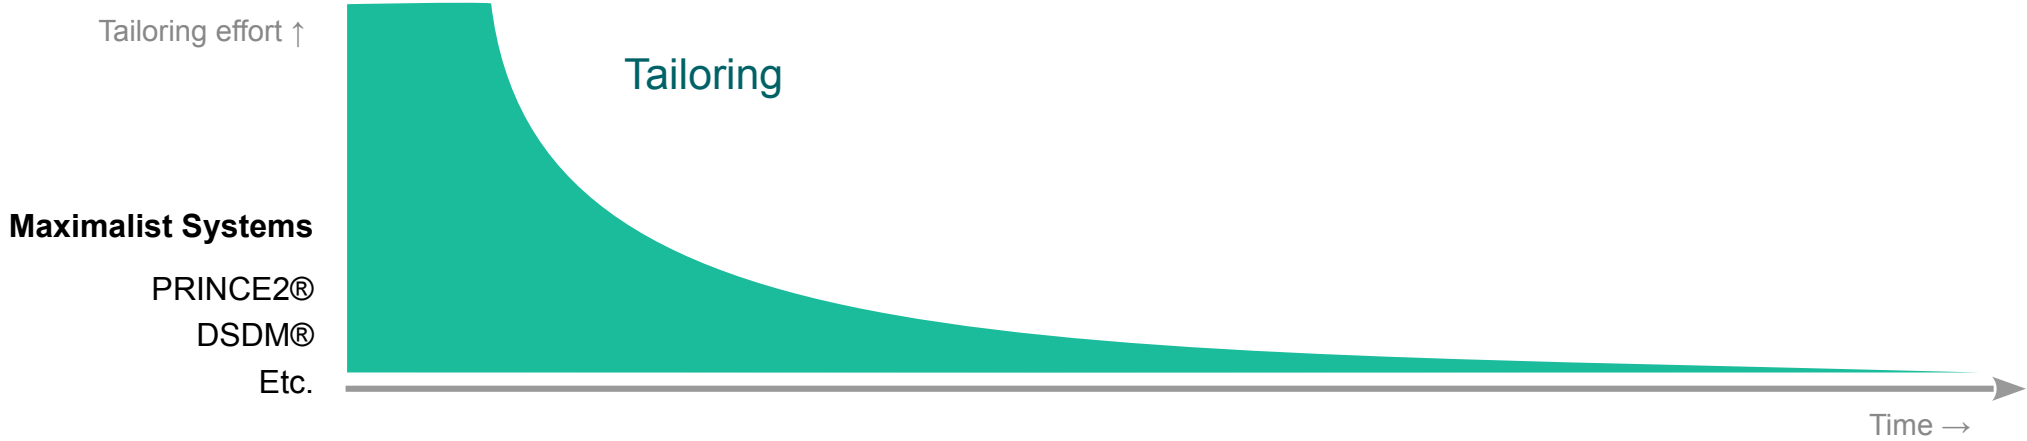

Upfront
Tailoring

Continuous
Tailoring

Minimalist Systems

P3.express
micro.P3.express
Etc.




Tailoring effort ↑

Maximalist Systems

PRINCE2®
DSDM®
Etc.



Time →

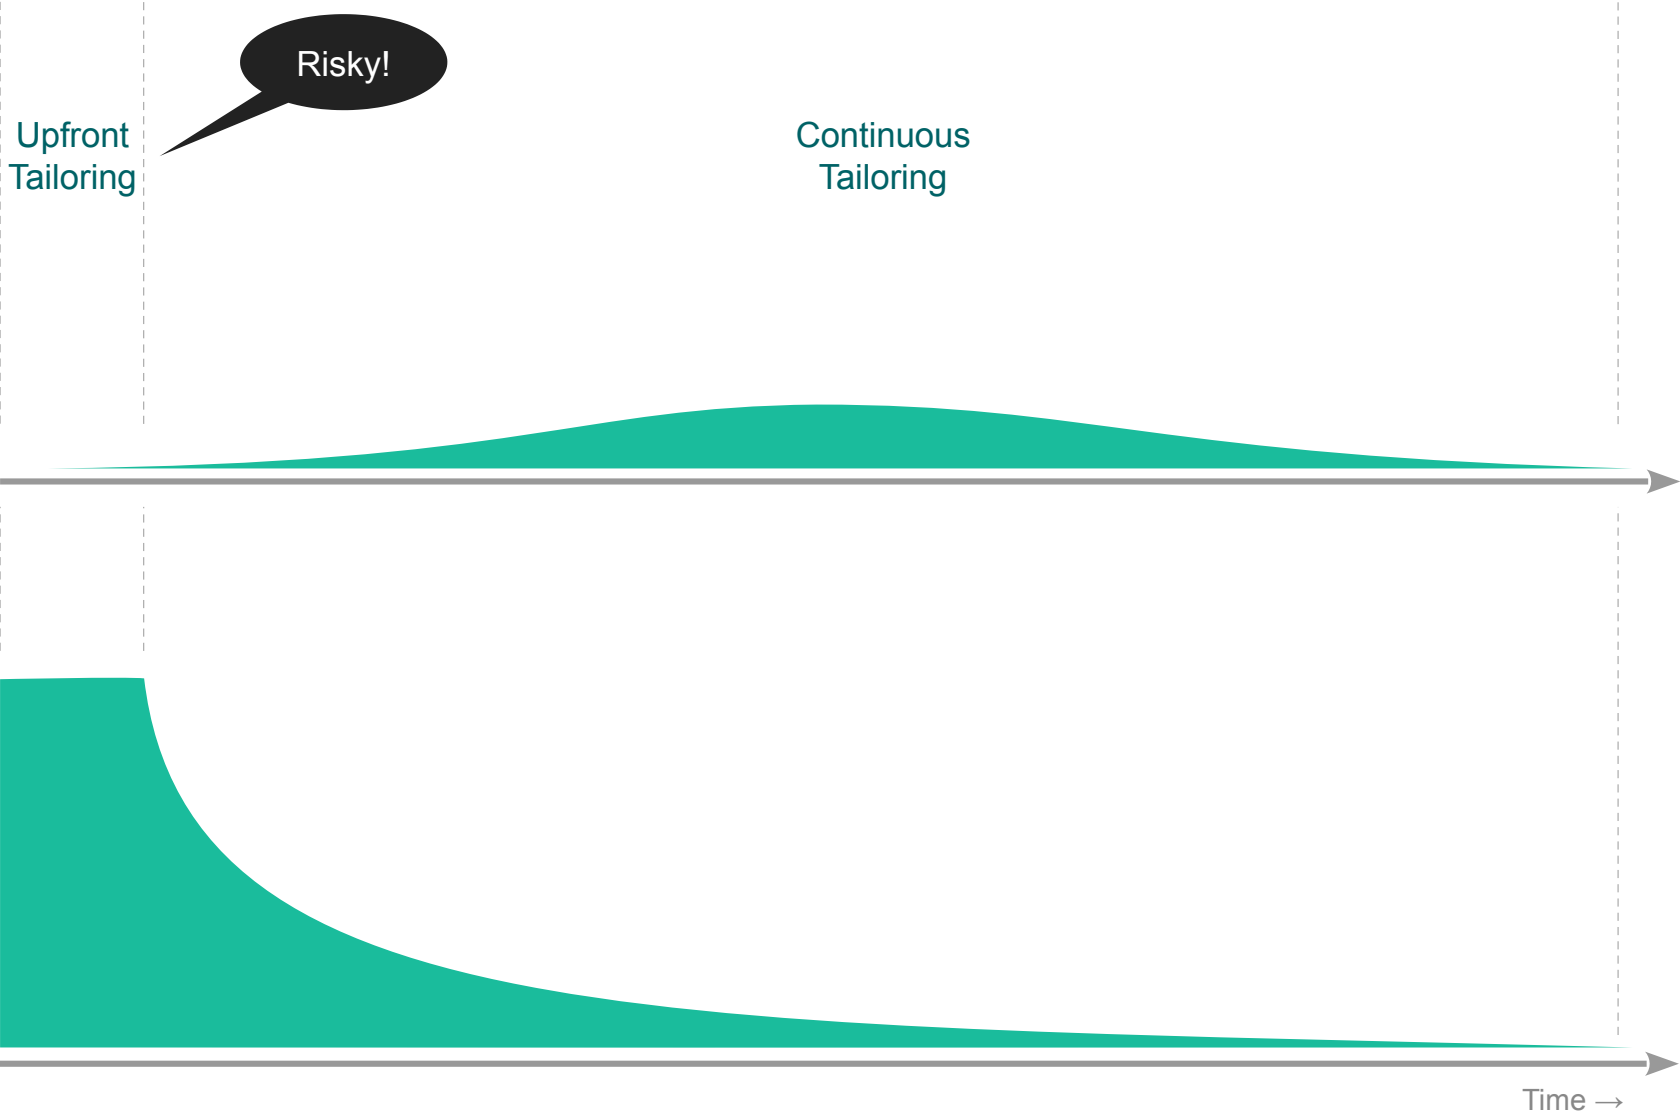

Minimalist Systems

P3.express
micro.P3.express
Etc.

Upfront
Tailoring

Risky!

Continuous
Tailoring

Tailoring effort ↑

Maximalist Systems

PRINCE2®
DSDM®
Etc.

Time →

Upfront Tailoring

Risky!

Continuous Tailoring

Always necessary

Minimalist Systems

P3.express
micro.P3.express
Etc.



Tailoring effort ↑

Maximalist Systems

PRINCE2®
DSDM®
Etc.



Time →

Minimalist Systems

P3.express
micro.P3.express
Etc.

Upfront
Tailoring

Risky!

Continuous
Tailoring

Always
necessary


Adaptation



Maximalist Systems

PRINCE2®
DSDM®
Etc.

Tailoring effort ↑

Time →

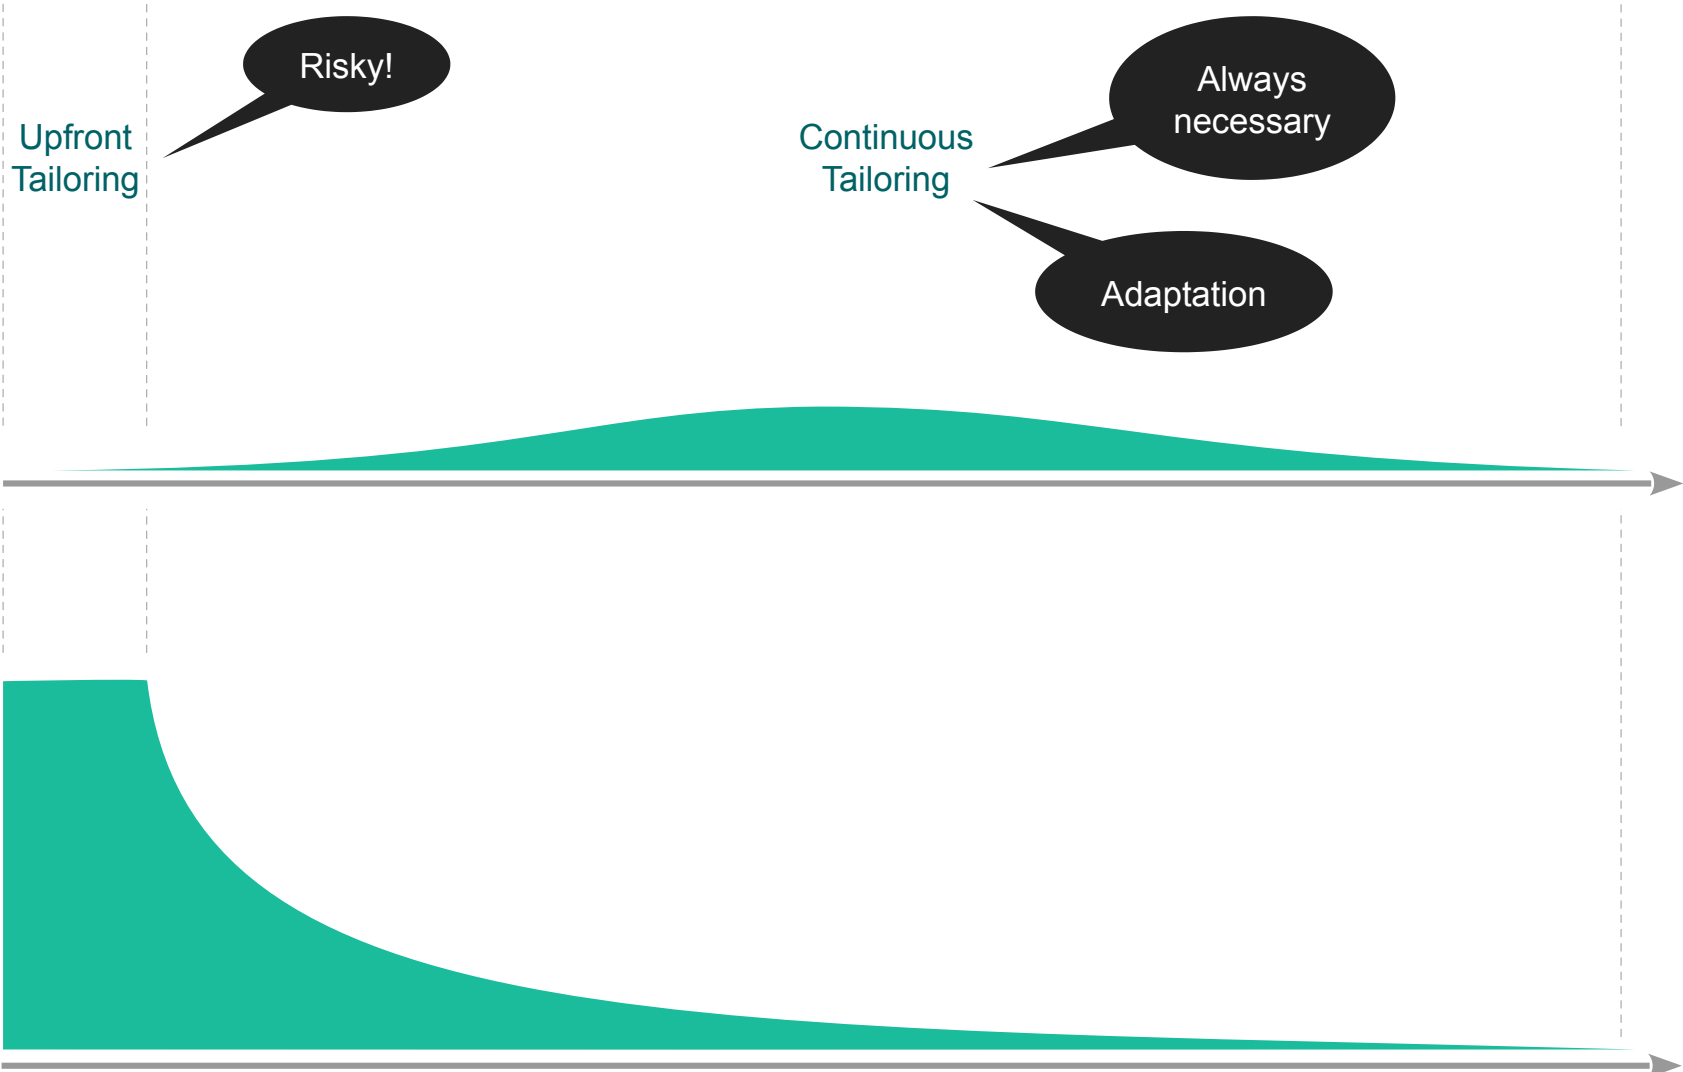

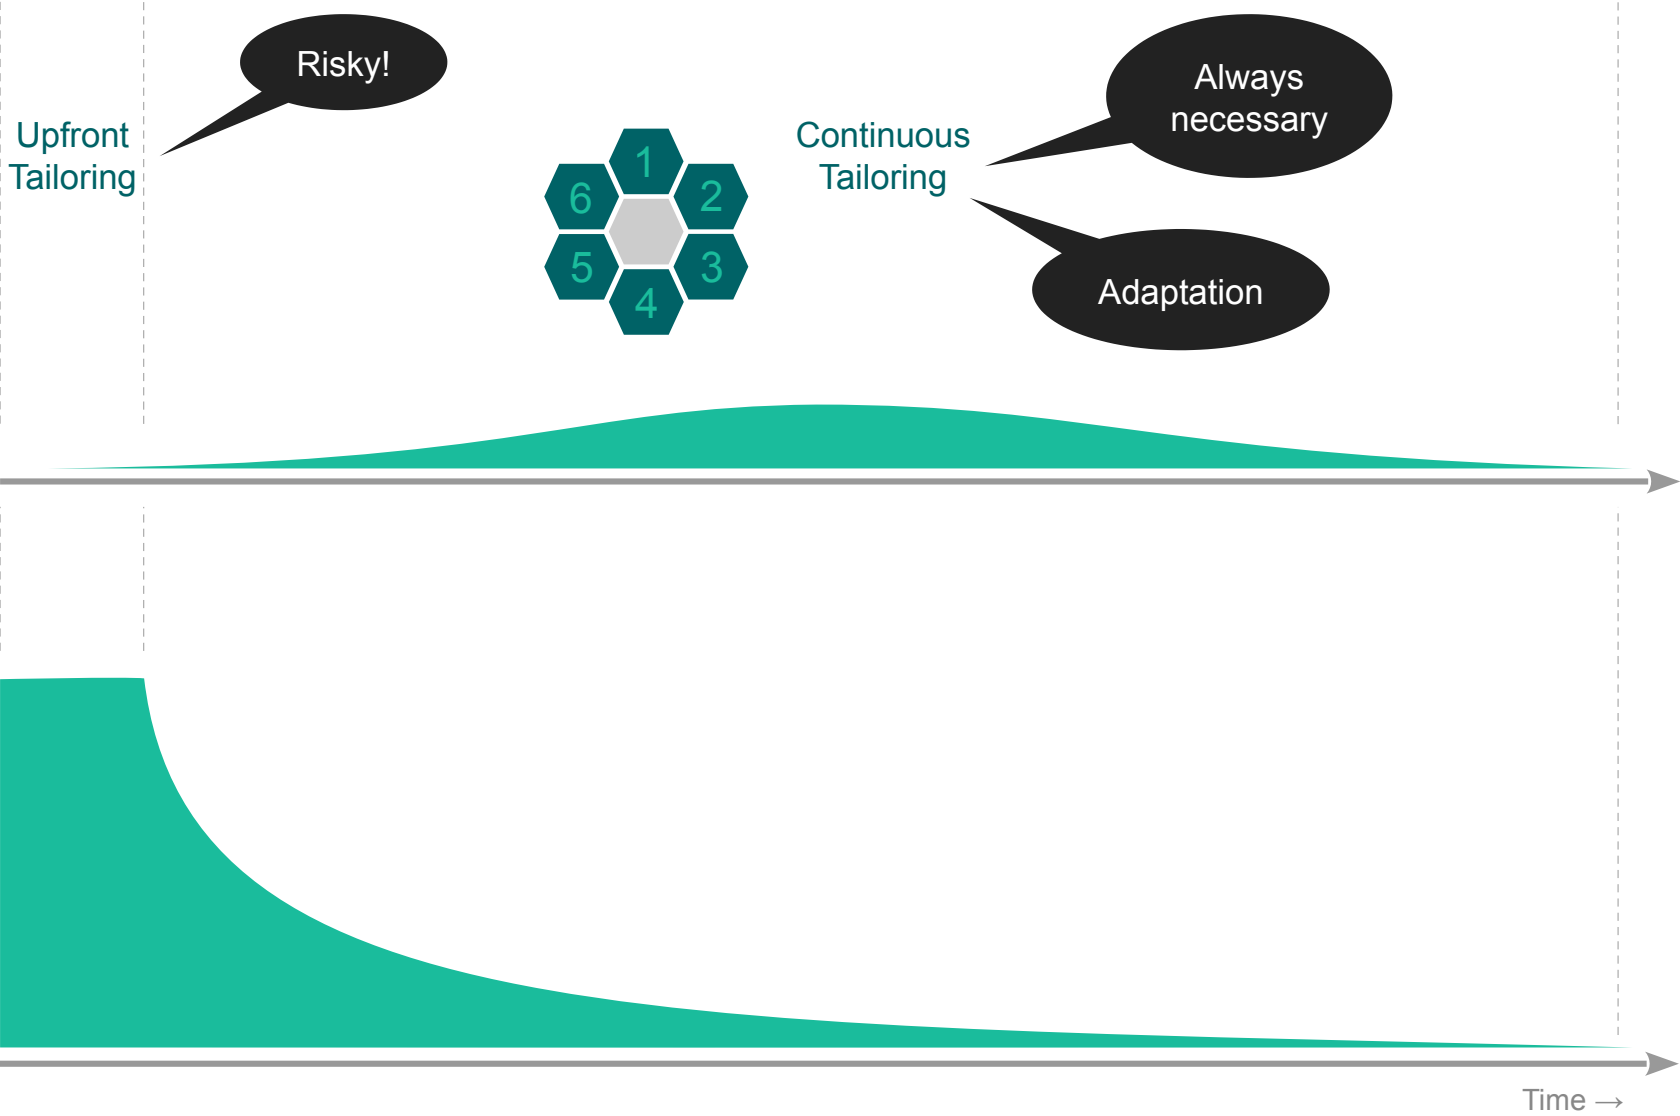

micro.P3.express

minimalist project management system for micro-projects

